


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

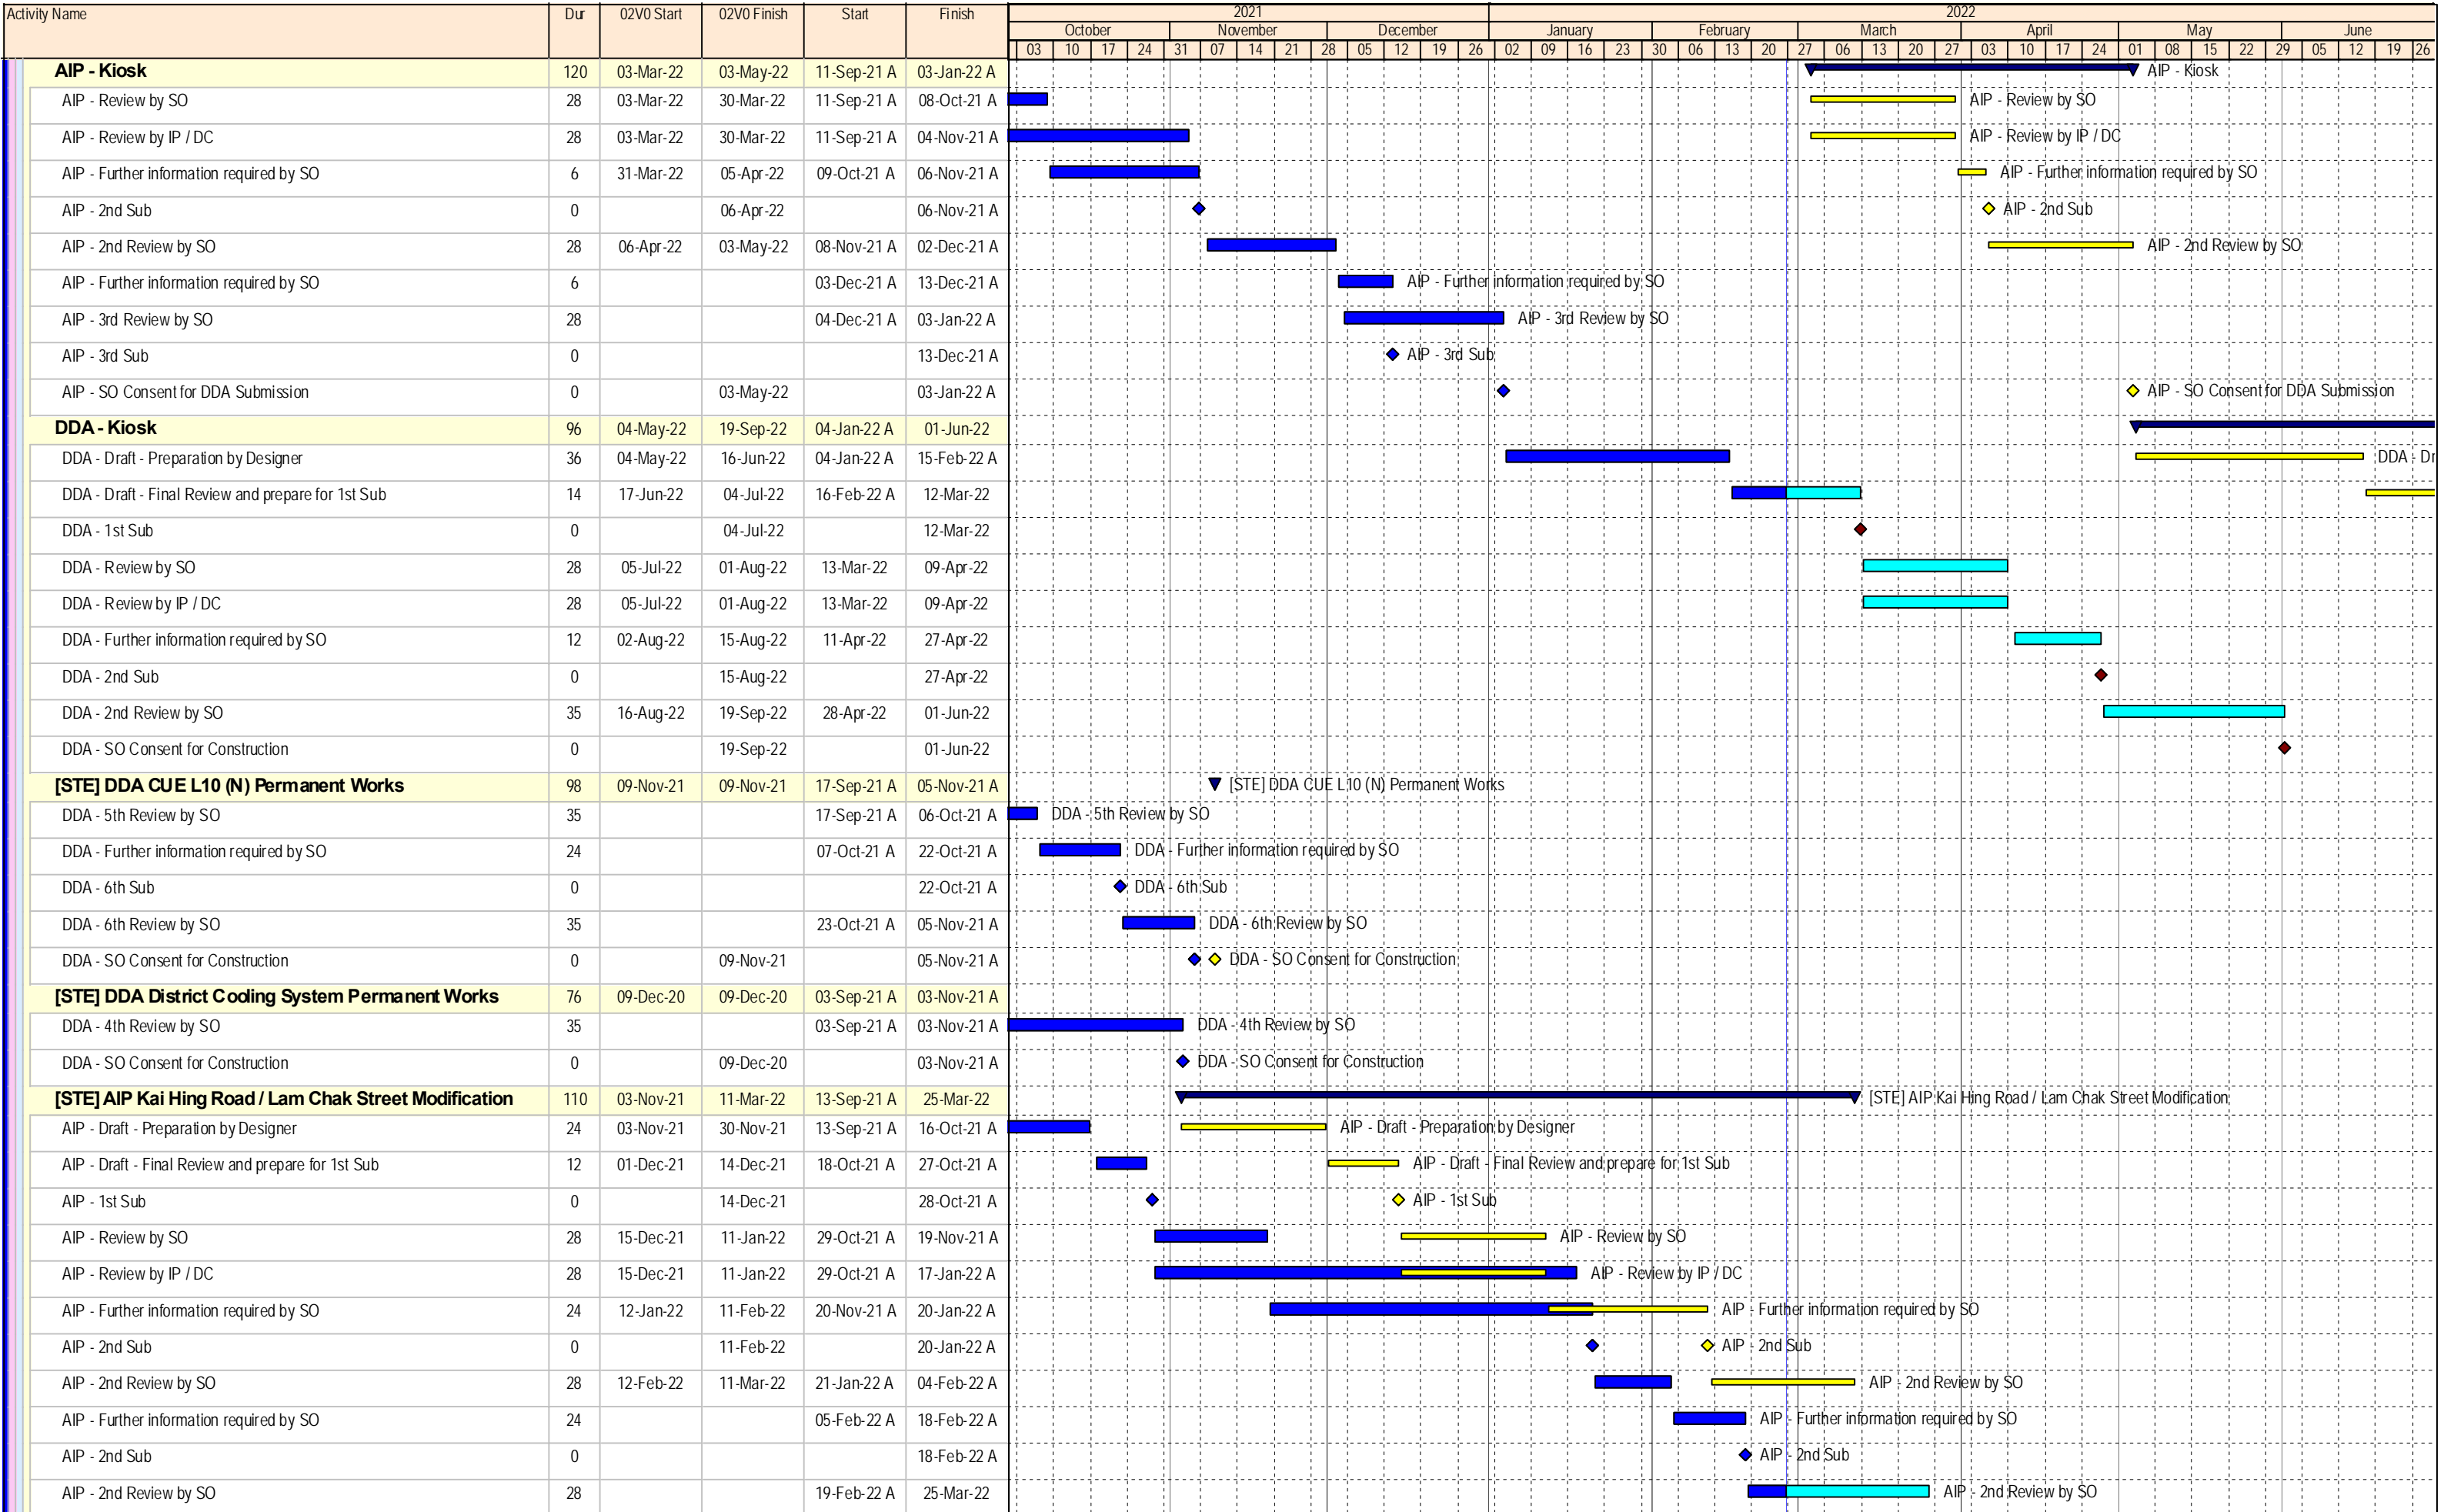


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

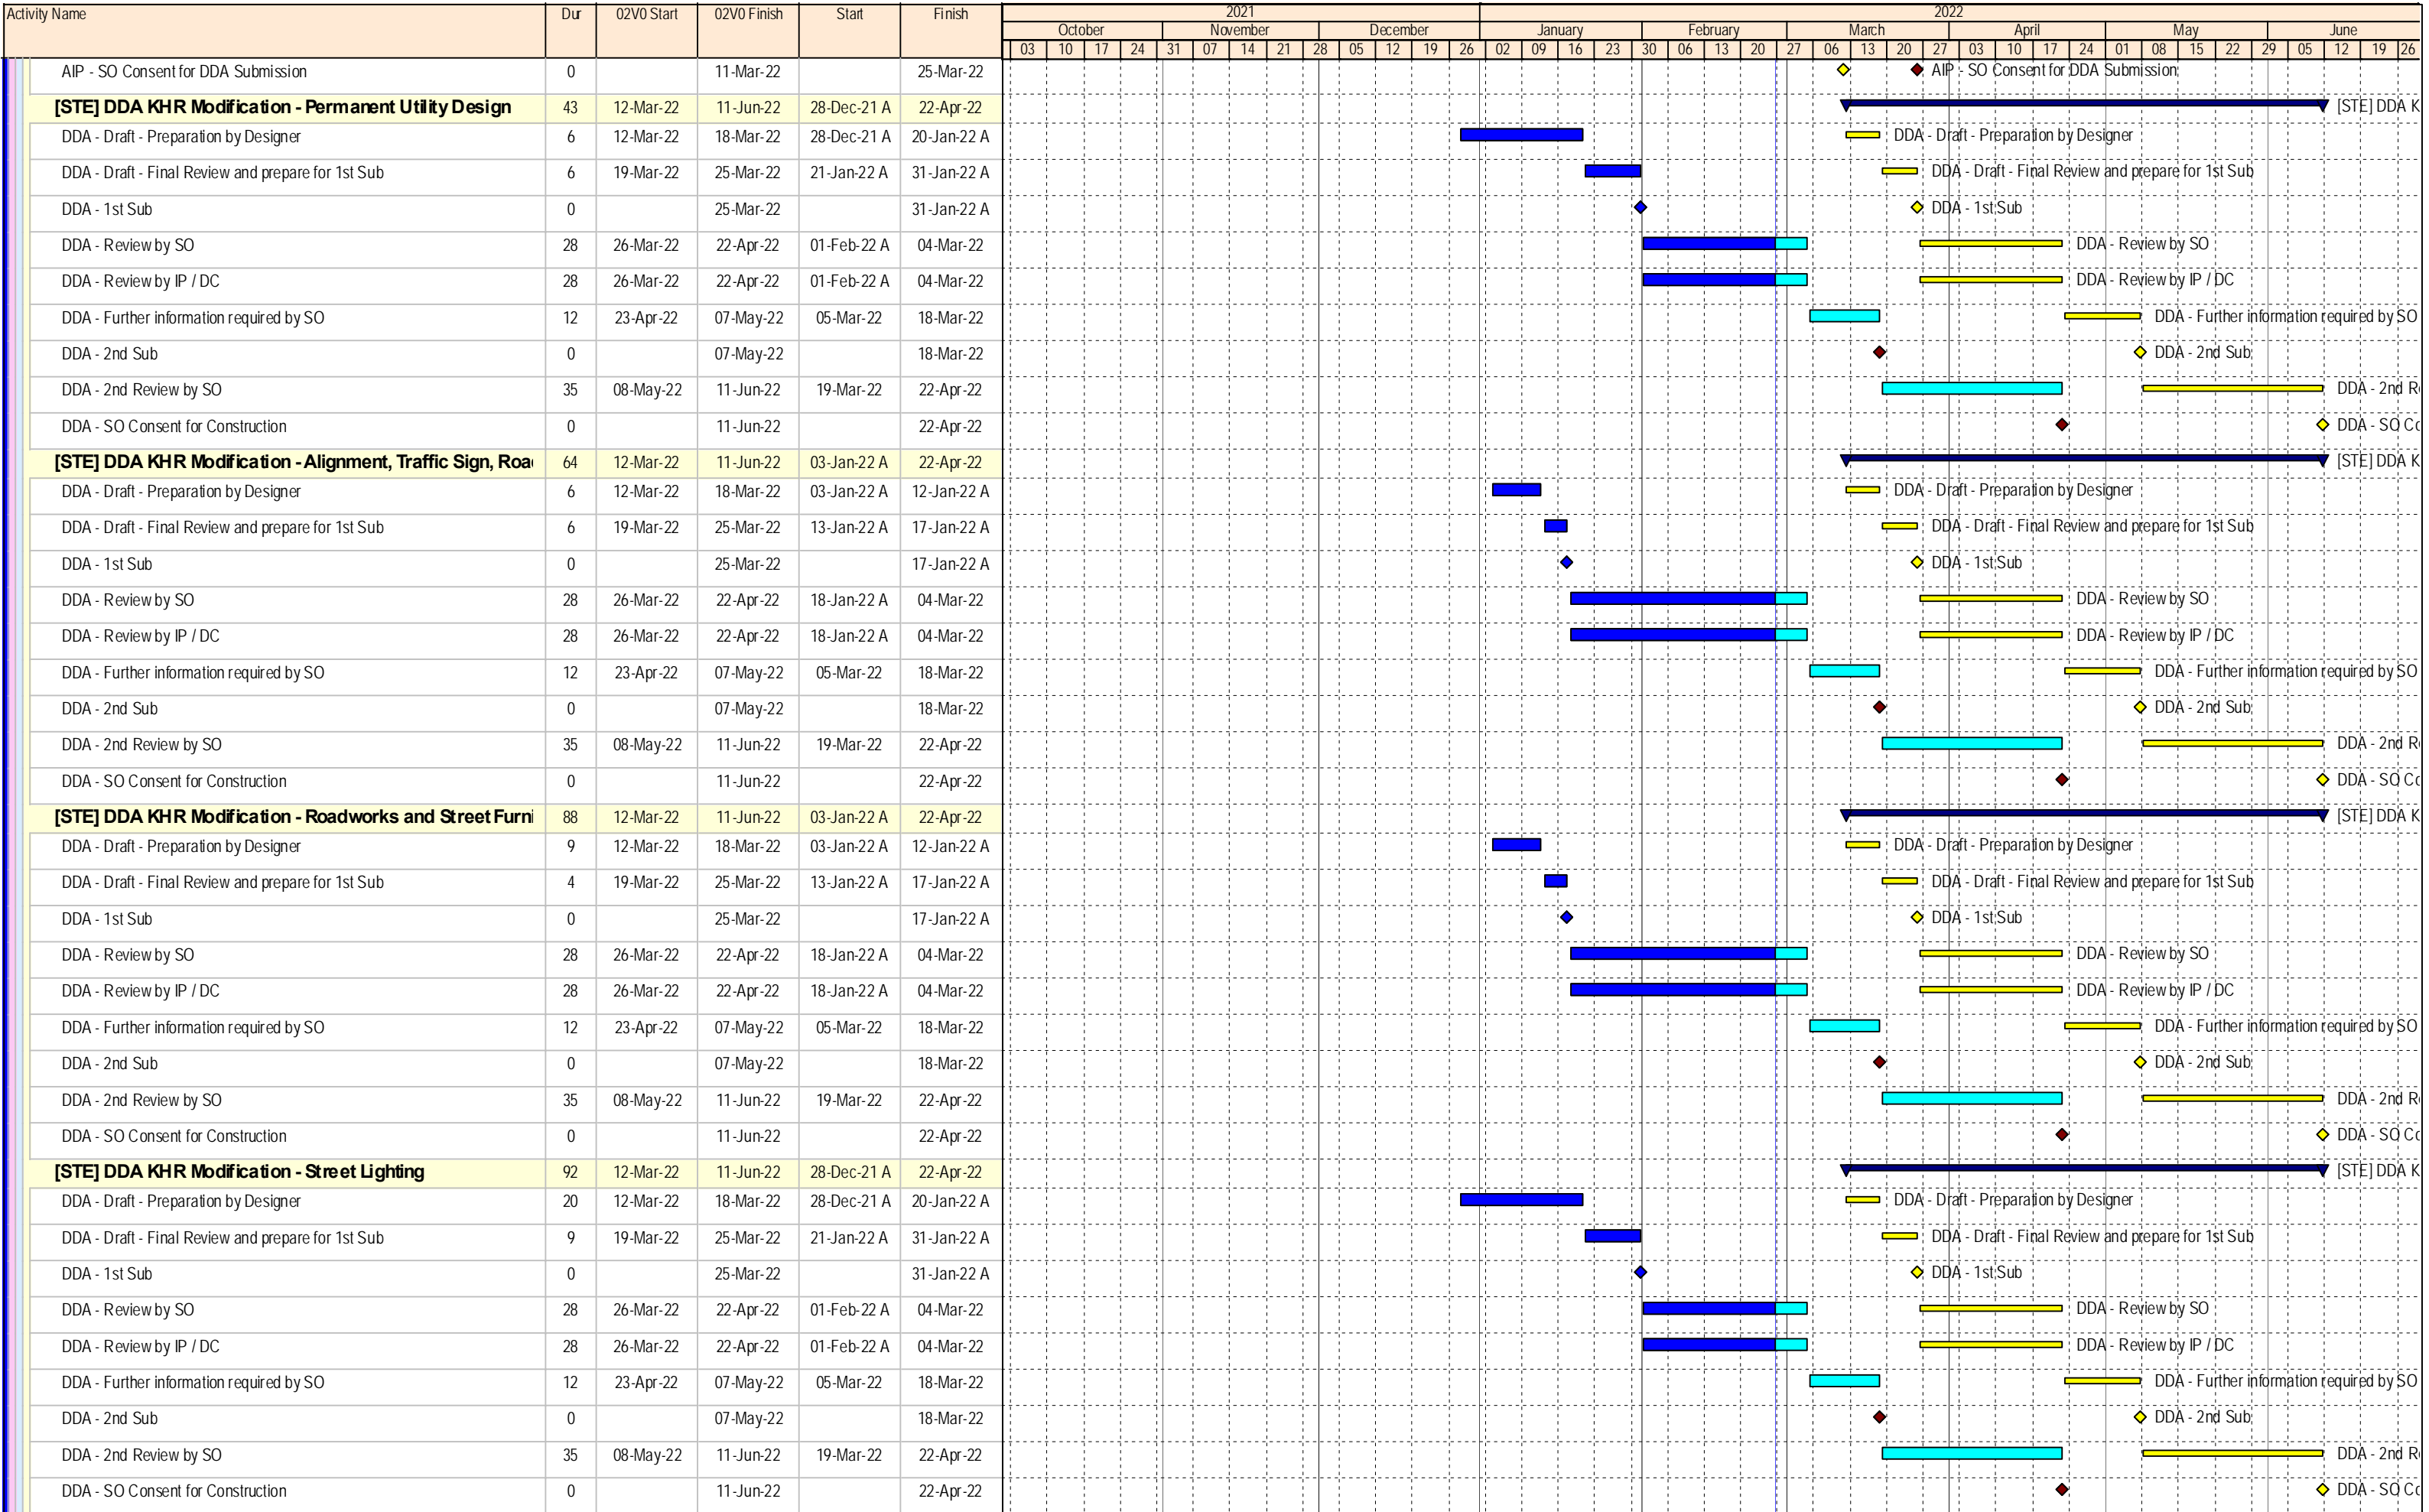


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

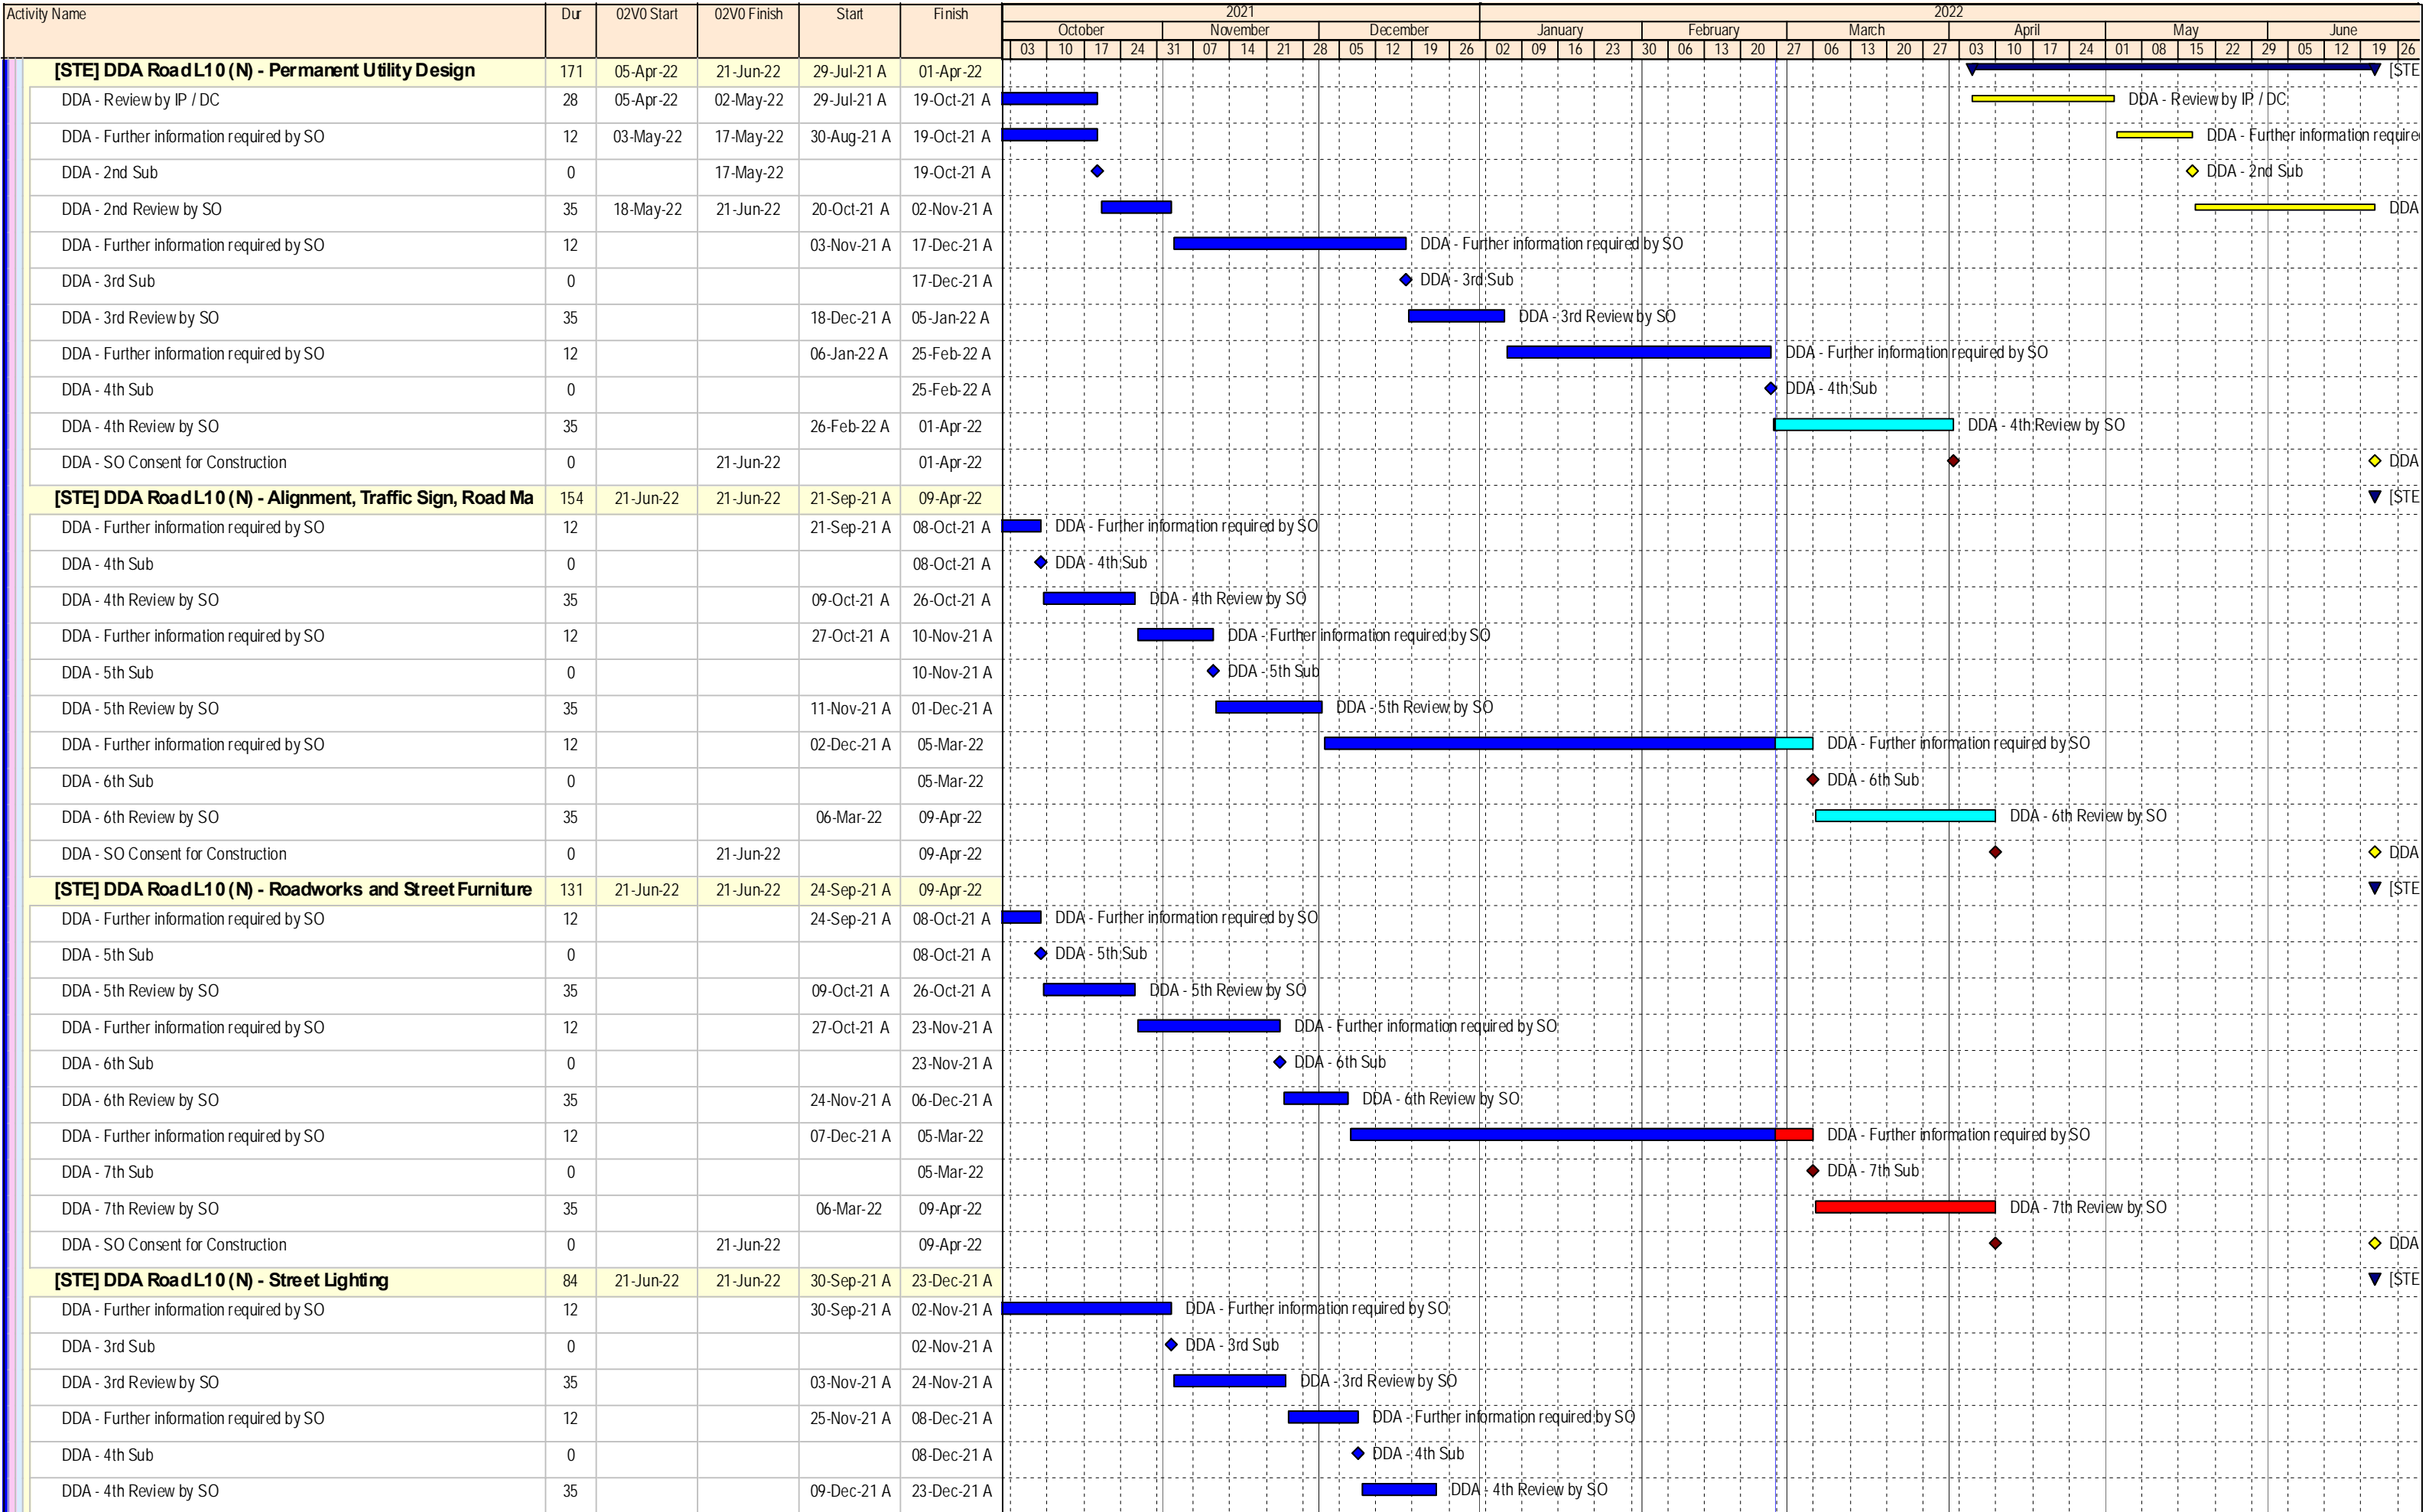


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

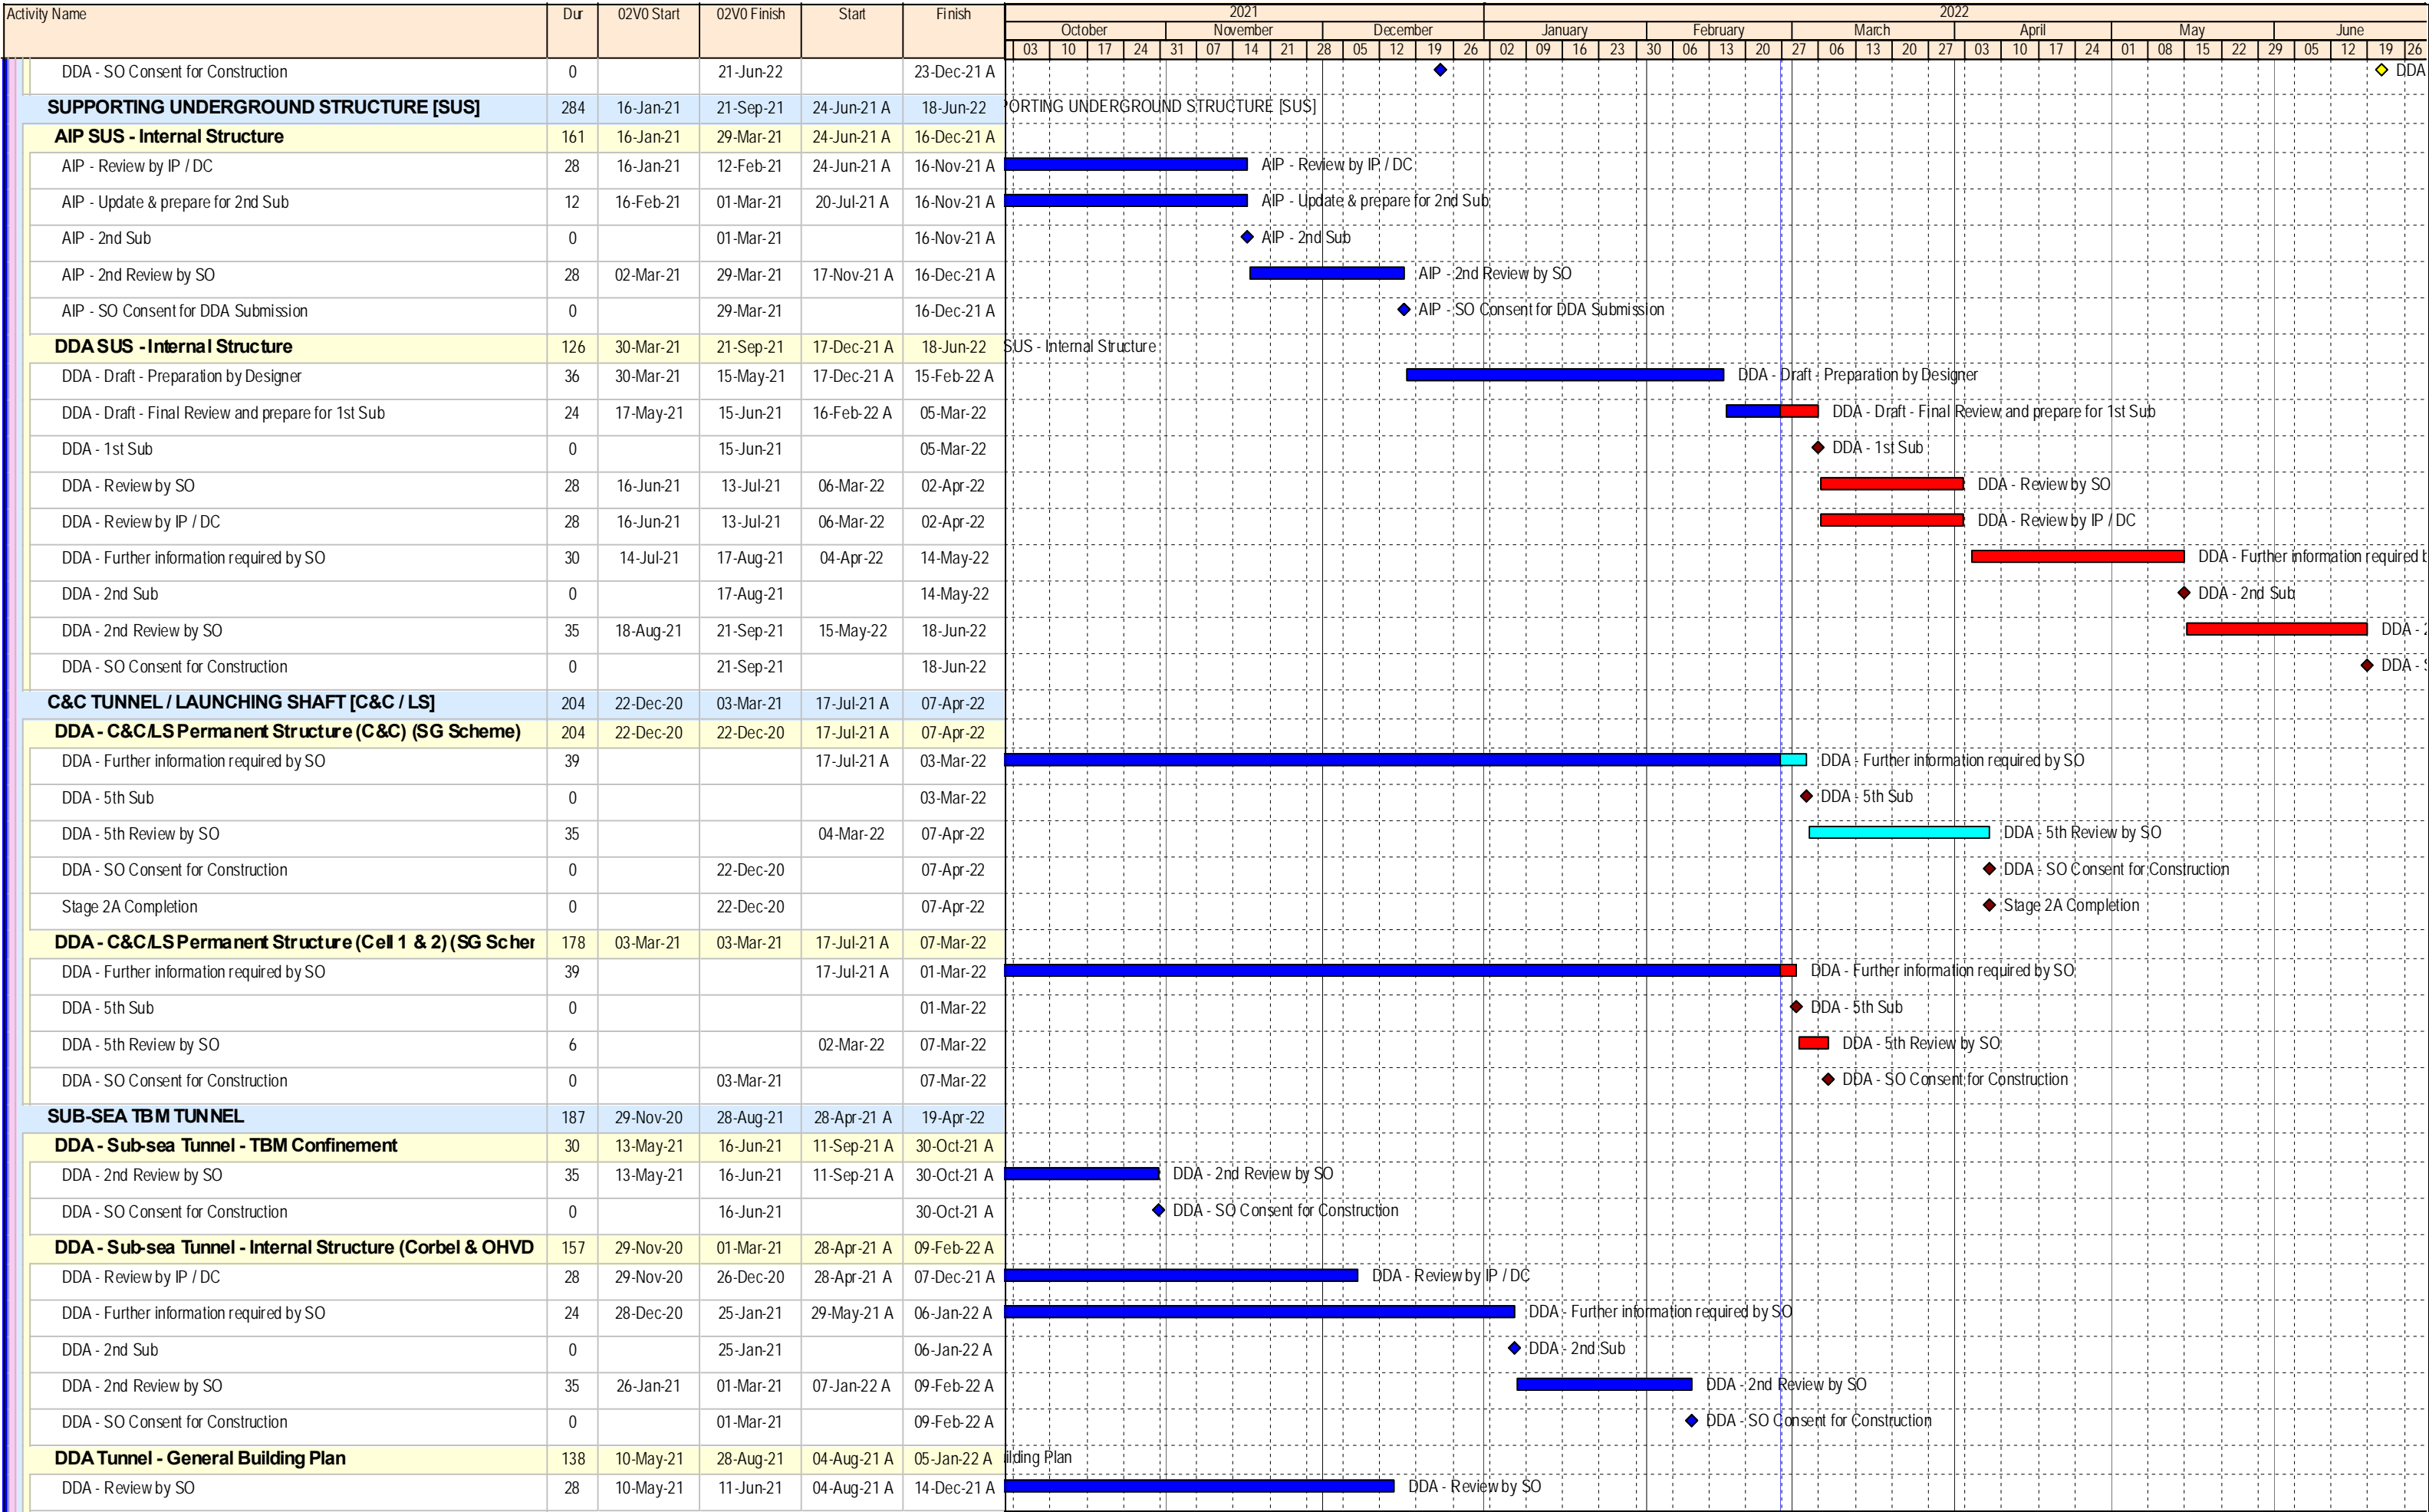


Page 6 of 30
Data Date: 26-Feb-22


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

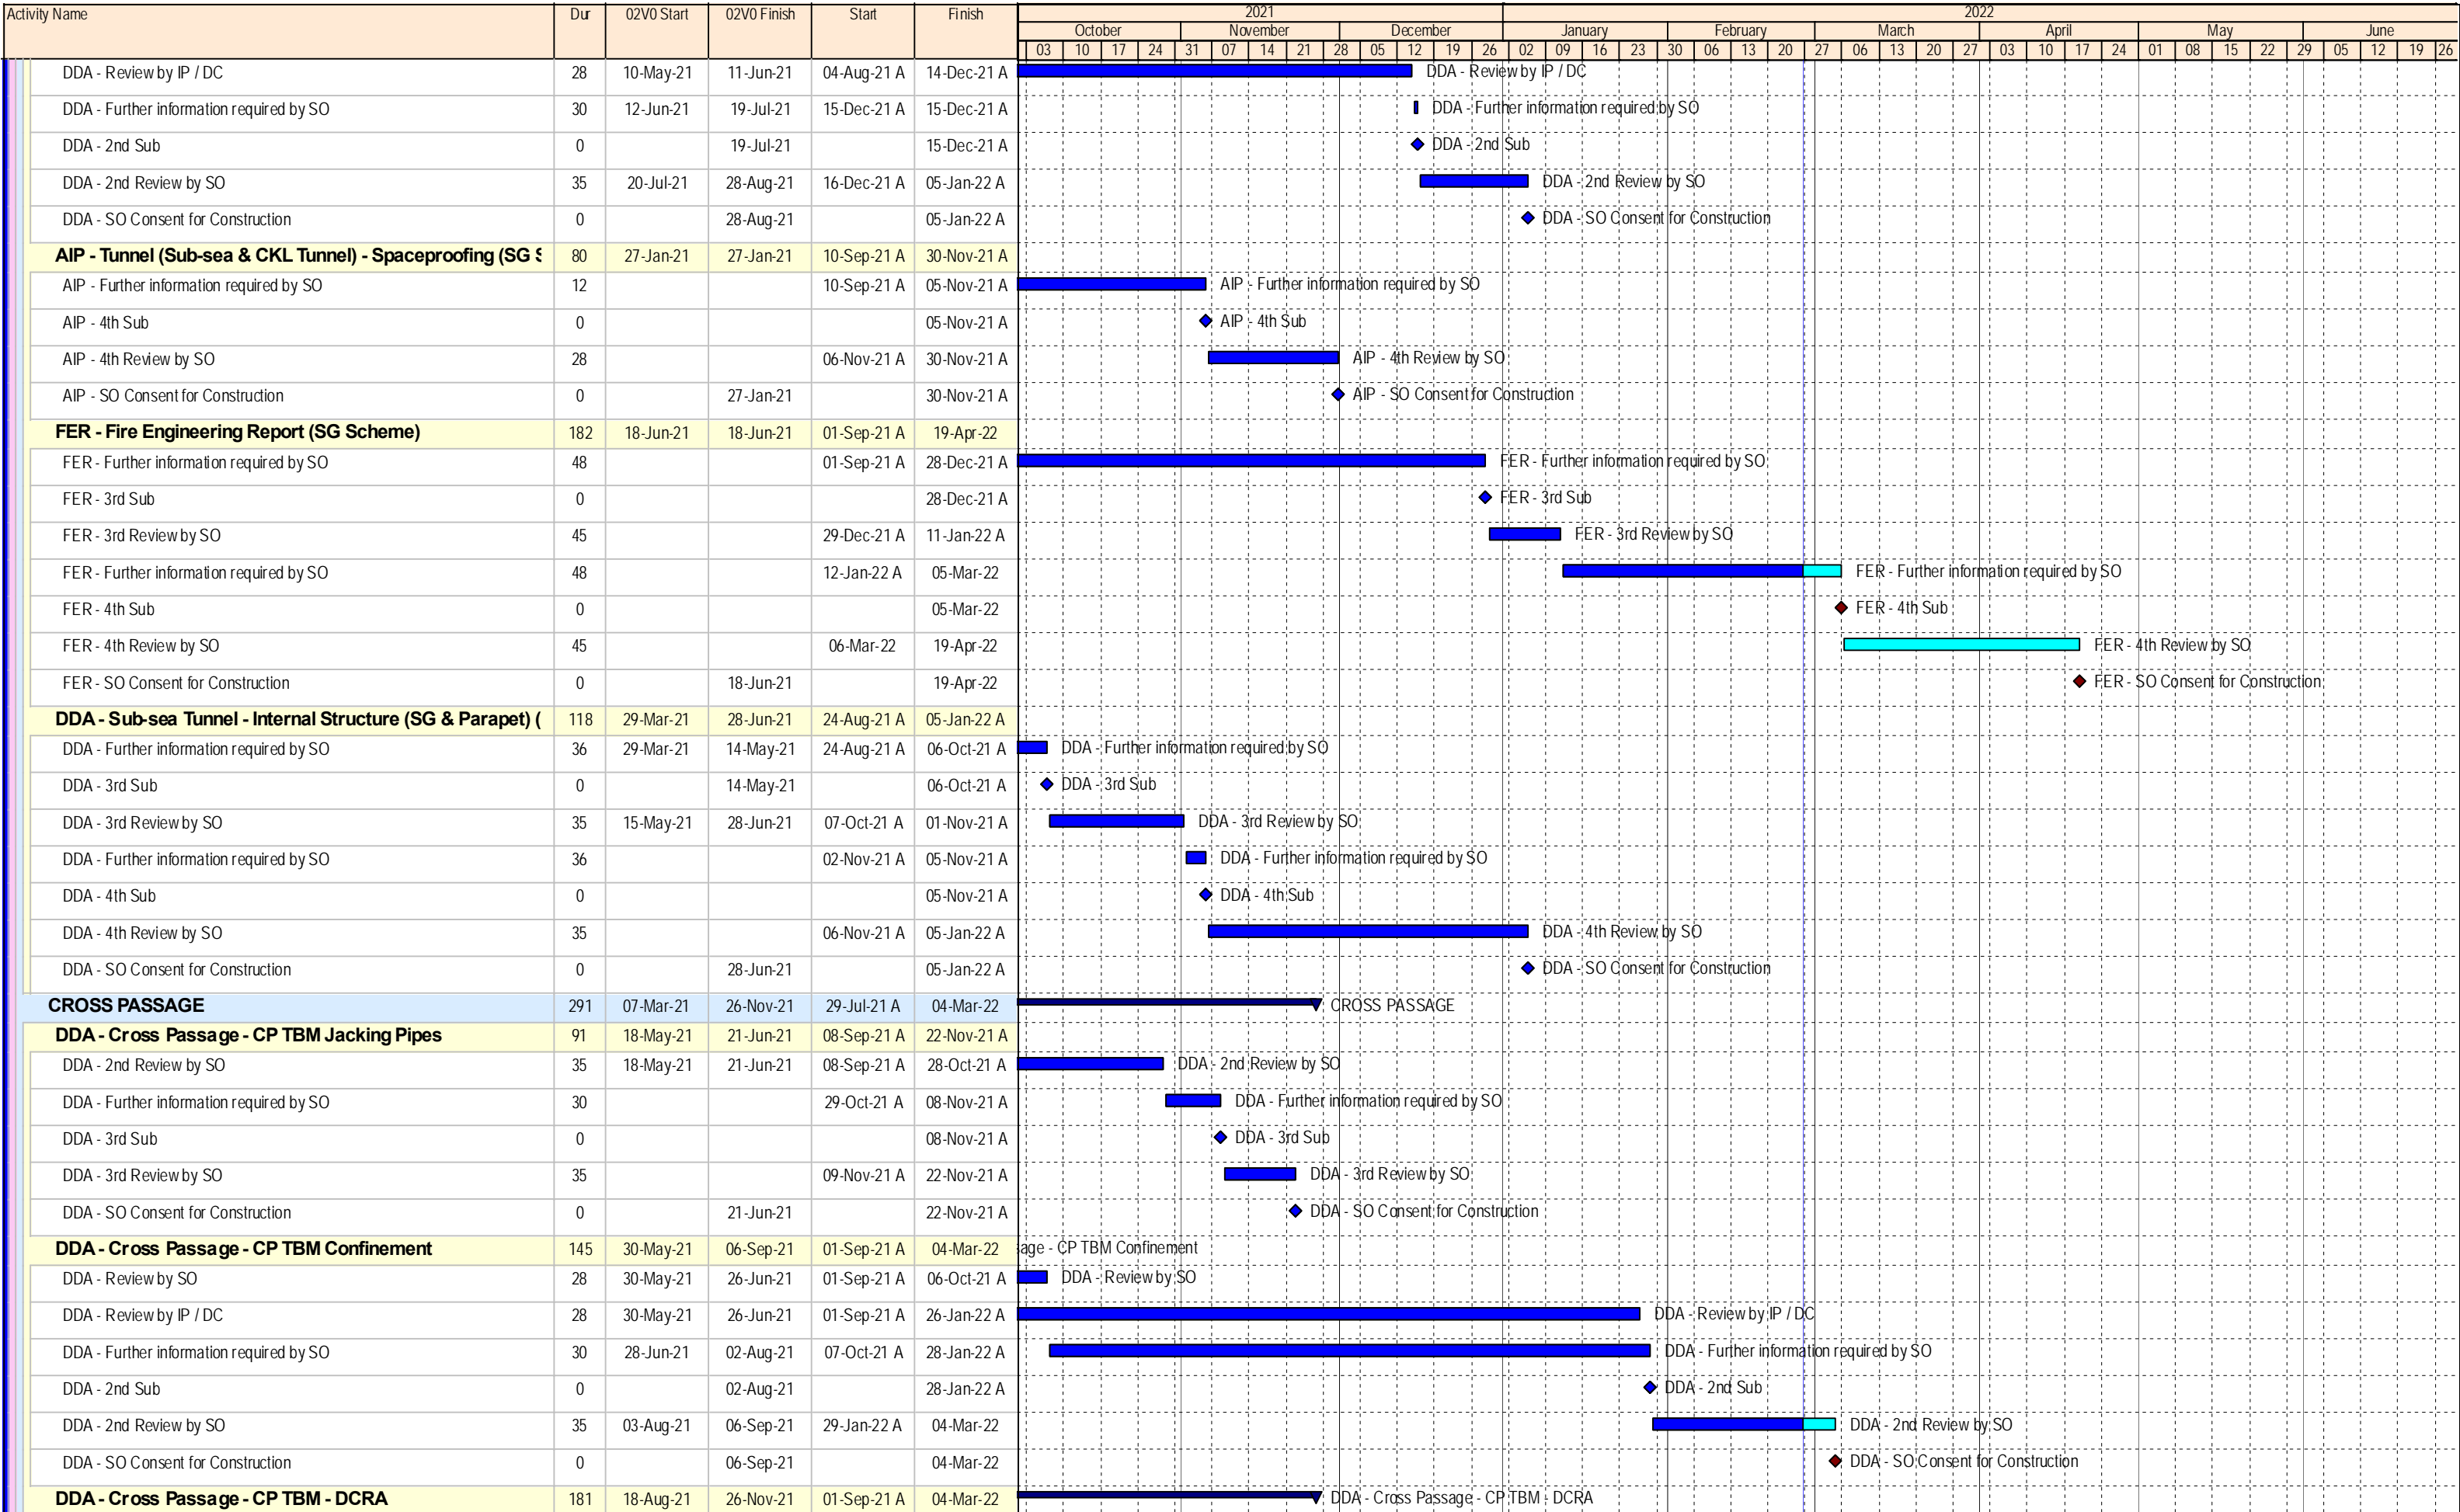


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

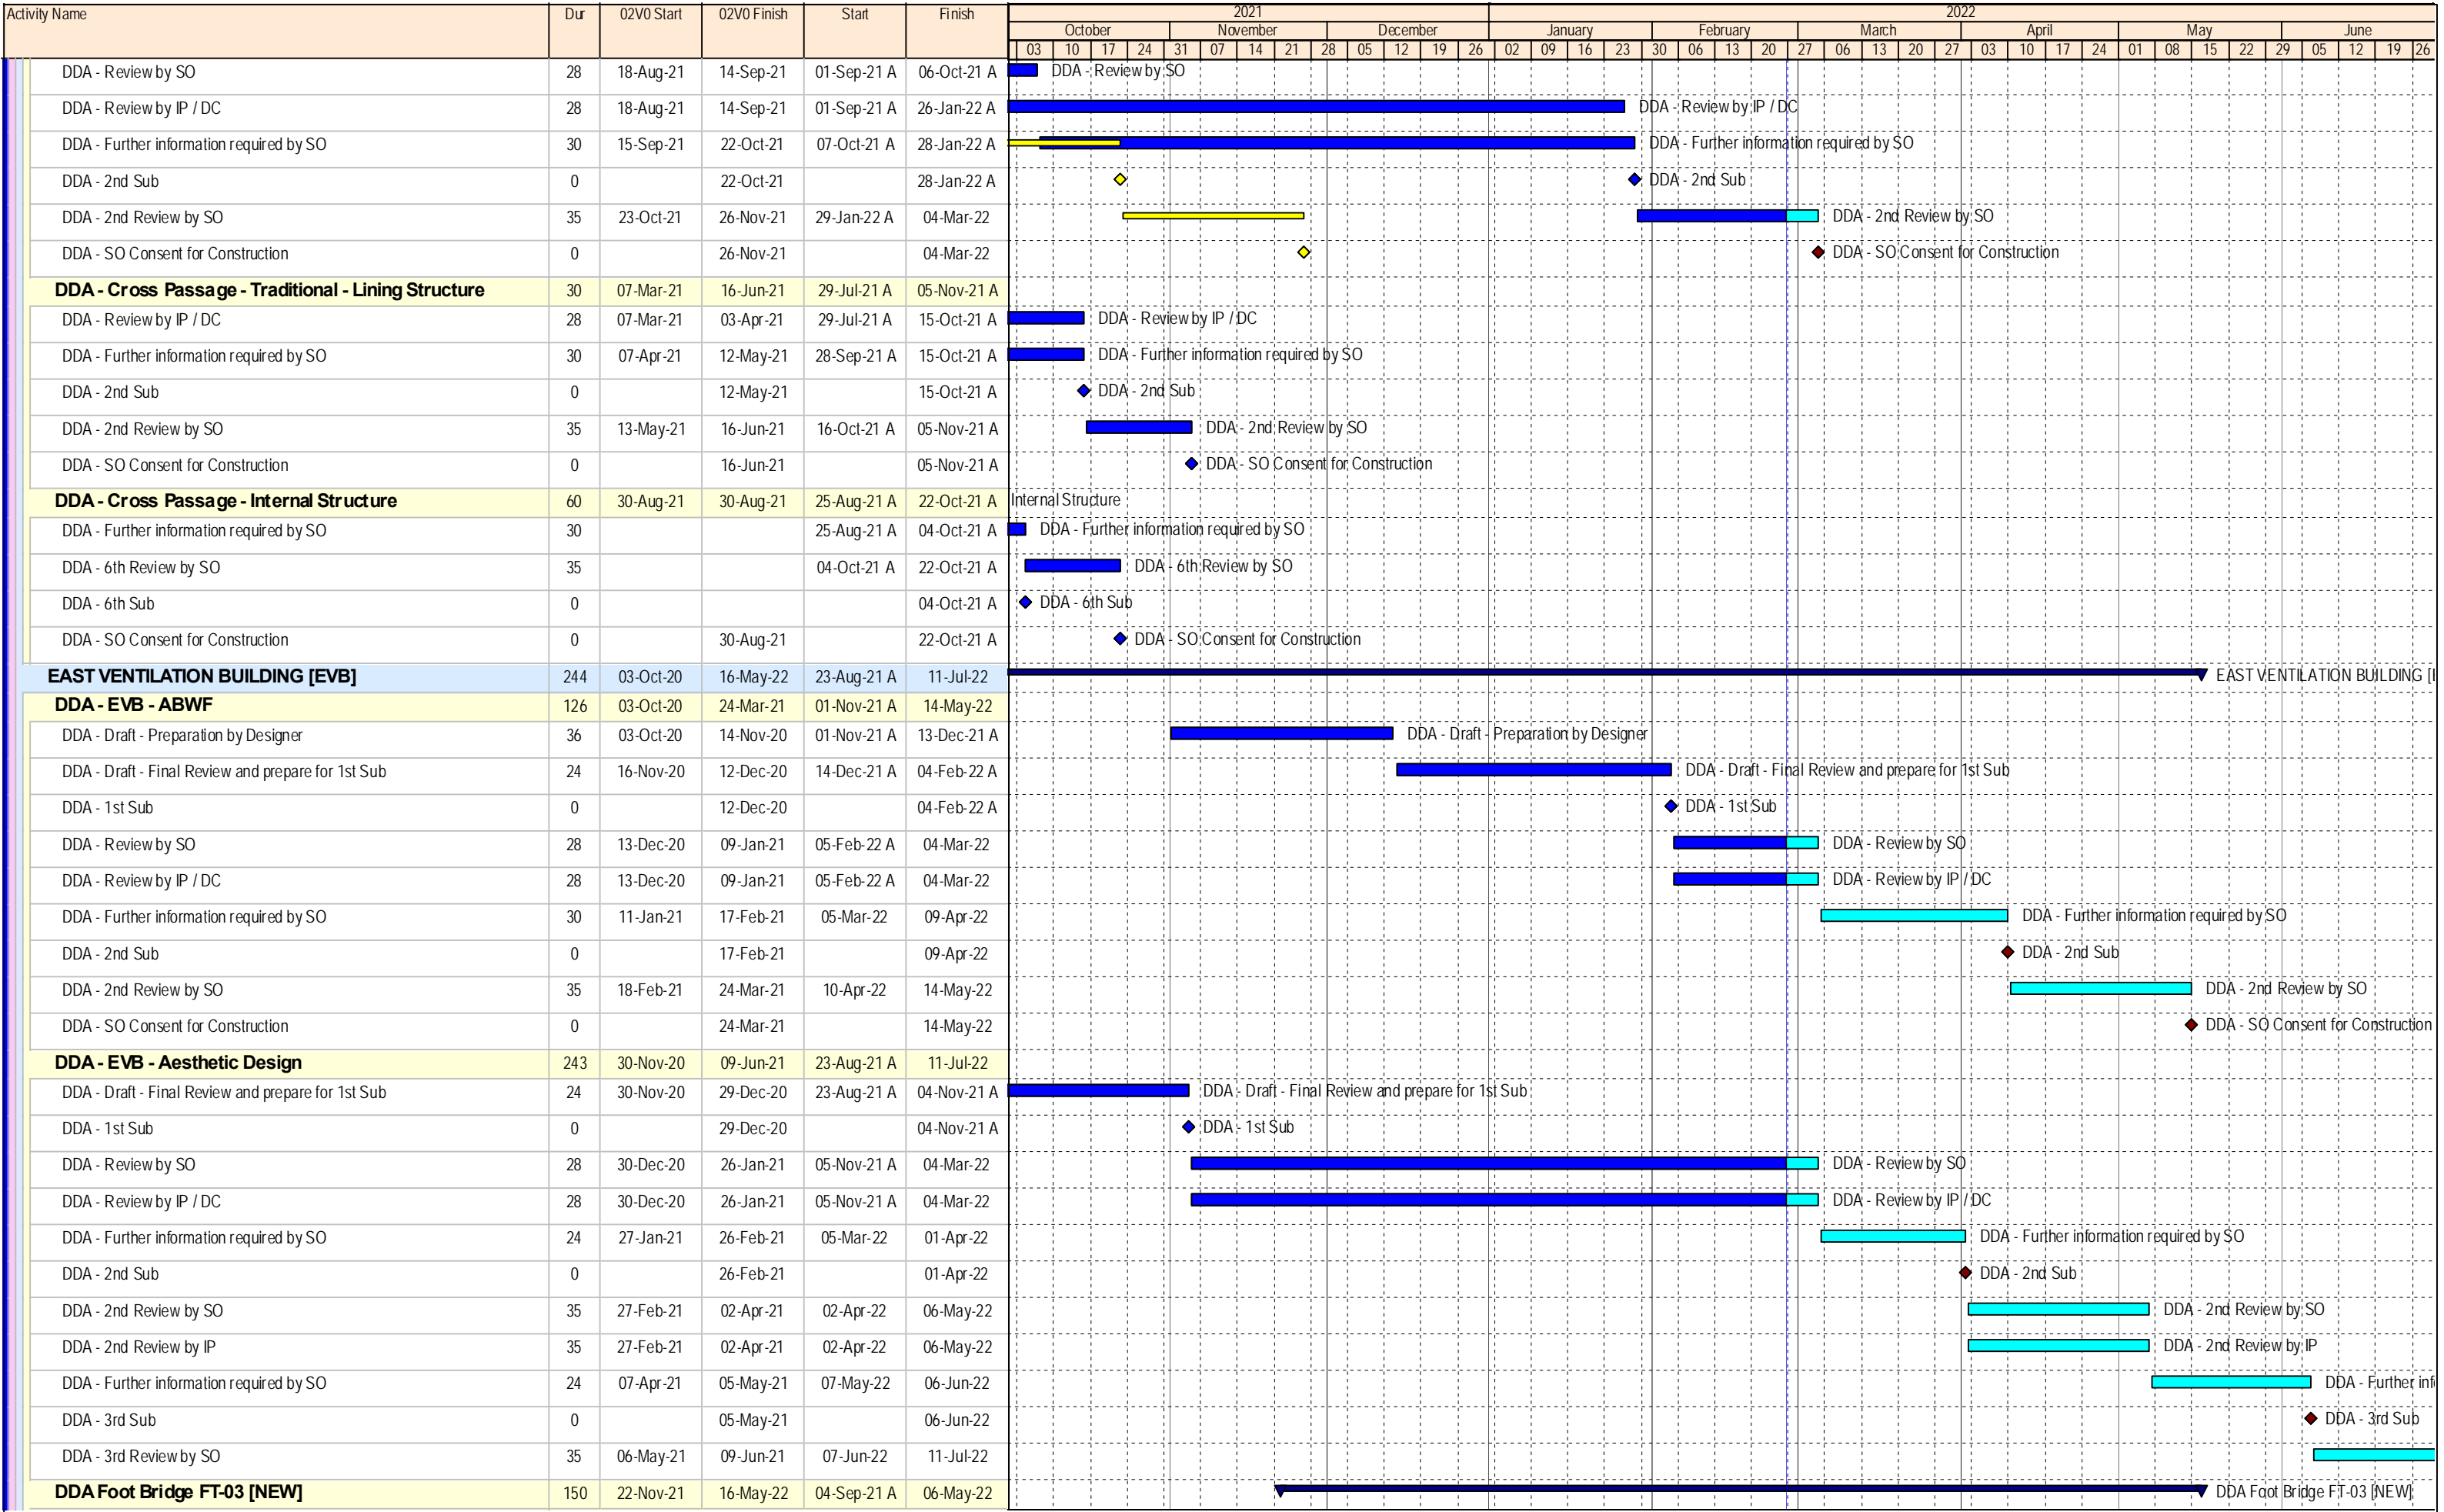


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

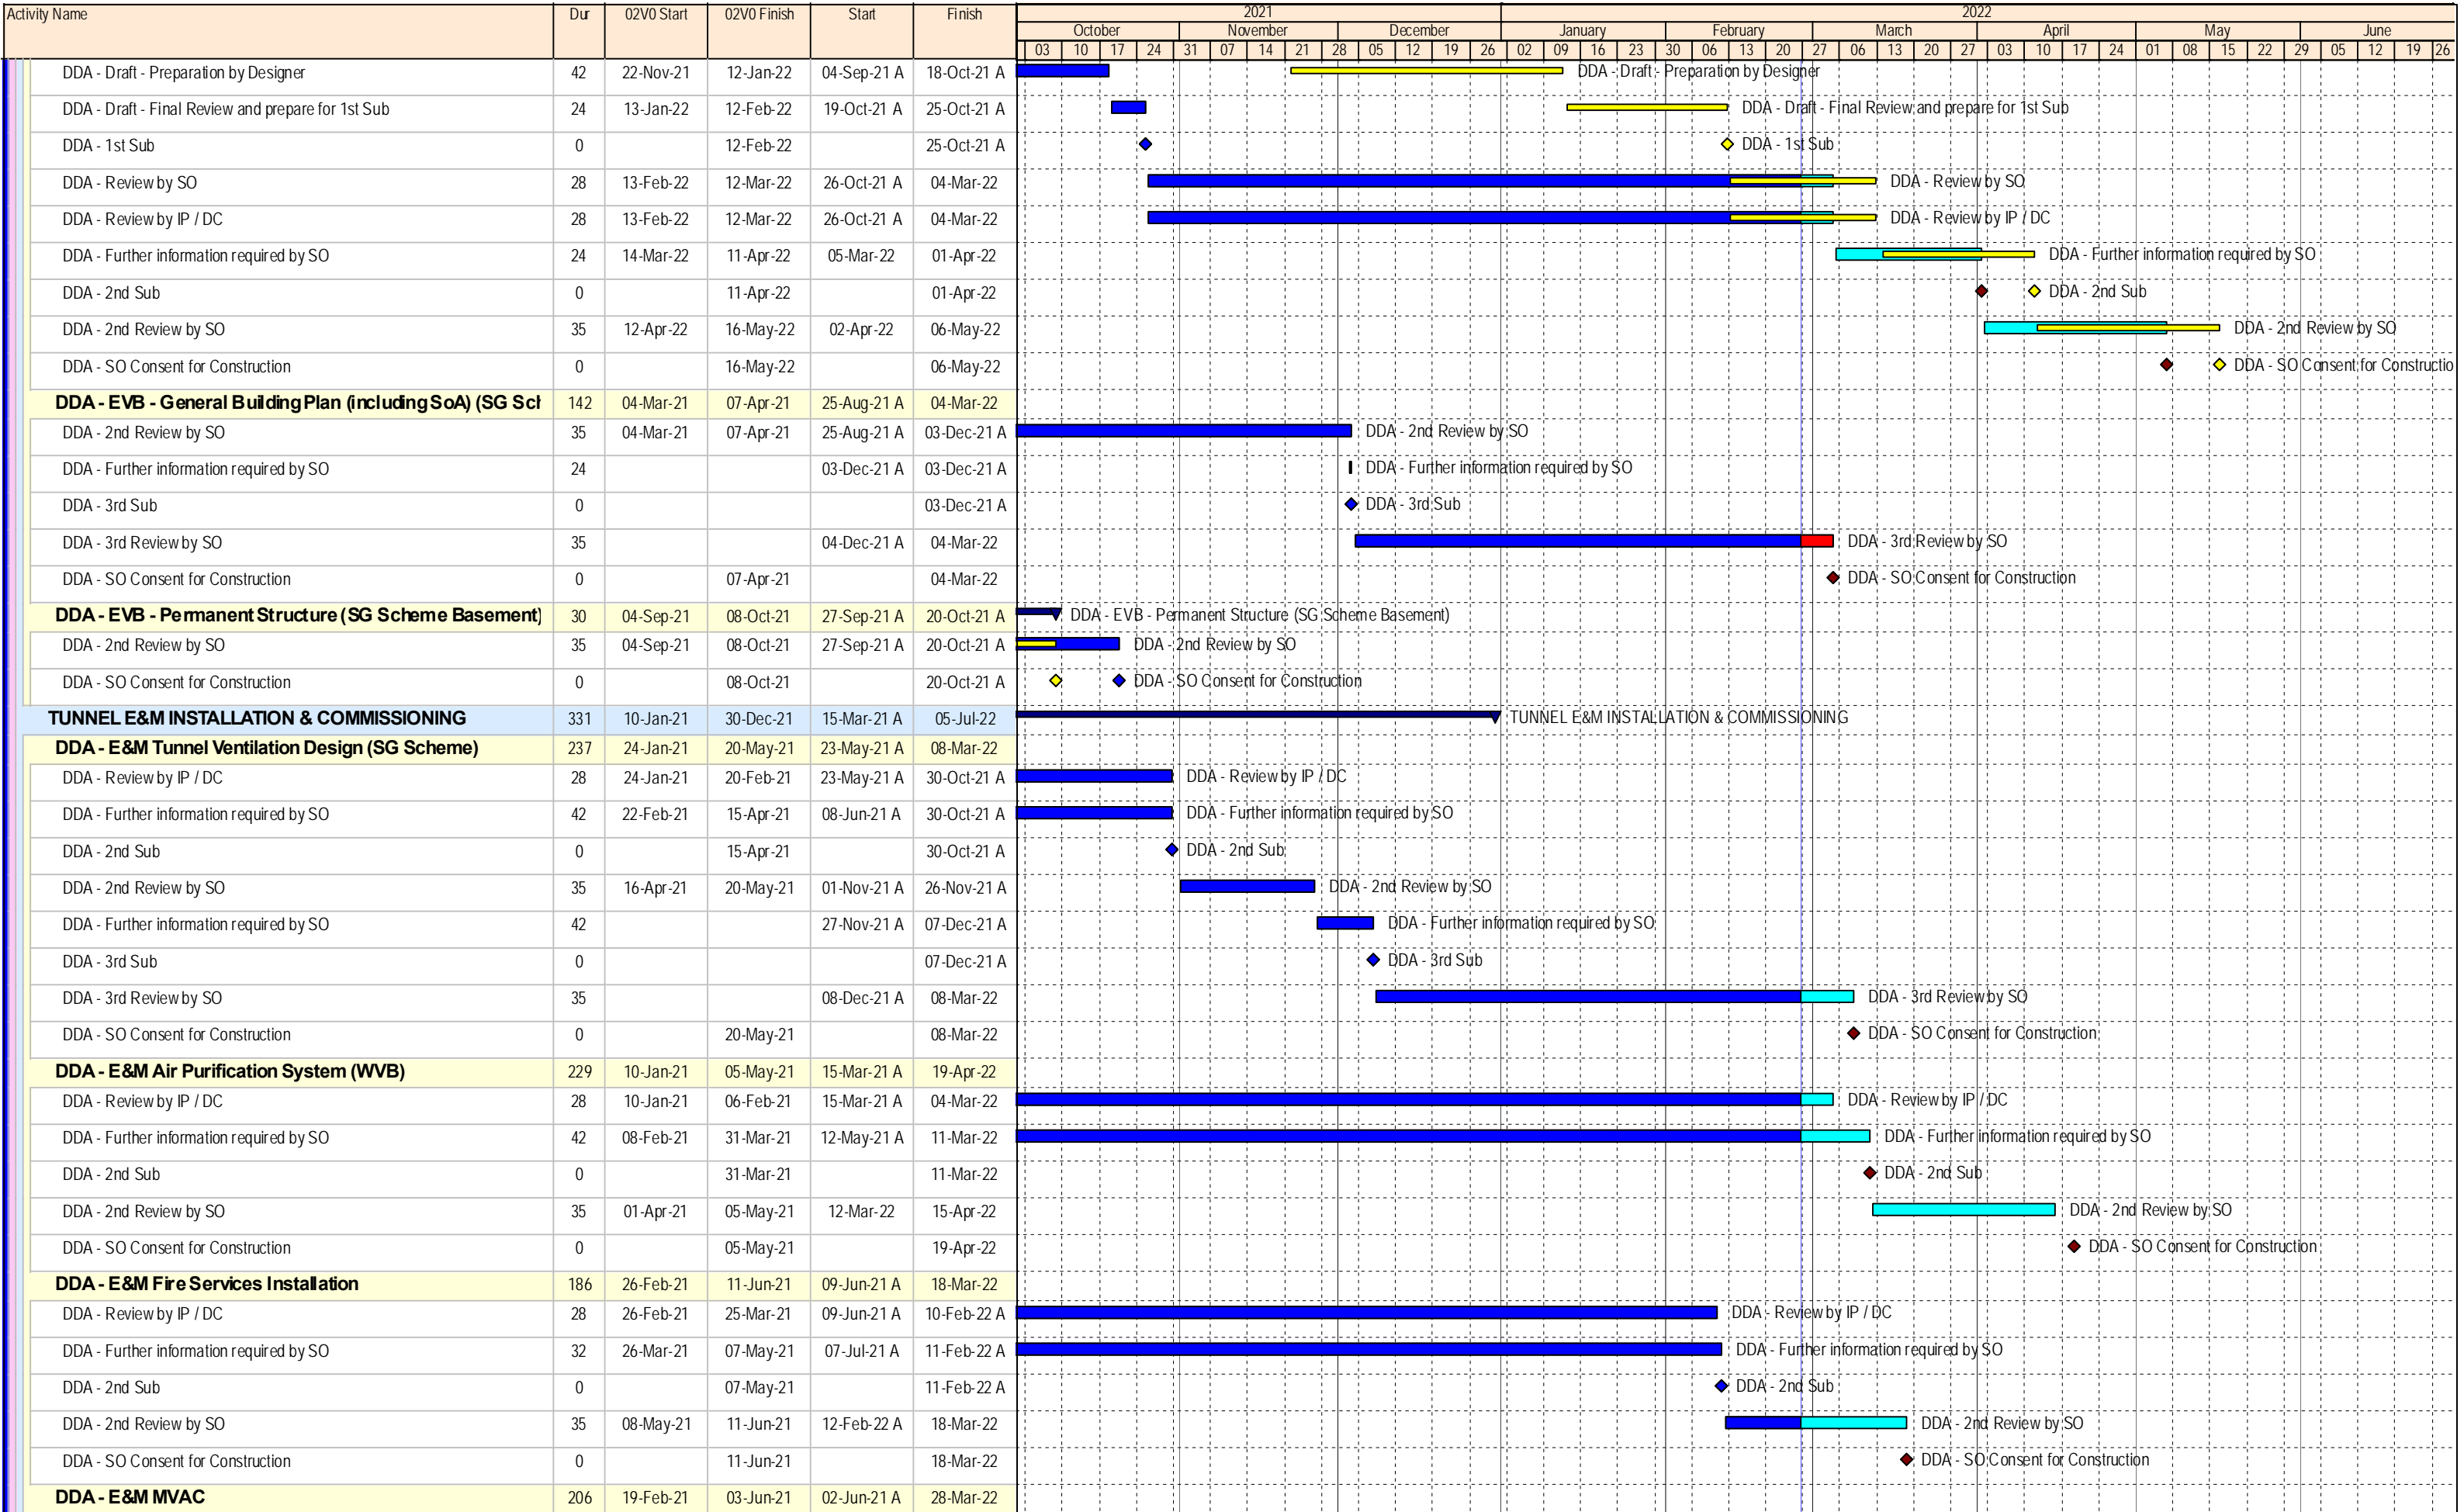


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

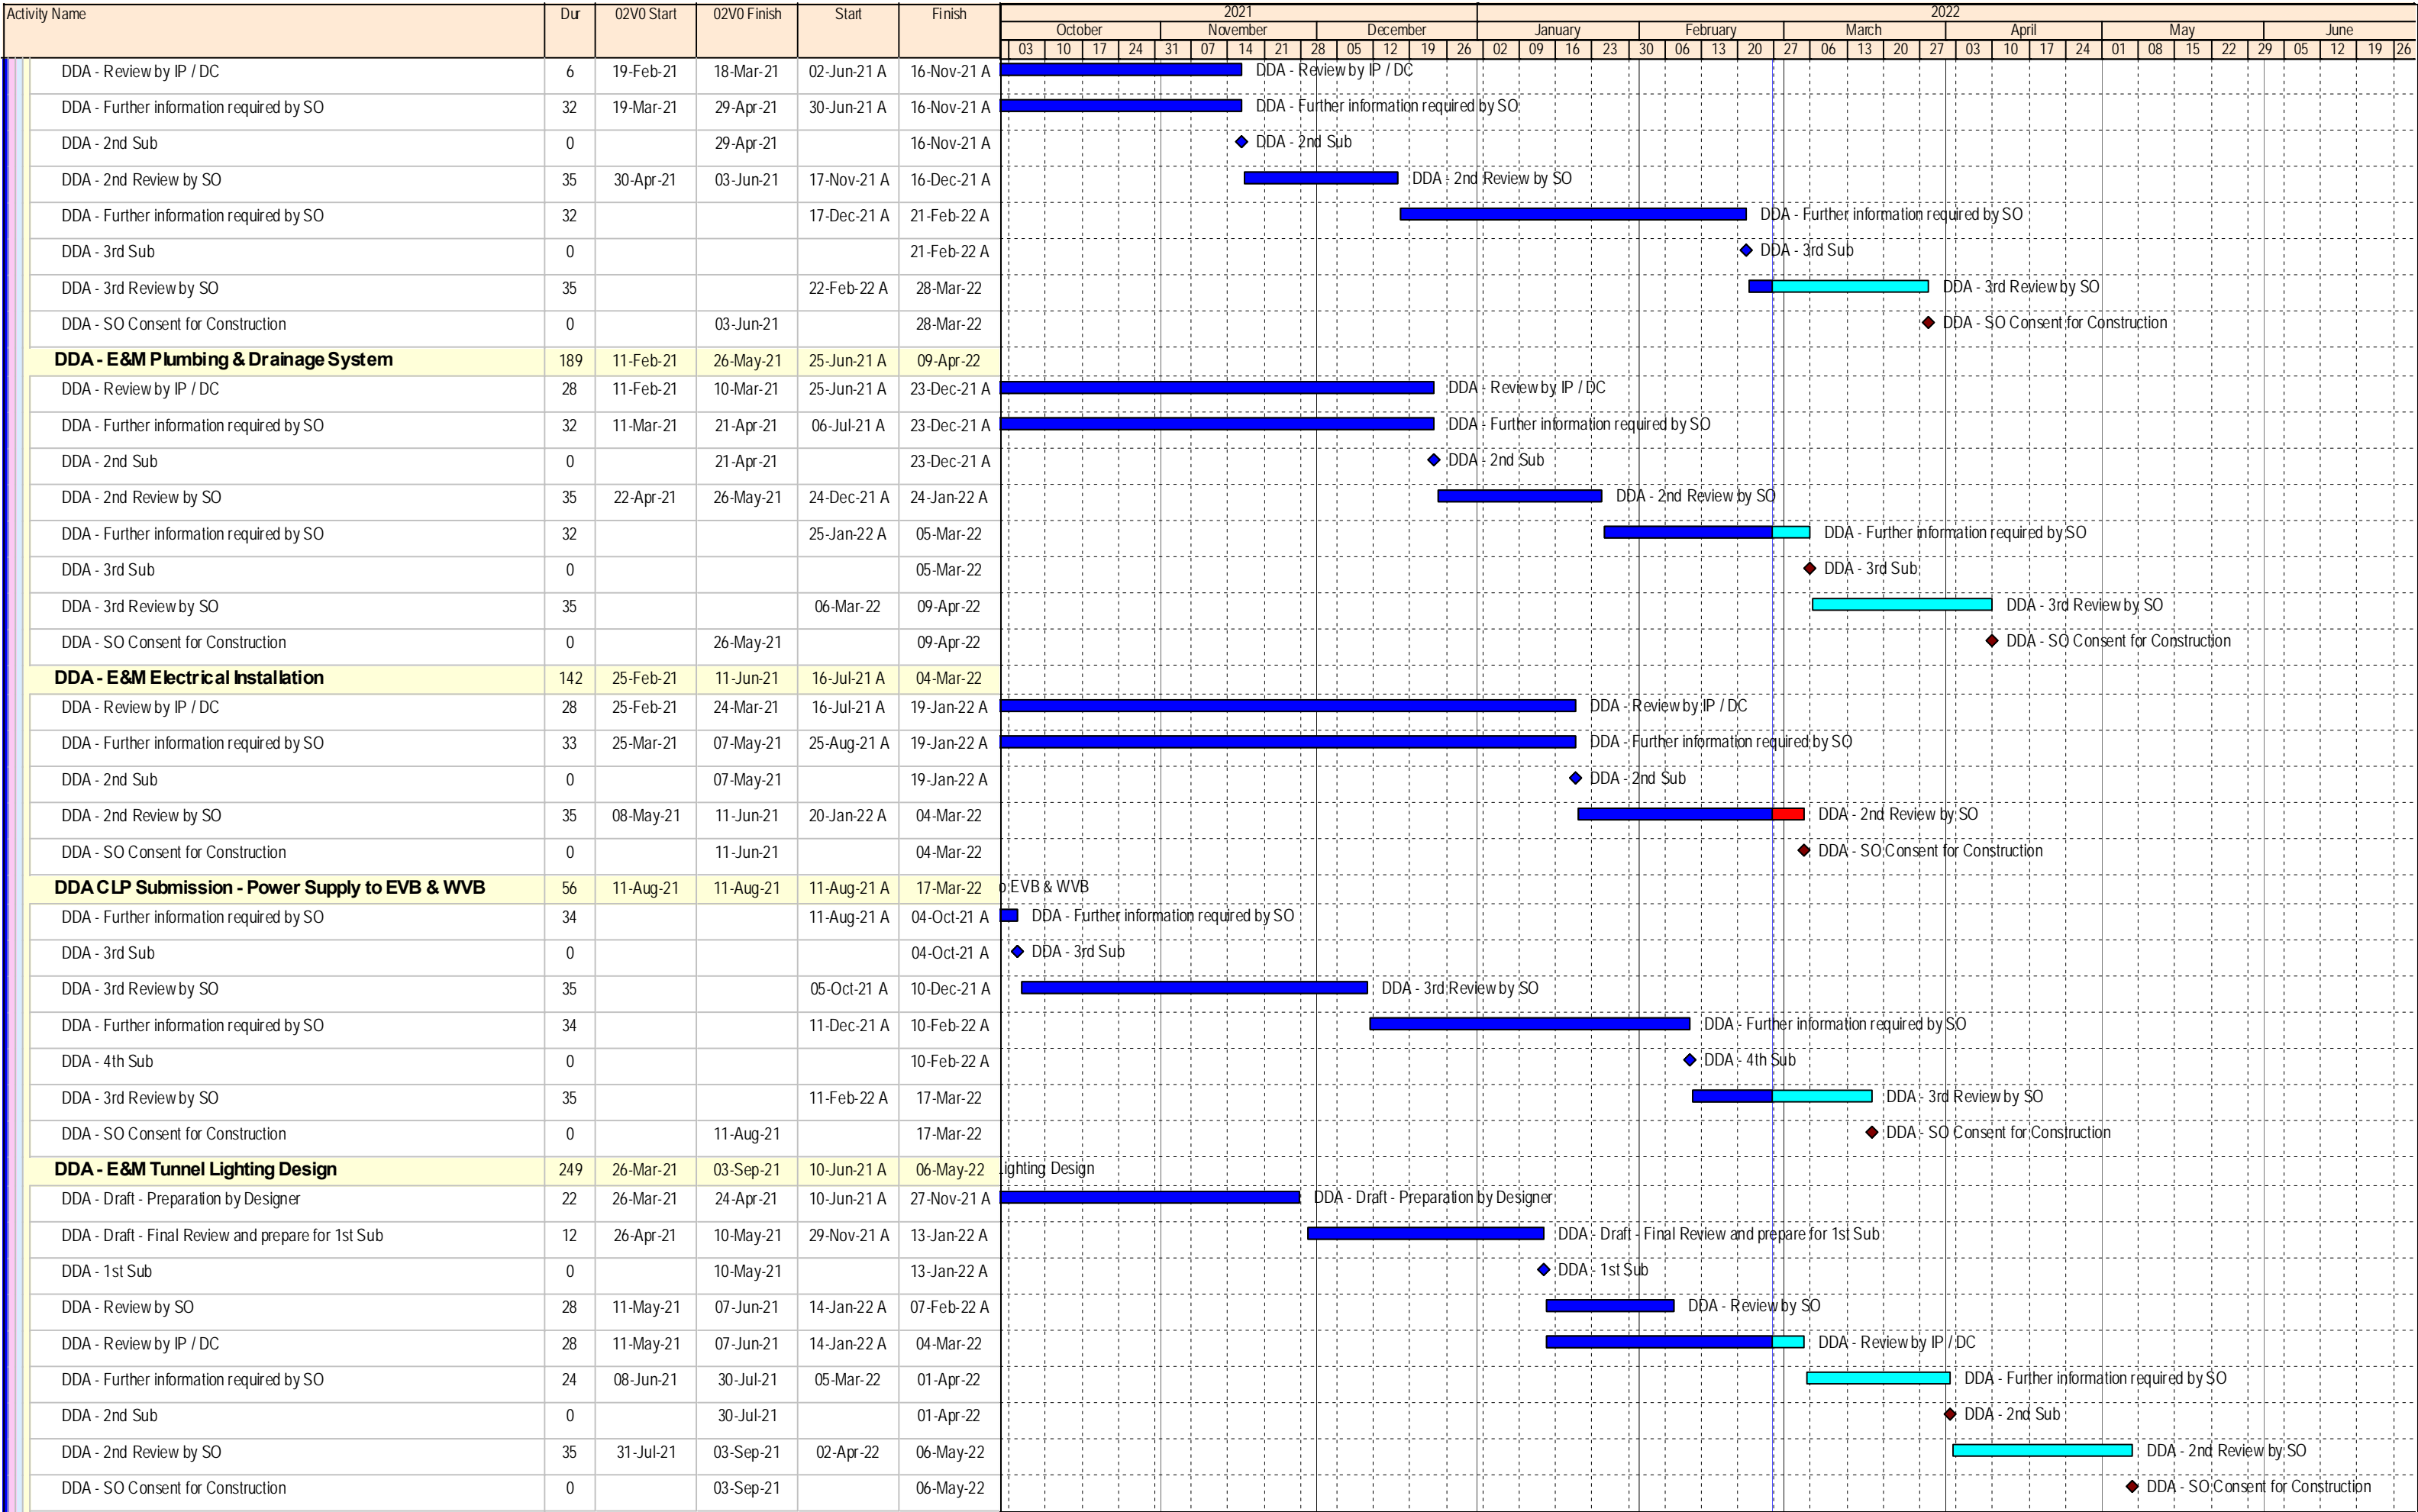

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021																								2022											
						October				November				December				January				February				March				April				May				June			
						03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15	22	29	05
DDA - E&M CMCS	210	26-May-21	13-Oct-21	23-Jul-21 A	19-Apr-22	DDA - E&M CMCS																																			
DDA - Draft - Preparation by Designer	22	26-May-21	21-Jun-21	23-Jul-21 A	27-Nov-21 A	DDA - Draft - Preparation by Designer																																			
DDA - Draft - Final Review and prepare for 1st Sub	12	22-Jun-21	06-Jul-21	29-Nov-21 A	03-Dec-21 A	DDA - Draft - Final Review and prepare for 1st Sub																																			
DDA - 1st Sub	0		06-Jul-21		03-Dec-21 A	DDA - 1st Sub																																			
DDA - Review by SO	28	07-Jul-21	03-Aug-21	04-Dec-21 A	22-Dec-21 A	DDA - Review by SO																																			
DDA - Review by IP / DC	36	07-Jul-21	11-Aug-21	04-Dec-21 A	04-Mar-22	DDA - Review by IP / DC																																			
DDA - Further information required by SO	24	12-Aug-21	08-Sep-21	23-Dec-21 A	11-Mar-22	DDA - Further information required by SO																																			
DDA - 2nd Sub	0		08-Sep-21		11-Mar-22	DDA - 2nd Sub																																			
DDA - 2nd Review by SO	35	09-Sep-21	13-Oct-21	12-Mar-22	15-Apr-22	DDA - 2nd Review by SO																																			
DDA - SO Consent for Construction	0		13-Oct-21		19-Apr-22	DDA - SO Consent for Construction																																			
AIP - Civil Provision for TCSS	63	15-Oct-21	30-Dec-21	19-Apr-22	05-Jul-22	AIP - Civil Provision for TCSS																																			
AIP - Draft - Preparation by Designer	22	15-Oct-21	09-Nov-21	19-Apr-22	16-May-22	AIP - Draft - Preparation by Designer																																			
AIP - Draft - Final Review and prepare for 1st Sub	12	10-Nov-21	23-Nov-21	17-May-22	30-May-22	AIP - Draft - Final Review and prepare for 1st Sub																																			
AIP - 1st Sub	0		23-Nov-21		30-May-22	AIP - 1st Sub																																			
AIP - Review by SO	28	24-Nov-21	21-Dec-21	31-May-22	27-Jun-22	AIP - Review by SO																																			
AIP - Review by IP / DC	28	24-Nov-21	21-Dec-21	31-May-22	27-Jun-22	AIP - Review by IP / DC																																			
AIP - Update & prepare for 2nd Sub	6	22-Dec-21	30-Dec-21	28-Jun-22	05-Jul-22	AIP - Update & prepare for 2nd Sub																																			
PAYMENT MILESTONE	1075	30-Sep-20	28-Feb-25	13-Oct-21 A	27-Jun-22	PAYMENT MILESTONE																																			
1.1 Preliminaries and General Requirements	83	13-Oct-21	13-Apr-22	13-Oct-21 A	13-Apr-22	1.1 Preliminaries and General Requirements																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 23	0		13-Oct-21		13-Oct-21 A	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 23																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 24	0		13-Nov-21		13-Nov-21 A	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 24																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 25	0		13-Dec-21		13-Dec-21 A	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 25																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 26	0		13-Jan-22		13-Jan-22 A	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 26																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 27	0		14-Feb-22		26-Feb-22*	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 27																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 28	0		14-Mar-22		14-Mar-22*	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 28																																			
1.1.42 Monthly Remaining value of this Cost Centre 1 Month 29	0		13-Apr-22		13-Apr-22*	1.1.42 Monthly Remaining value of this Cost Centre 1 Month 29																																			
3.1 for Trunk Road T2	134	30-Sep-20	21-Sep-21	13-Oct-21 A	18-Jun-22	Trunk Road T2																																			
3.1 .46 Approval AIP for EVB	0		30-Sep-20		13-Oct-21 A	3.1 .46 Approval AIP for EVB																																			
3.1 .40 Approval DDA for Drill-and-blast Tunnel	0		09-Oct-20		13-Nov-21 A	3.1 .40 Approval DDA for Drill-and-blast Tunnel																																			
3.1 .48 Approval DDA for EVB	0		30-Sep-20		13-Nov-21 A	3.1 .48 Approval DDA for EVB																																			
3.1 .50 Approval AIP for completion of SUS	0		29-Mar-21		13-Jan-22 A	3.1 .50 Approval AIP for completion of SUS																																			
3.1 .52 Approval DDA for completion of SUS	0		21-Sep-21		18-Jun-22	3.1 .52 Approval DDA for completion of SUS																																			
3.2 for Road S20 and Associated Infrastructure Works for C	0	30-Sep-20	30-Sep-20	13-Dec-21 A	13-Dec-21 A	3.2 for Road S20 and Associated Infrastructure Works for C																																			
3.2 .27 Complete whole activities of this cost centre	0		30-Sep-20		13-Dec-21 A	3.2 .27 Complete whole activities of this cost centre																																			
3.3 for the Remaining Stage 5 Infrastructure Works - Road I	24	26-Feb-21	03-Jun-21	13-Dec-21 A	13-Jan-22 A	3.3 for the Remaining Stage 5 Infrastructure Works - Road I																																			
3.3 .23 Submit DDA for landscape works	0		03-Jun-21		13-Dec-21 A	3.3 .23 Submit DDA for landscape works																																			
3.3 .16 Approval DDA for waterworks	0		26-Feb-21		13-Jan-22 A	3.3 .16 Approval DDA for waterworks																																			
3.4 for the Remaining Stage 5 Infrastructure Works - FT02	45	22-Dec-20	09-Mar-21	13-Oct-21 A	26-Feb-22	3.4 for the Remaining Stage 5 Infrastructure Works - FT02																																			
3.4 .8 Approval DDA for Landscaped elevated walkway	0		09-Mar-21		13-Oct-21 A	3.4 .8 Approval DDA for Landscaped elevated walkway																																			
3.4 .11 Submit Demolition plan for existing footbridge	0		22-Dec-20		13-Nov-21 A	3.4 .11 Submit Demolition plan for existing footbridge																																			
3.4 .10 Approval DDA for modification of existing footbridge	0		09-Mar-21		13-Jan-22 A	3.4 .10 Approval DDA for modification of existing footbridge																																			


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary







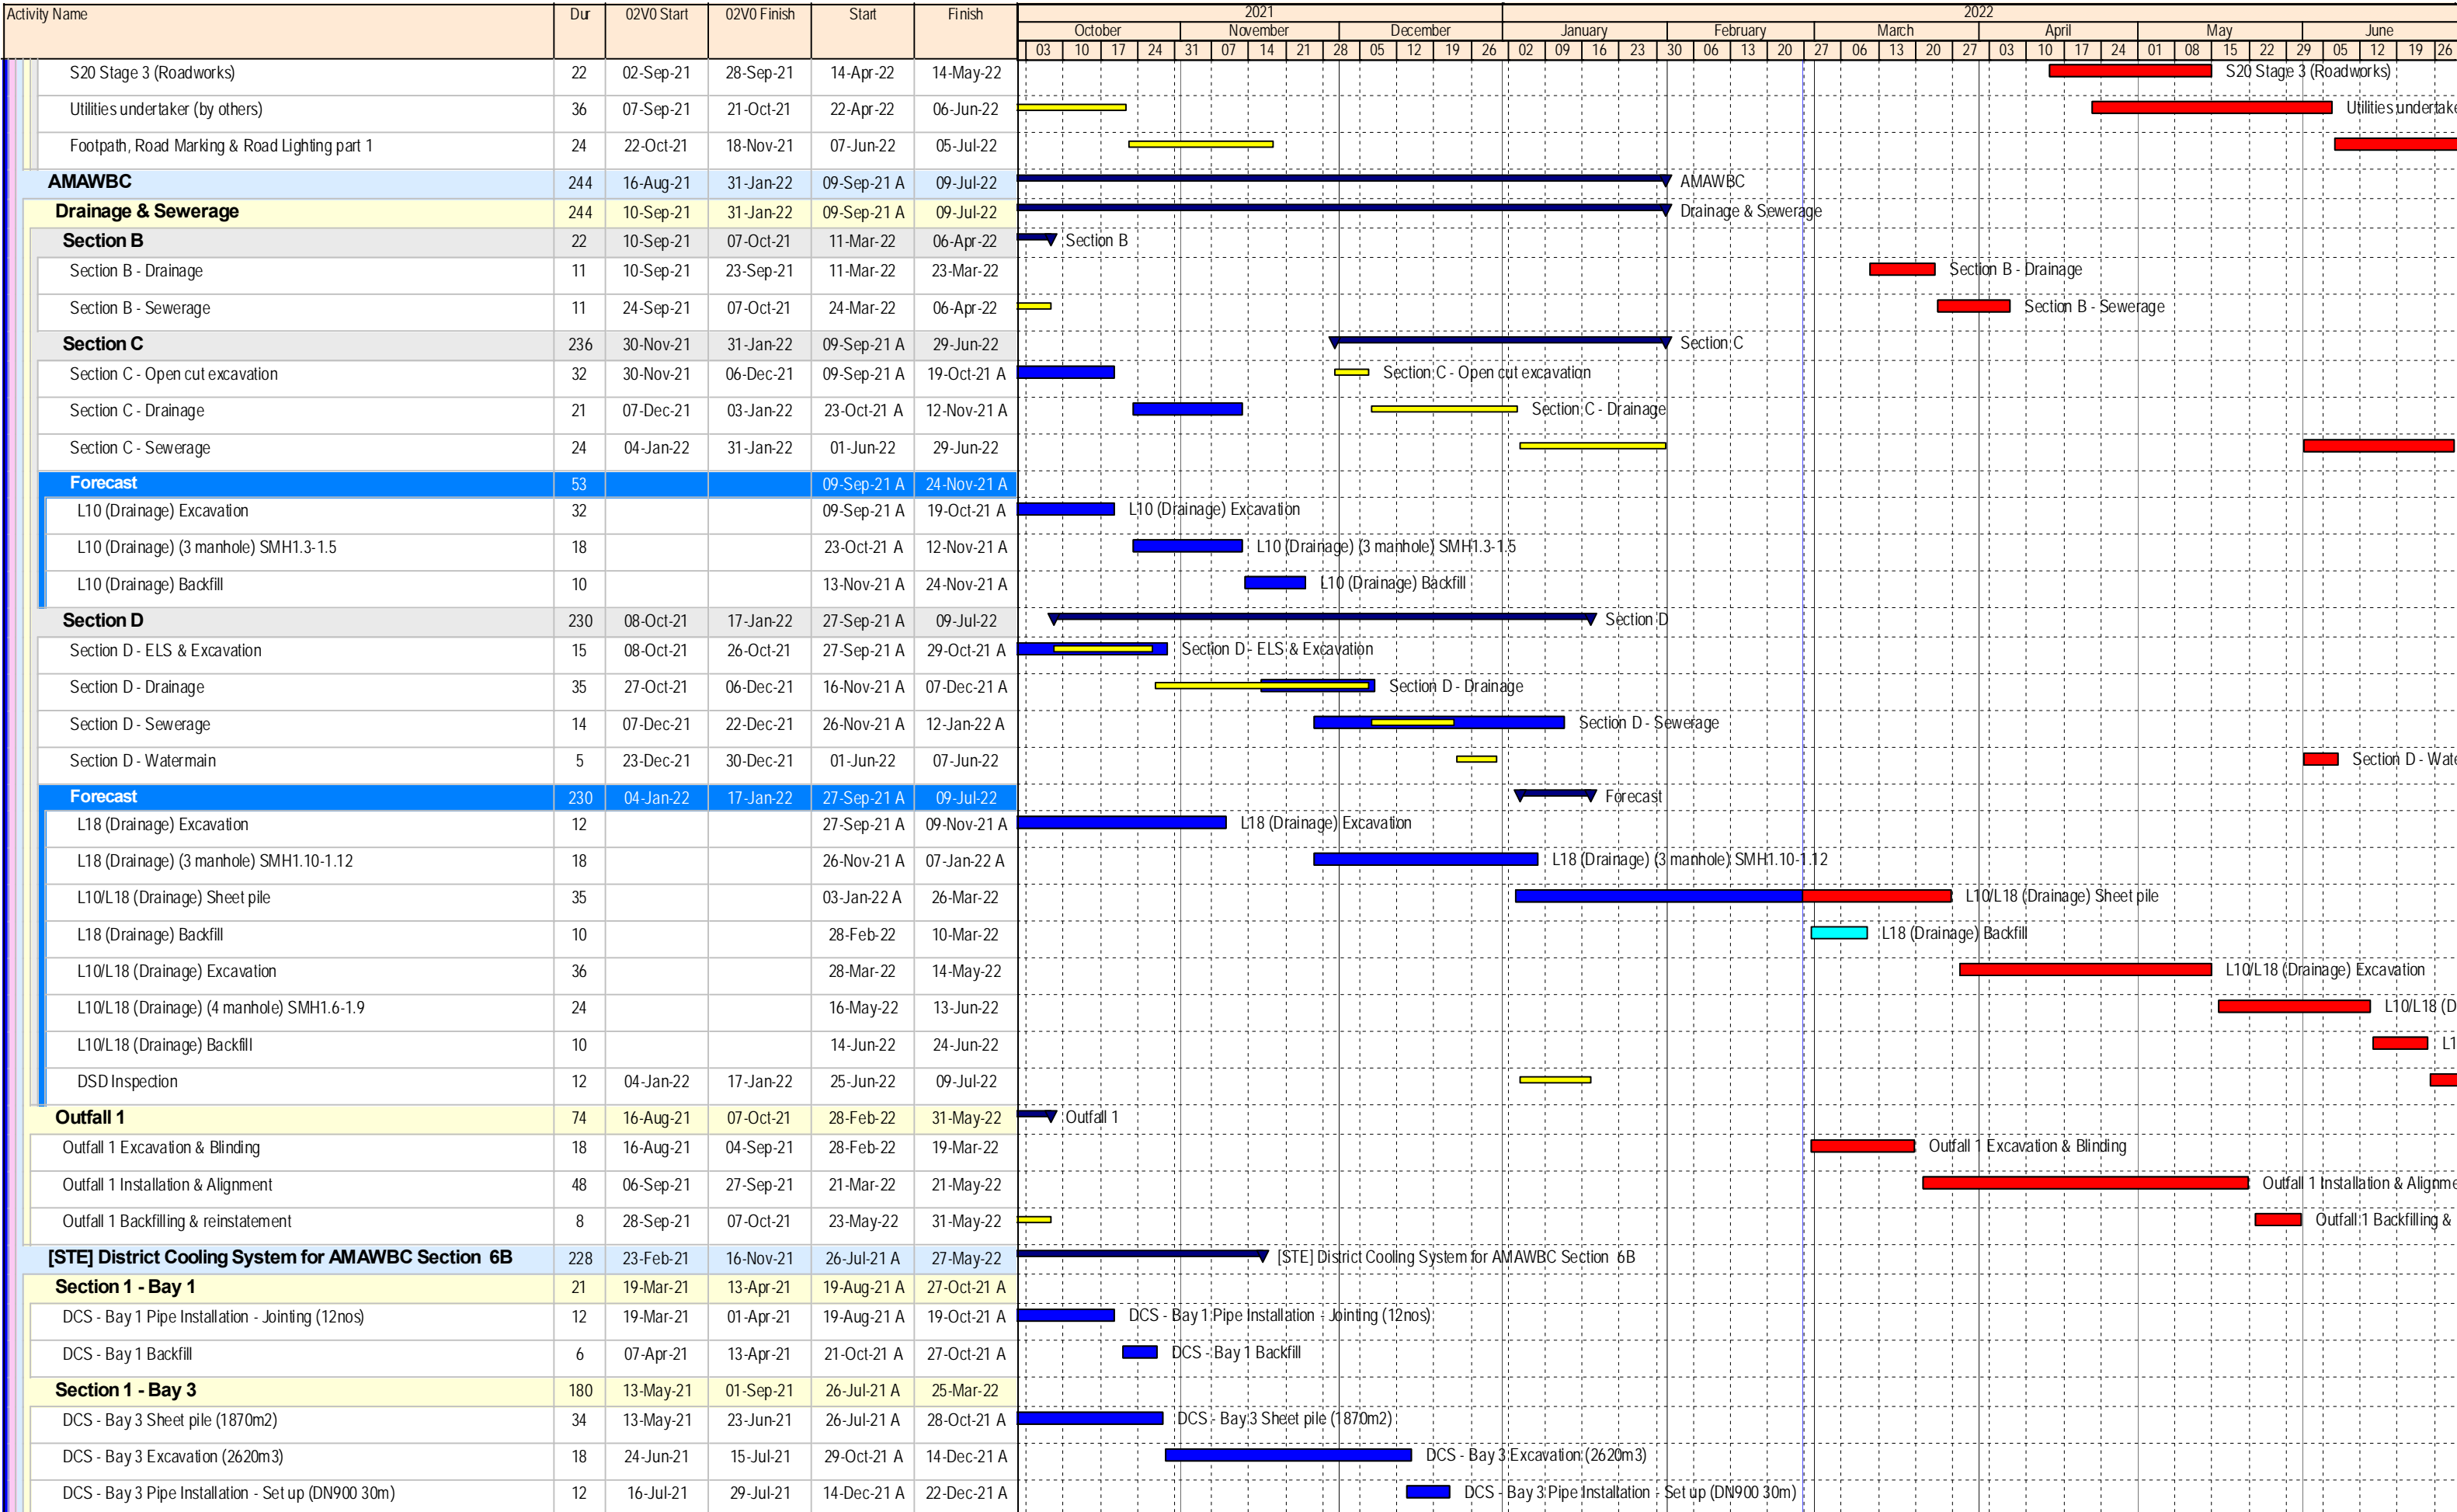

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu




	Milestone		Summary
	Planned Bar		
	Critical Activity		
	Actual Milestone		
	Actual Work		
	Baseline Milestone		
	Baseline Bar		

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

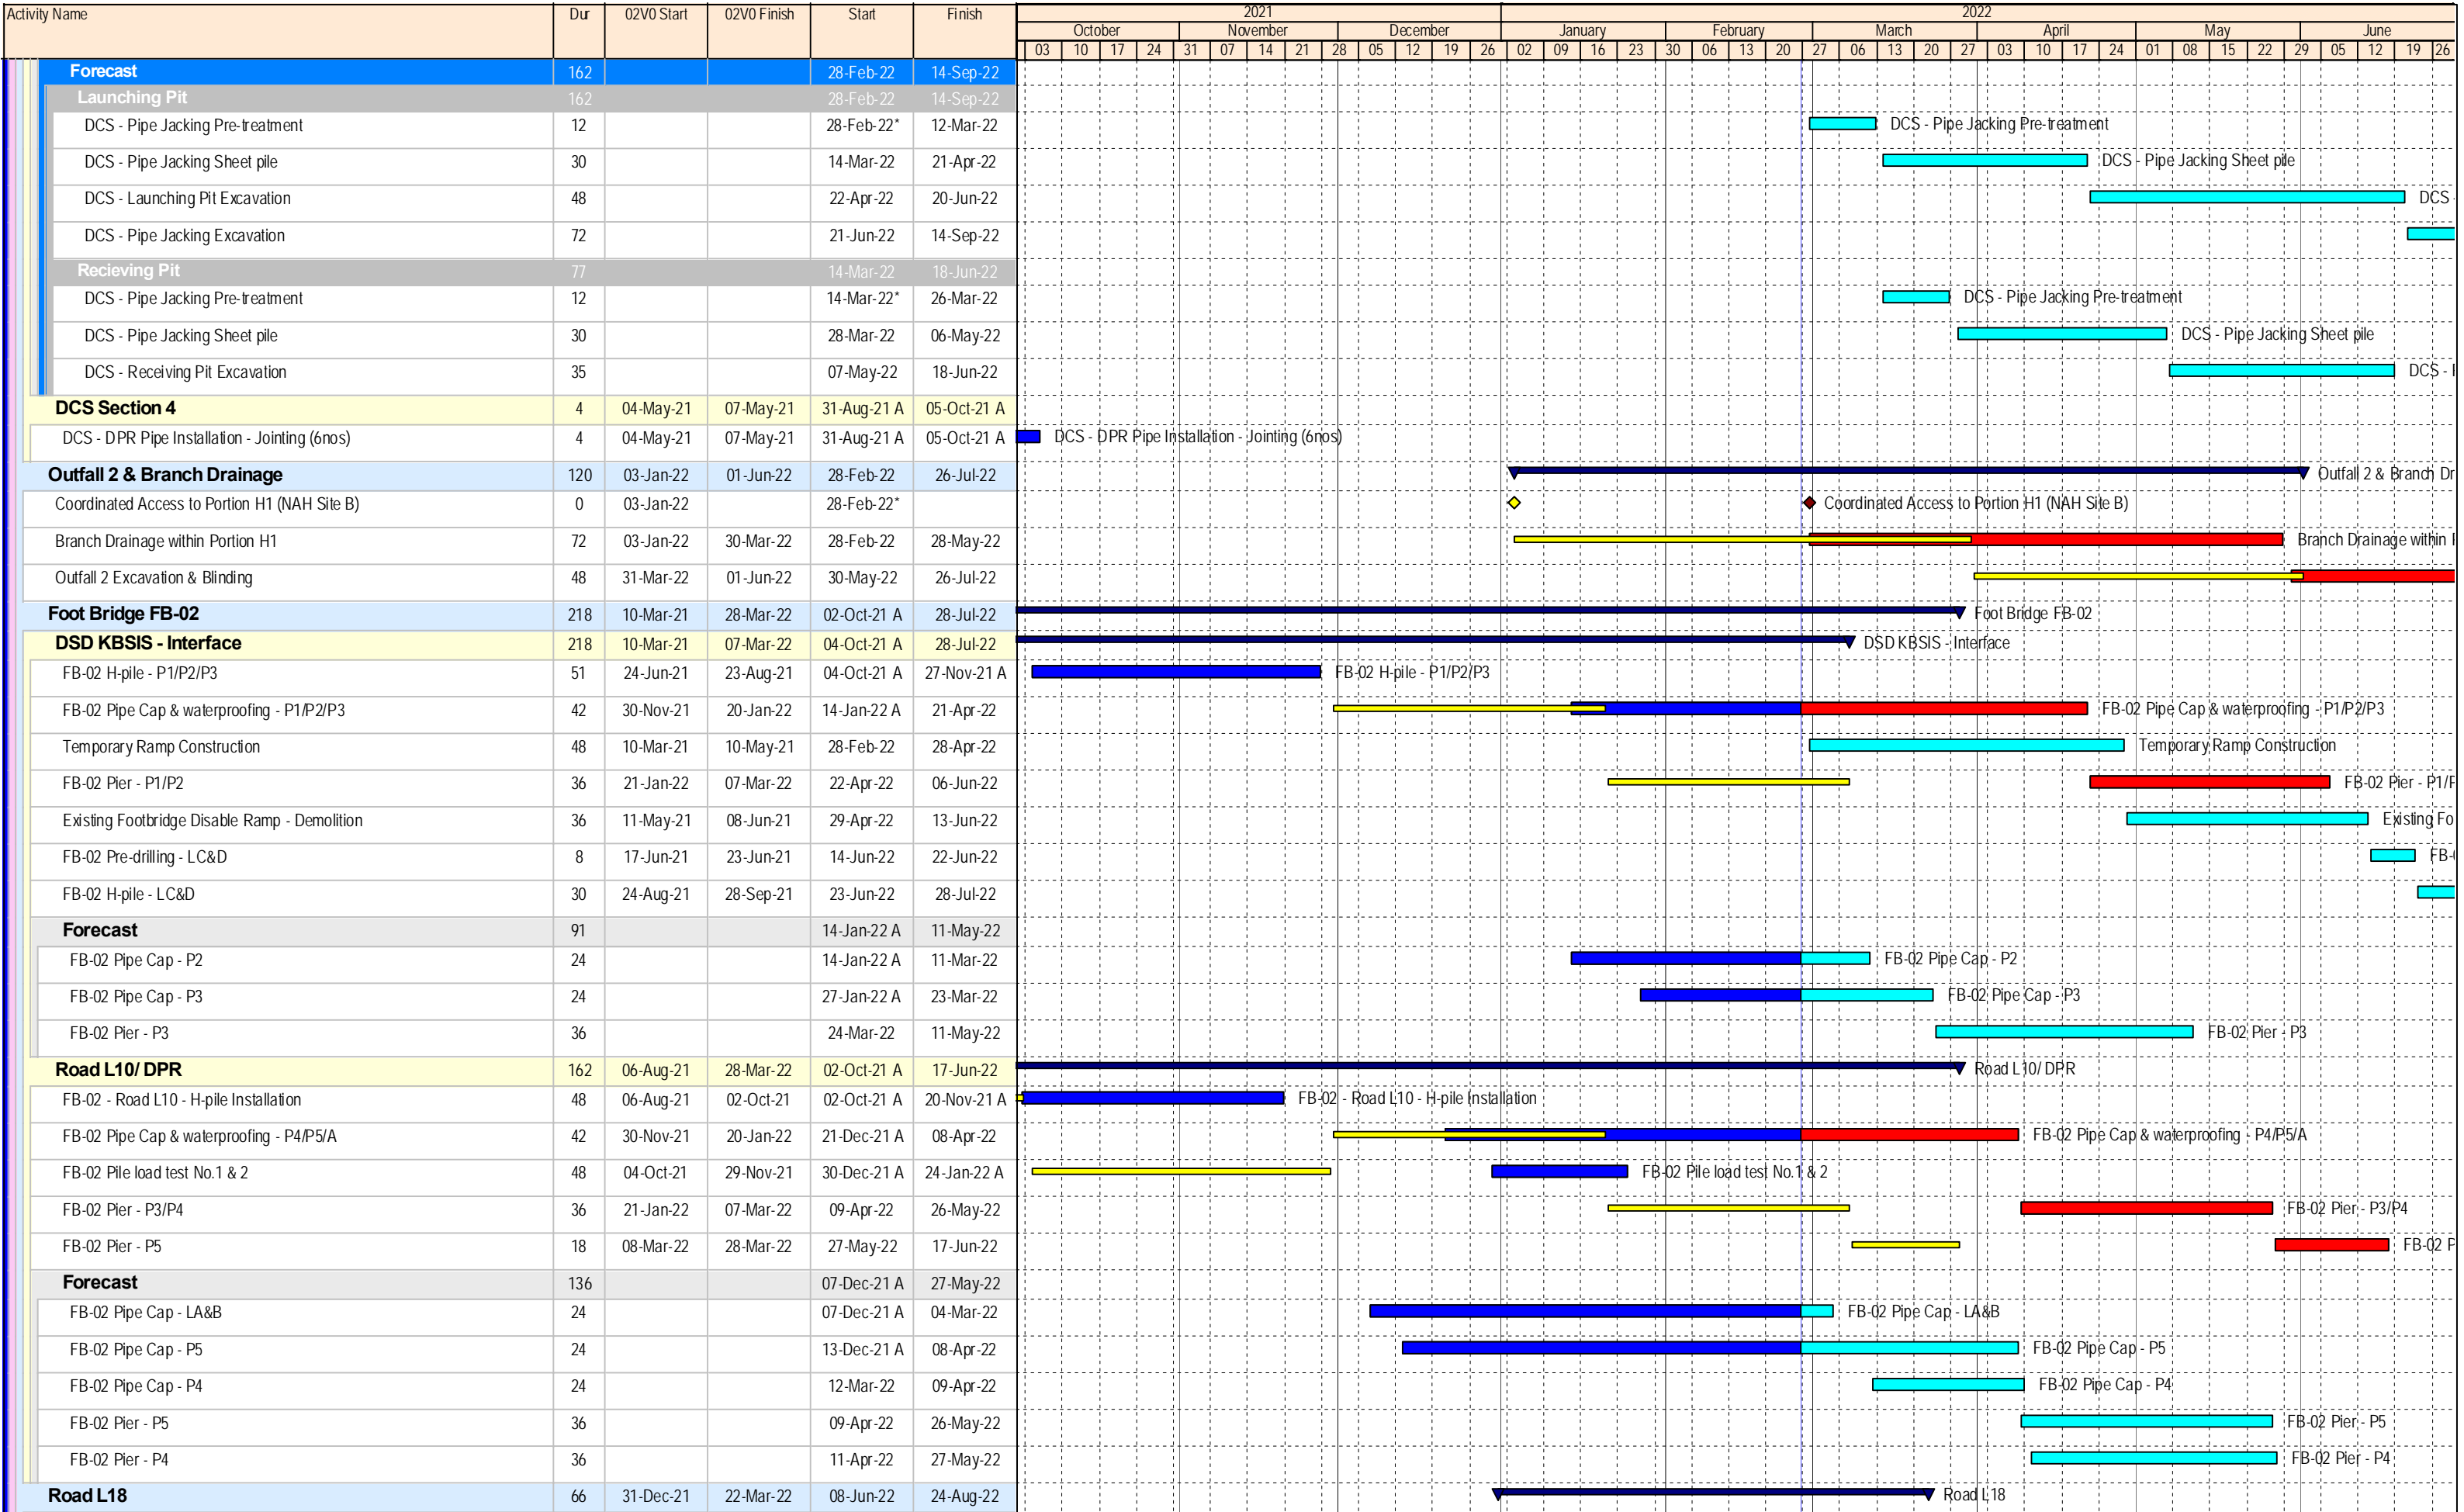


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

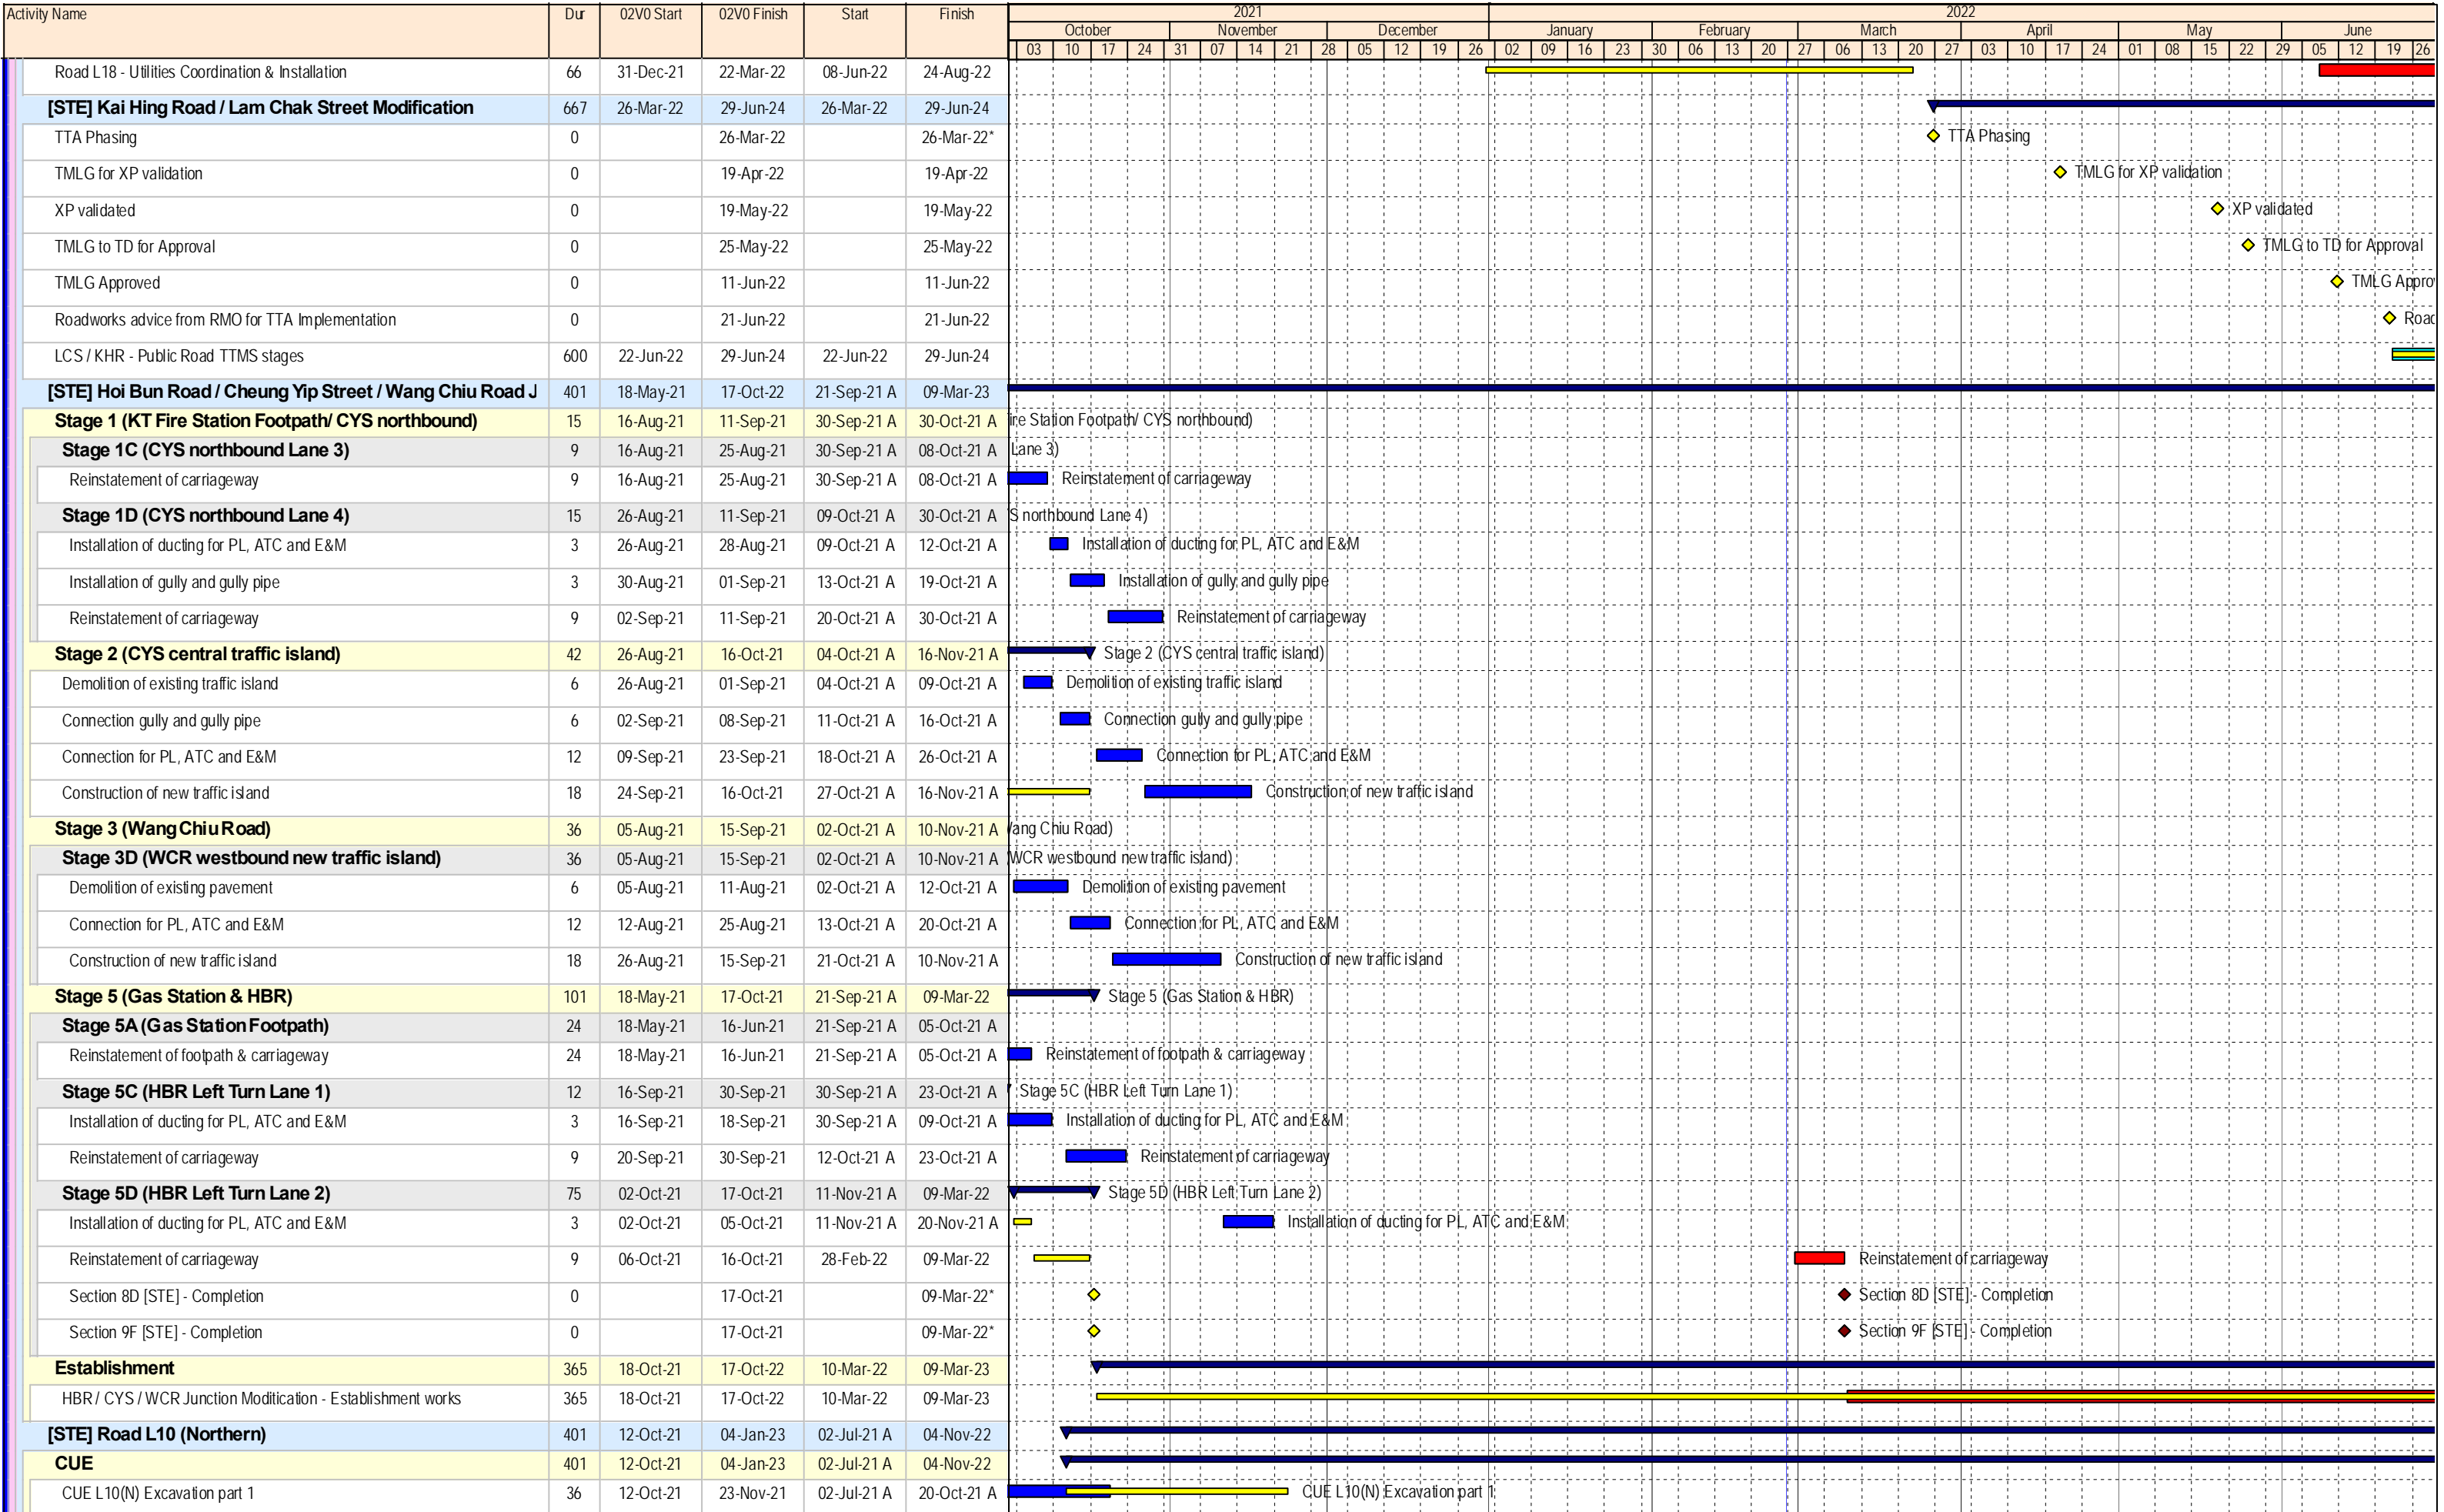


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu

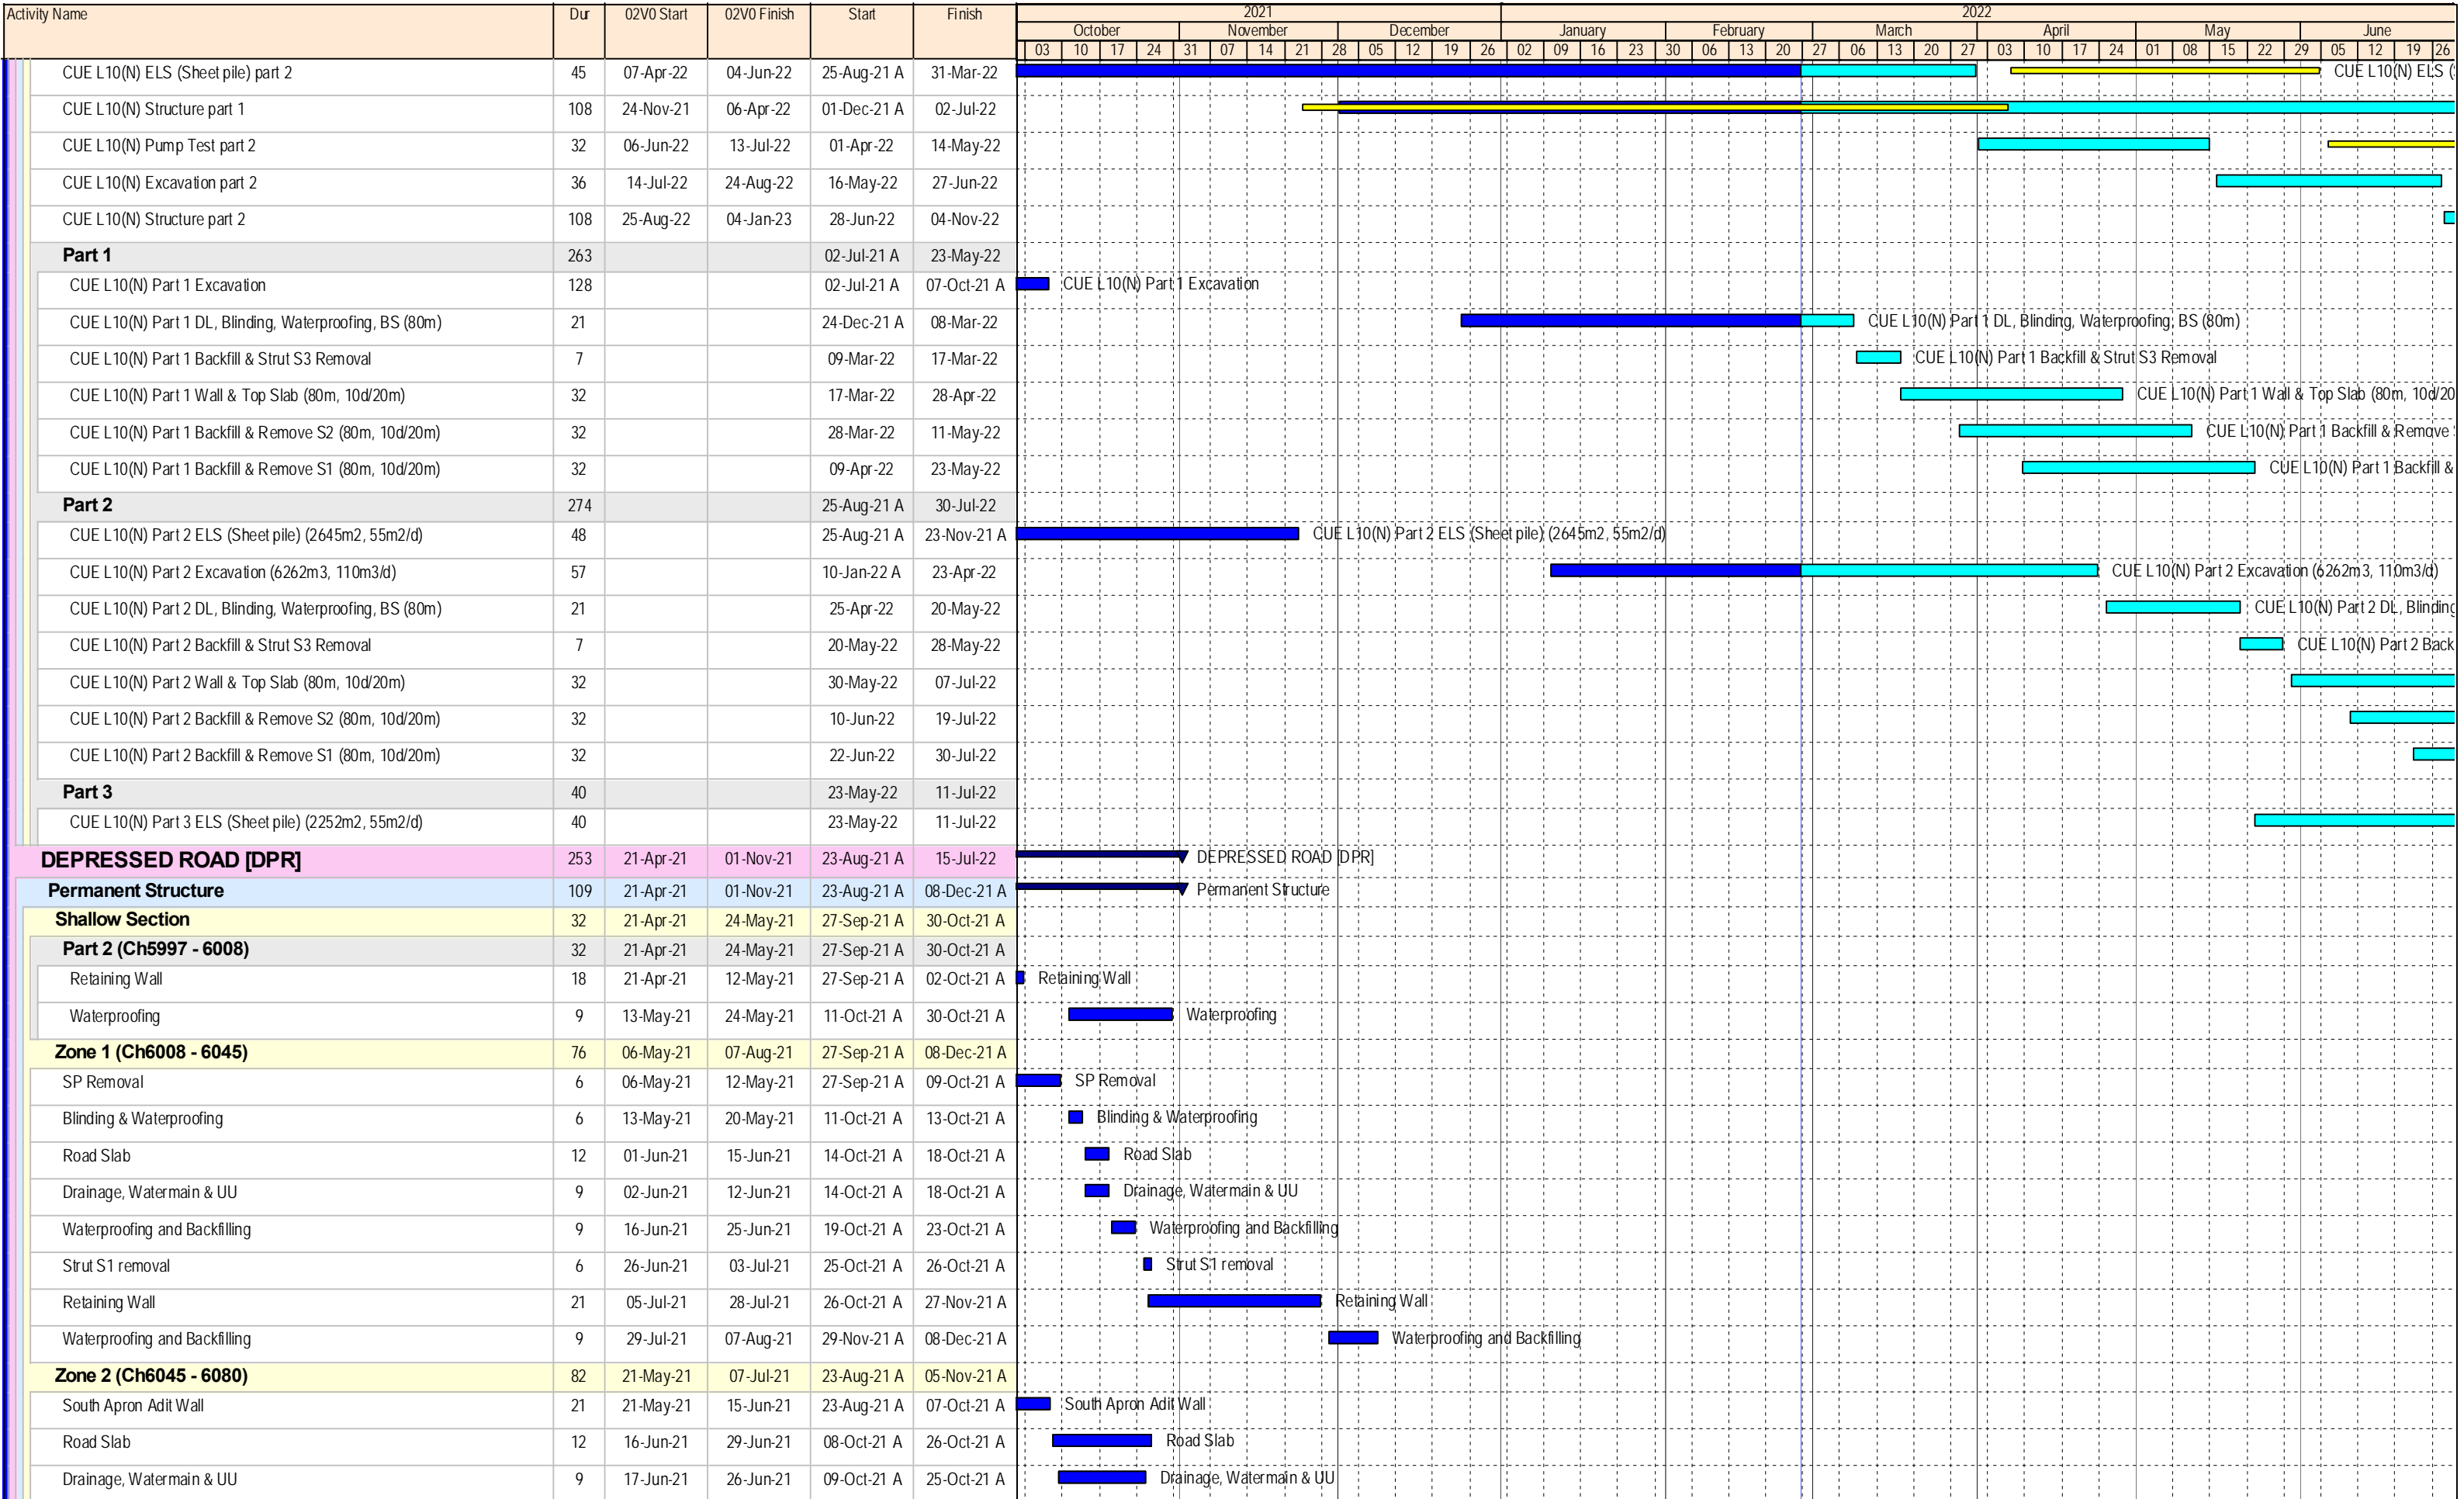


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ▬ Actual Work
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

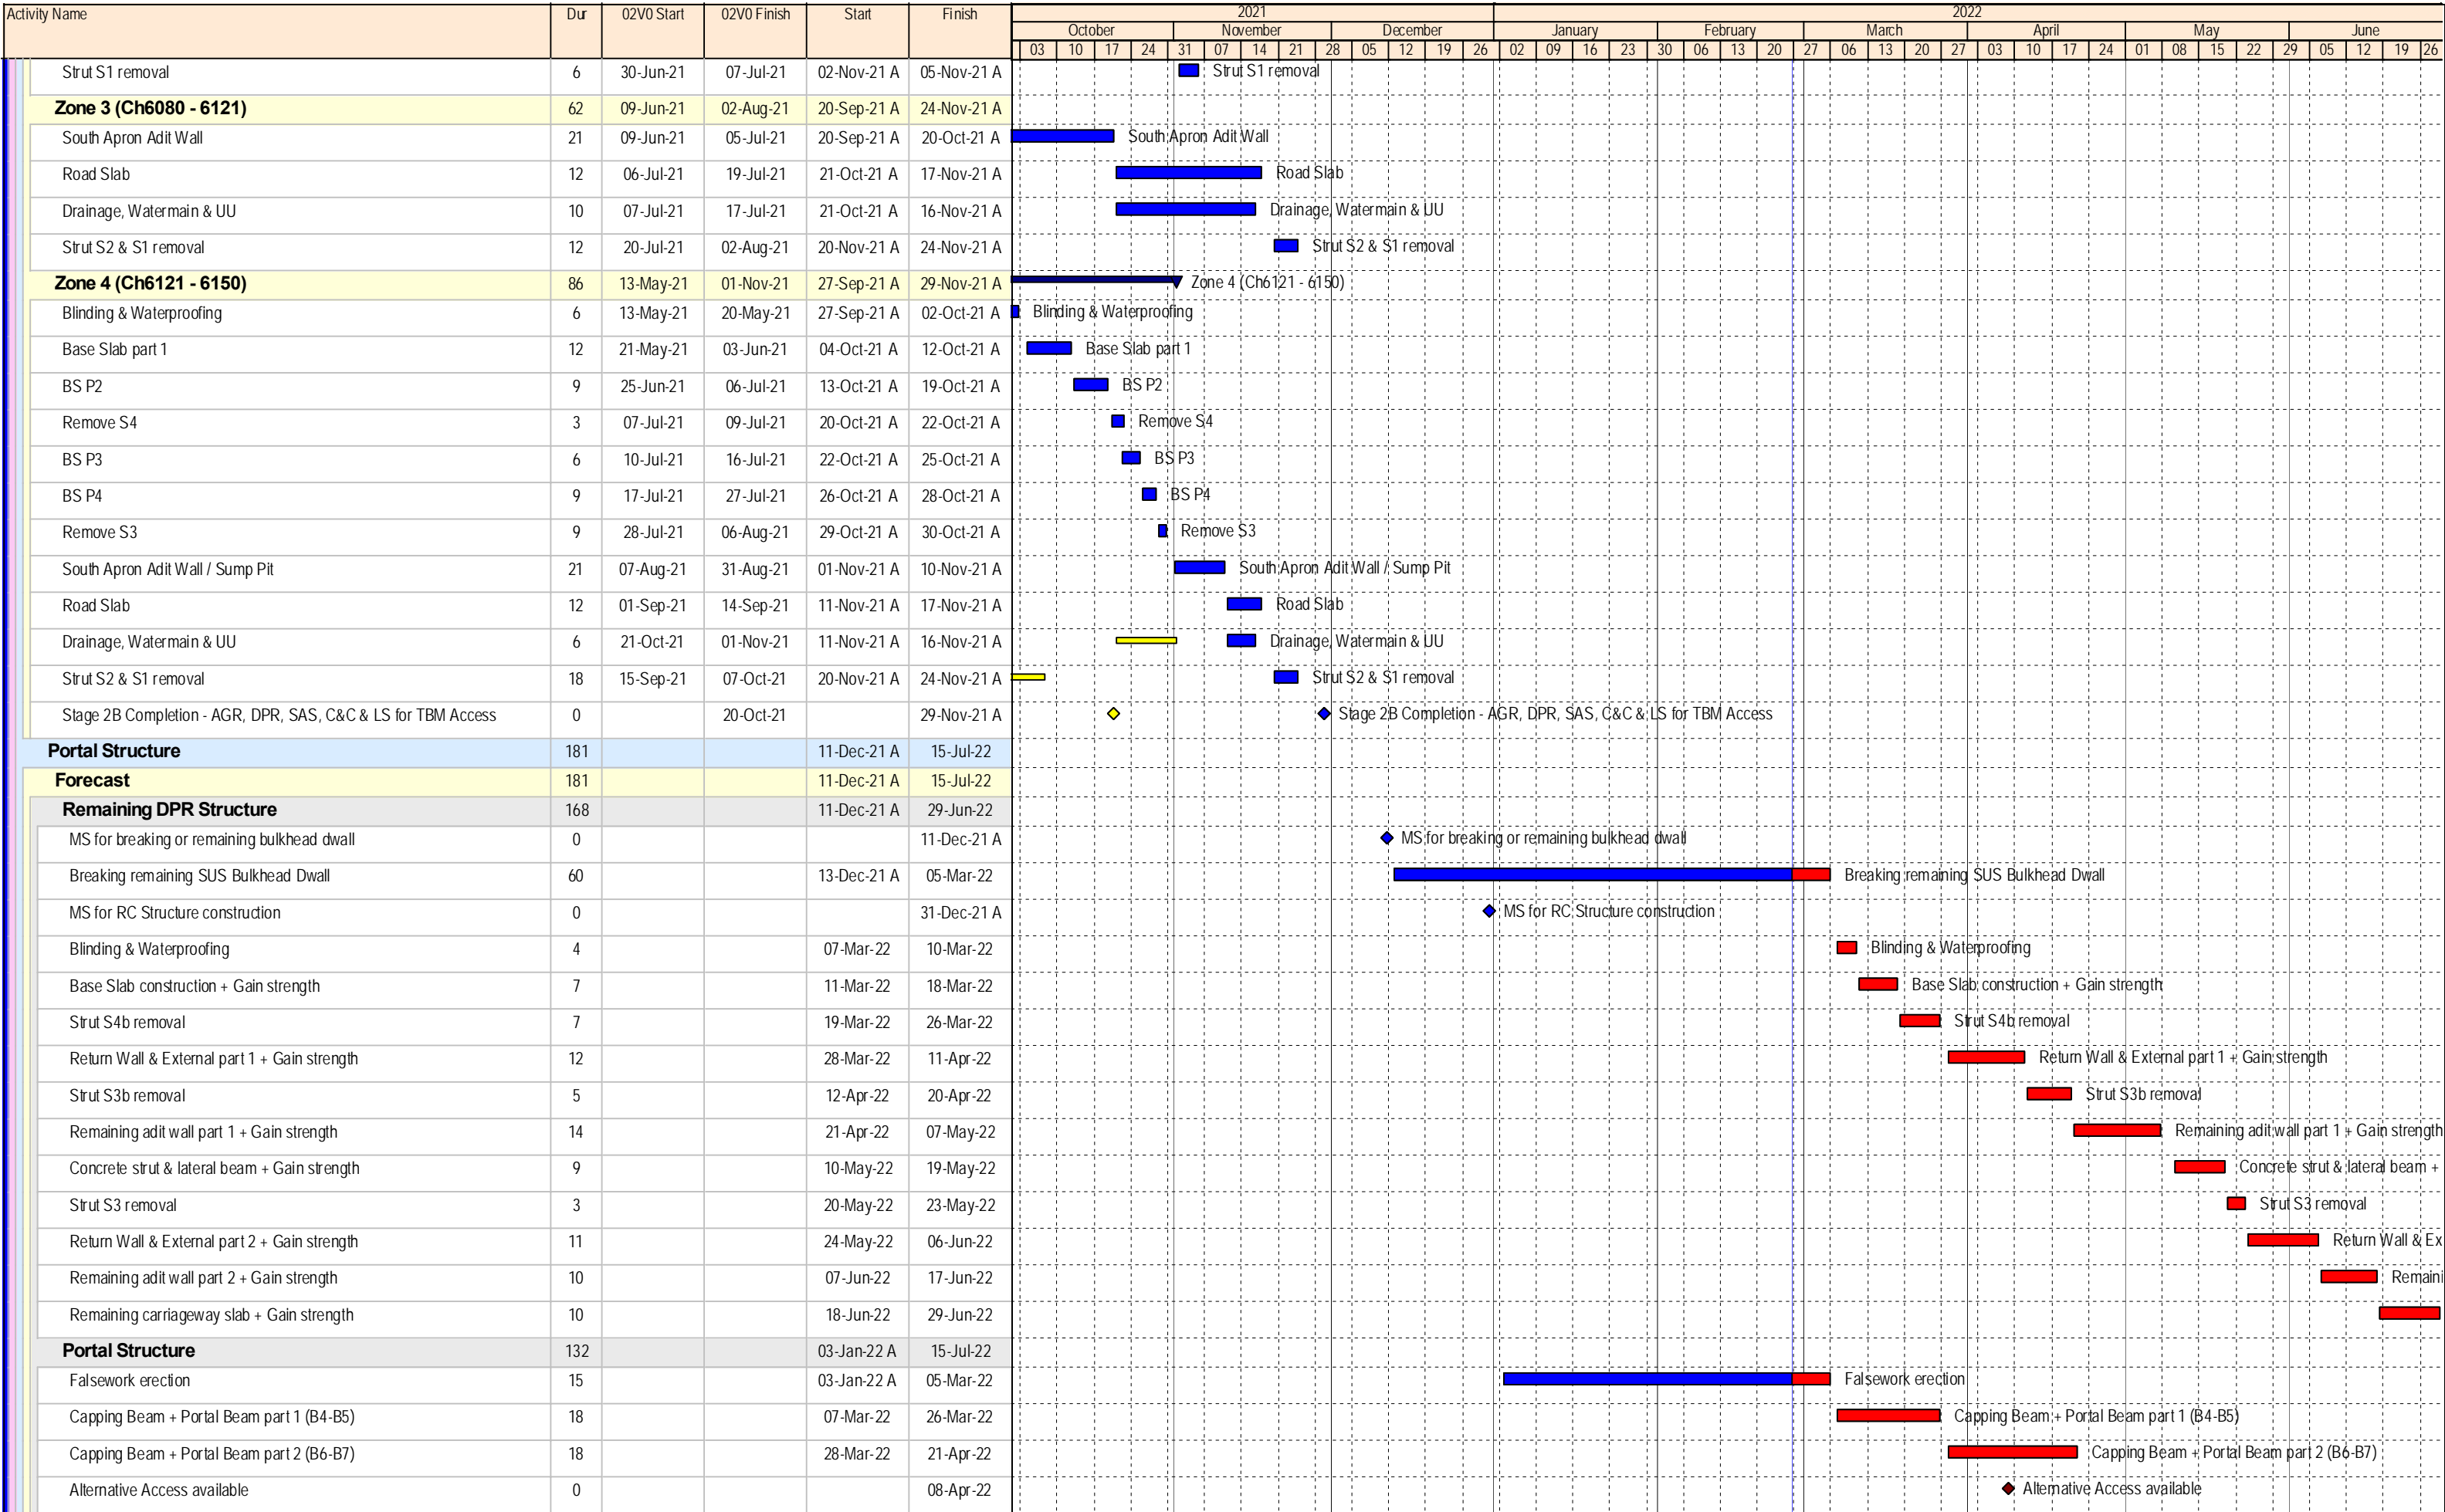


Page 21 of 30
Data Date: 26-Feb-22


- Milestone (Red Diamond)
- Planned Bar (Cyan Bar)
- Critical Activity (Red Bar)
- Actual Milestone (Blue Diamond)
- Actual Work (Blue Bar)
- Baseline Milestone (Yellow Diamond)
- Baseline Bar (Yellow Bar)
- Summary (Arrow)

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

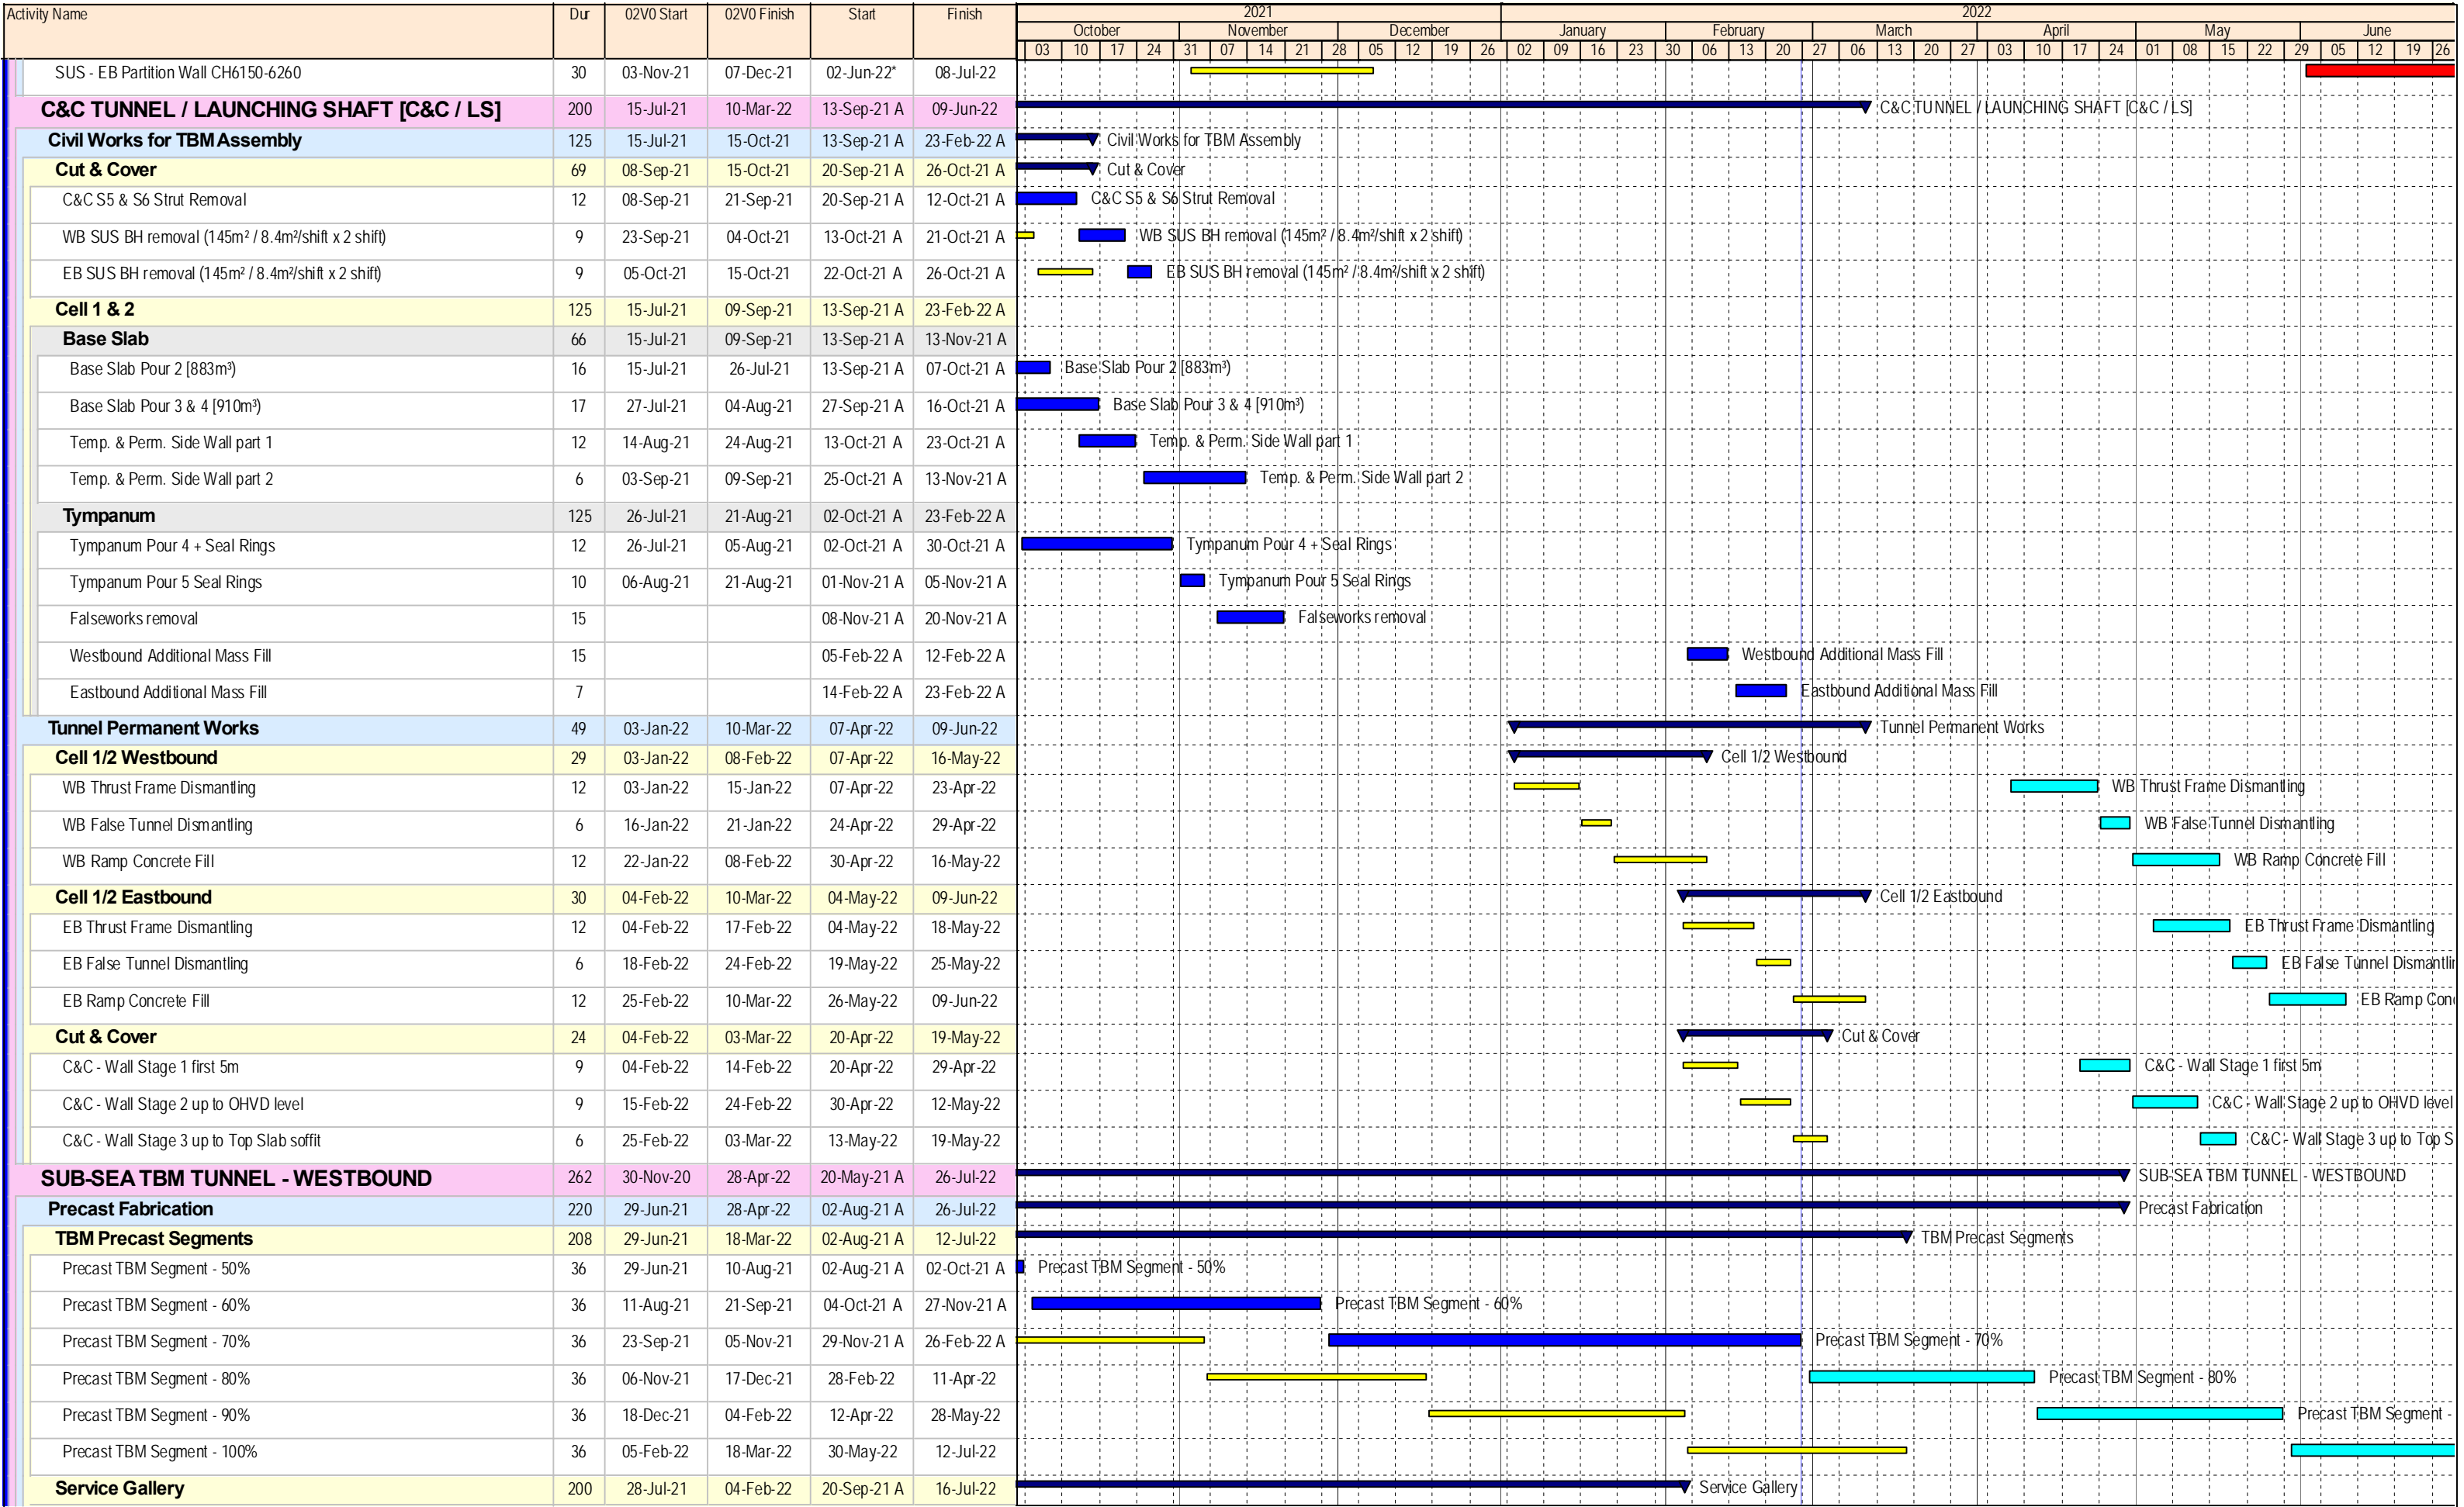


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

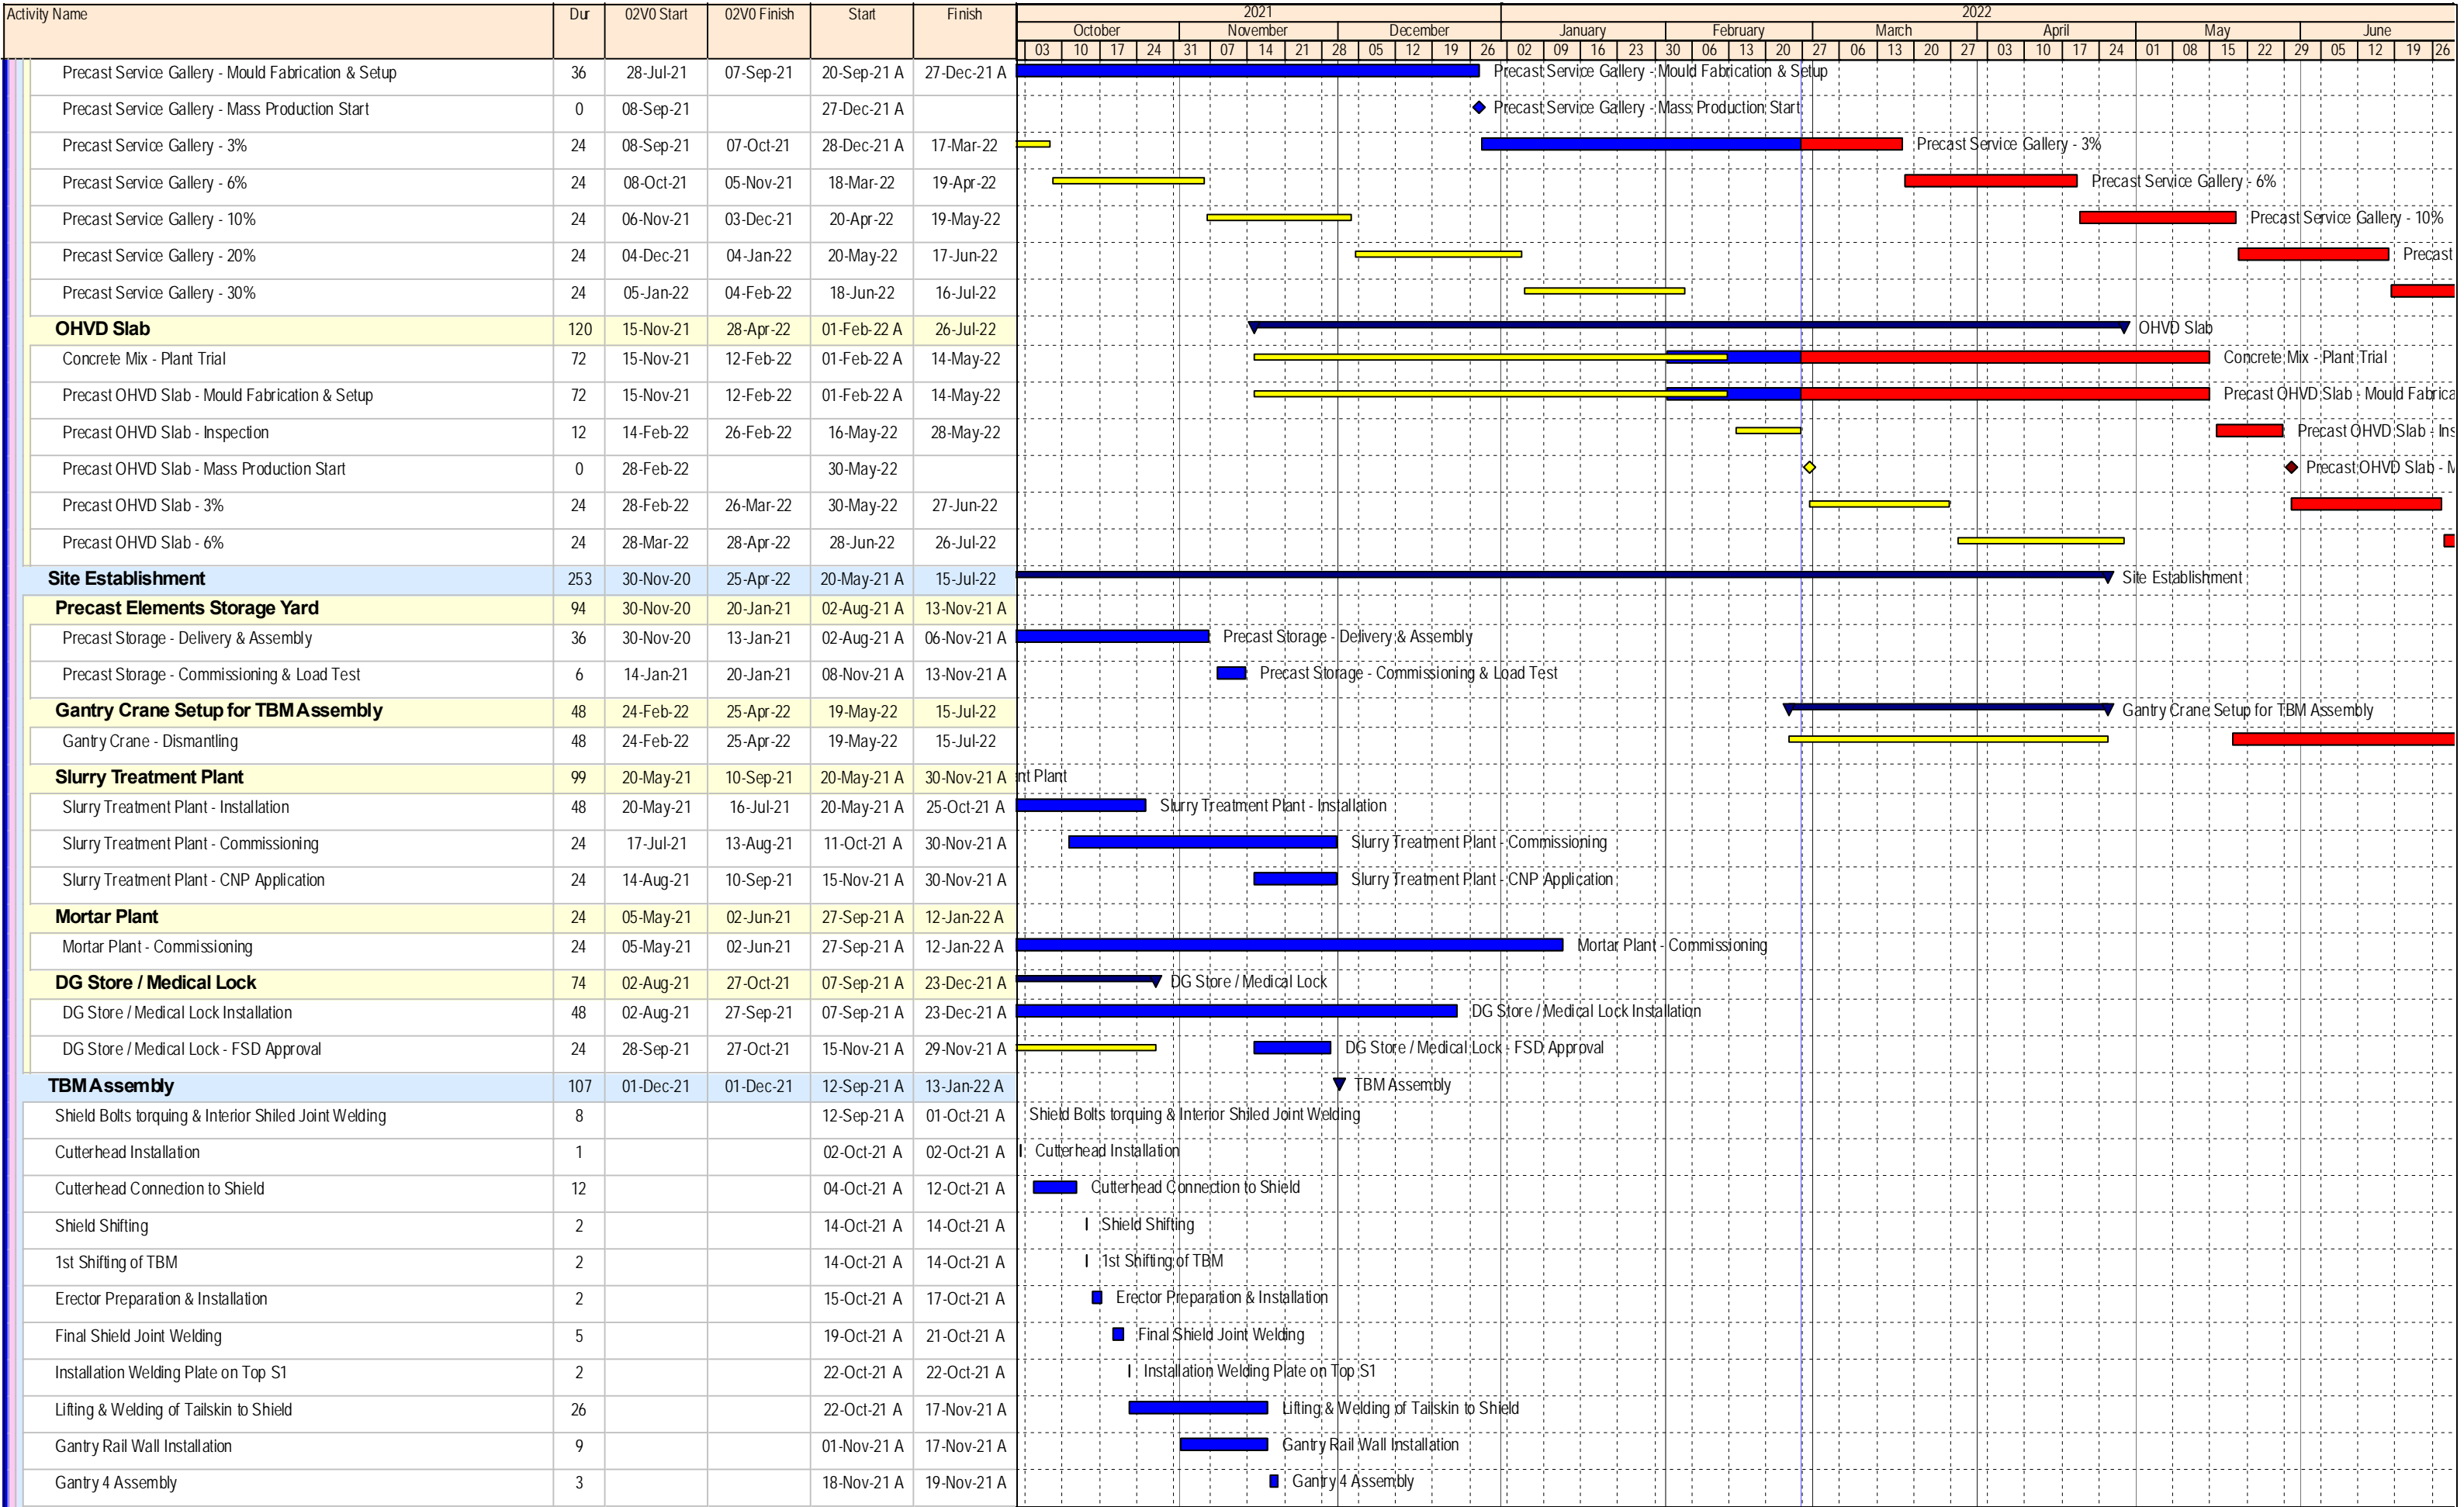


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

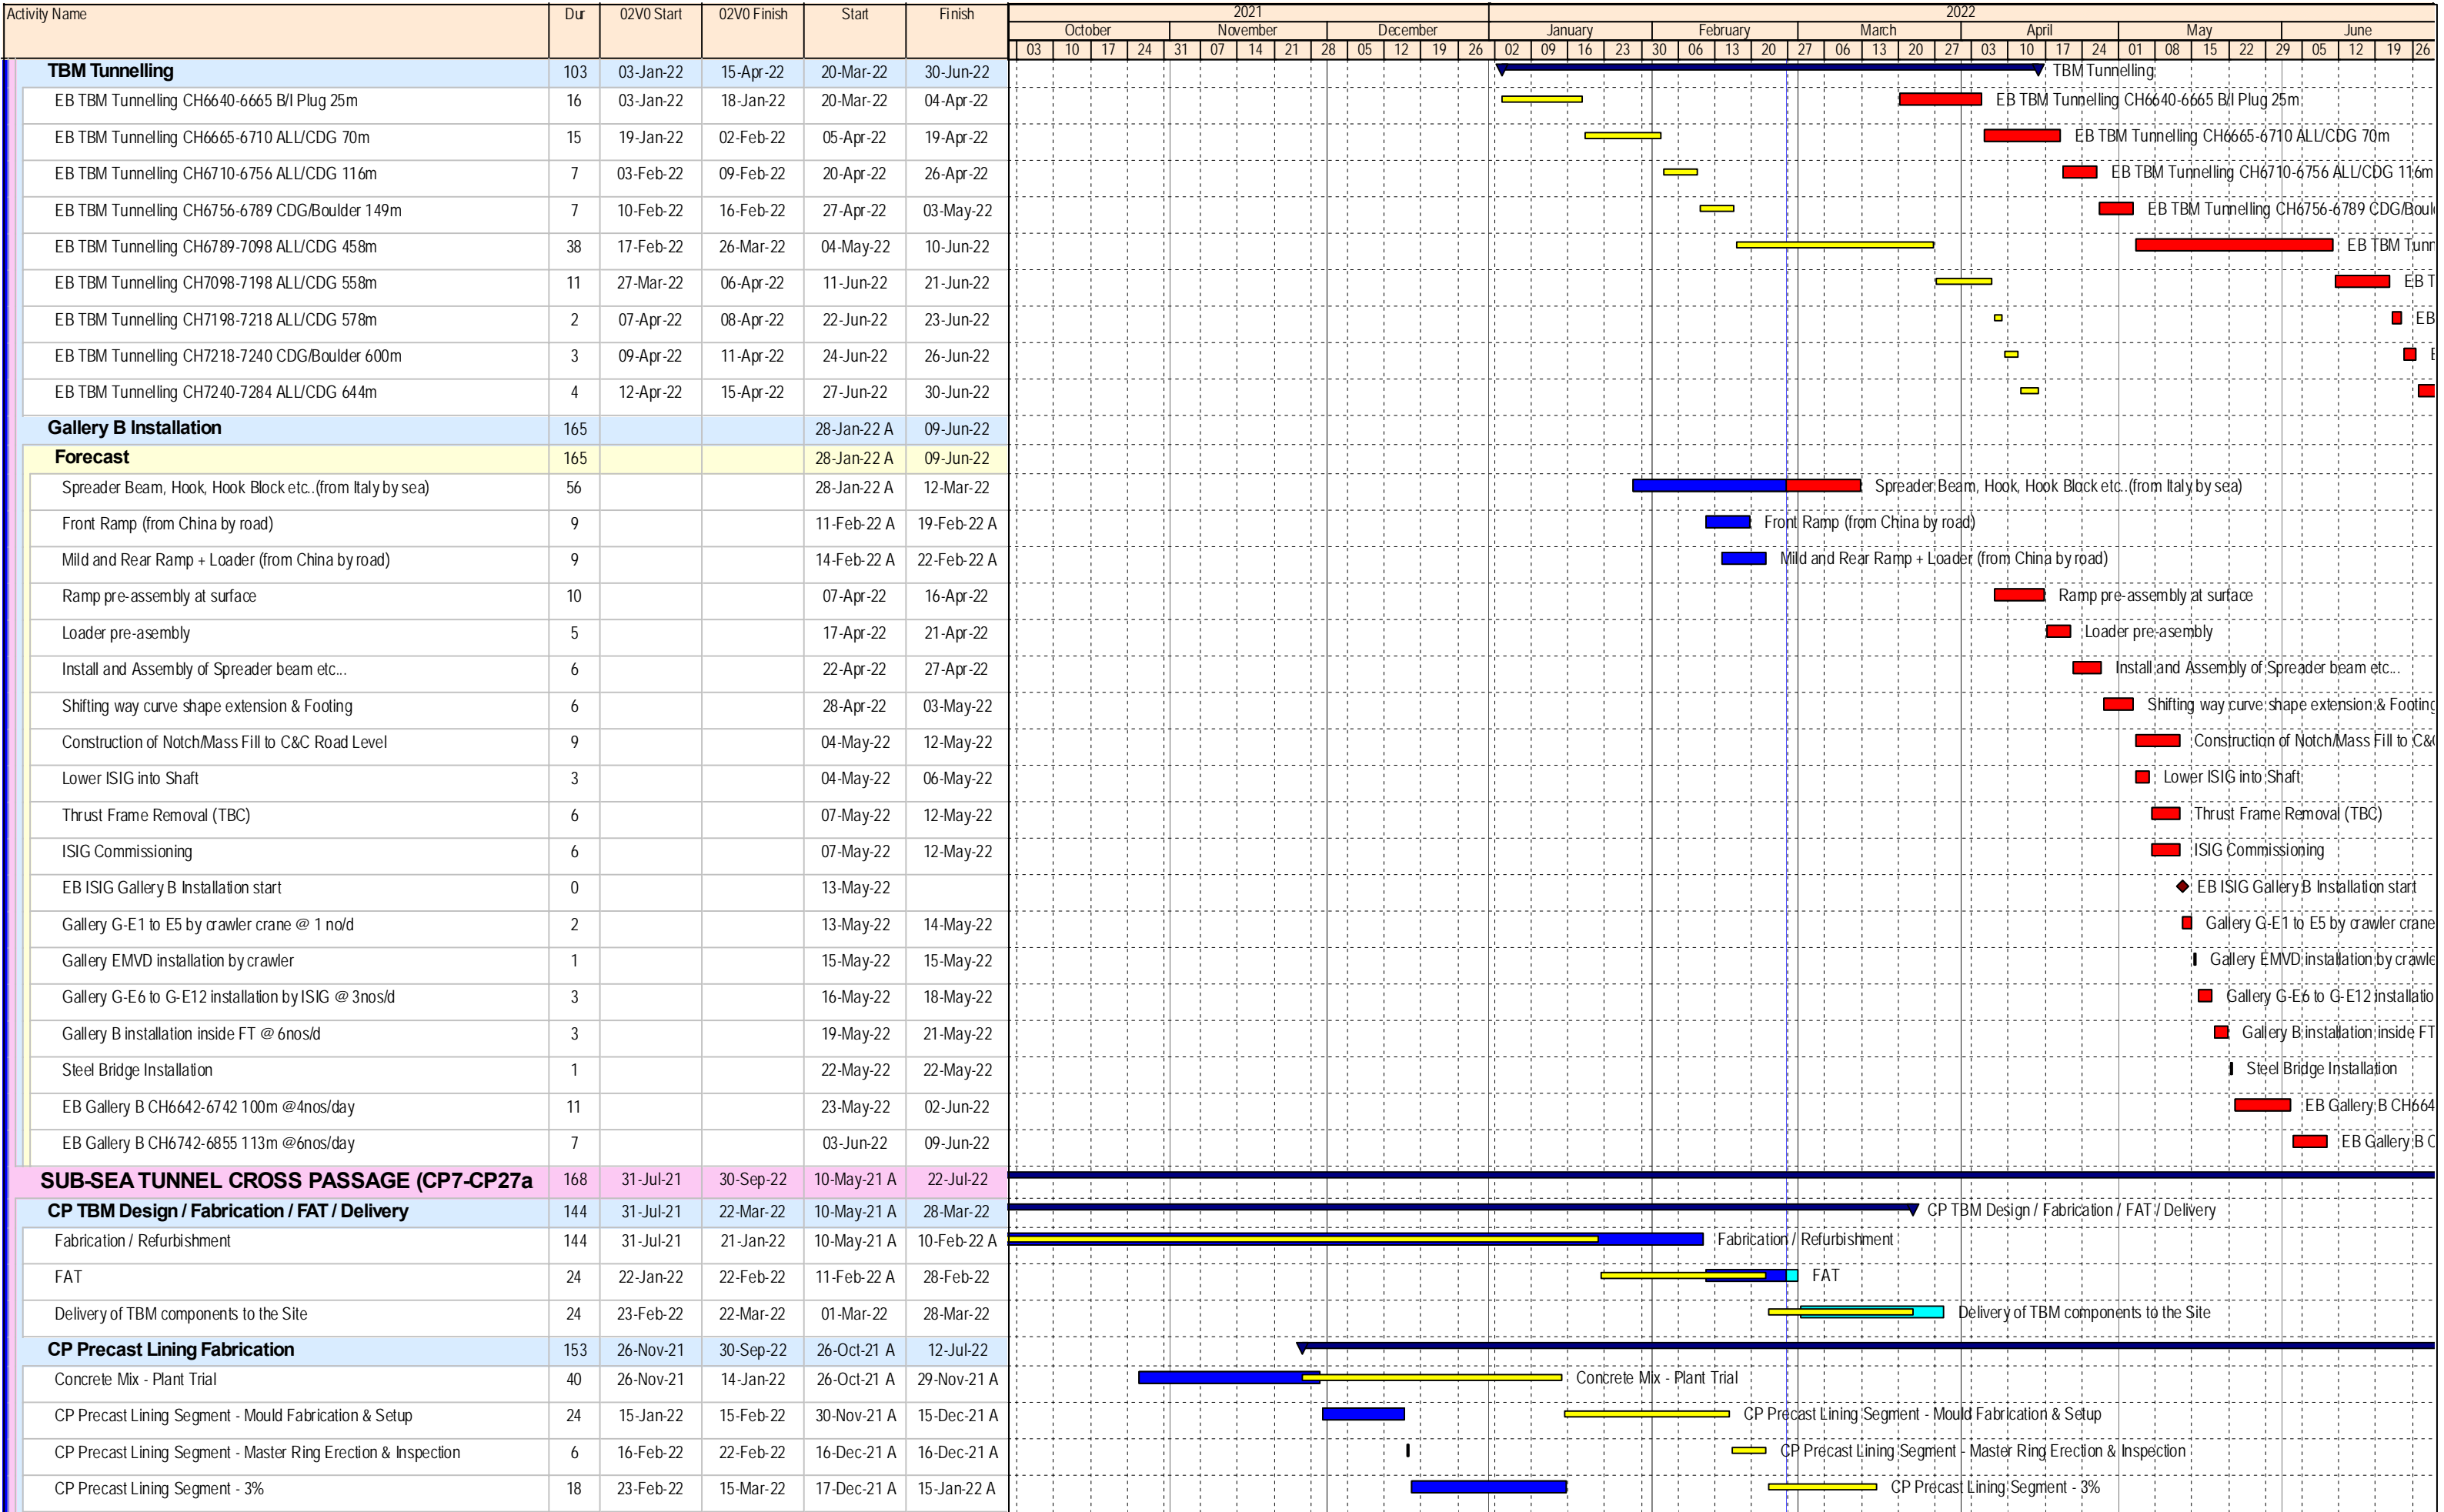


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar
- ▶ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

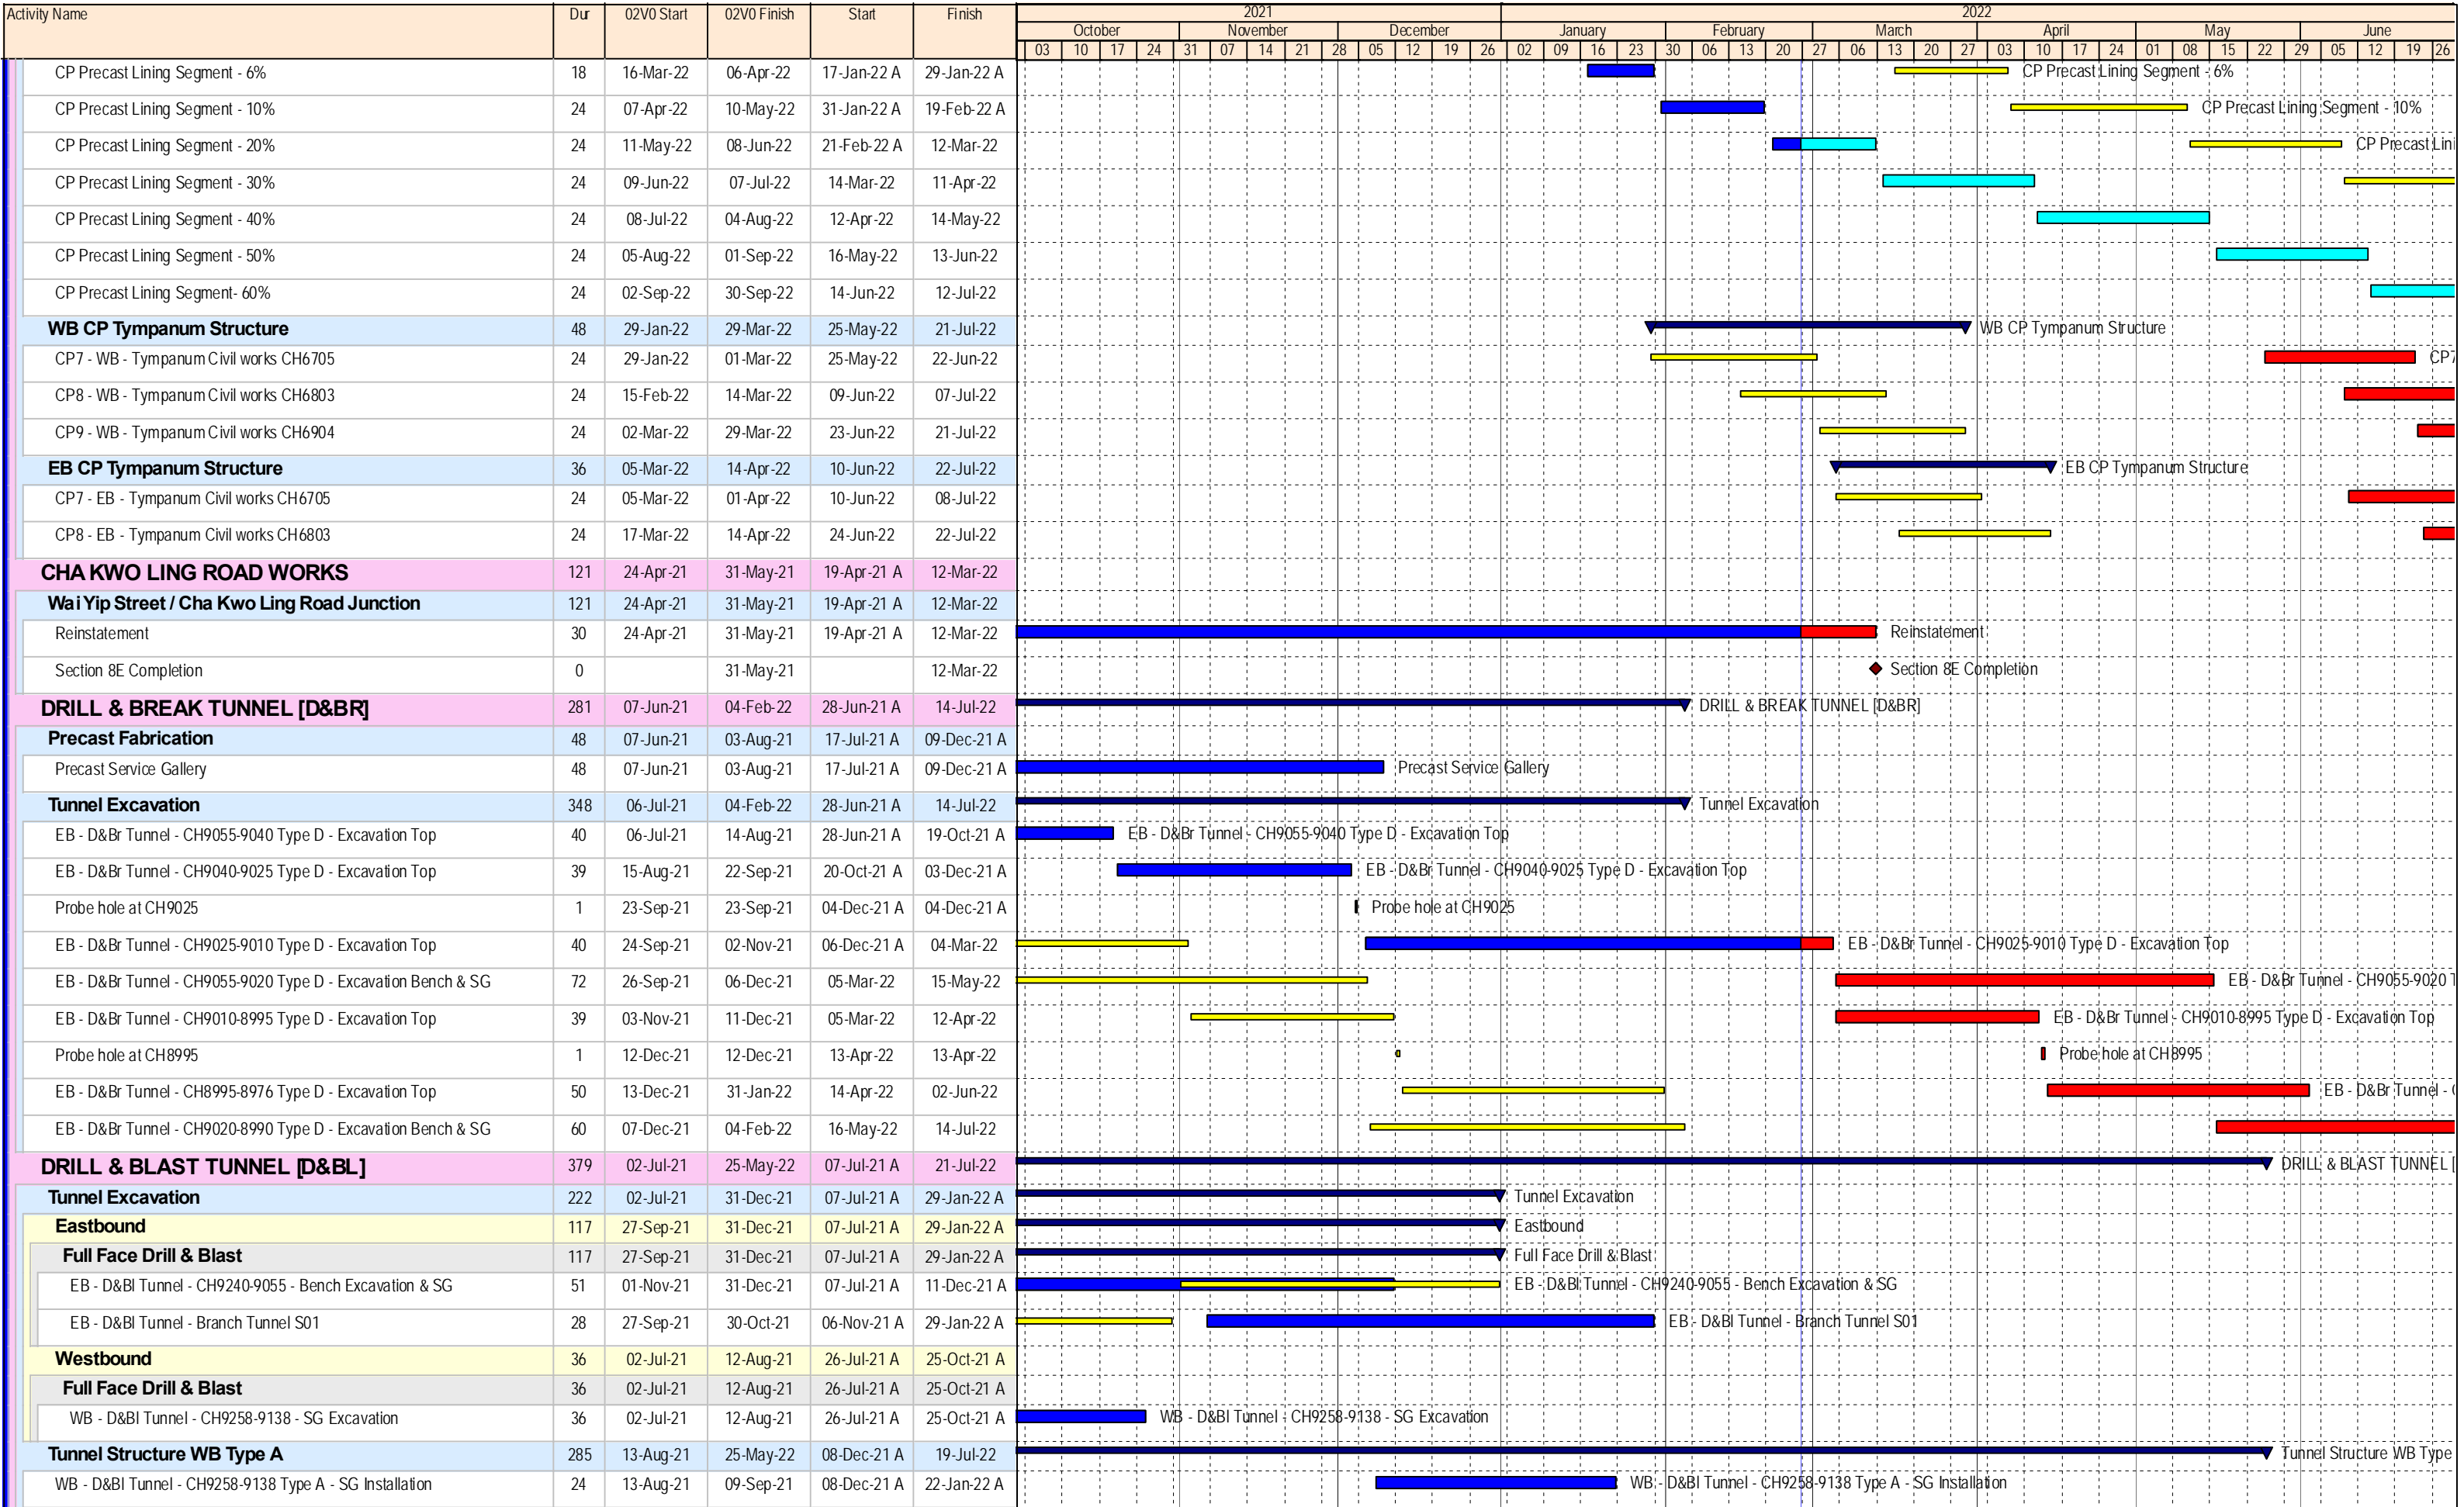


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

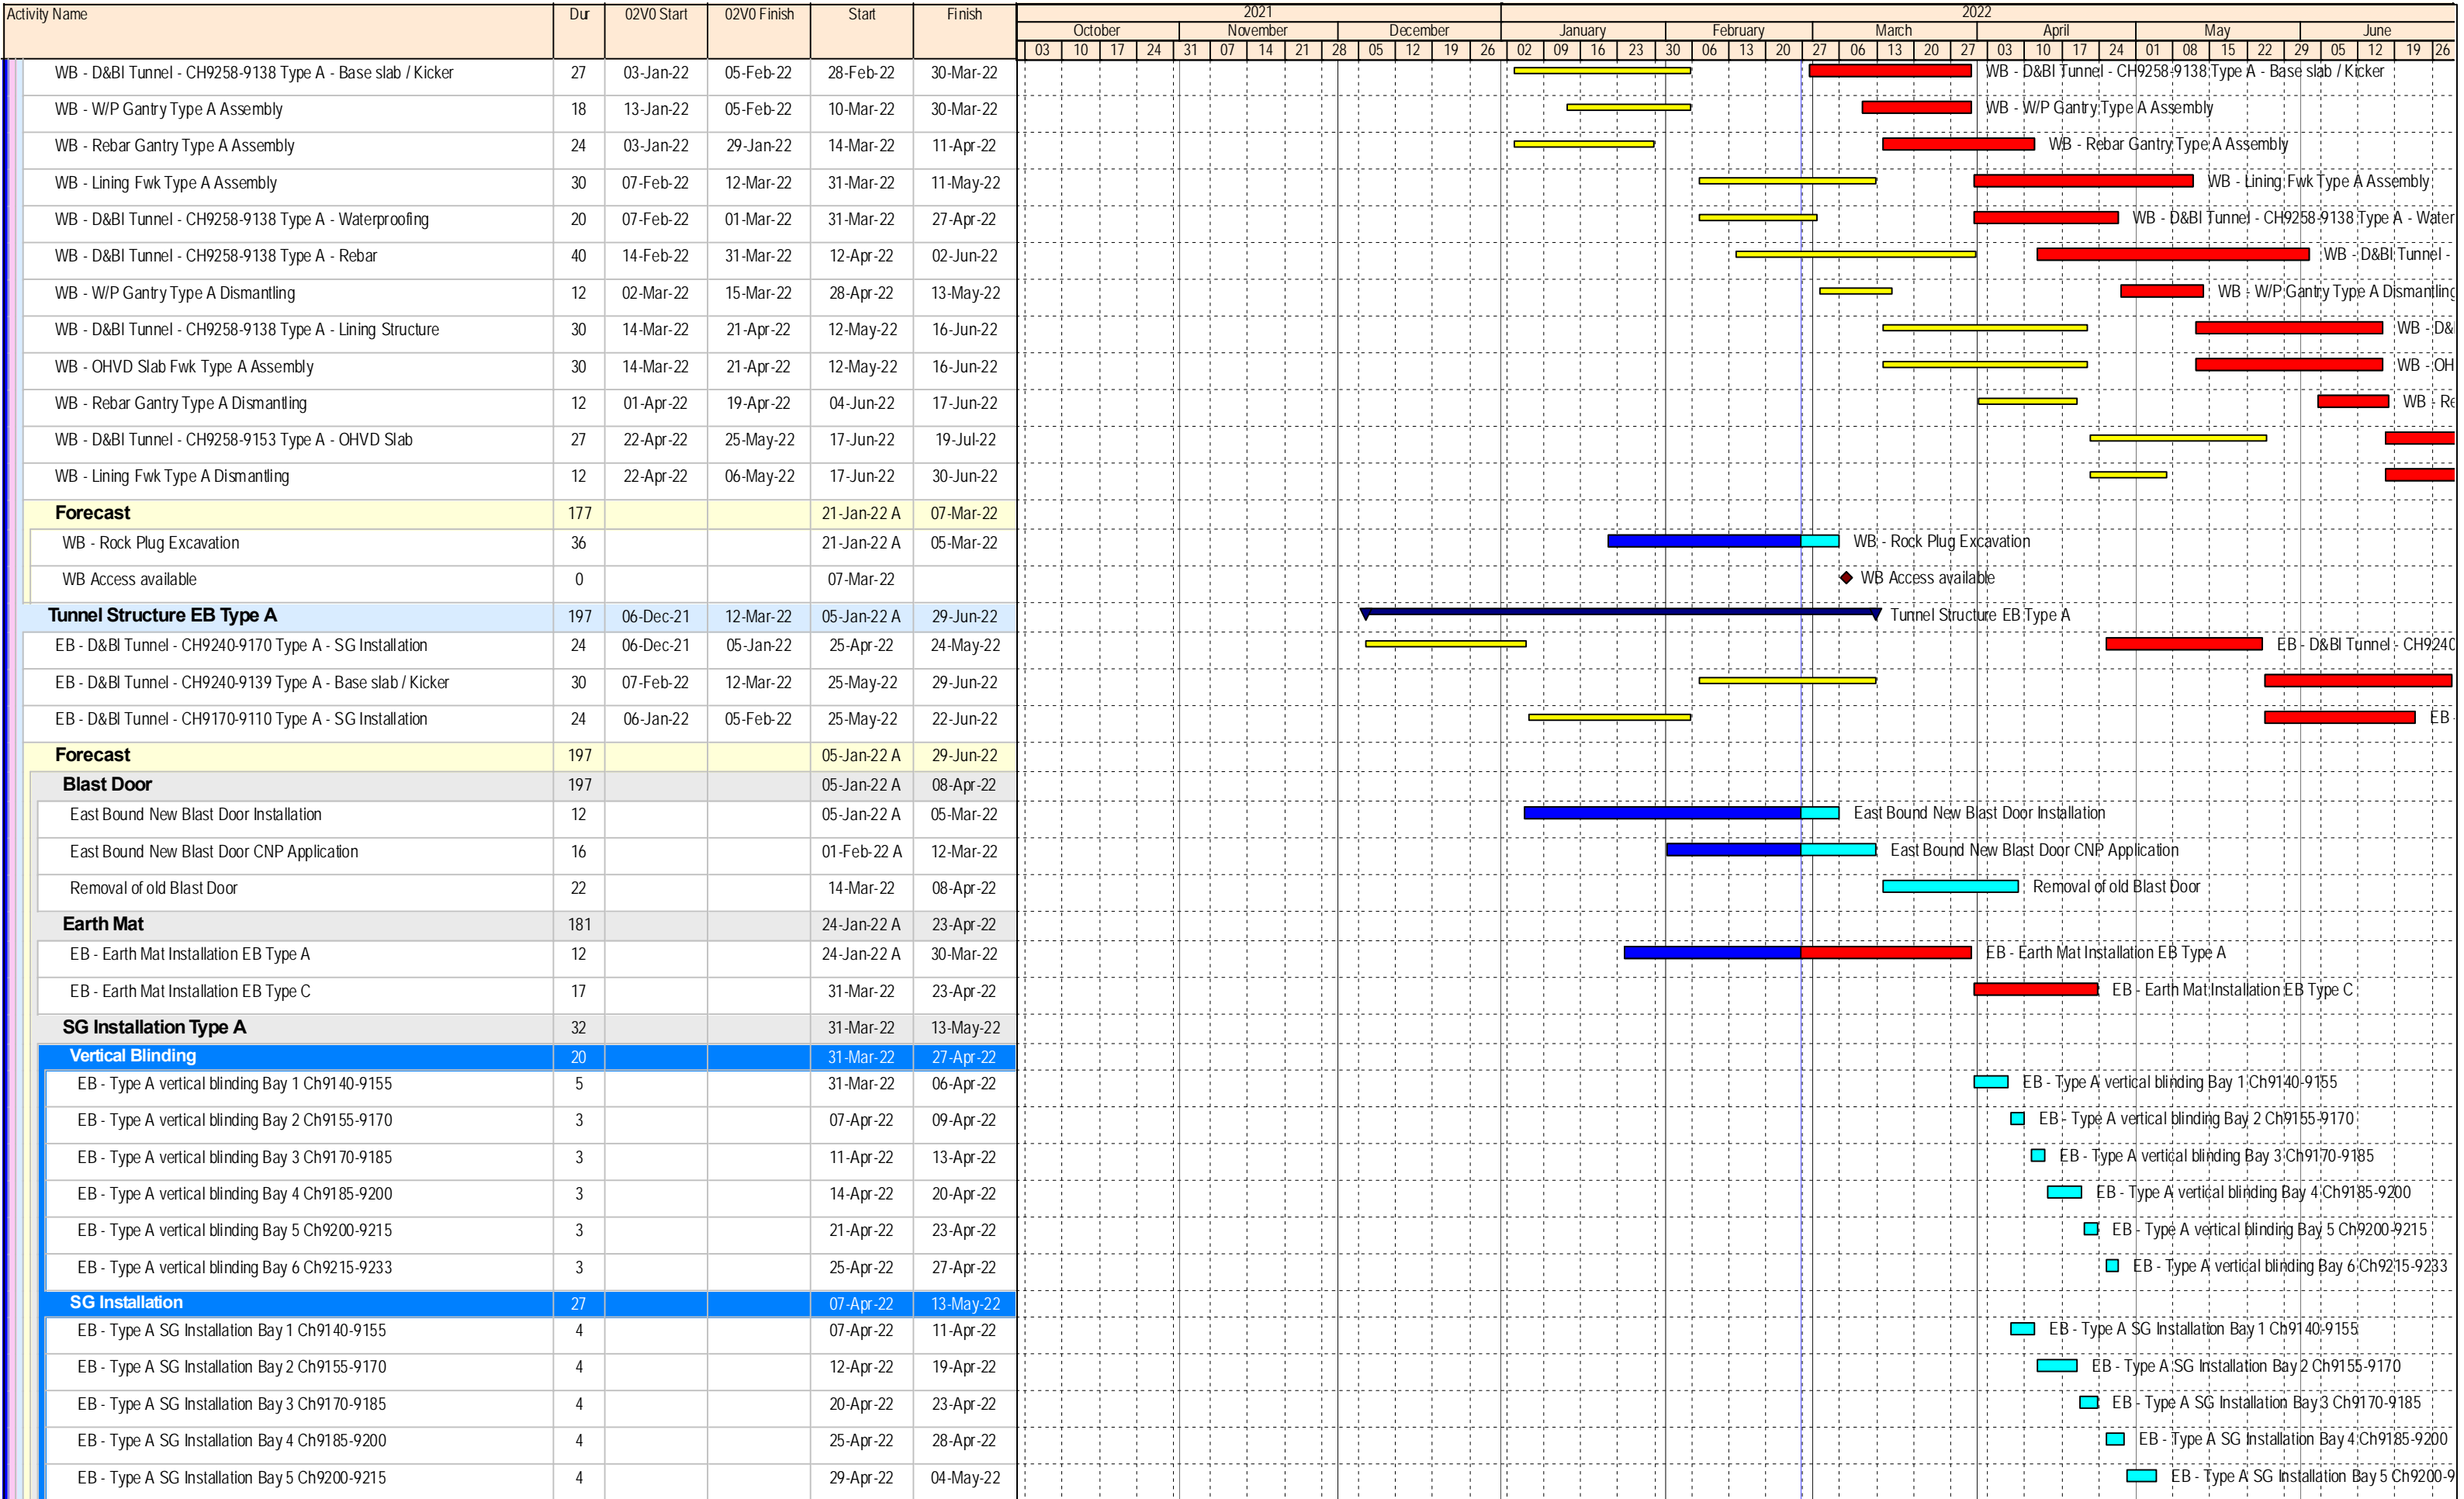

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

