

Page 1 of 27
Data Date: 28-Feb-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

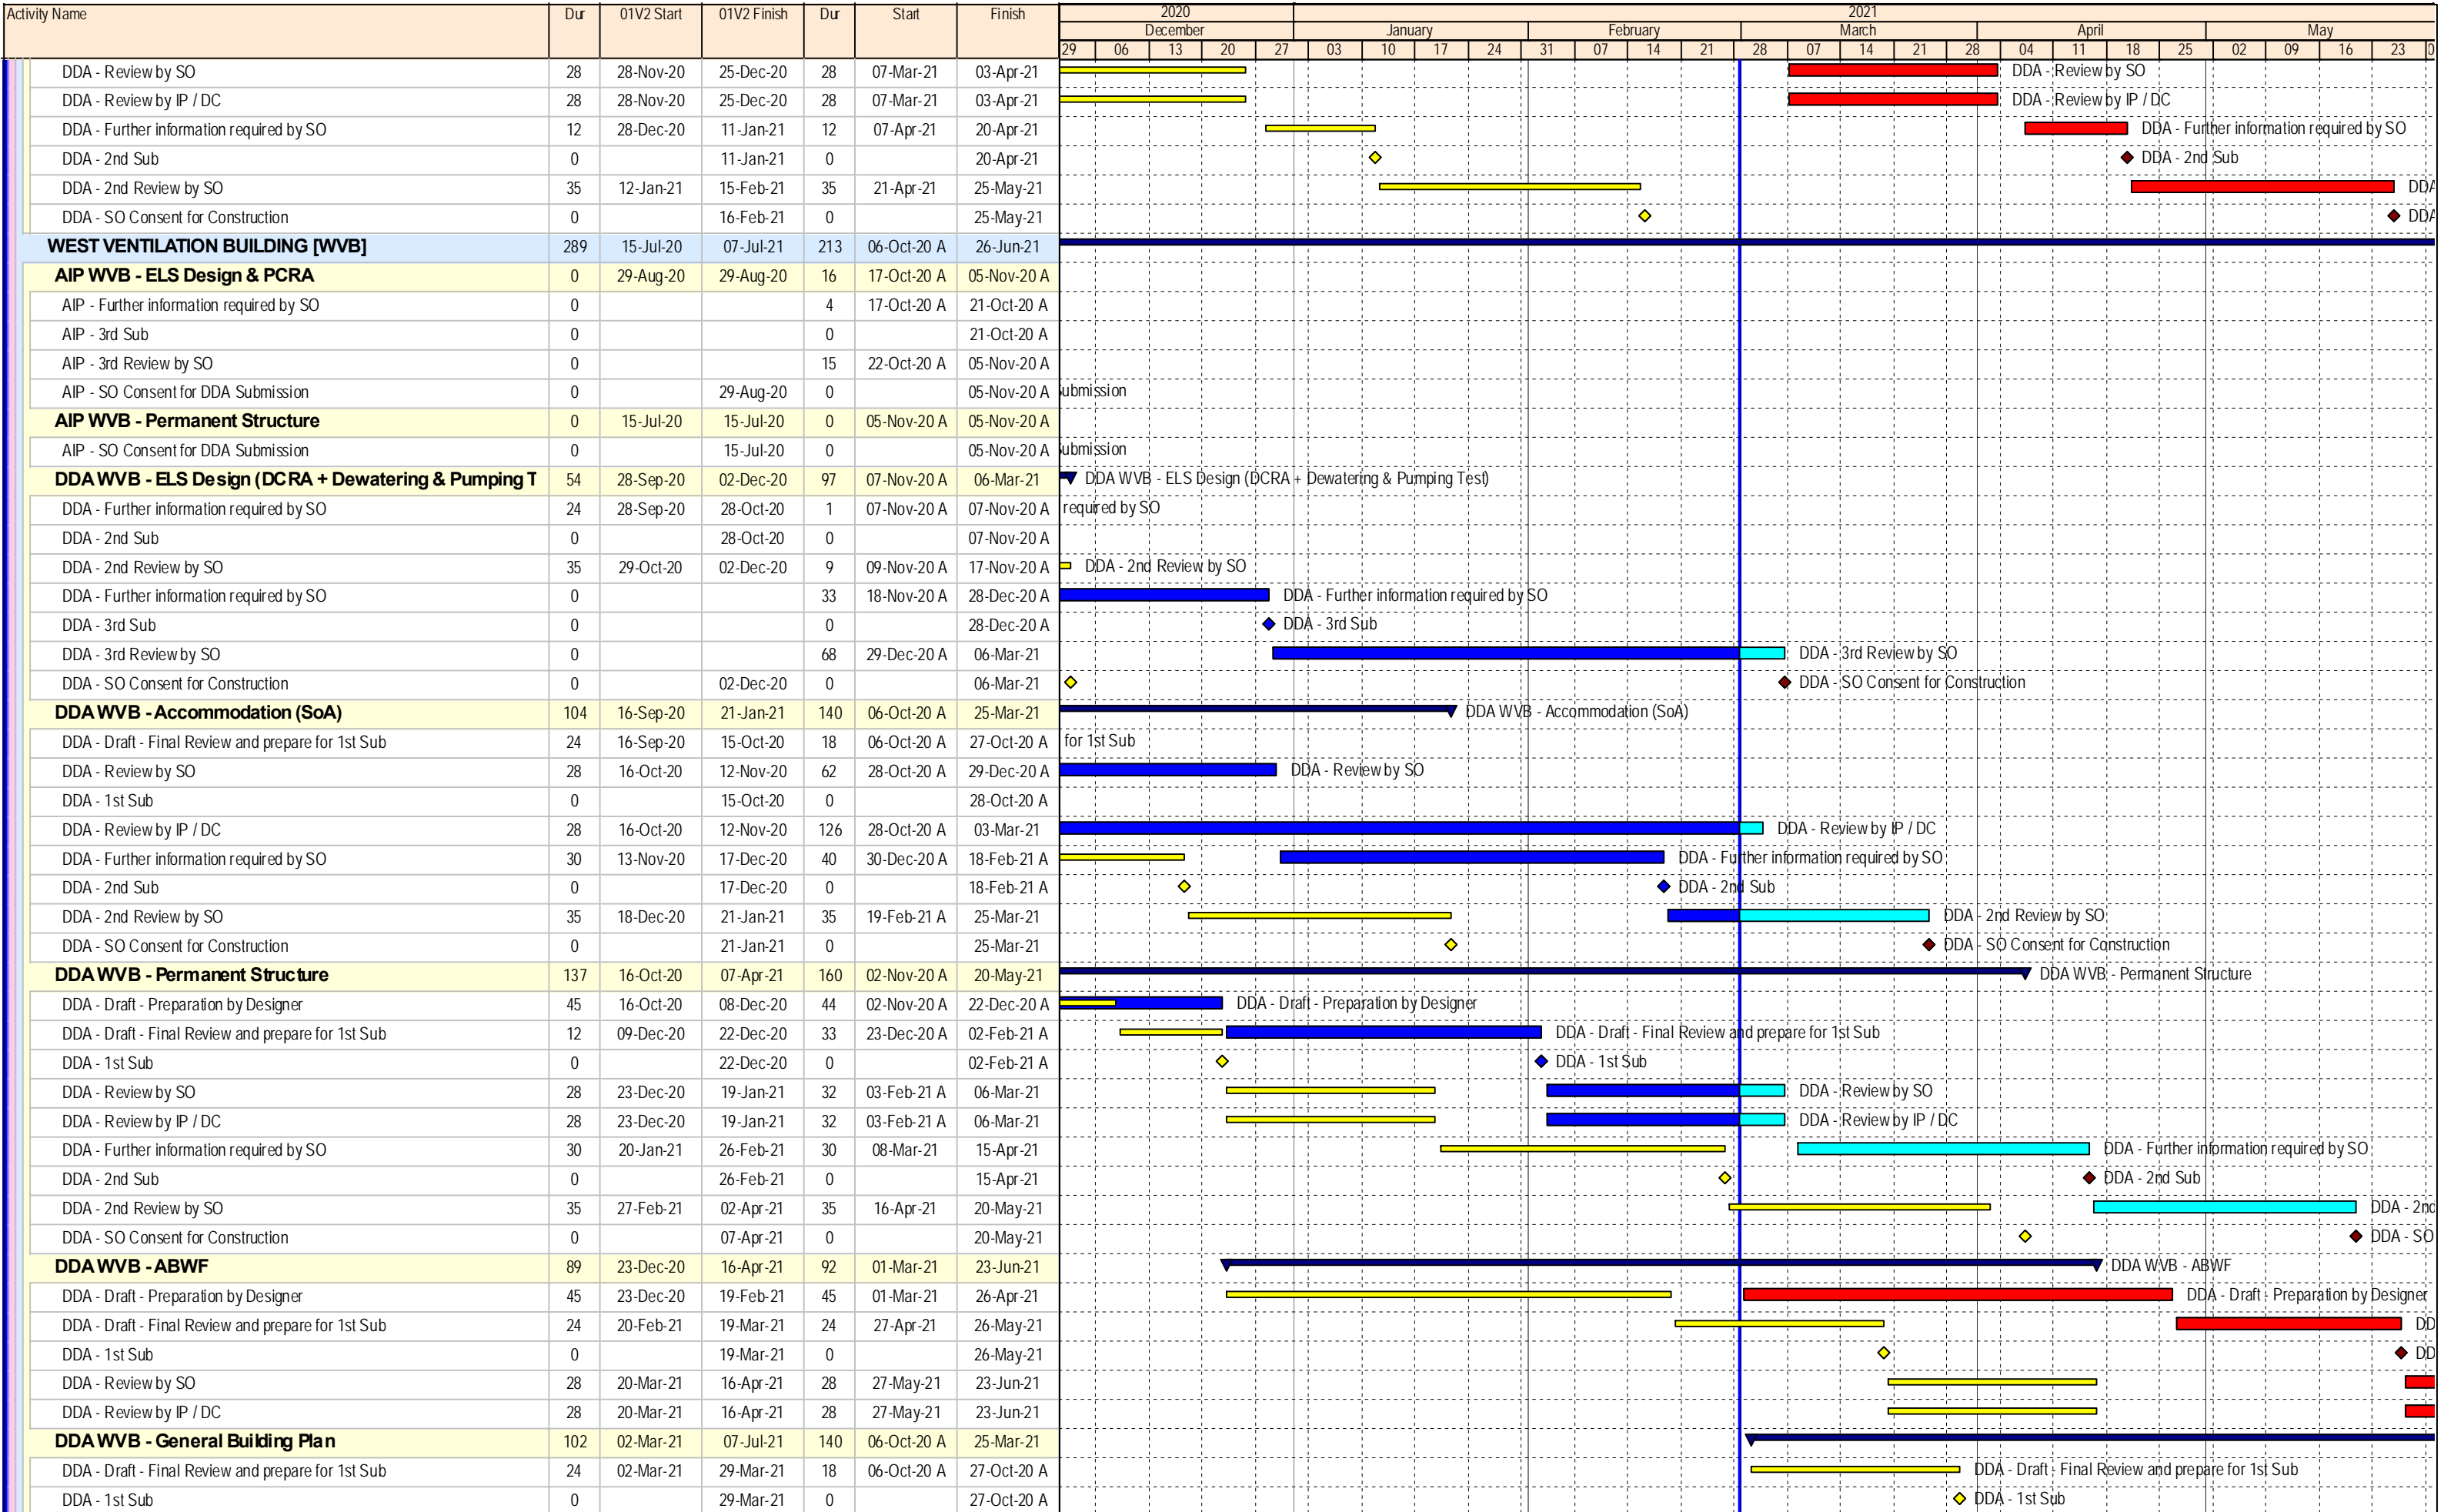

Page 4 of 27
Data Date: 28-Feb-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

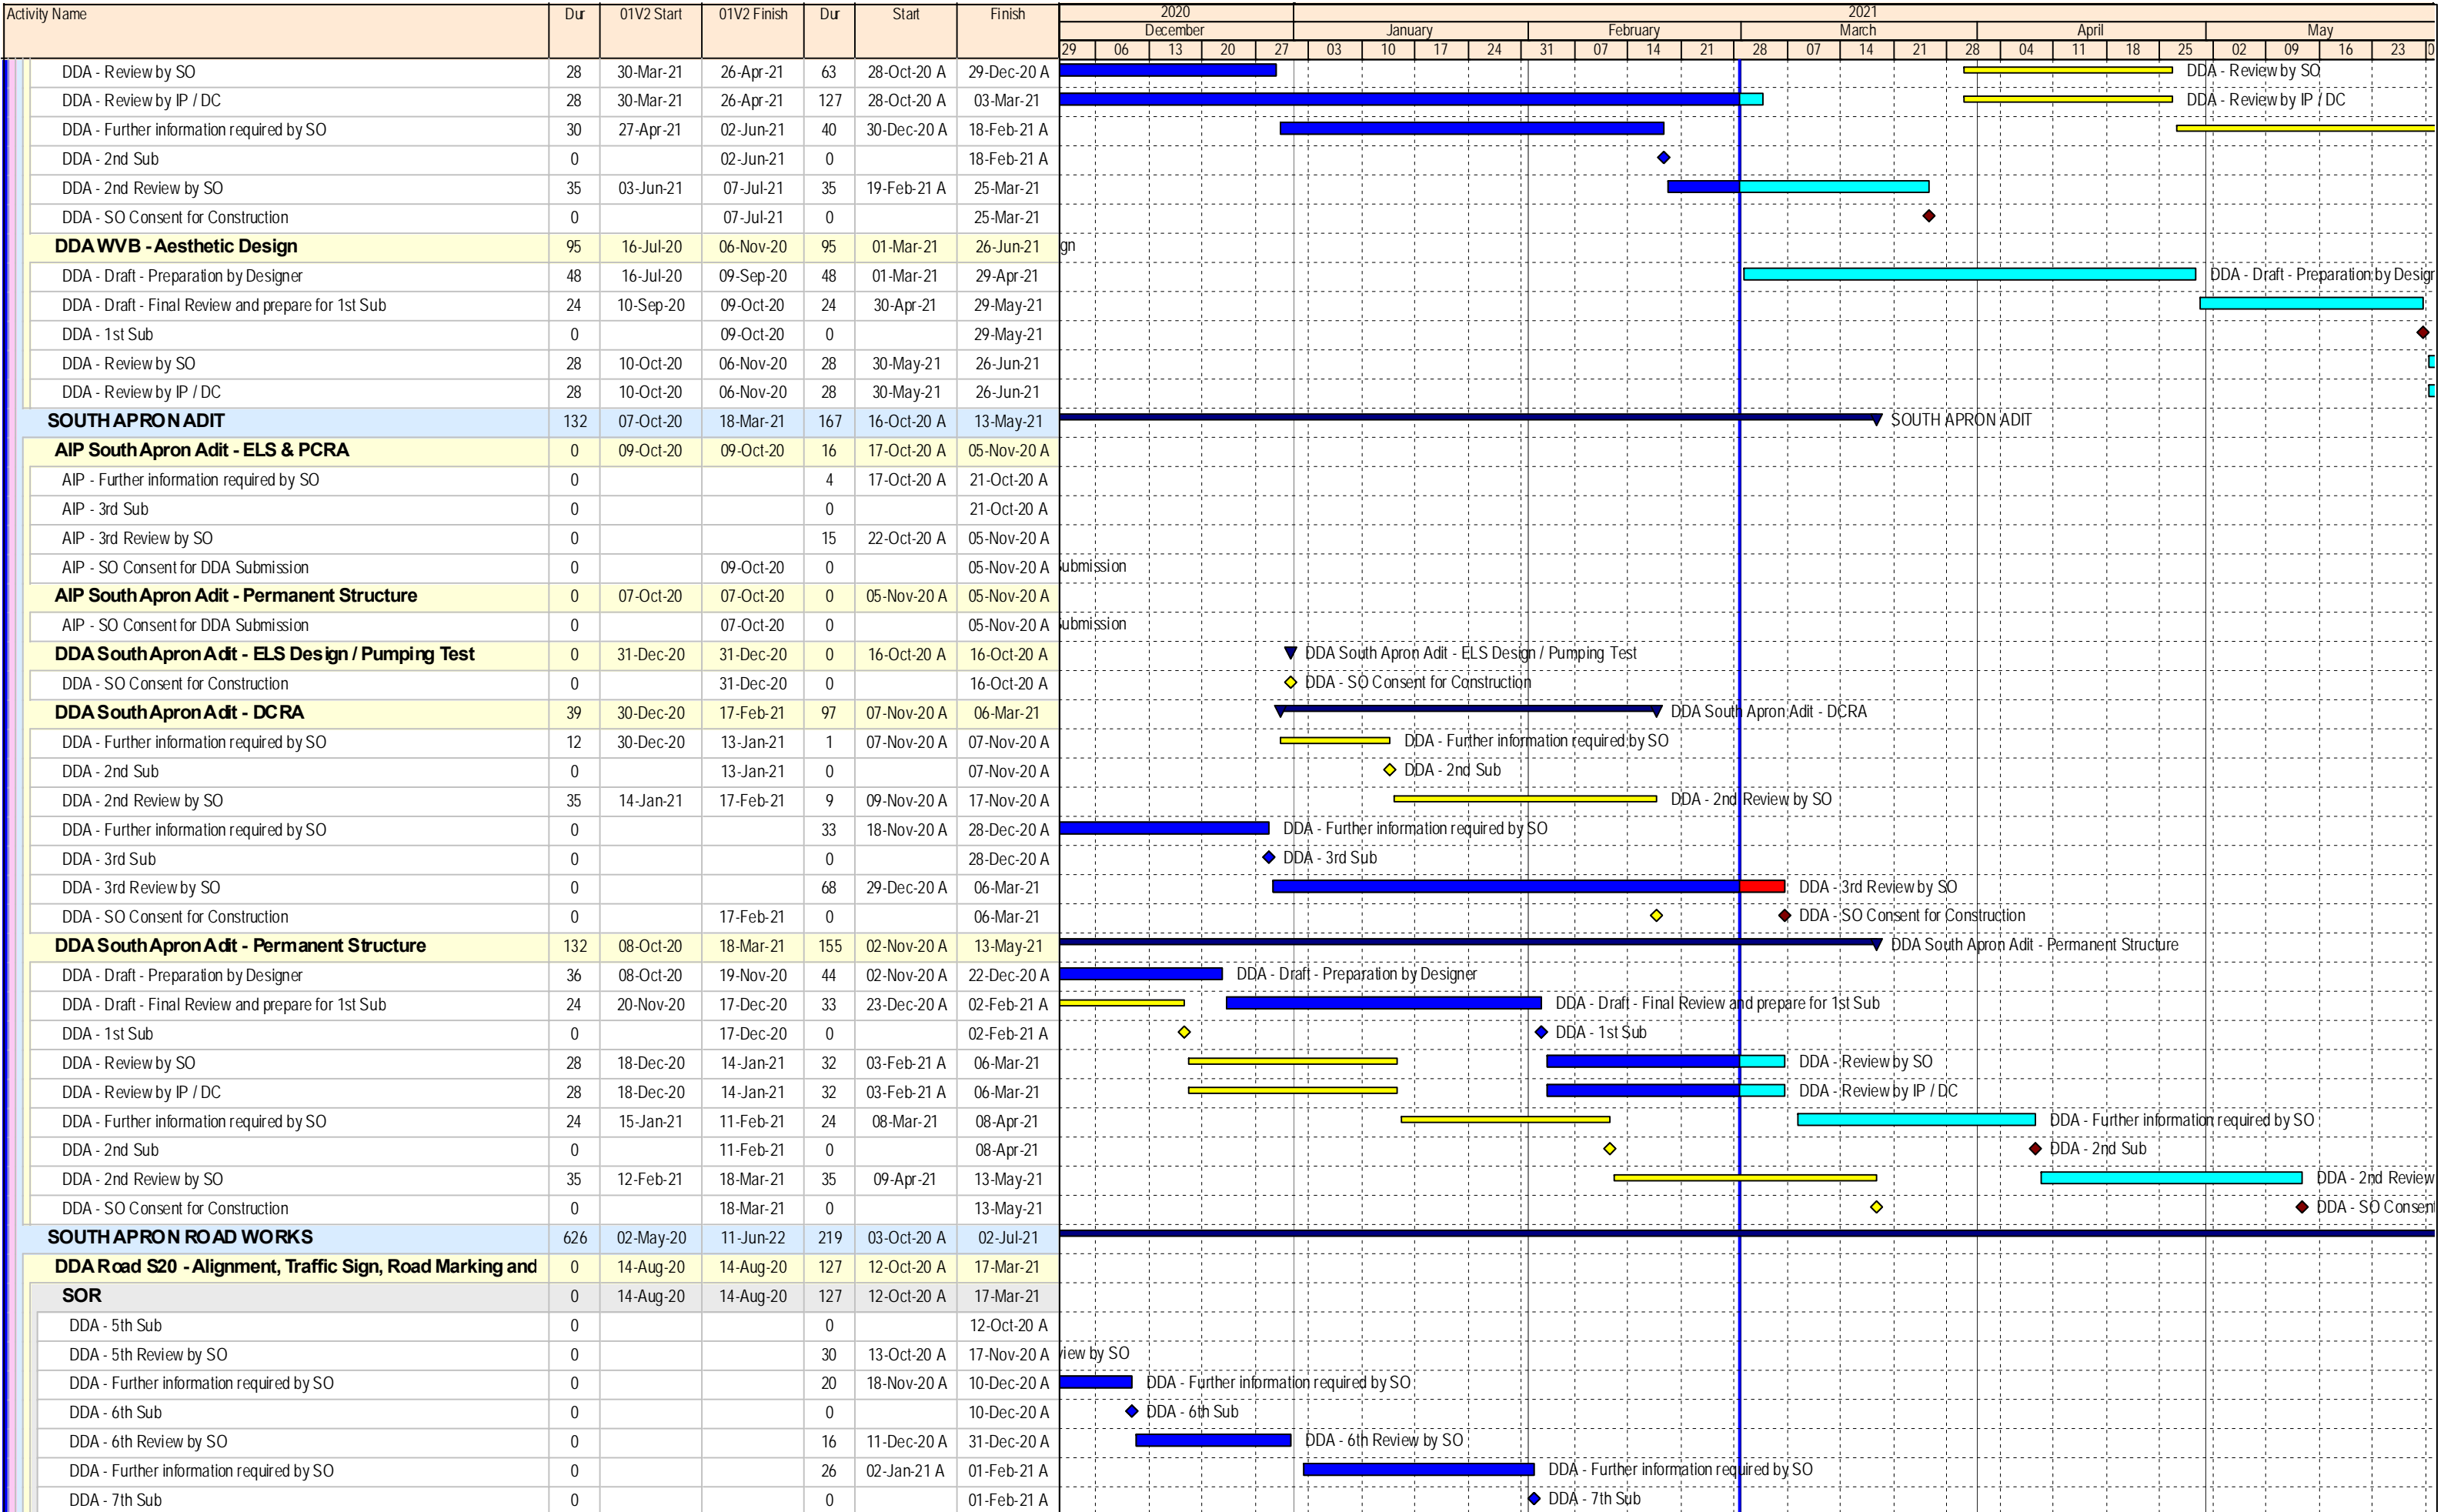

Page 5 of 27
Data Date: 28-Feb-21


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

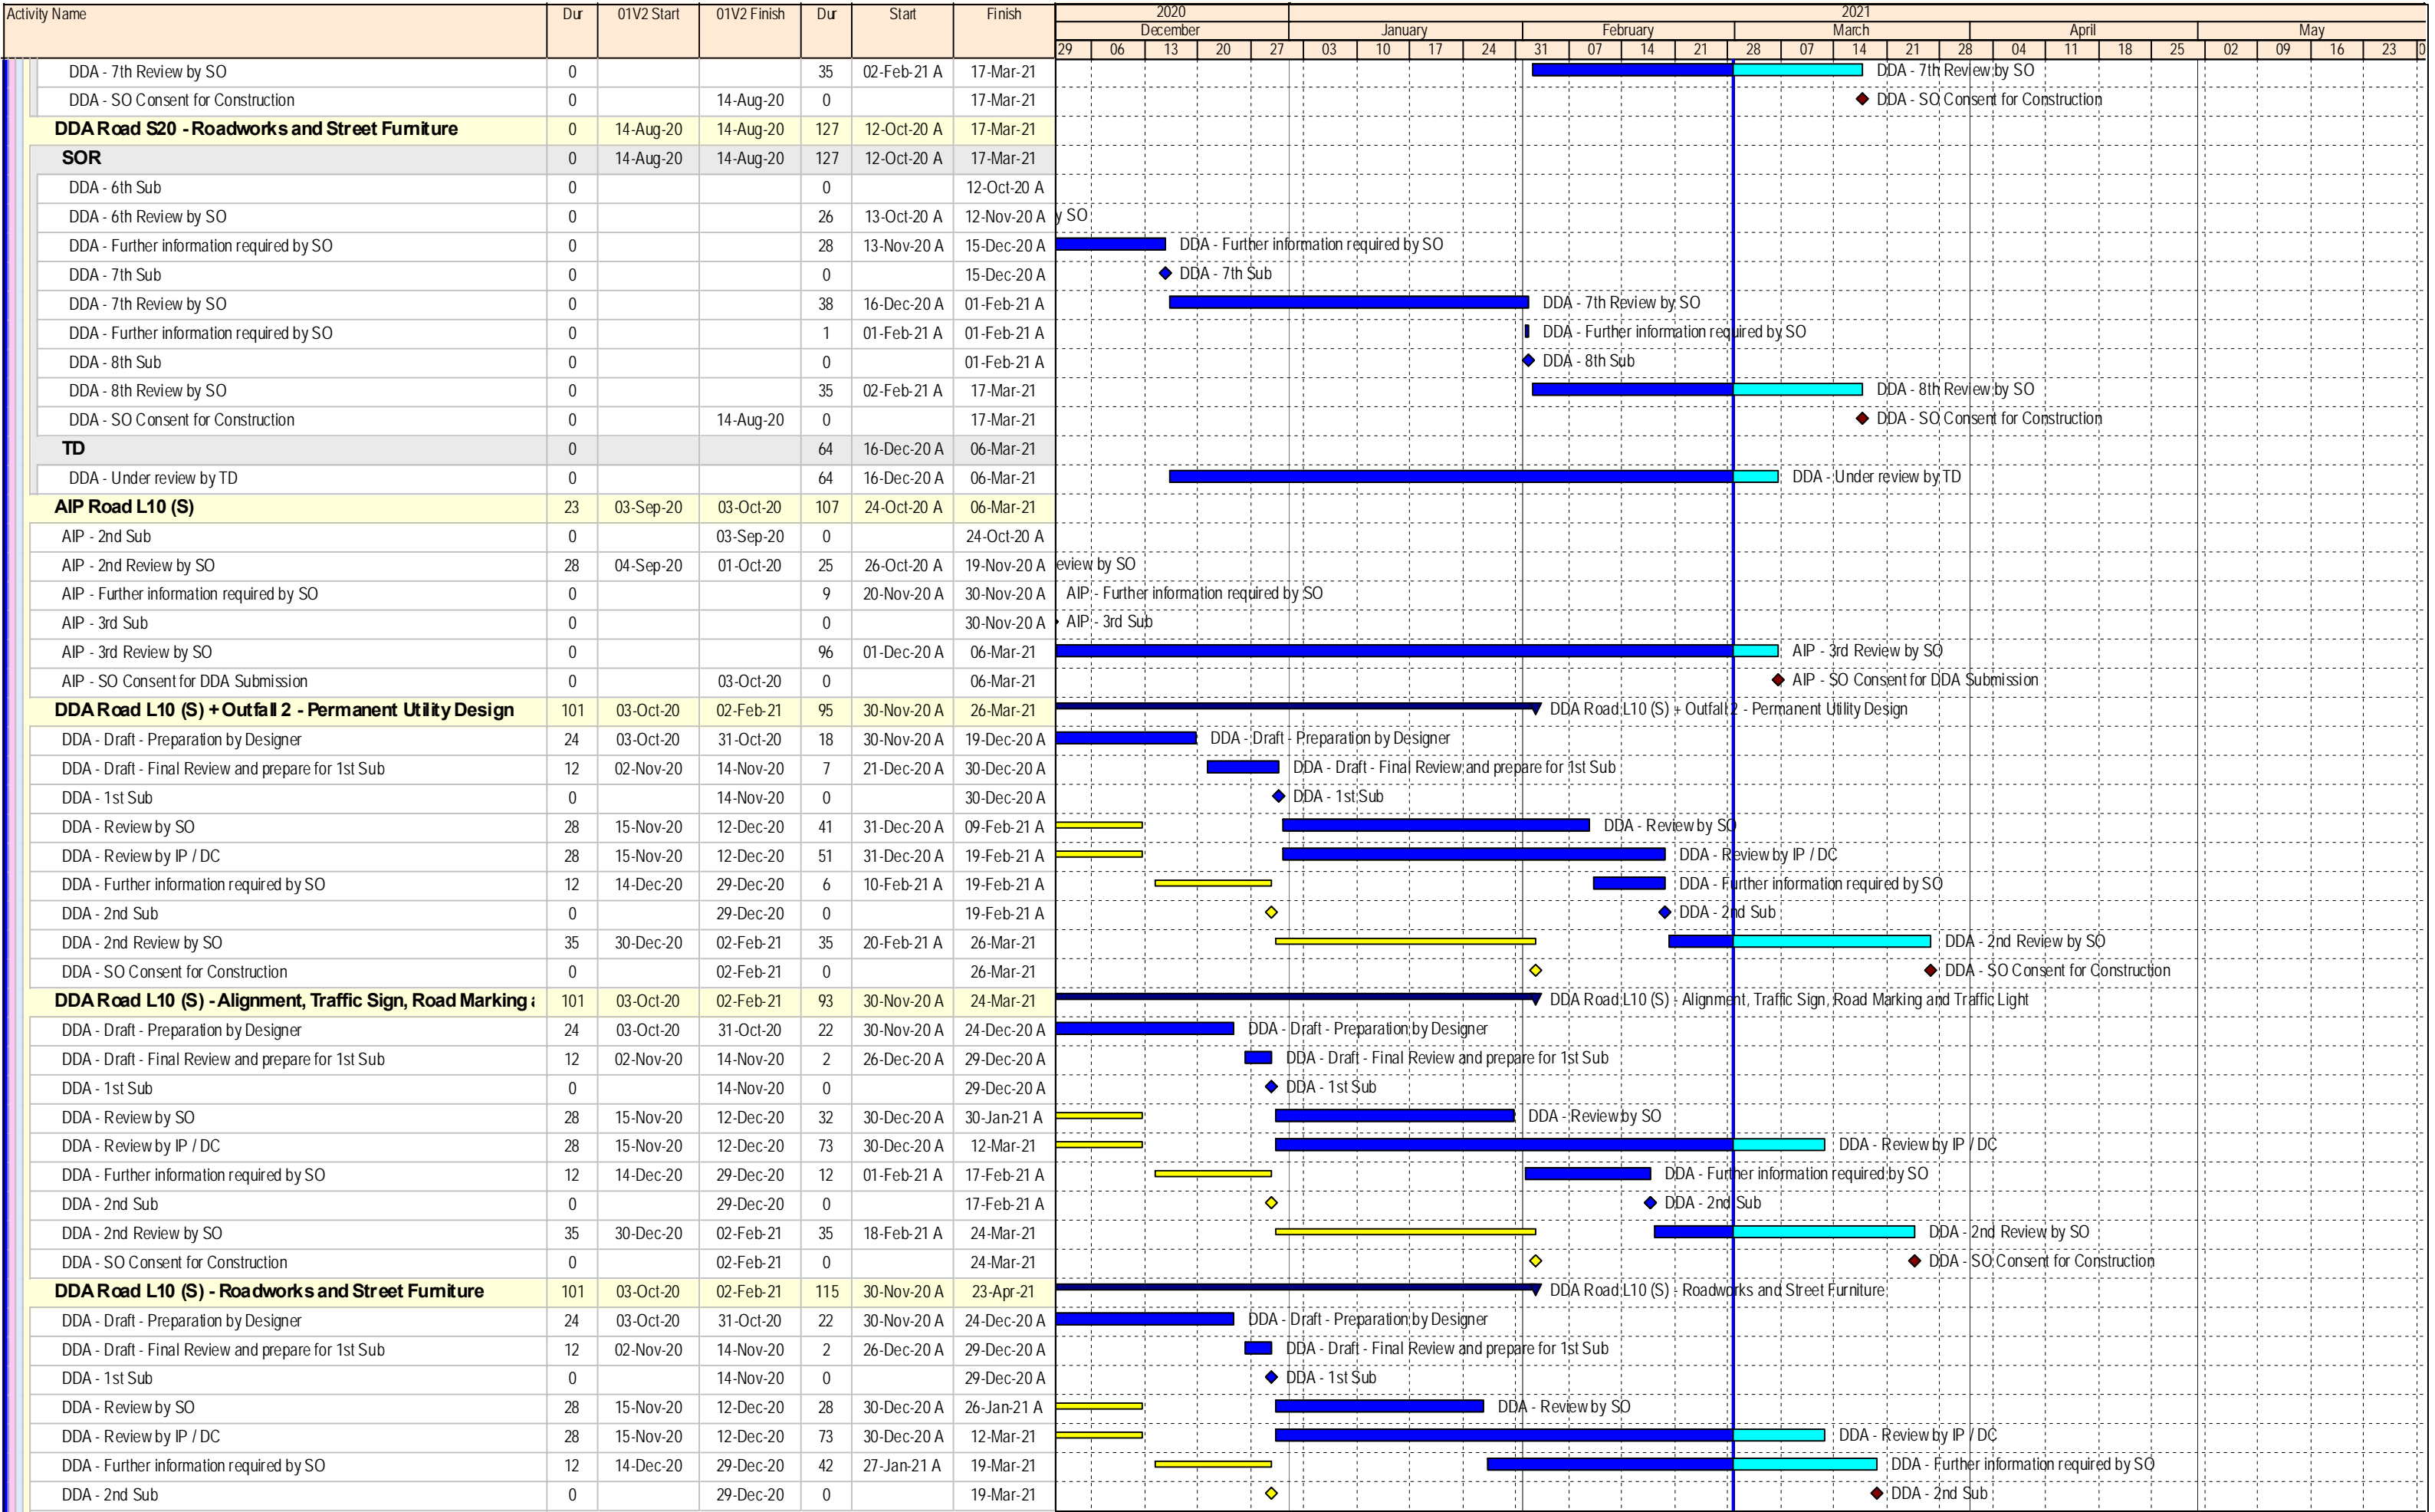

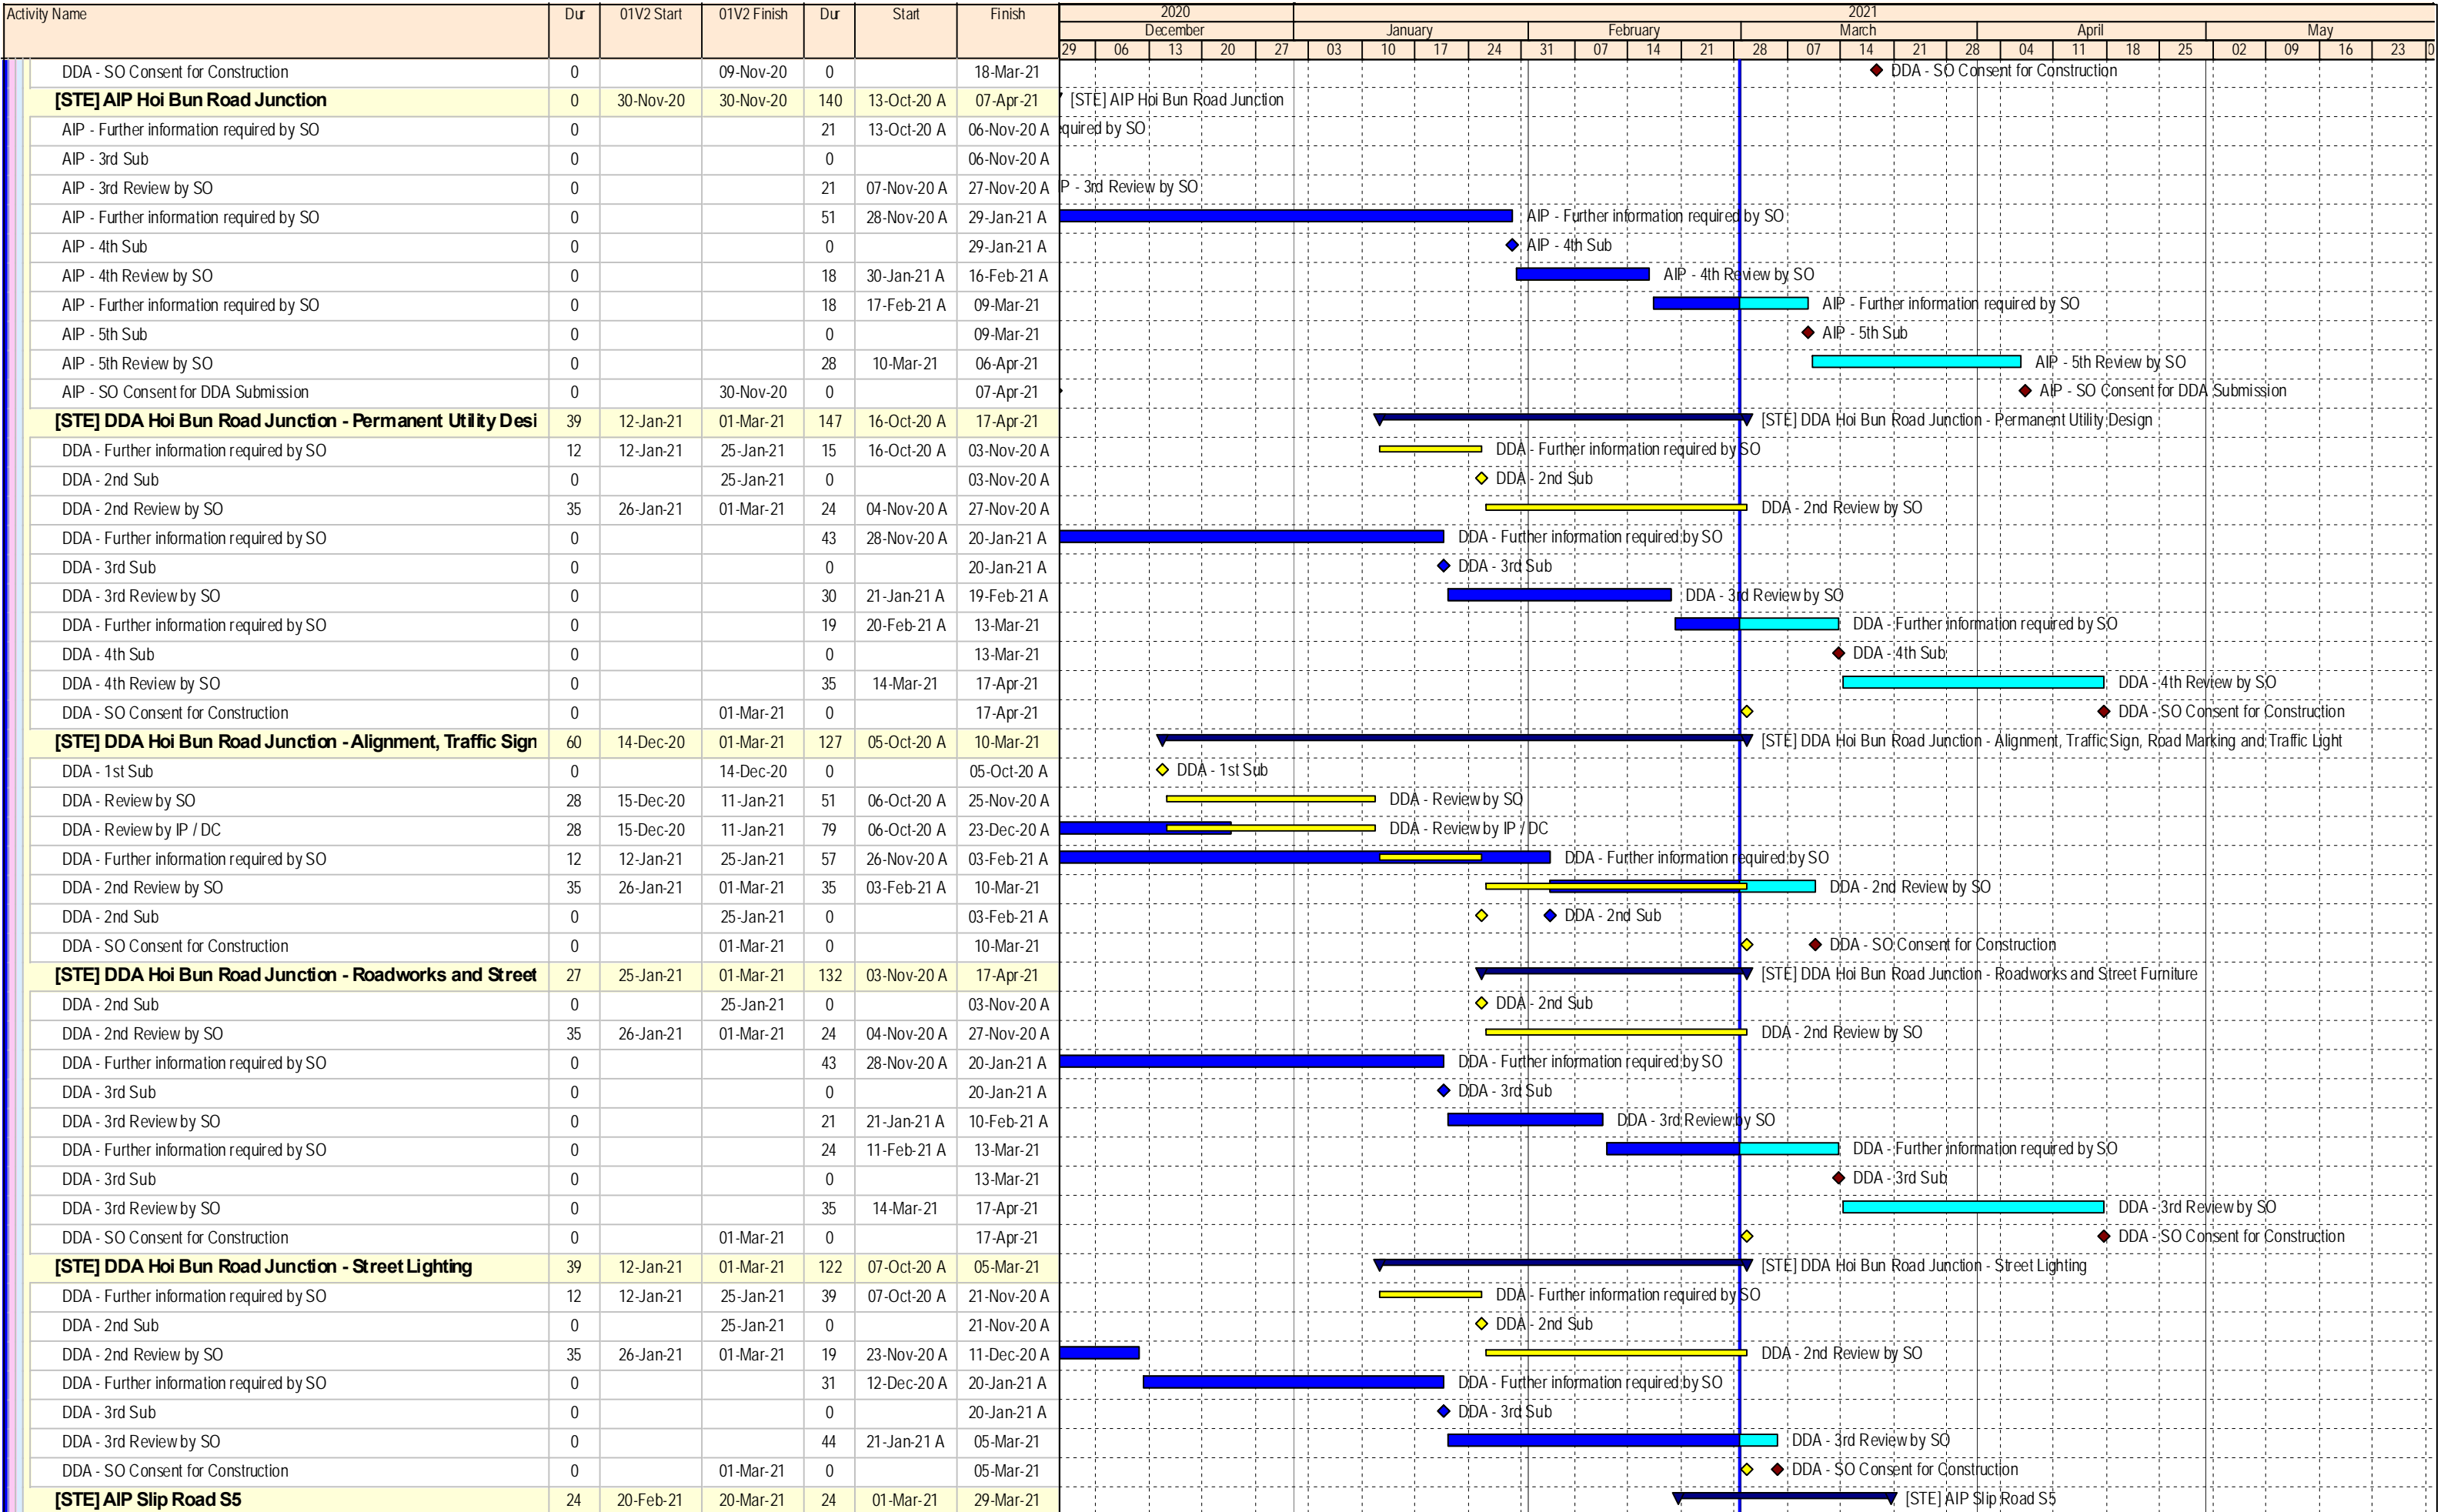


Page 9 of 27
Data Date: 28-Feb-21


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

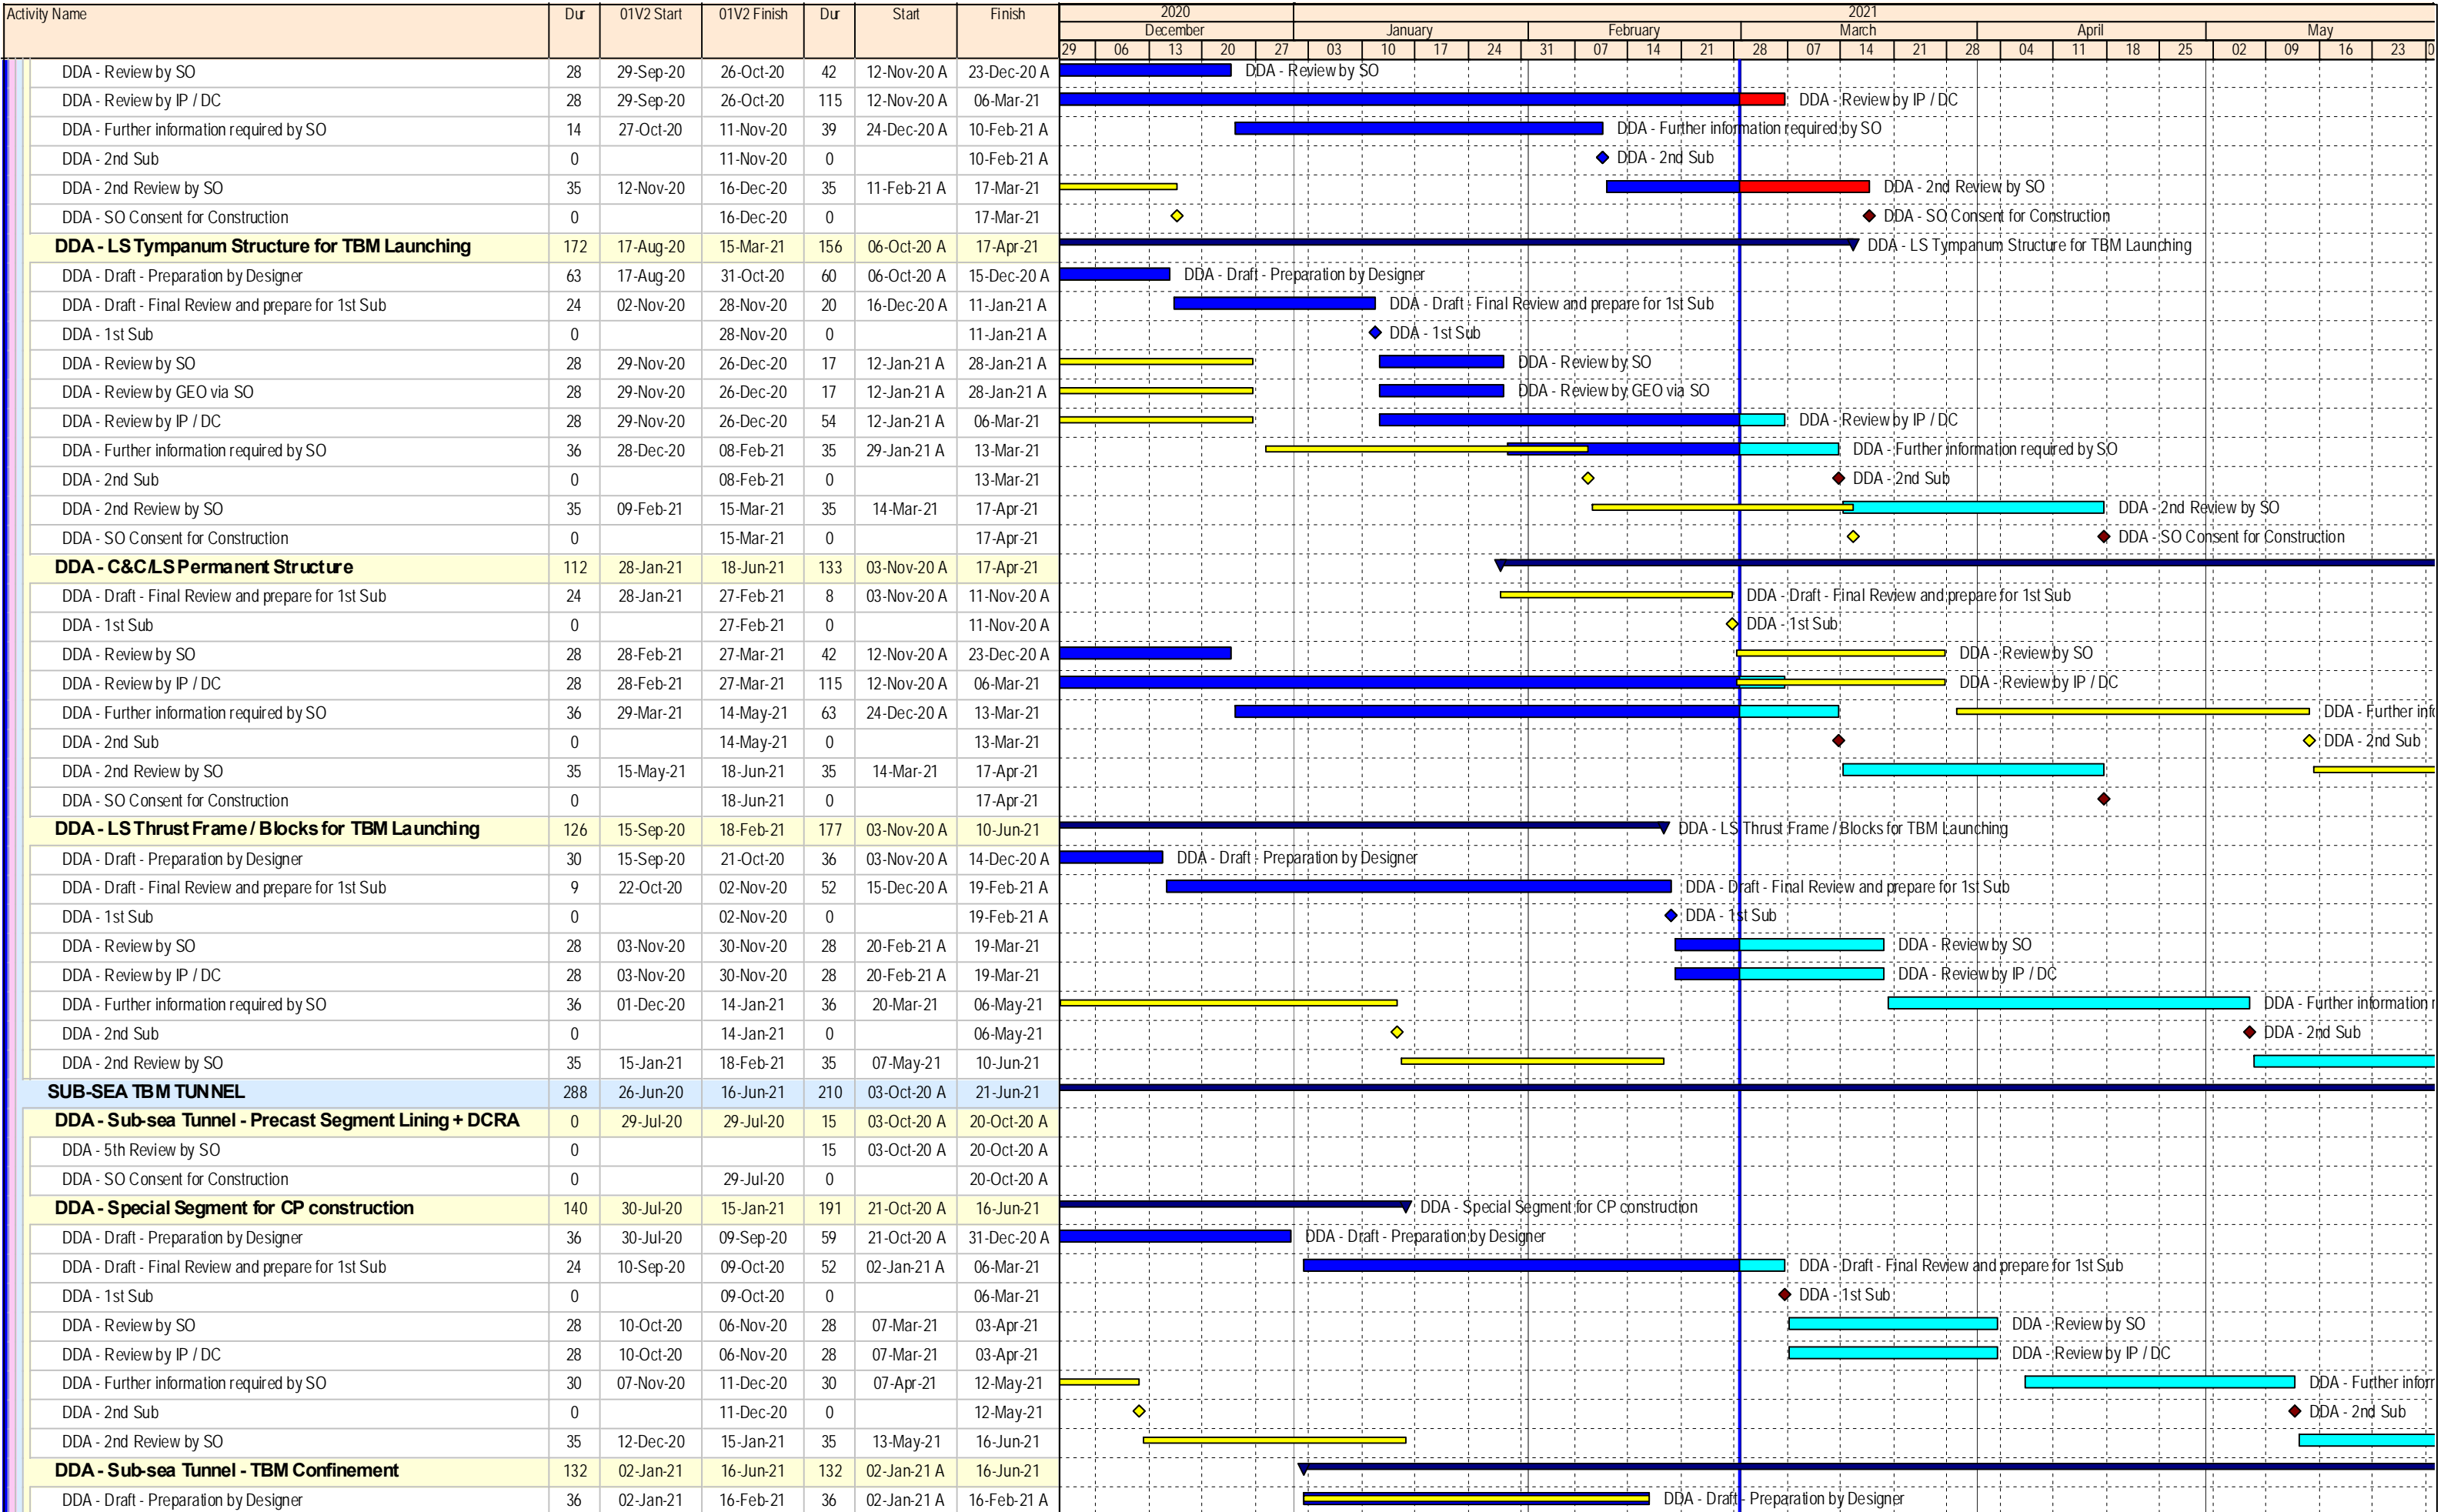


Page 11 of 27
Data Date: 28-Feb-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

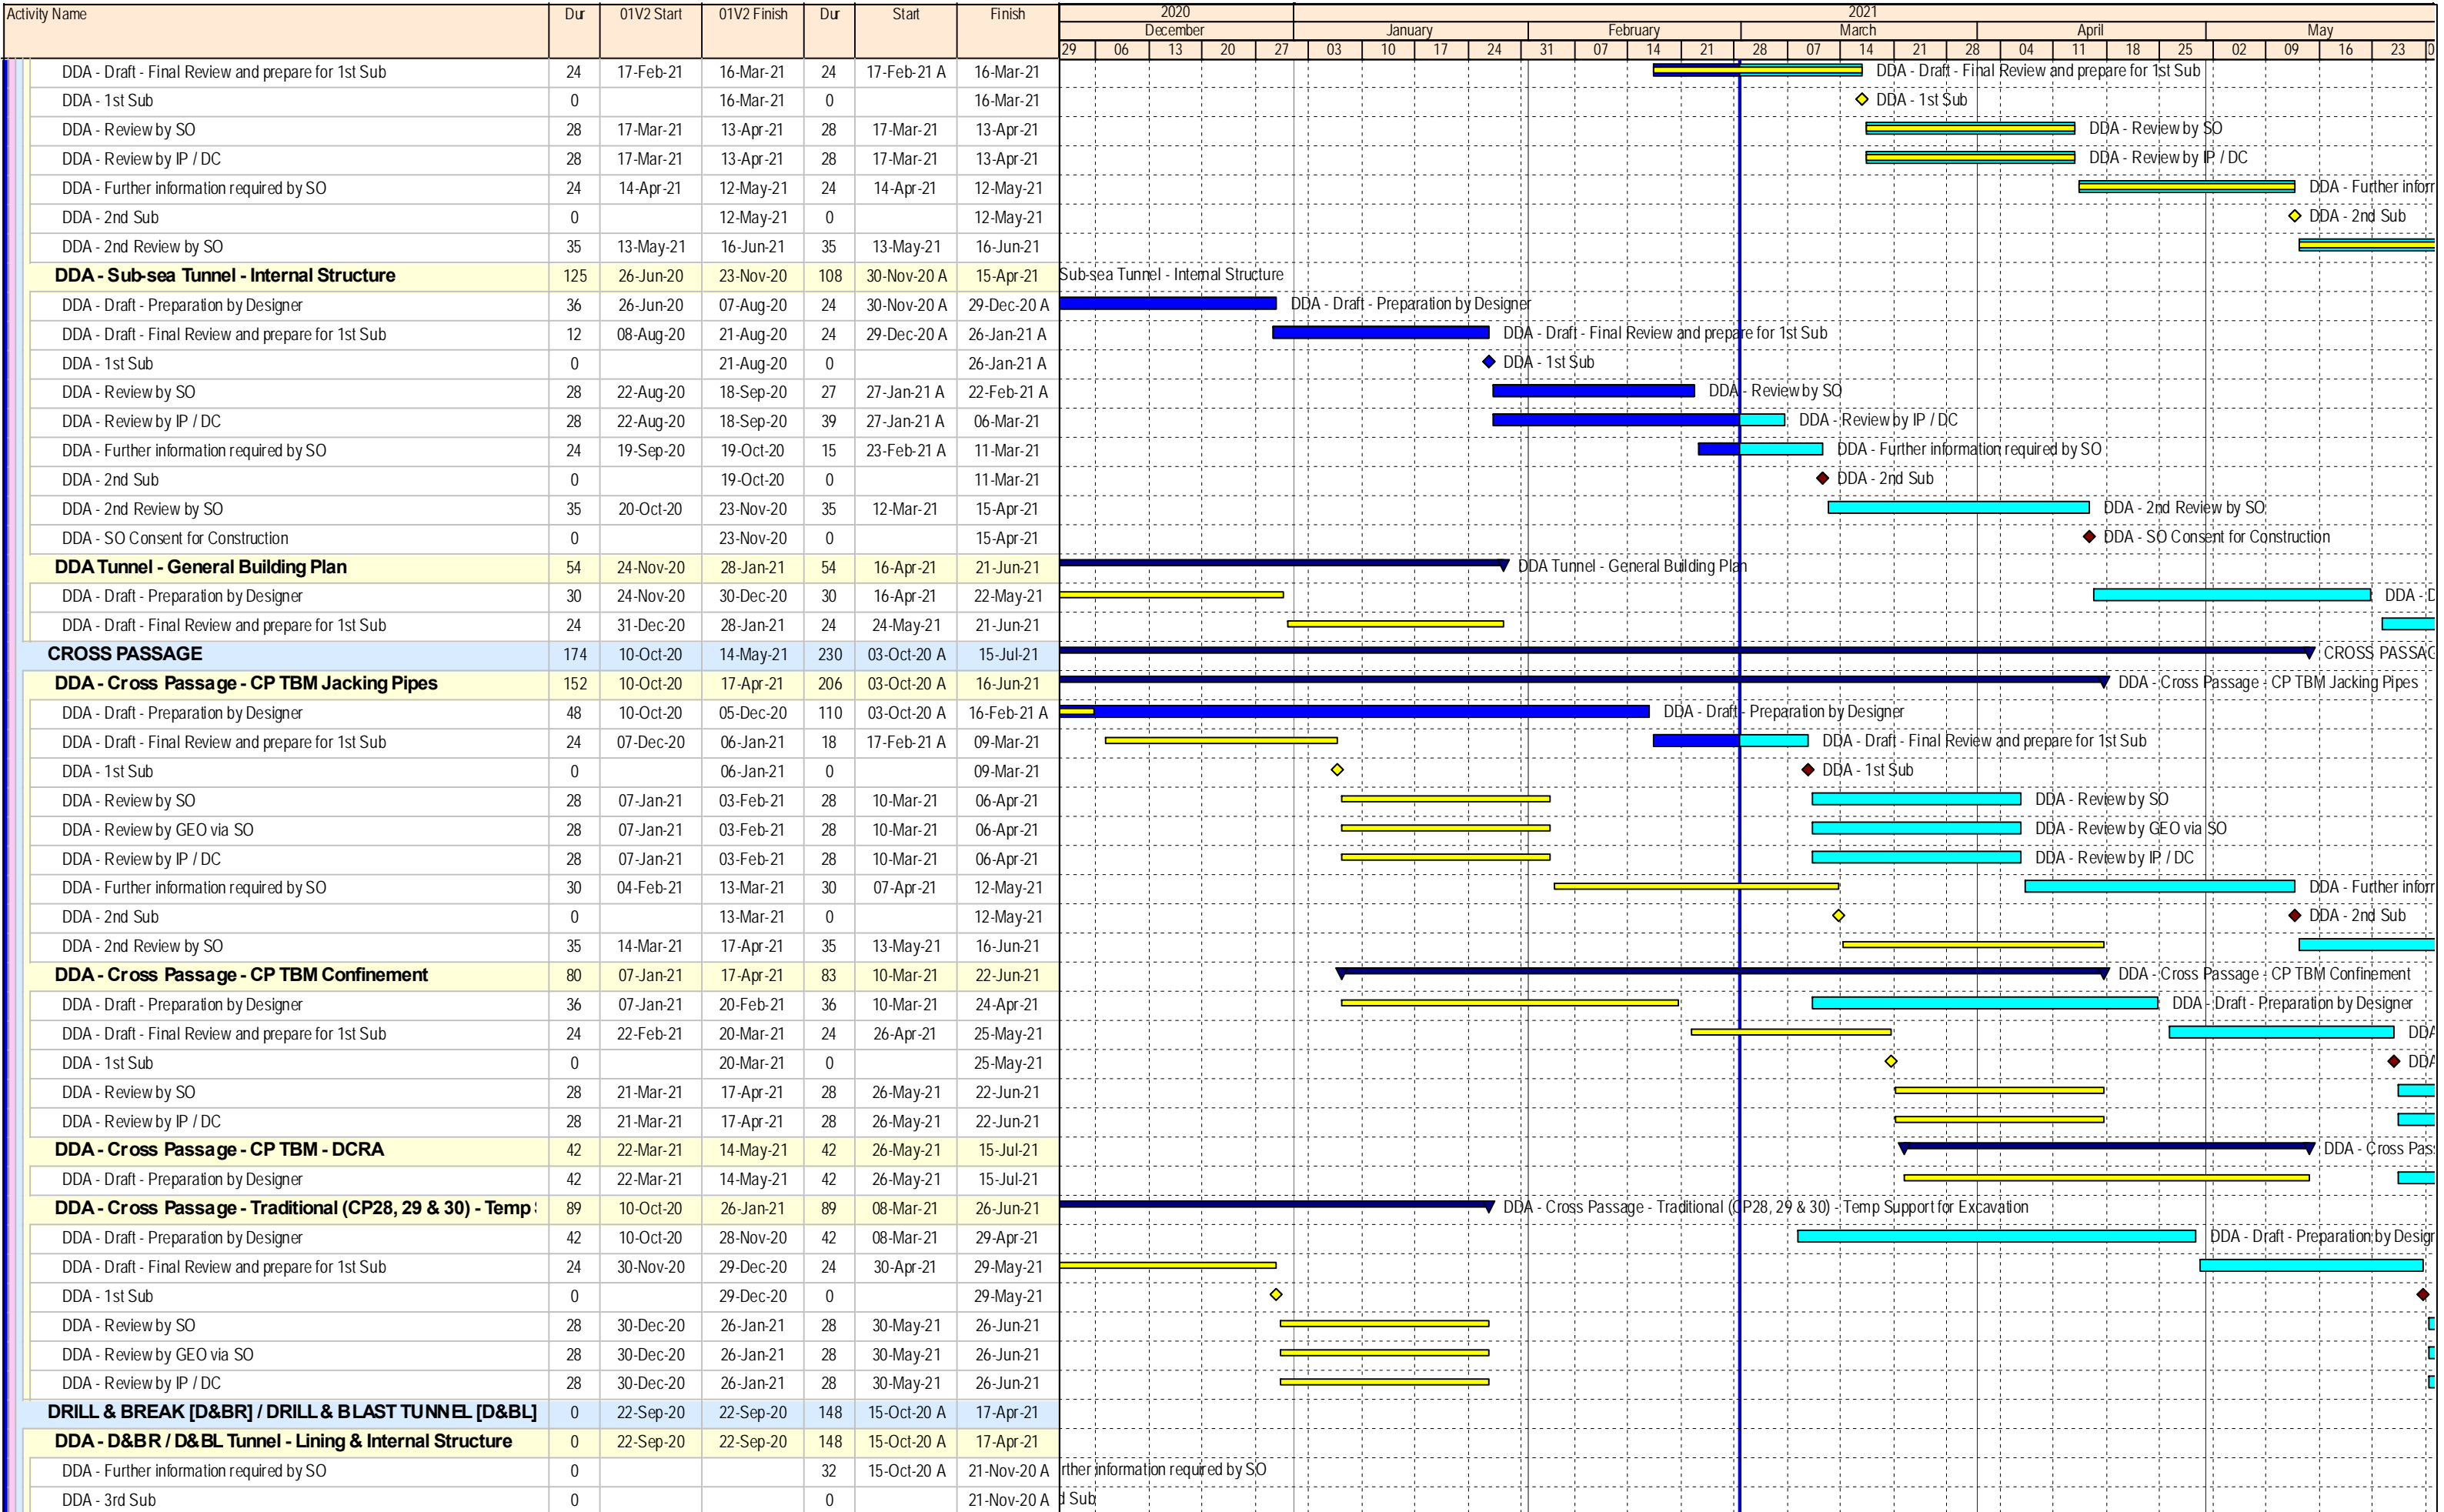


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

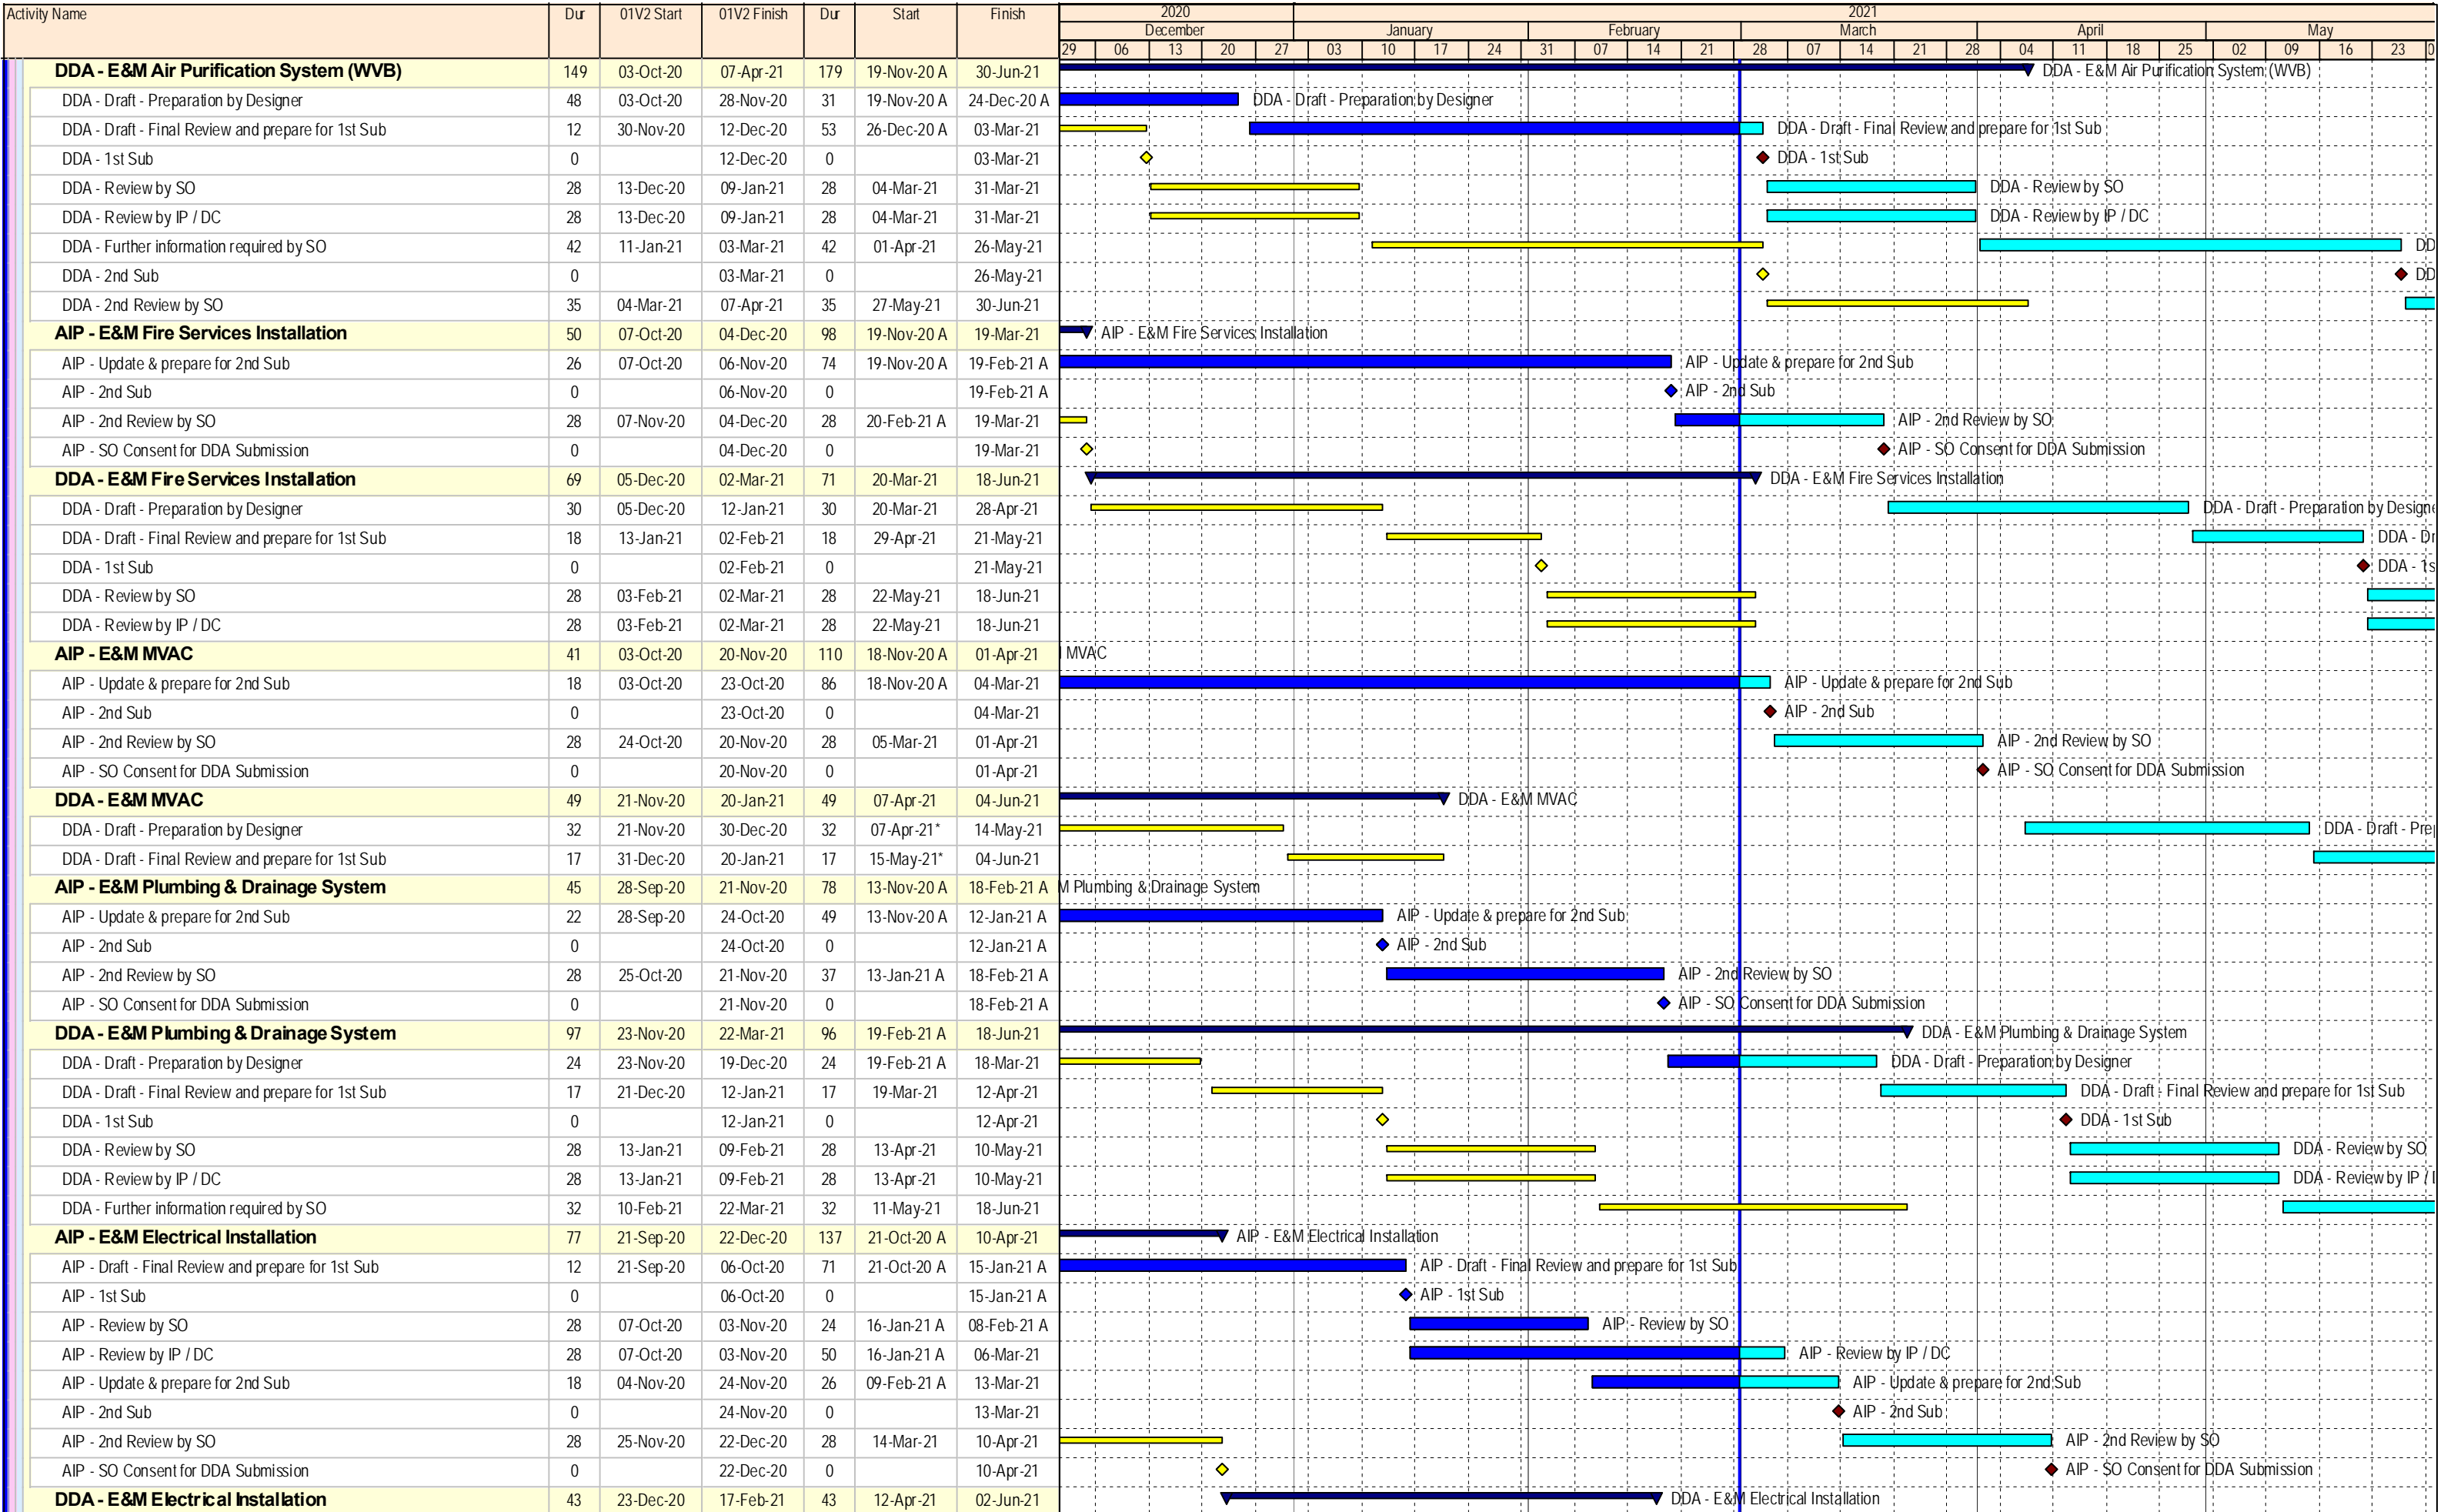

Page 14 of 27
Data Date: 28-Feb-21


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

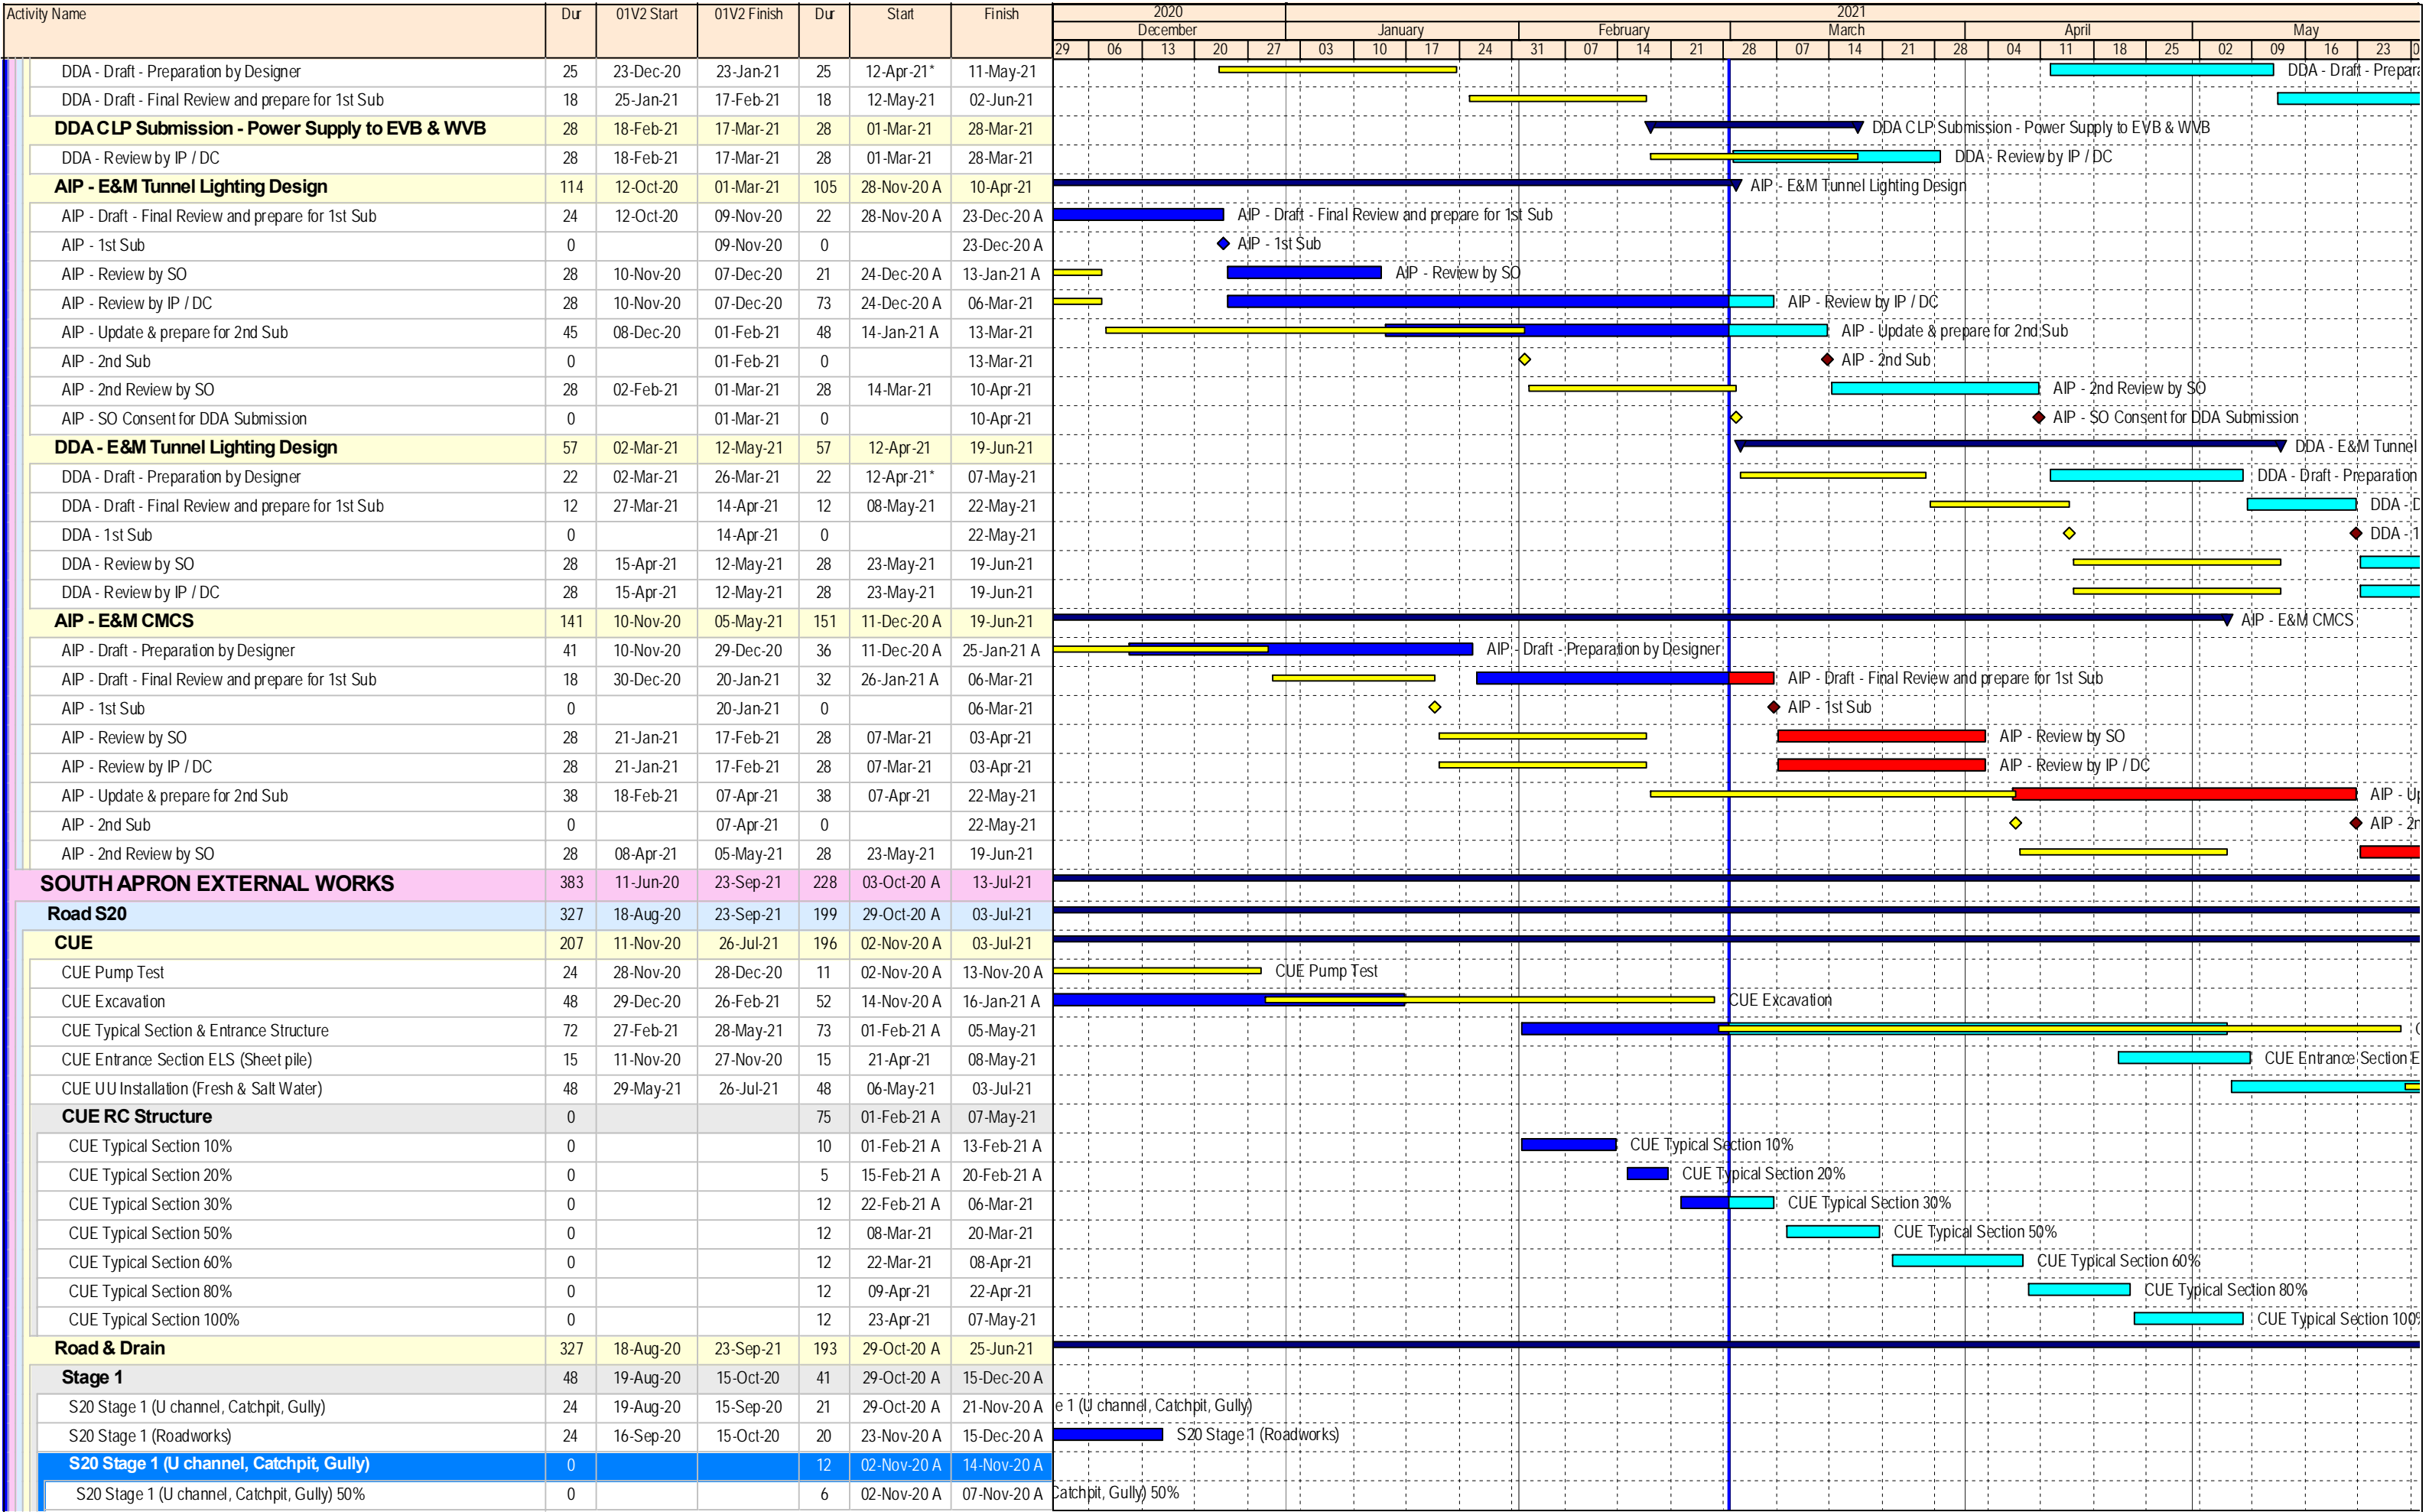


Page 15 of 27
Data Date: 28-Feb-21

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar


Summary ▬

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

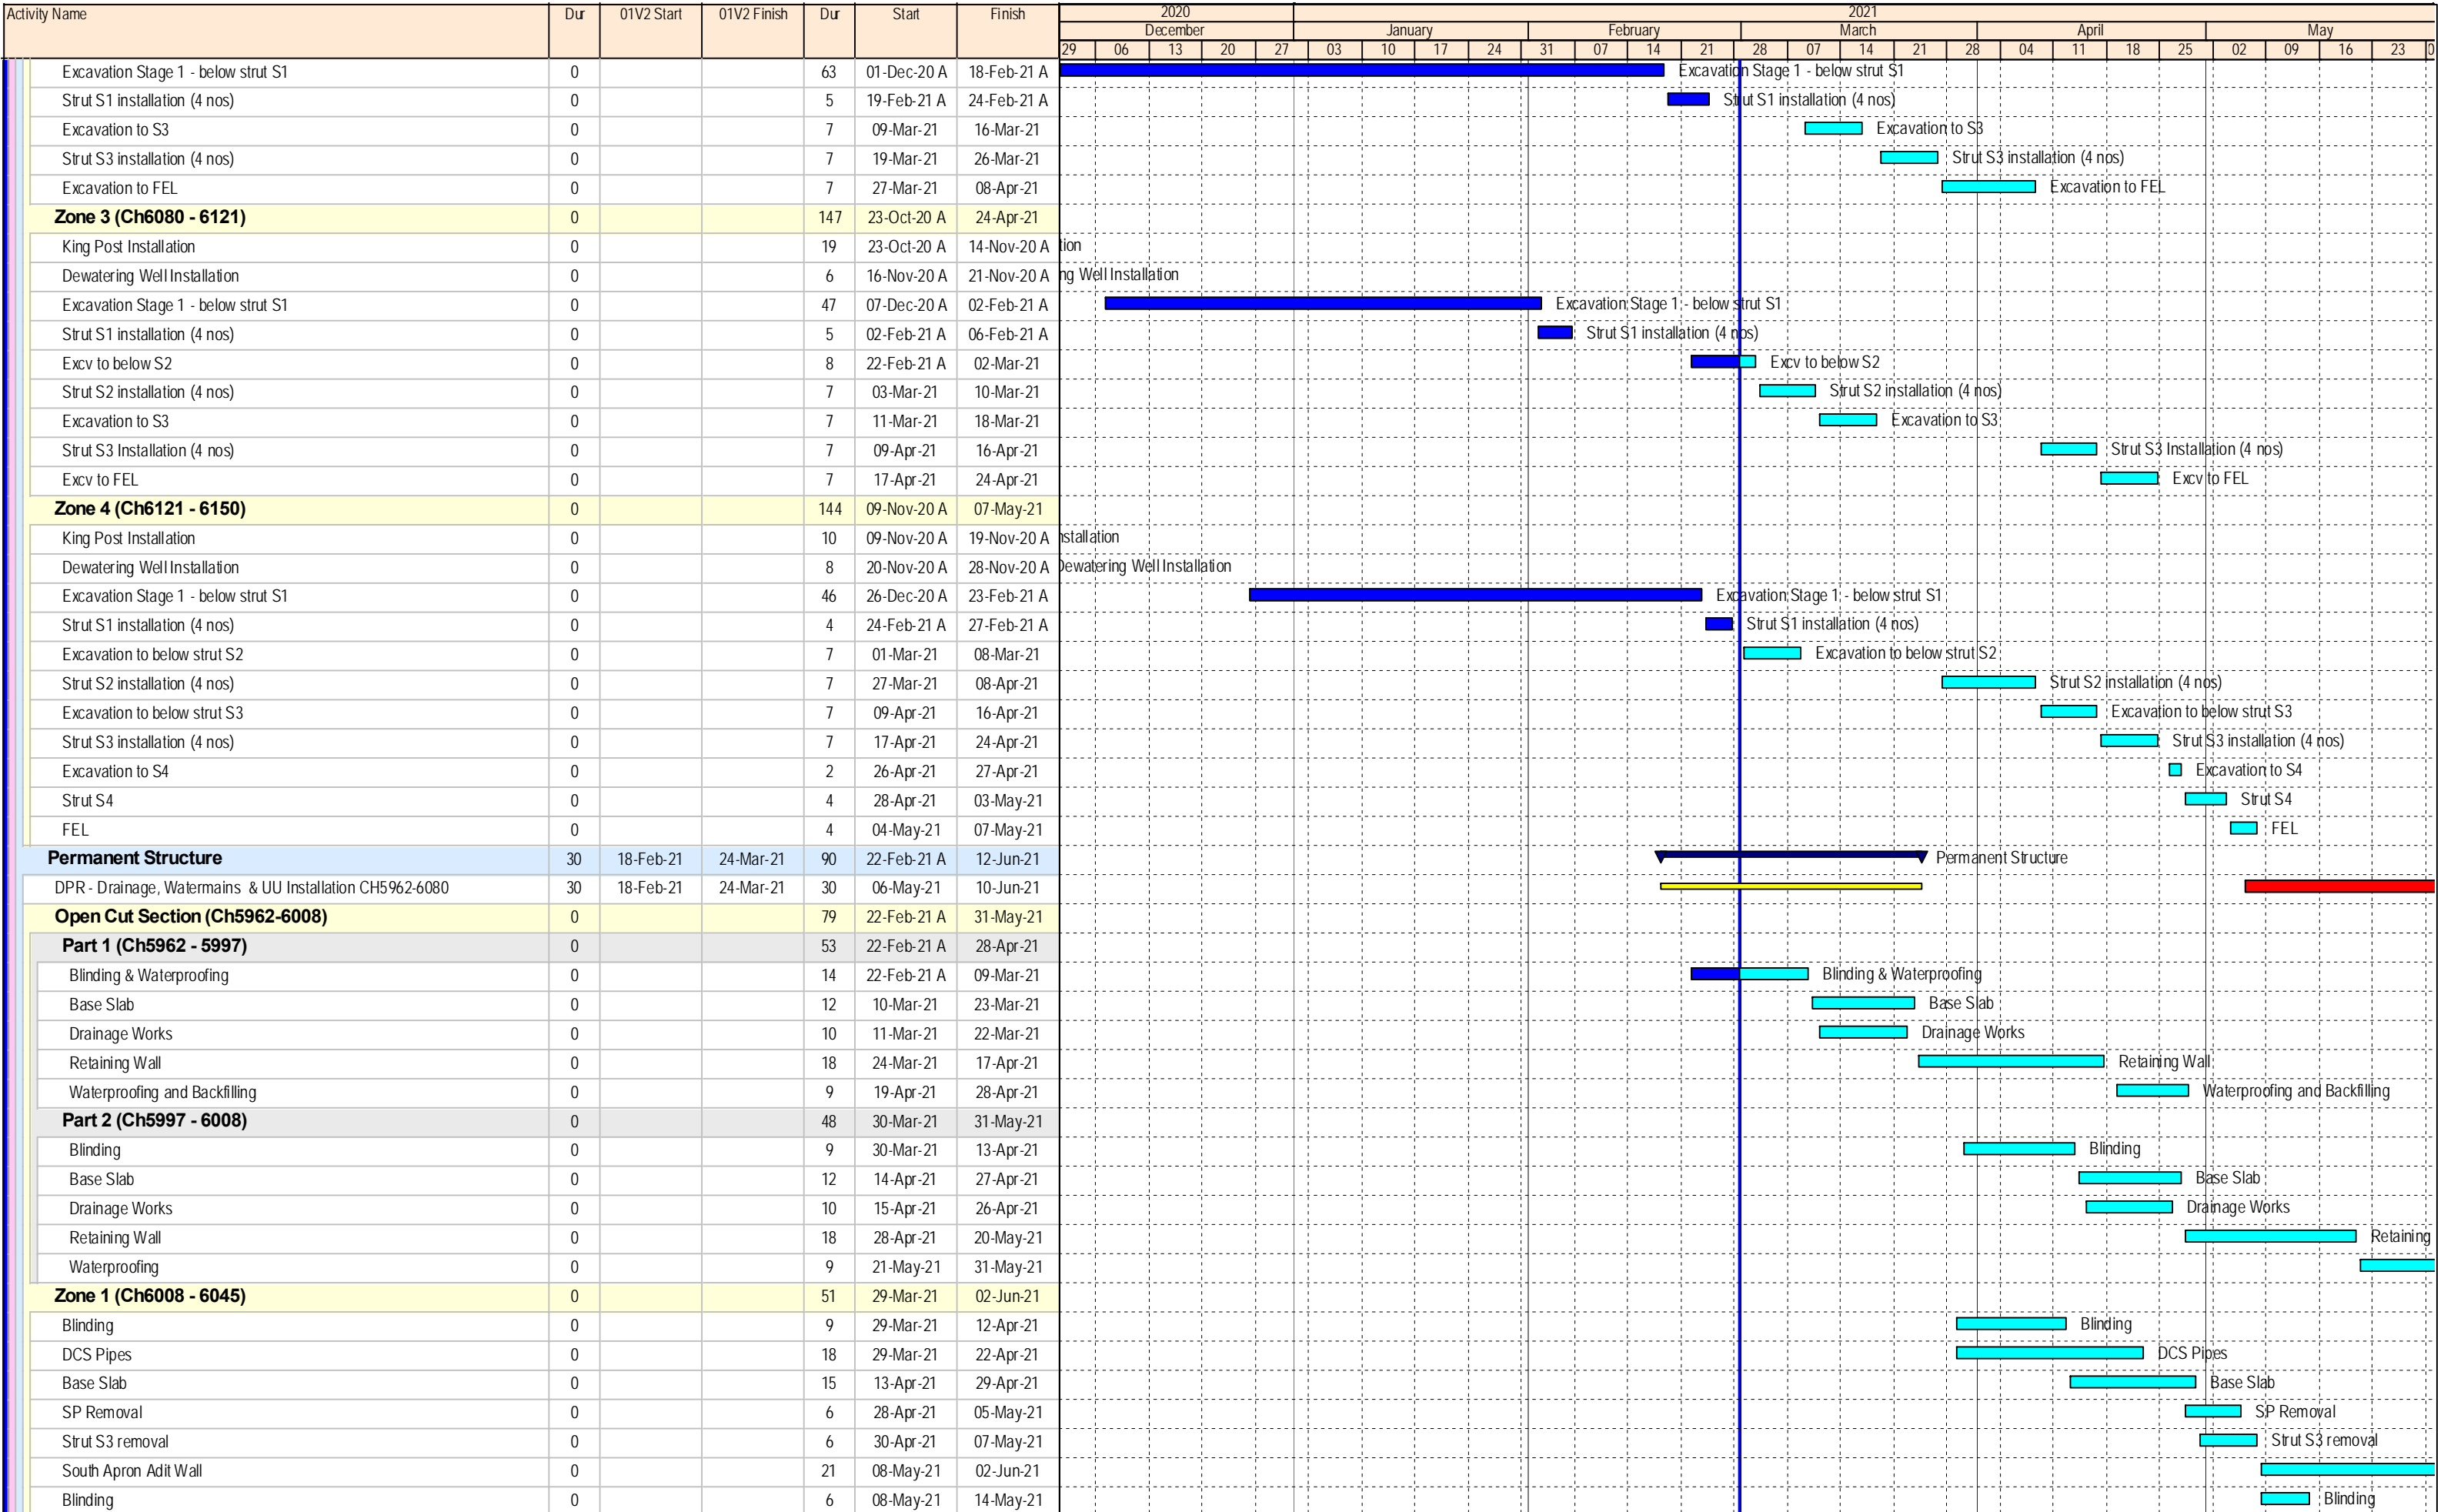


Page 18 of 27
Data Date: 28-Feb-21


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

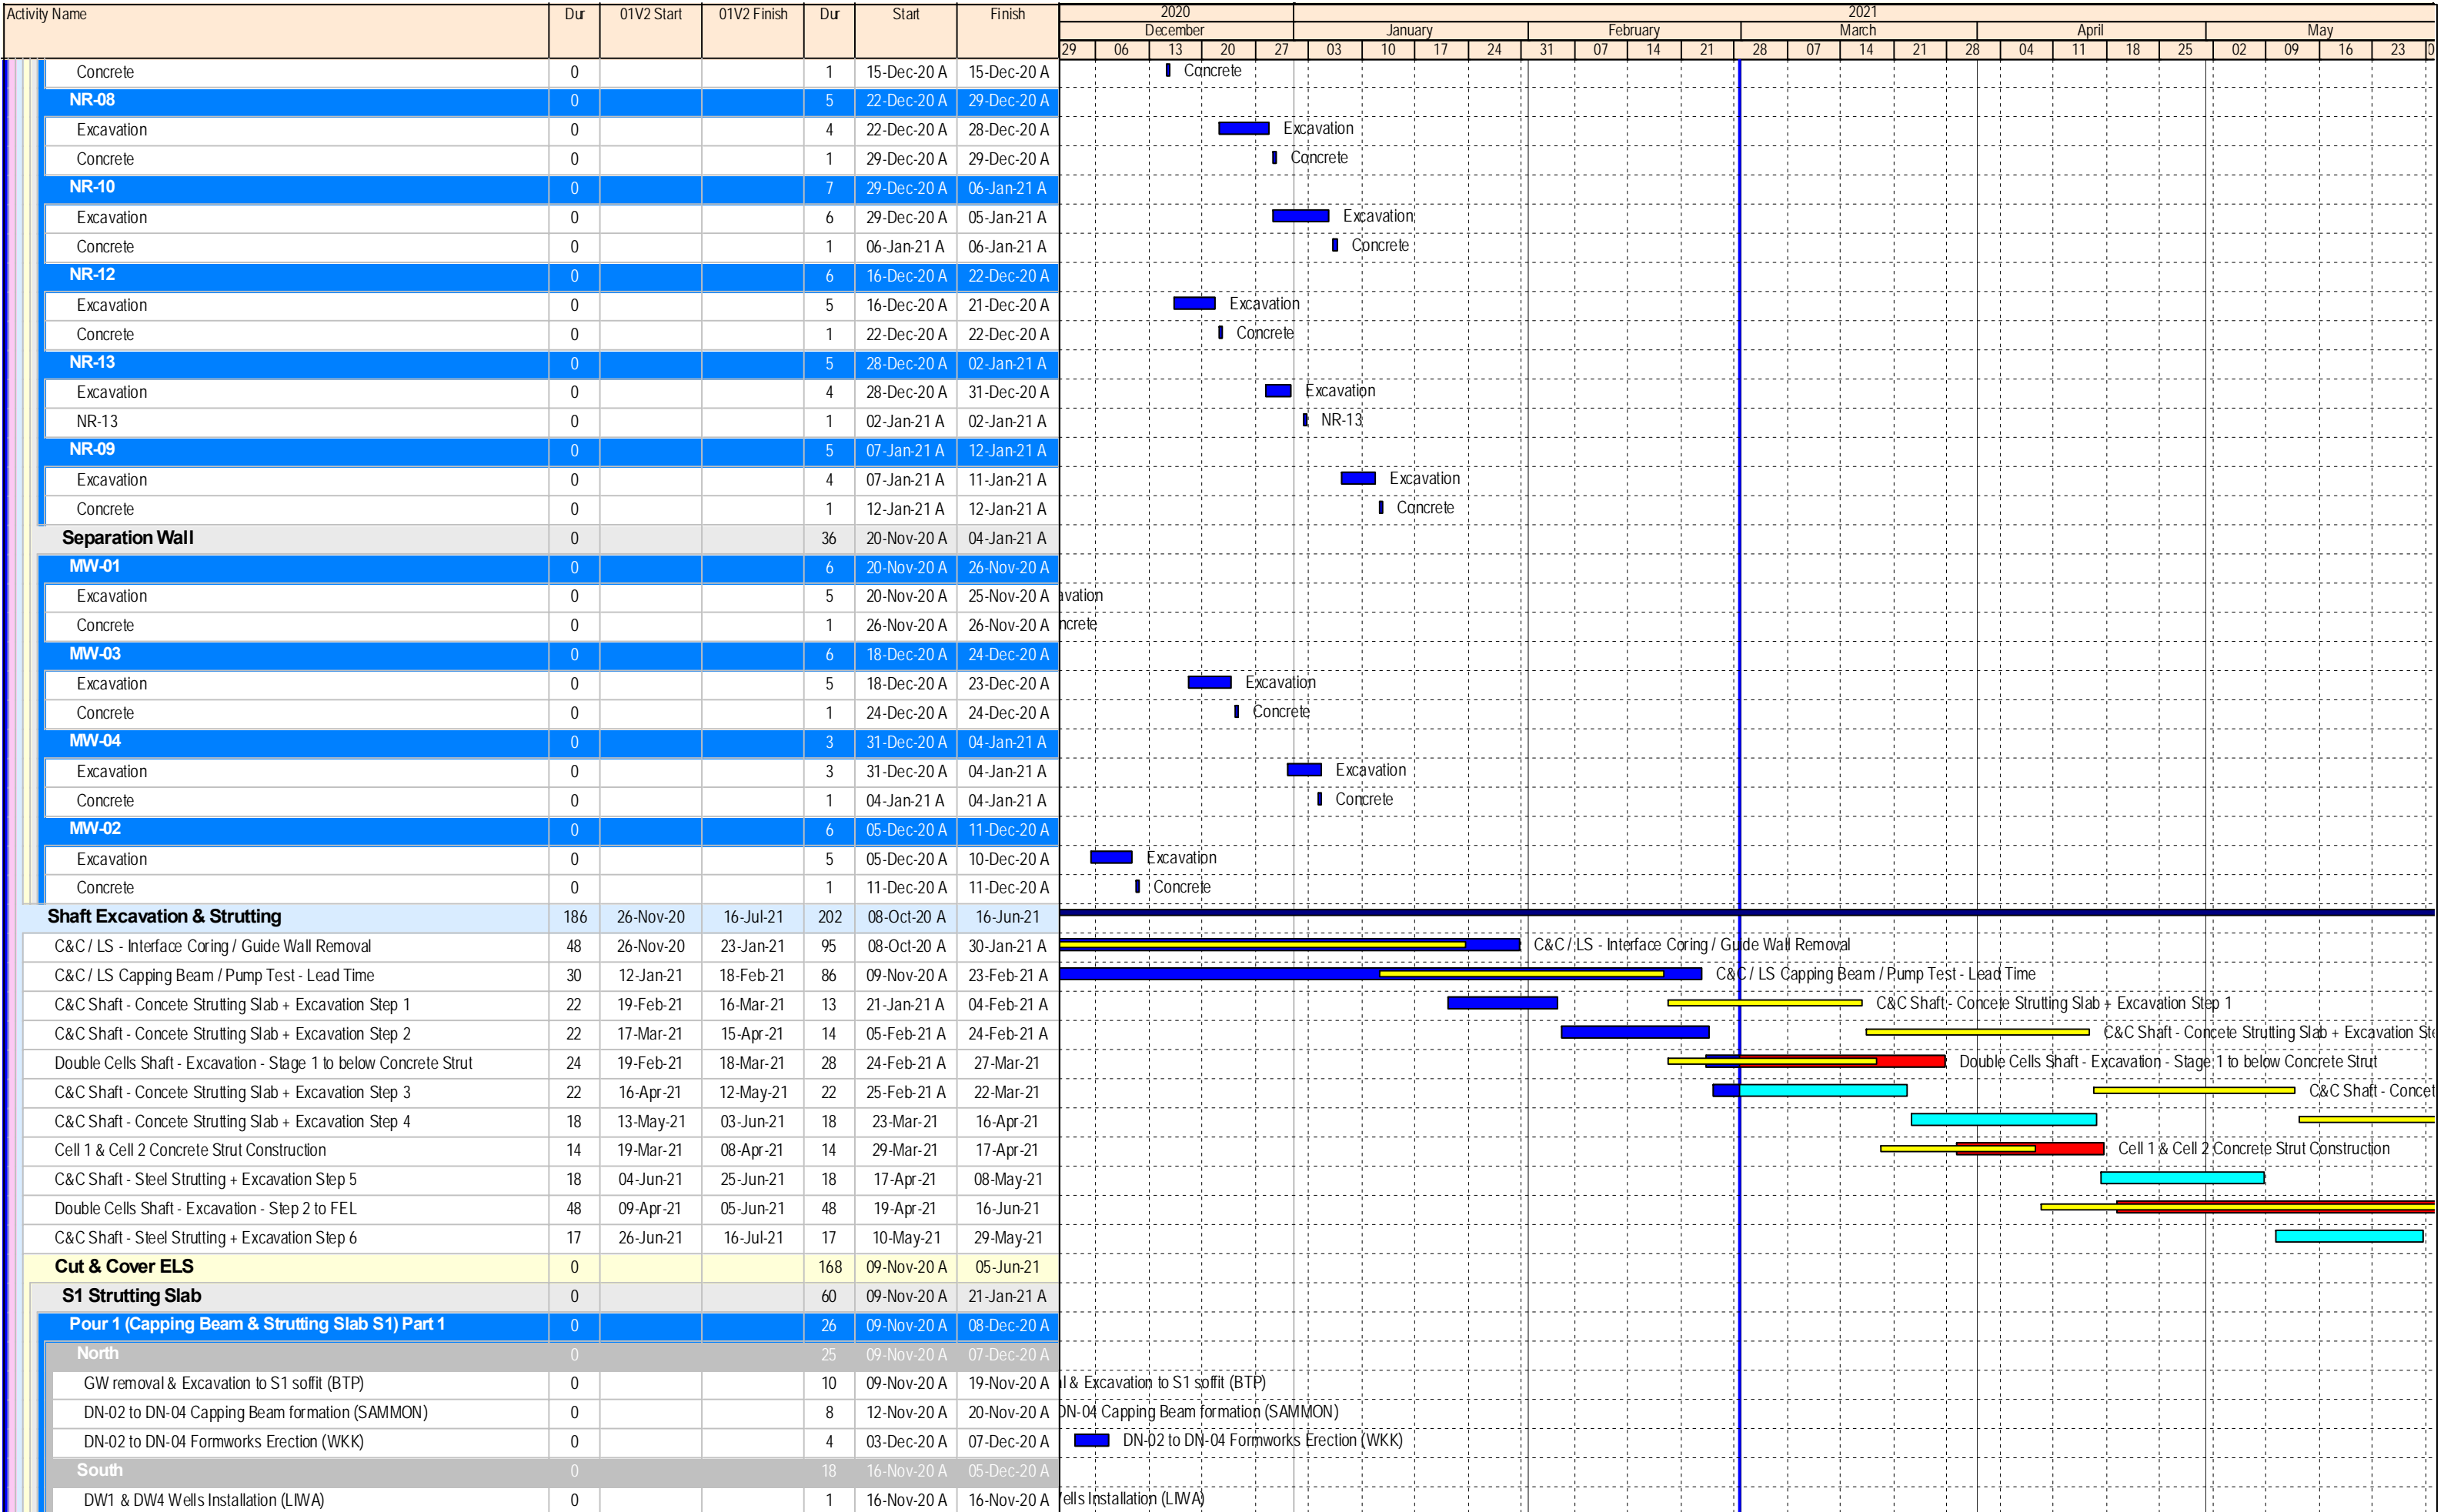


Page 21 of 27
Data Date: 28-Feb-21

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu


Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2020												2021											
							December				January				February				March				April				May			
							29	06	13	20	27	03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09
GW removal & Excavation to S1 soffit (BTP)	0			3	21-Nov-20 A	24-Nov-20 A	Removal & Excavation to S1 soffit (BTP)																							
DS-02 to DS-04 Capping Beam formation (SAMMON)	0			6	25-Nov-20 A	01-Dec-20 A	DS-02 to DS-04 Capping Beam formation (SAMMON)																							
DS-02 to DS-04 Formworks Erection (WKK)	0			4	02-Dec-20 A	05-Dec-20 A	DS-02 to DS-04 Formworks Erection (WKK)																							
Overall	0			18	18-Nov-20 A	08-Dec-20 A																								
OW1 Drilling Works (DriITech)	0			4	18-Nov-20 A	21-Nov-20 A	Drilling Works (DriITech)																							
Blinding Concrete	0			1	30-Nov-20 A	30-Nov-20 A	Blinding Concrete																							
Steel Fixing for Capping Beam & Strutting Slab	0			4	01-Dec-20 A	04-Dec-20 A	Steel Fixing for Capping Beam & Strutting Slab																							
Pour 1 Concreting	0			1	07-Dec-20 A	07-Dec-20 A	Pour 1 Concreting																							
Formwork removal & CJ cleaning	0			1	08-Dec-20 A	08-Dec-20 A	Formwork removal & CJ cleaning																							
Pour 2 (Gantry Beam)	0			46	09-Nov-20 A	04-Jan-21 A																								
North	0			34	18-Nov-20 A	29-Dec-20 A																								
Y2N Interface Core (ITF)	0			1	18-Nov-20 A	18-Nov-20 A	Interface Core (ITF)																							
GW removal & Excavation to Gantry Beam soffit (BTP)	0			5	24-Nov-20 A	28-Nov-20 A	GW removal & Excavation to Gantry Beam soffit (BTP)																							
Gantry Beam & Y2N formation works (SAMMON)	0			8	11-Dec-20 A	18-Dec-20 A	Gantry Beam & Y2N formation works (SAMMON)																							
Blinding Concrete (WKK)	0			1	19-Dec-20 A	19-Dec-20 A	Blinding Concrete (WKK)																							
Steel Fixing of Gantry Beam (BP)	0			4	21-Dec-20 A	26-Dec-20 A	Steel Fixing of Gantry Beam (BP)																							
Formworks erection of Gantry Beam (WKK)	0			6	21-Dec-20 A	29-Dec-20 A	Formworks erection of Gantry Beam (WKK)																							
South	0			44	09-Nov-20 A	31-Dec-20 A																								
Zone B & D Sheet Pile installation up to cut off line (DARWIN)	0			7	09-Nov-20 A	16-Nov-20 A	Sheet Pile installation up to cut off line (DARWIN)																							
OW16 Well Installation (FUGRO)	0			8	09-Nov-20 A	17-Nov-20 A	Installation (FUGRO)																							
Y2S Interface Core (ITF)	0			1	17-Nov-20 A	17-Nov-20 A	Interface Core (ITF)																							
ELS Waling & Struts Installation (BTP)	0			4	10-Dec-20 A	14-Dec-20 A	ELS Waling & Struts Installation (BTP)																							
GW removal & Excavation to Gantry Beam soffit (BTP)	0			2	15-Dec-20 A	16-Dec-20 A	GW removal & Excavation to Gantry Beam soffit (BTP)																							
Gantry Beam & Y2S formation works (SAMMON)	0			5	17-Dec-20 A	22-Dec-20 A	Gantry Beam & Y2S formation works (SAMMON)																							
Blinding Concrete (WKK)	0			1	22-Dec-20 A	22-Dec-20 A	Blinding Concrete (WKK)																							
Steel Fixing of Gantry Beam (BP)	0			8	23-Dec-20 A	30-Dec-20 A	Steel Fixing of Gantry Beam (BP)																							
Formworks erection of Gantry Beam (WKK)	0			4	28-Dec-20 A	31-Dec-20 A	Formworks erection of Gantry Beam (WKK)																							
Overall	0			2	02-Jan-21 A	04-Jan-21 A																								
Pour 2 Concreting (WKK)	0			1	02-Jan-21 A	02-Jan-21 A	Pour 2 Concreting (WKK)																							
Pour 2 Formworks removal & CJ Cleaning (WKK & BTP)	0			1	04-Jan-21 A	04-Jan-21 A	Pour 2 Formworks removal & CJ Cleaning (WKK & BTP)																							
Pour 3 (Capping Beam & Strutting Slab S1) Part 2	0			50	20-Nov-20 A	21-Jan-21 A																								
North	0			8	20-Nov-20 A	27-Nov-20 A																								
GW removal & Excavation to S1 soffit (BTP)	0			5	20-Nov-20 A	24-Nov-20 A	Removal & Excavation to S1 soffit (BTP)																							
Capping Beam formation works (SAMMON)	0			3	25-Nov-20 A	27-Nov-20 A	Capping Beam formation works (SAMMON)																							
South	0			34	25-Nov-20 A	06-Jan-21 A																								
GW removal & Excavation to S1 soffit (BTP)	0			4	25-Nov-20 A	28-Nov-20 A	GW removal & Excavation to S1 soffit (BTP)																							
Capping Beam formation works (SAMMON)	0			3	26-Nov-20 A	28-Nov-20 A	Capping Beam formation works (SAMMON)																							
ELS Removal at Zone C (DARWIN)	0			2	05-Jan-21 A	06-Jan-21 A	ELS Removal at Zone C (DARWIN)																							
Overall	0			13	06-Jan-21 A	21-Jan-21 A																								
Blinding Concrete (WKK)	0			2	06-Jan-21 A	07-Jan-21 A	Blinding Concrete (WKK)																							
Backfilling & Formation	0			2	08-Jan-21 A	09-Jan-21 A	Backfilling & Formation																							
Steel Fixing Pour 3 (BP)	0			4	11-Jan-21 A	14-Jan-21 A	Steel Fixing Pour 3 (BP)																							
Pour 3 Concreting (WKK)	0			1	15-Jan-21 A	15-Jan-21 A	Pour 3 Concreting (WKK)																							
Concrete Strength Gain	0			3	16-Jan-21 A	18-Jan-21 A	Concrete Strength Gain																							
Cut & Cover Bulk Excavation Start	0			0	21-Jan-21 A		Cut & Cover Bulk Excavation Start																							
Cut & Cover Bulk Excavation	0			108	21-Jan-21 A	05-Jun-21																								
Excavation to below S2	0			15	21-Jan-21 A	04-Feb-21 A	Excavation to below S2																							
Strut S2 Construction	0			9	05-Feb-21 A	13-Feb-21 A	Strut S2 Construction																							
Excavation to below S3	0			8	16-Feb-21 A	23-Feb-21 A	Excavation to below S3																							
Strut S3 Construction	0			11	24-Feb-21 A	06-Mar-21	Strut S3 Construction																							

Page 22 of 27
Data Date: 28-Feb-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Feb-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

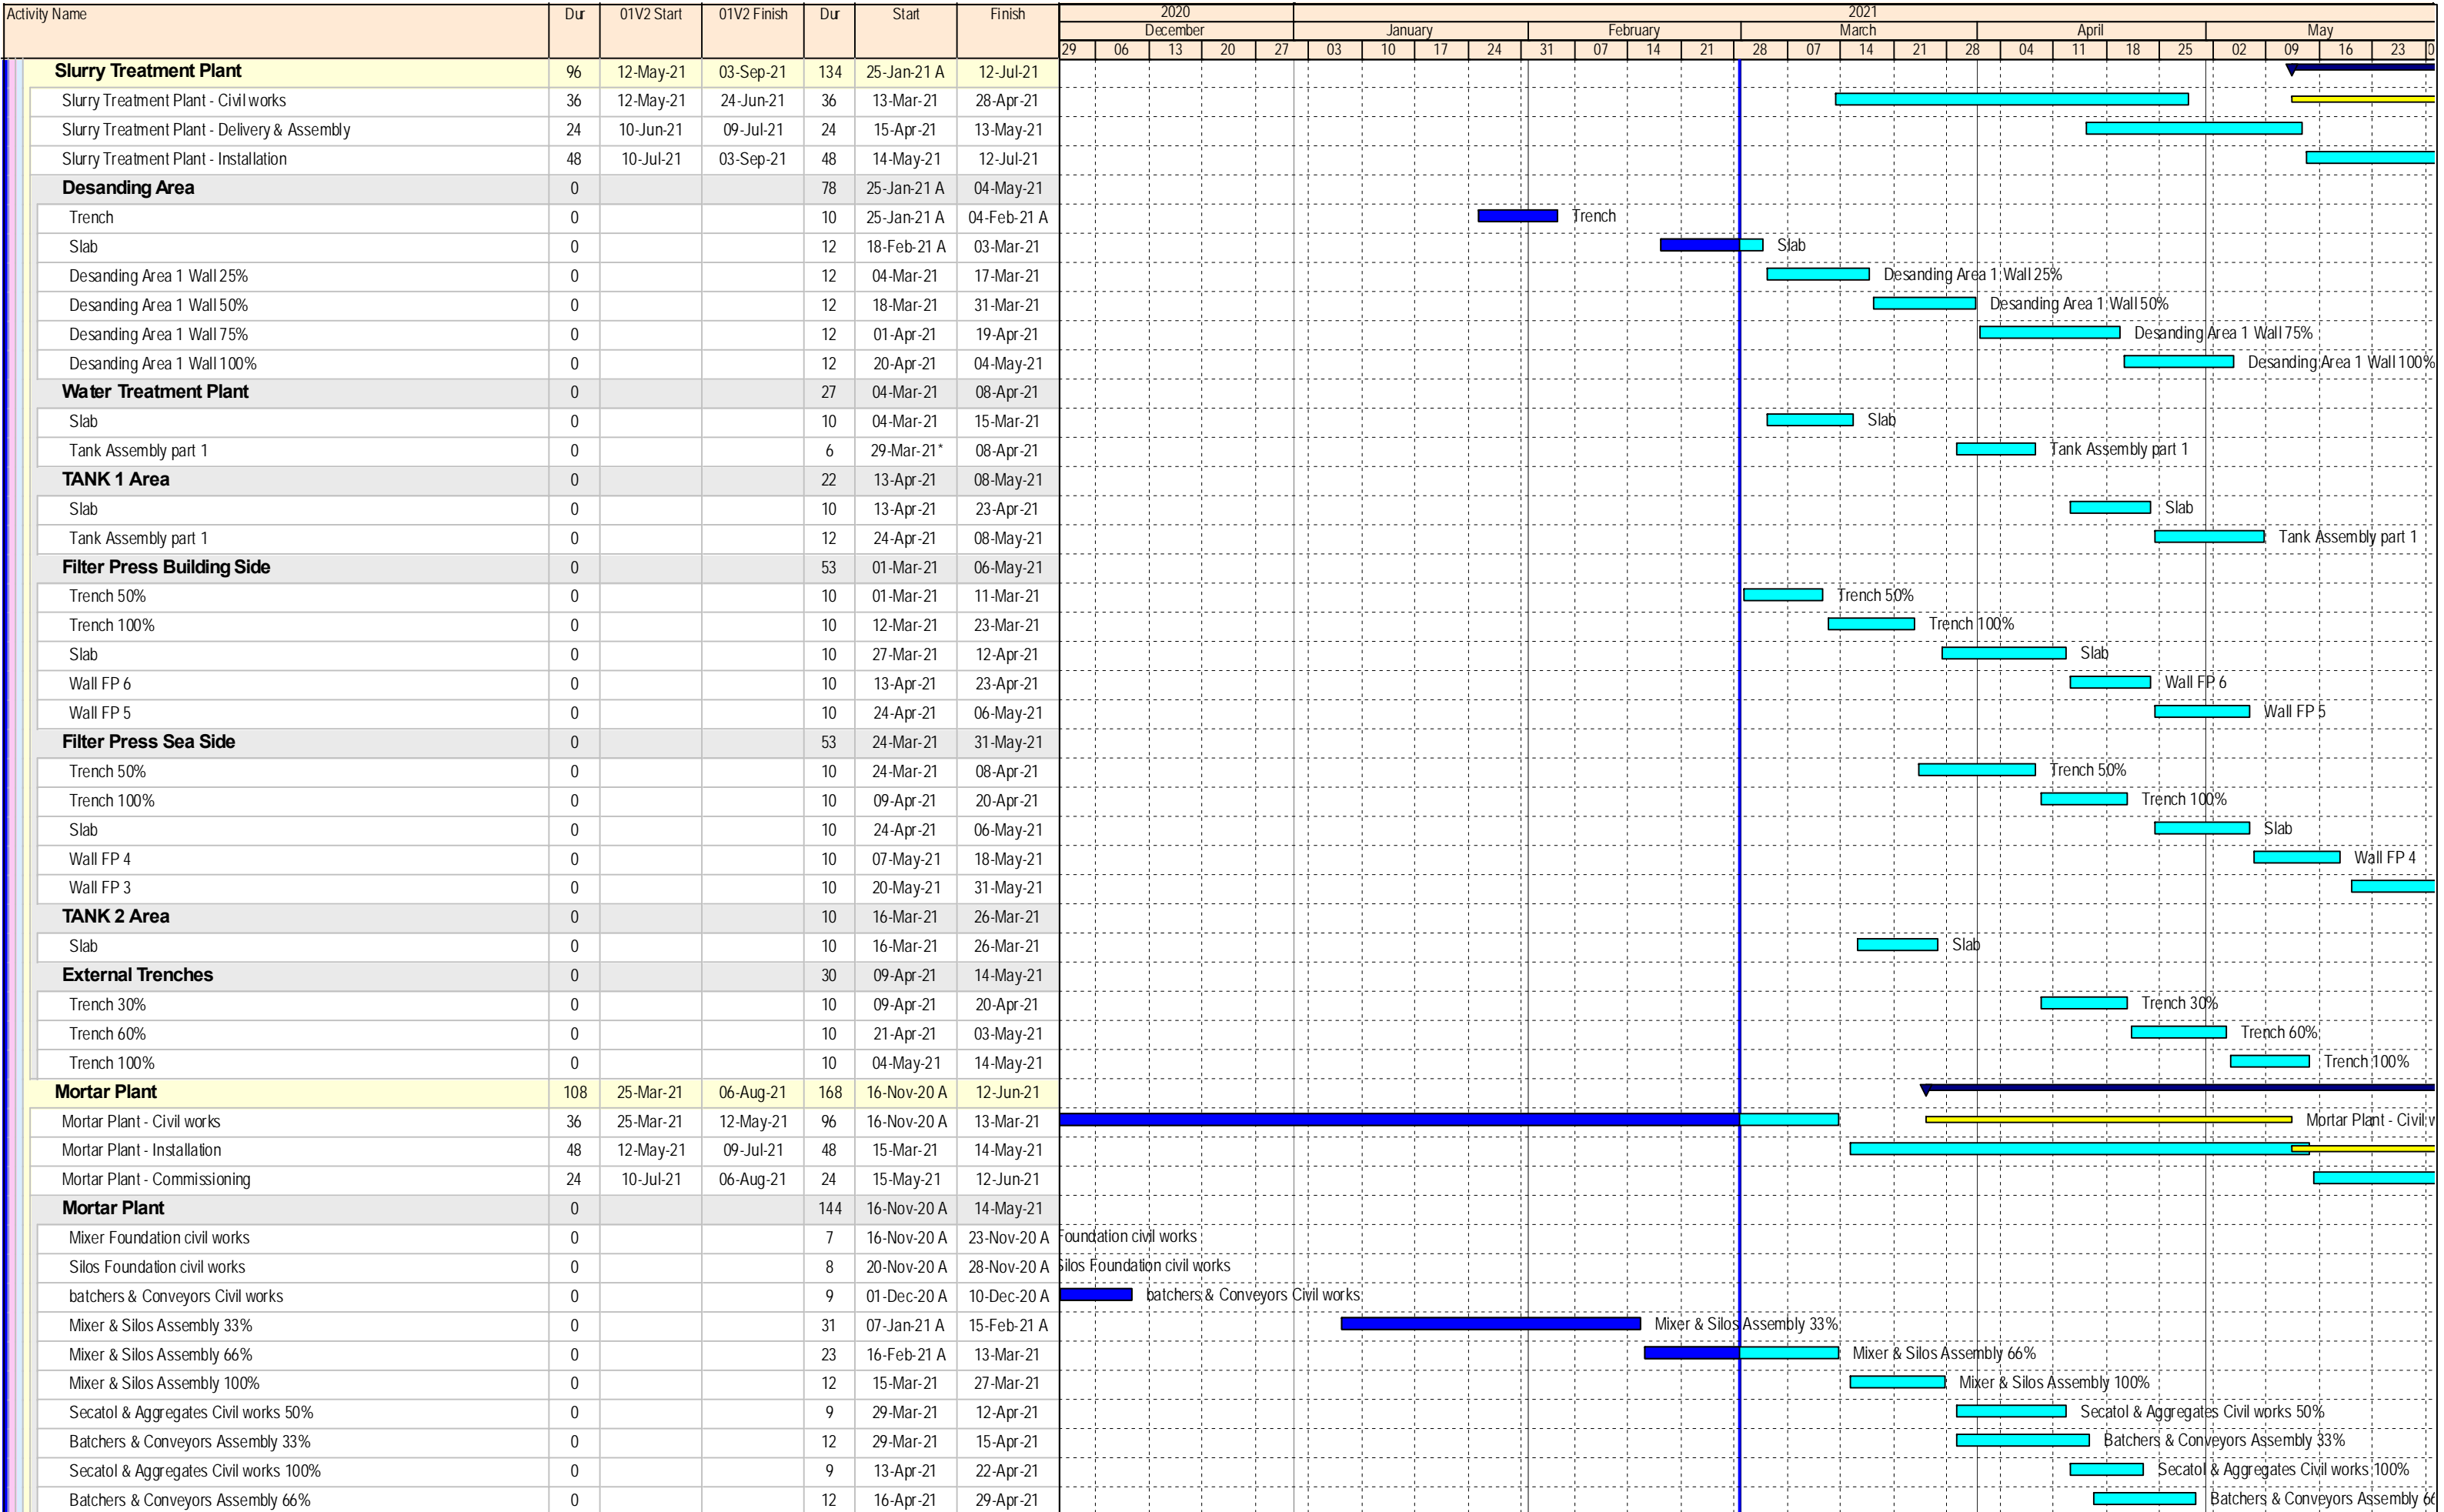

<p>Page 25 of 27 Data Date: 28-Feb-21</p>	<ul style="list-style-type: none"> ◆ Milestone ▬ Planned Bar ▬ Critical Activity ◆ Actual Milestone ▬ Actual Work ◆ Baseline Milestone ▬ Baseline Bar 	<h2 style="margin: 0;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="margin: 0;">Three Months Rolling Programme (Feb-21)</h3>		<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>05-Nov-19</td> <td>00V0</td> <td>WYu</td> <td></td> </tr> <tr> <td>18-Dec-19</td> <td>00V1</td> <td>WYu</td> <td></td> </tr> <tr> <td>22-Feb-20</td> <td>01V0</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Apr-20</td> <td>01V1</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>17-Jul-20</td> <td>01V2</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Oct-20</td> <td>01V3</td> <td>SPa/LLo</td> <td>WYu</td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																													
05-Nov-19	00V0	WYu																														
18-Dec-19	00V1	WYu																														
22-Feb-20	01V0	SPa/LLo	WYu																													
09-Apr-20	01V1	SPa/LLo	WYu																													
17-Jul-20	01V2	SPa/LLo	WYu																													
09-Oct-20	01V3	SPa/LLo	WYu																													

