



- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

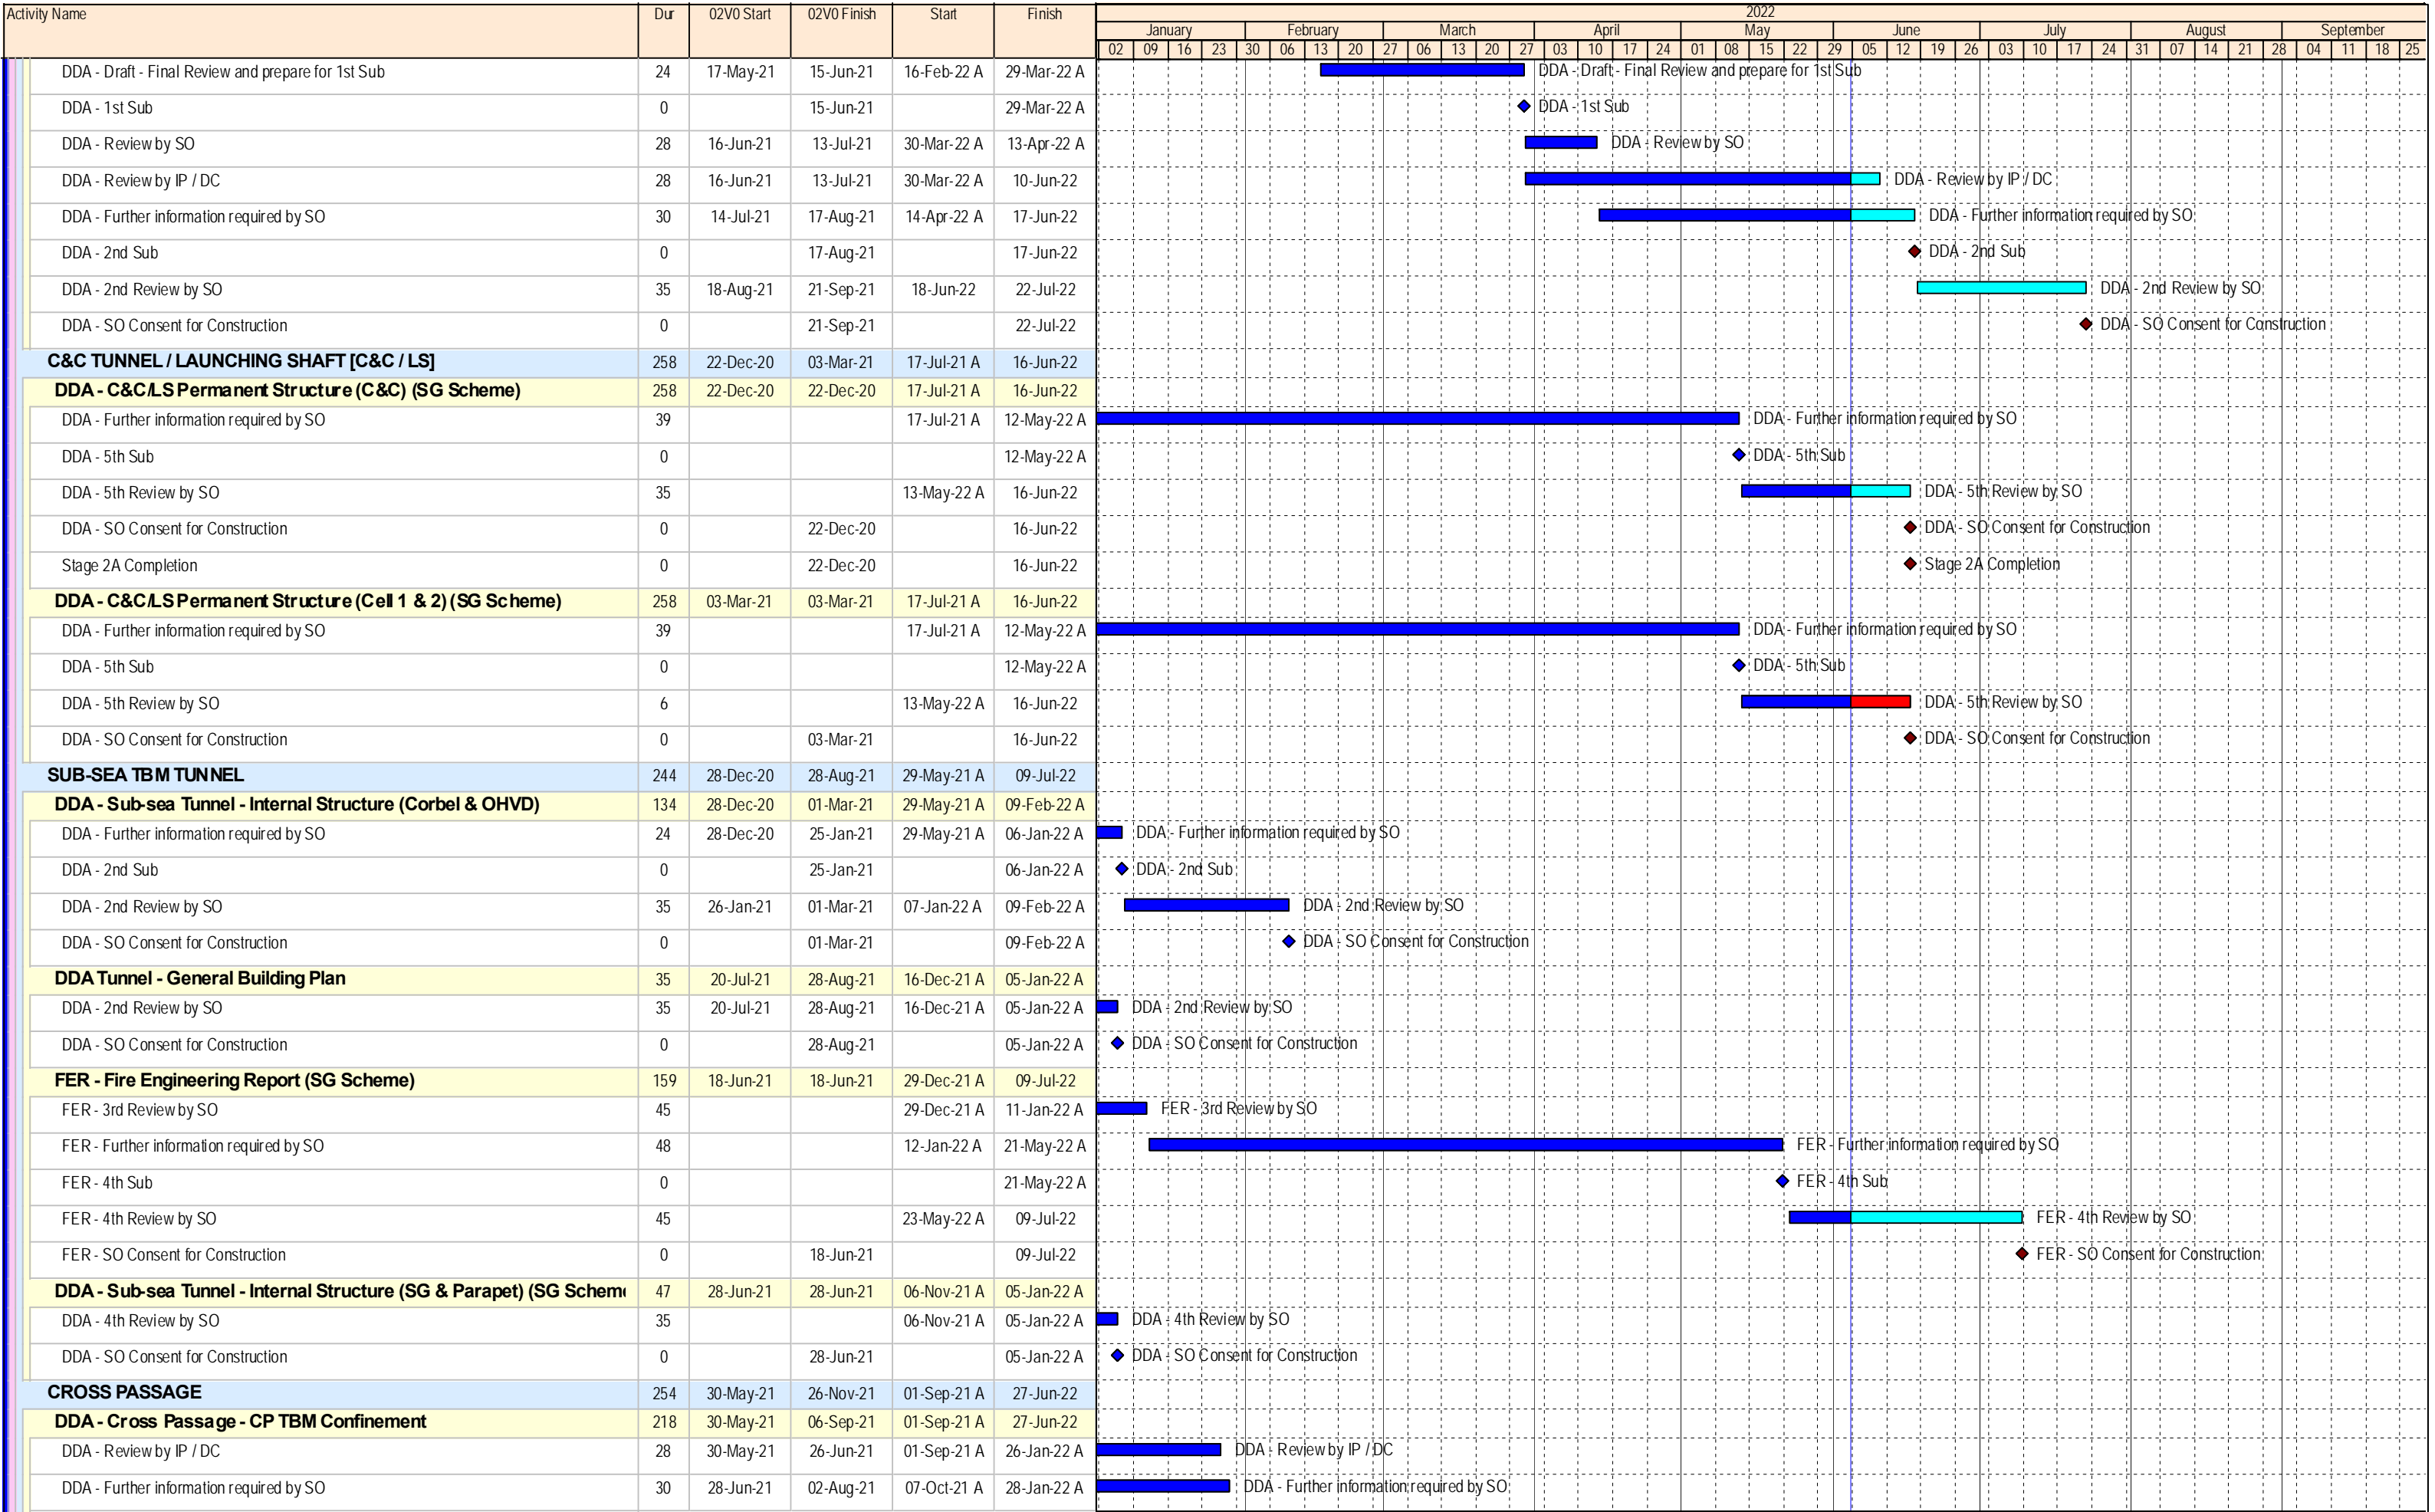


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

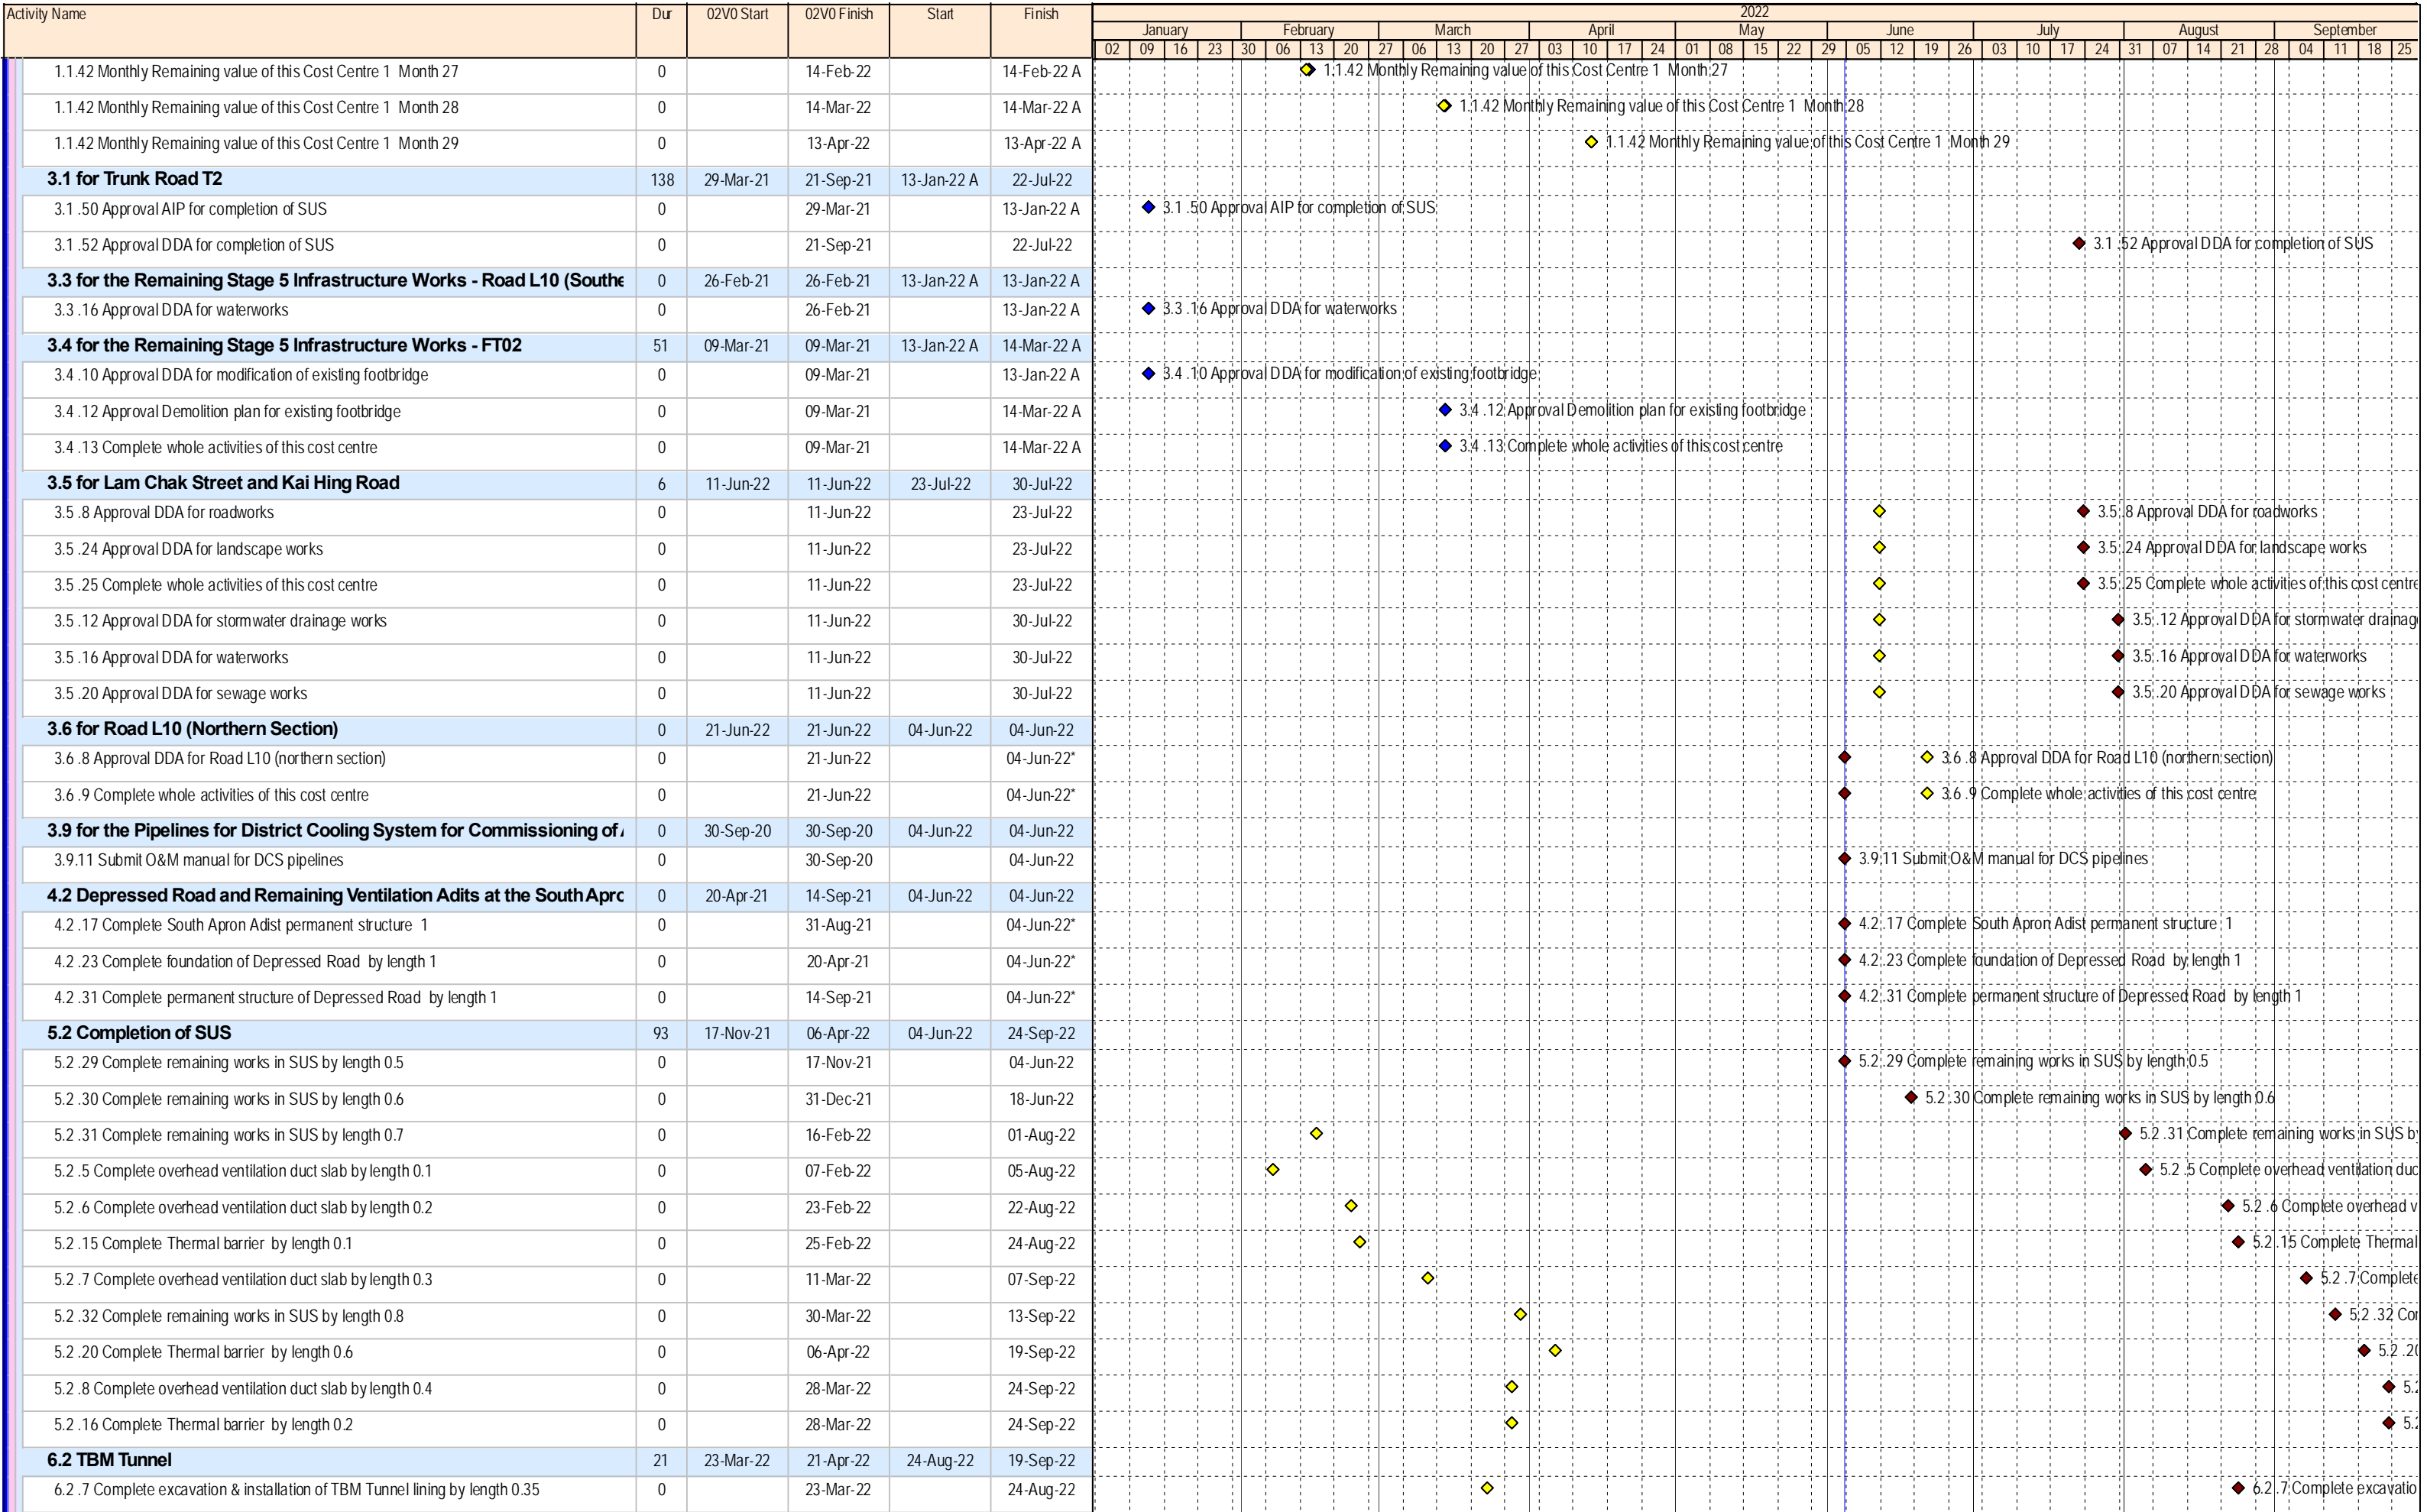

Page 9 of 24
Data Date: 04-Jun-22

- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

**ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (May-22)**



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2022																																								
						January				February				March				April				May				June				July				August				September								
						02	09	16	23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25		
35.17 Complete 40% of total length (measured on plan) of SG structures in Drill-and-Break and Drill-and-Blast Tunnel	0		04-Feb-22		04-Jun-22*																																									
35.33 Complete 75% of total volume (measured on plan) of excavation for Lower Basement of East Ventilation Building	0		30-Apr-22		17-Aug-22																																									
35.21 Complete 10% of total length (measured on plan) of Services Gallery structures and ancillaries in TRM Tunnel	0		04-Apr-22		31-Aug-22																																									
35.14 Complete 80% of total length (measured on plan) of SG excavation in Drill-and-Break and Drill-and-Blast Tunnel	0		07-Feb-22		14-Sep-22																																									
35.34 Complete 100% of total volume (measured on plan) of excavation for Lower Basement of East Ventilation Building	0		14-Jun-22		28-Sep-22																																									
35.35 Complete concreting works of 25% of the total gross plan area for the Lower Basement of East Ventilation Building	0		21-Mar-22		28-Sep-22																																									
SOUTH APRON EXTERNAL WORKS	827	10-Mar-21	29-Jun-24	26-Nov-21 A	08-Aug-24																																									
Road S20	231	19-Jul-21	17-Jan-22	13-Dec-21 A	14-Oct-22																																									
CUE	186	19-Jul-21	17-Jan-22	28-Dec-21 A	14-Oct-22																																									
CUE FSI Forms submission to FSD (if applicable)	0		21-Oct-21		19-Jul-22																																									
CUE FS Inspection & Commissioning (if applicable)	48	19-Nov-21	17-Jan-22	17-Aug-22	14-Oct-22																																									
Entrance	108	19-Jul-21	18-Nov-21	28-Dec-21 A	21-May-22 A																																									
Entrance- Remaining Structures (Wall & Top Slab)	12	19-Jul-21	31-Jul-21	28-Dec-21 A	15-Mar-22 A																																									
Entrance - Utilities & E&M	72	18-Sep-21	18-Nov-21	16-Mar-22 A	21-May-22 A																																									
Road & Drain	224	20-Jul-21	18-Nov-21	13-Dec-21 A	06-Oct-22																																									
Stage 3	224	20-Jul-21	18-Nov-21	13-Dec-21 A	06-Oct-22																																									
S20 Stage 3 (Watermain)	4	20-Jul-21	23-Jul-21	13-Dec-21 A	09-Jun-22																																									
S20 Stage 3 (UU Diversion)	12	24-Jul-21	06-Aug-21	10-Jun-22	23-Jun-22																																									
S20 Stage 3 (U channel, Catchpit, Gully)	22	07-Aug-21	01-Sep-21	24-Jun-22	20-Jul-22																																									
S20 Stage 3 (Roadworks)	22	02-Sep-21	28-Sep-21	21-Jul-22	15-Aug-22																																									
Utilities undertaker (by others)	36	07-Sep-21	21-Oct-21	26-Jul-22	05-Sep-22																																									
Footpath, Road Marking & Road Lighting part 1	24	22-Oct-21	18-Nov-21	06-Sep-22	06-Oct-22																																									
AMAWBC	242	16-Aug-21	10-Feb-22	26-Nov-21 A	17-Aug-22																																									
Drainage & Sewerage	242	10-Sep-21	10-Feb-22	26-Nov-21 A	17-Aug-22																																									
Section B	22	10-Sep-21	07-Oct-21	05-Apr-22 A	27-Apr-22 A																																									
Section B - Drainage	11	10-Sep-21	23-Sep-21	05-Apr-22 A	15-Apr-22 A																																									
Section B - Sewerage	11	24-Sep-21	07-Oct-21	16-Apr-22 A	27-Apr-22 A																																									
Section C	191	07-Dec-21	10-Feb-22	28-Feb-22 A	17-Jun-22																																									
Section C - Drainage	21	07-Dec-21	03-Jan-22	28-Feb-22 A	05-Apr-22 A																																									
Section C - Sewerage	24	04-Jan-22	31-Jan-22	06-Apr-22 A	26-Apr-22 A																																									
Section C - Watermain	6	04-Feb-22	10-Feb-22	11-Jun-22	17-Jun-22																																									
Section D	236	07-Dec-21	17-Jan-22	26-Nov-21 A	17-Aug-22																																									
Section D - Sewerage	14	07-Dec-21	22-Dec-21	26-Nov-21 A	12-Jan-22 A																																									
Section D - Watermain	5	23-Dec-21	30-Dec-21	06-Jun-22	10-Jun-22																																									
Forecast	236	04-Jan-22	17-Jan-22	26-Nov-21 A	17-Aug-22																																									
L18 (Drainage) (3 manhole) SMH1.10-1.12	18			26-Nov-21 A	07-Jan-22 A																																									
L10/L18 (Drainage) Sheet pile	35			03-Jan-22 A	12-Feb-22 A																																									
L18 (Drainage) Backfill	10			07-Feb-22 A	12-Feb-22 A																																									
L10/L18 (Drainage) Excavation	36			14-Feb-22 A	19-Mar-22 A																																									
L10/L18 (Drainage) (4 manhole) SMH1.6-1.9	24			21-Mar-22 A	11-Jun-22																																									
L10/L18 (Drainage) Backfill	10			13-Jun-22	23-Jun-22																																									
DSD Inspection	12	04-Jan-22	17-Jan-22	24-Jun-22	08-Jul-22																																									

Page 12 of 24
Data Date: 04-Jun-22


- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

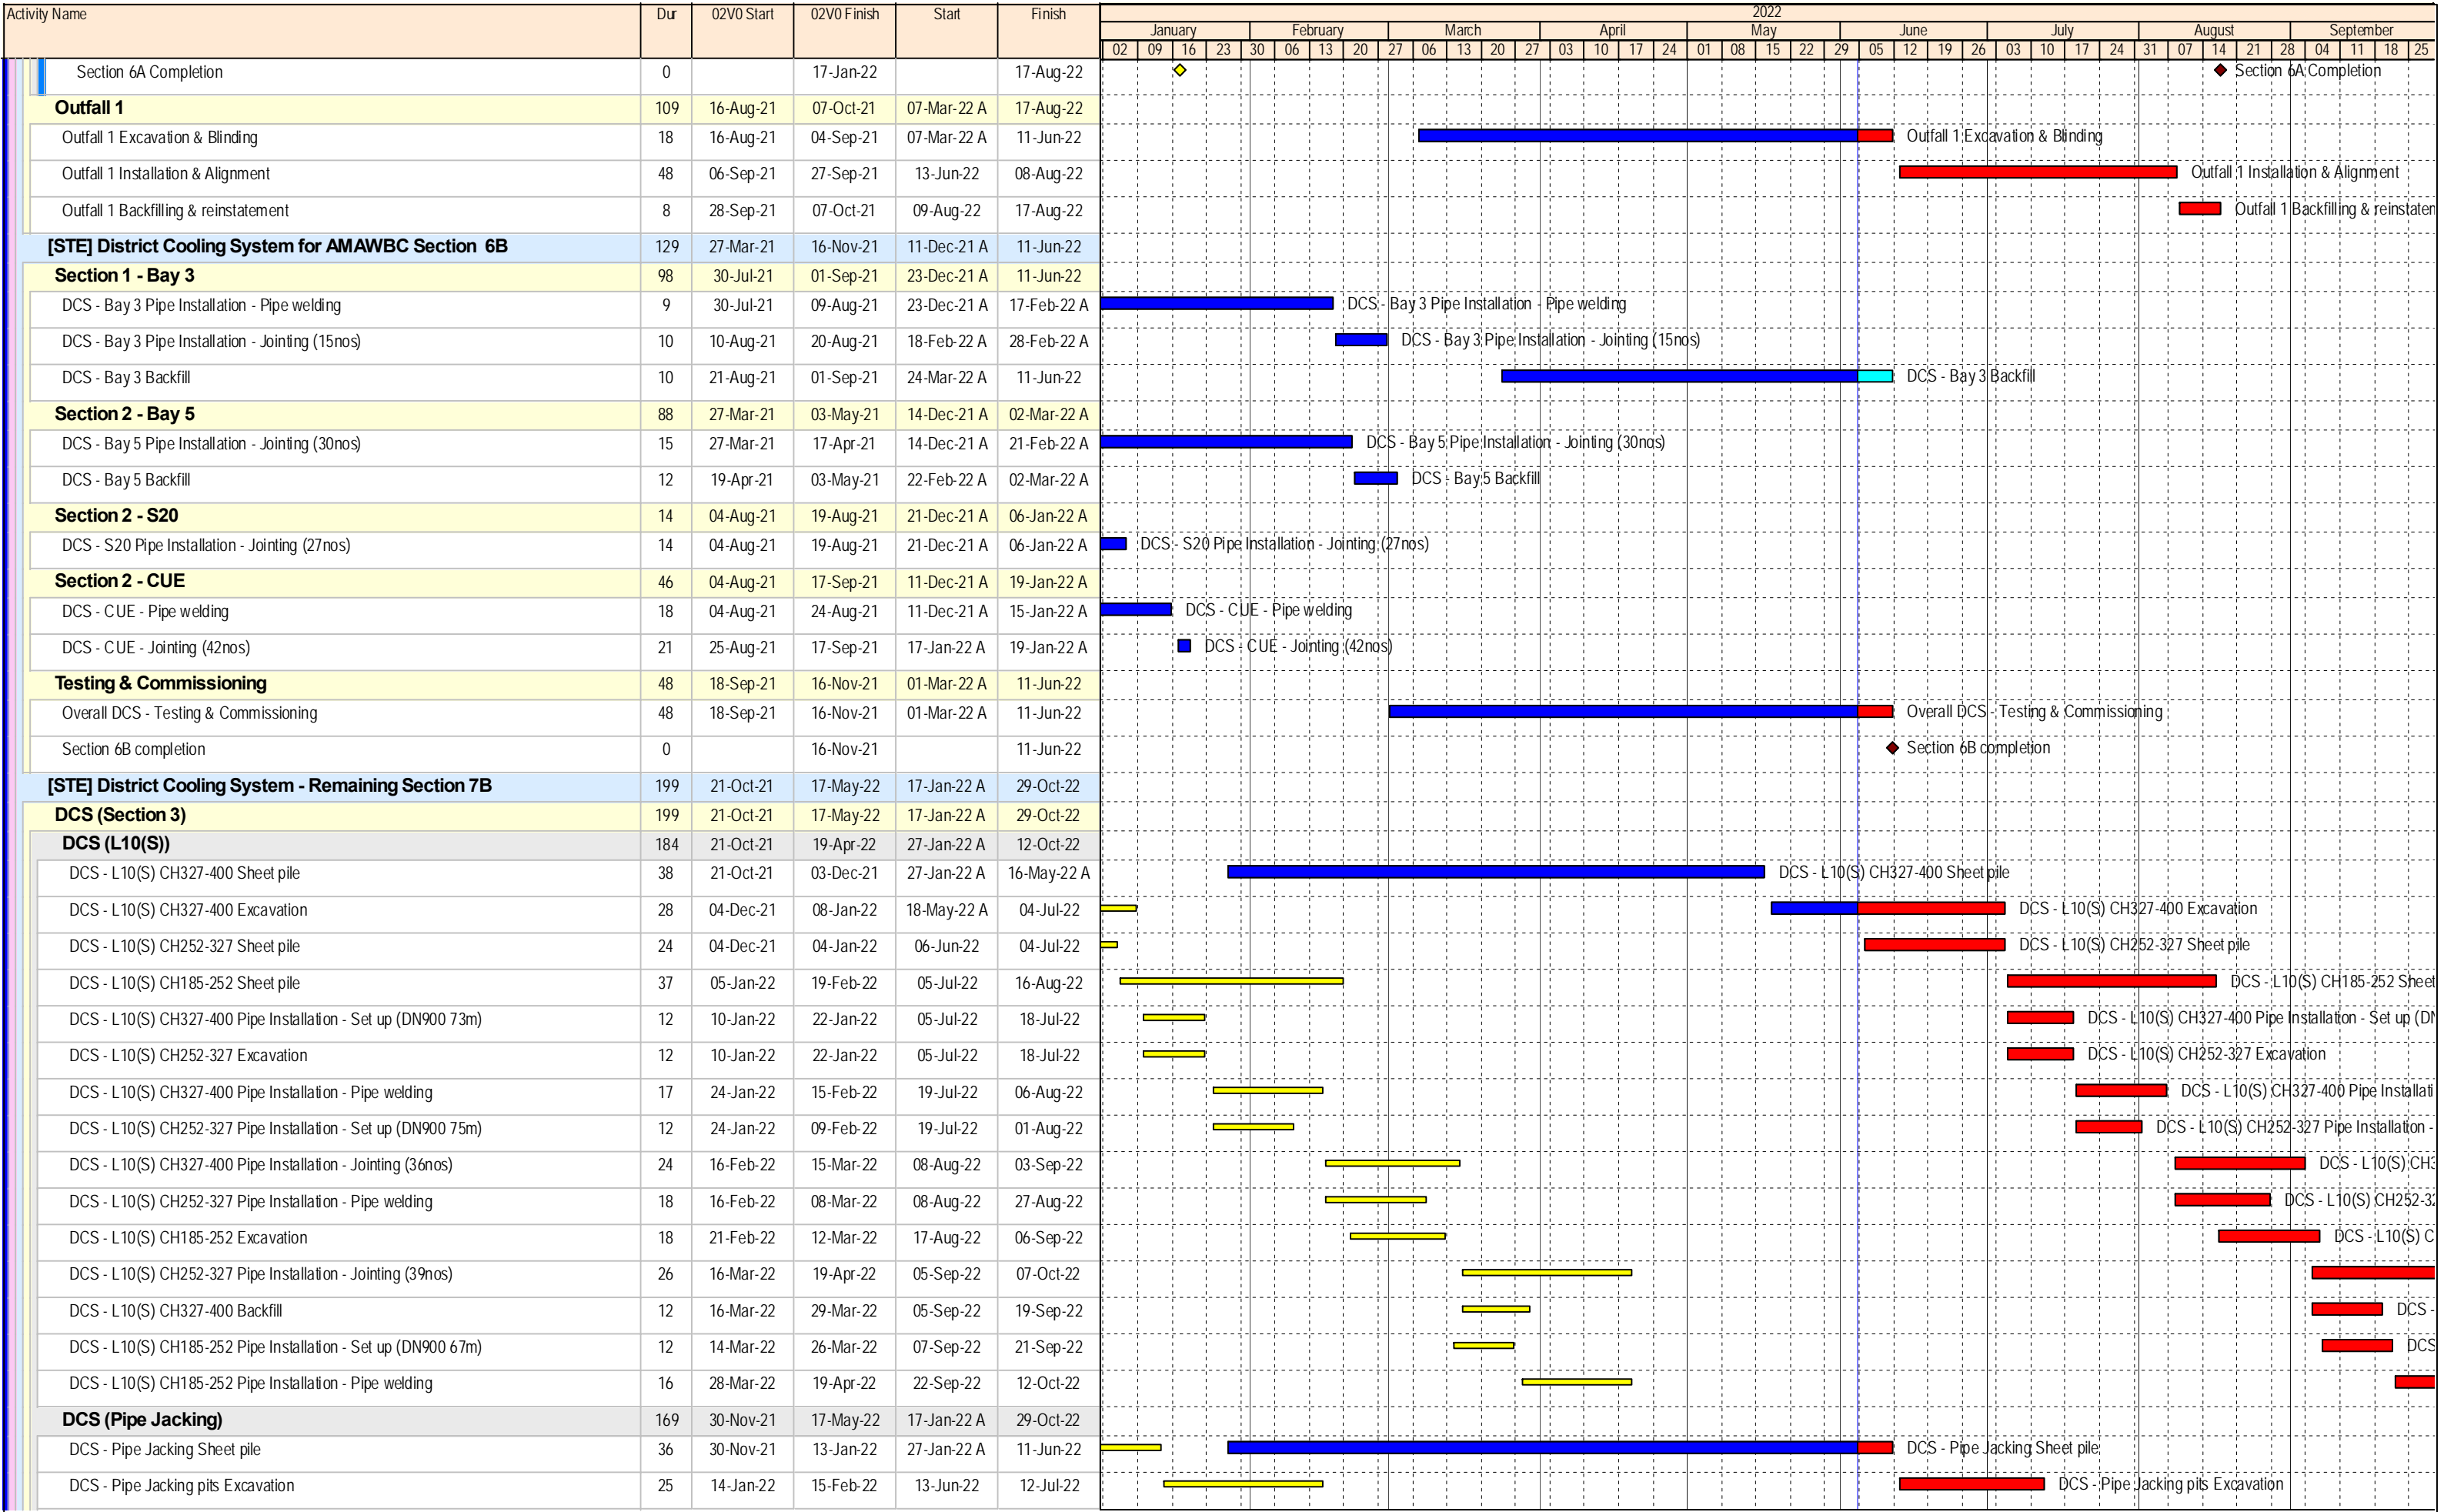

Page 13 of 24
 Data Date: 04-Jun-22


- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar








ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)

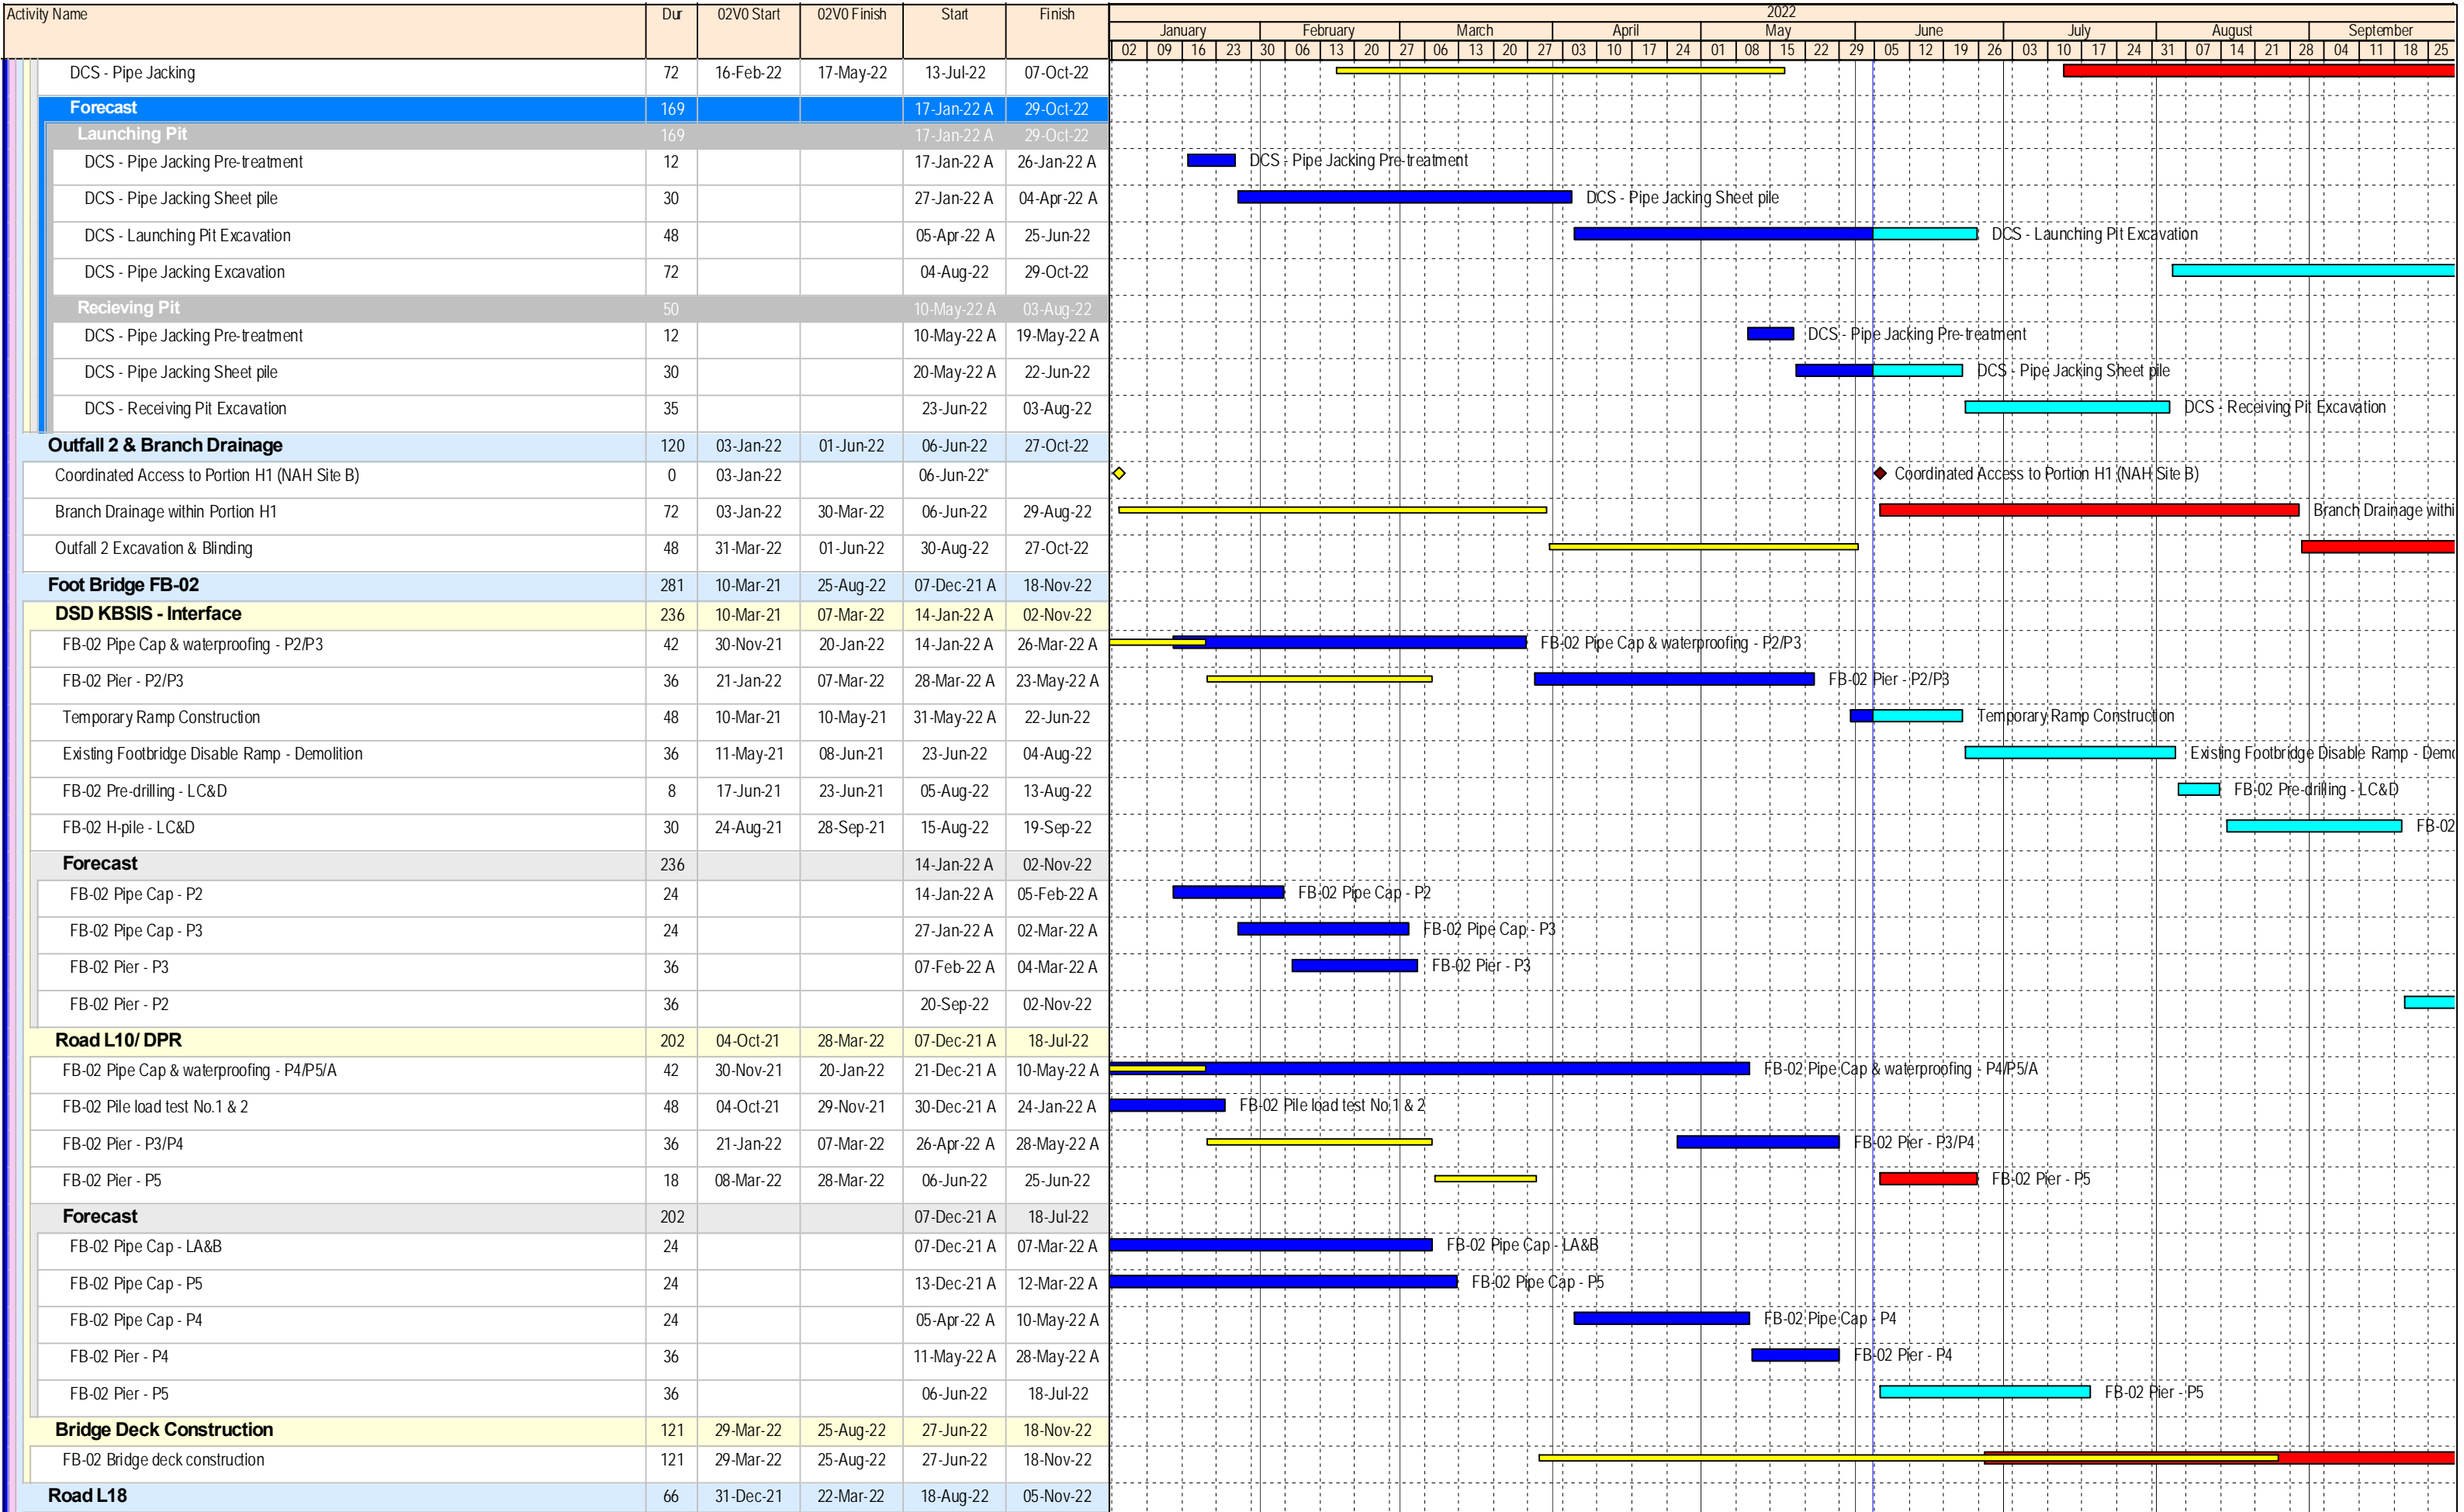


Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu




-  Milestone
-  Planned Bar
-  Critical Activity
-  Actual Milestone
-  Actual Work
-  Baseline Milestone
-  Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

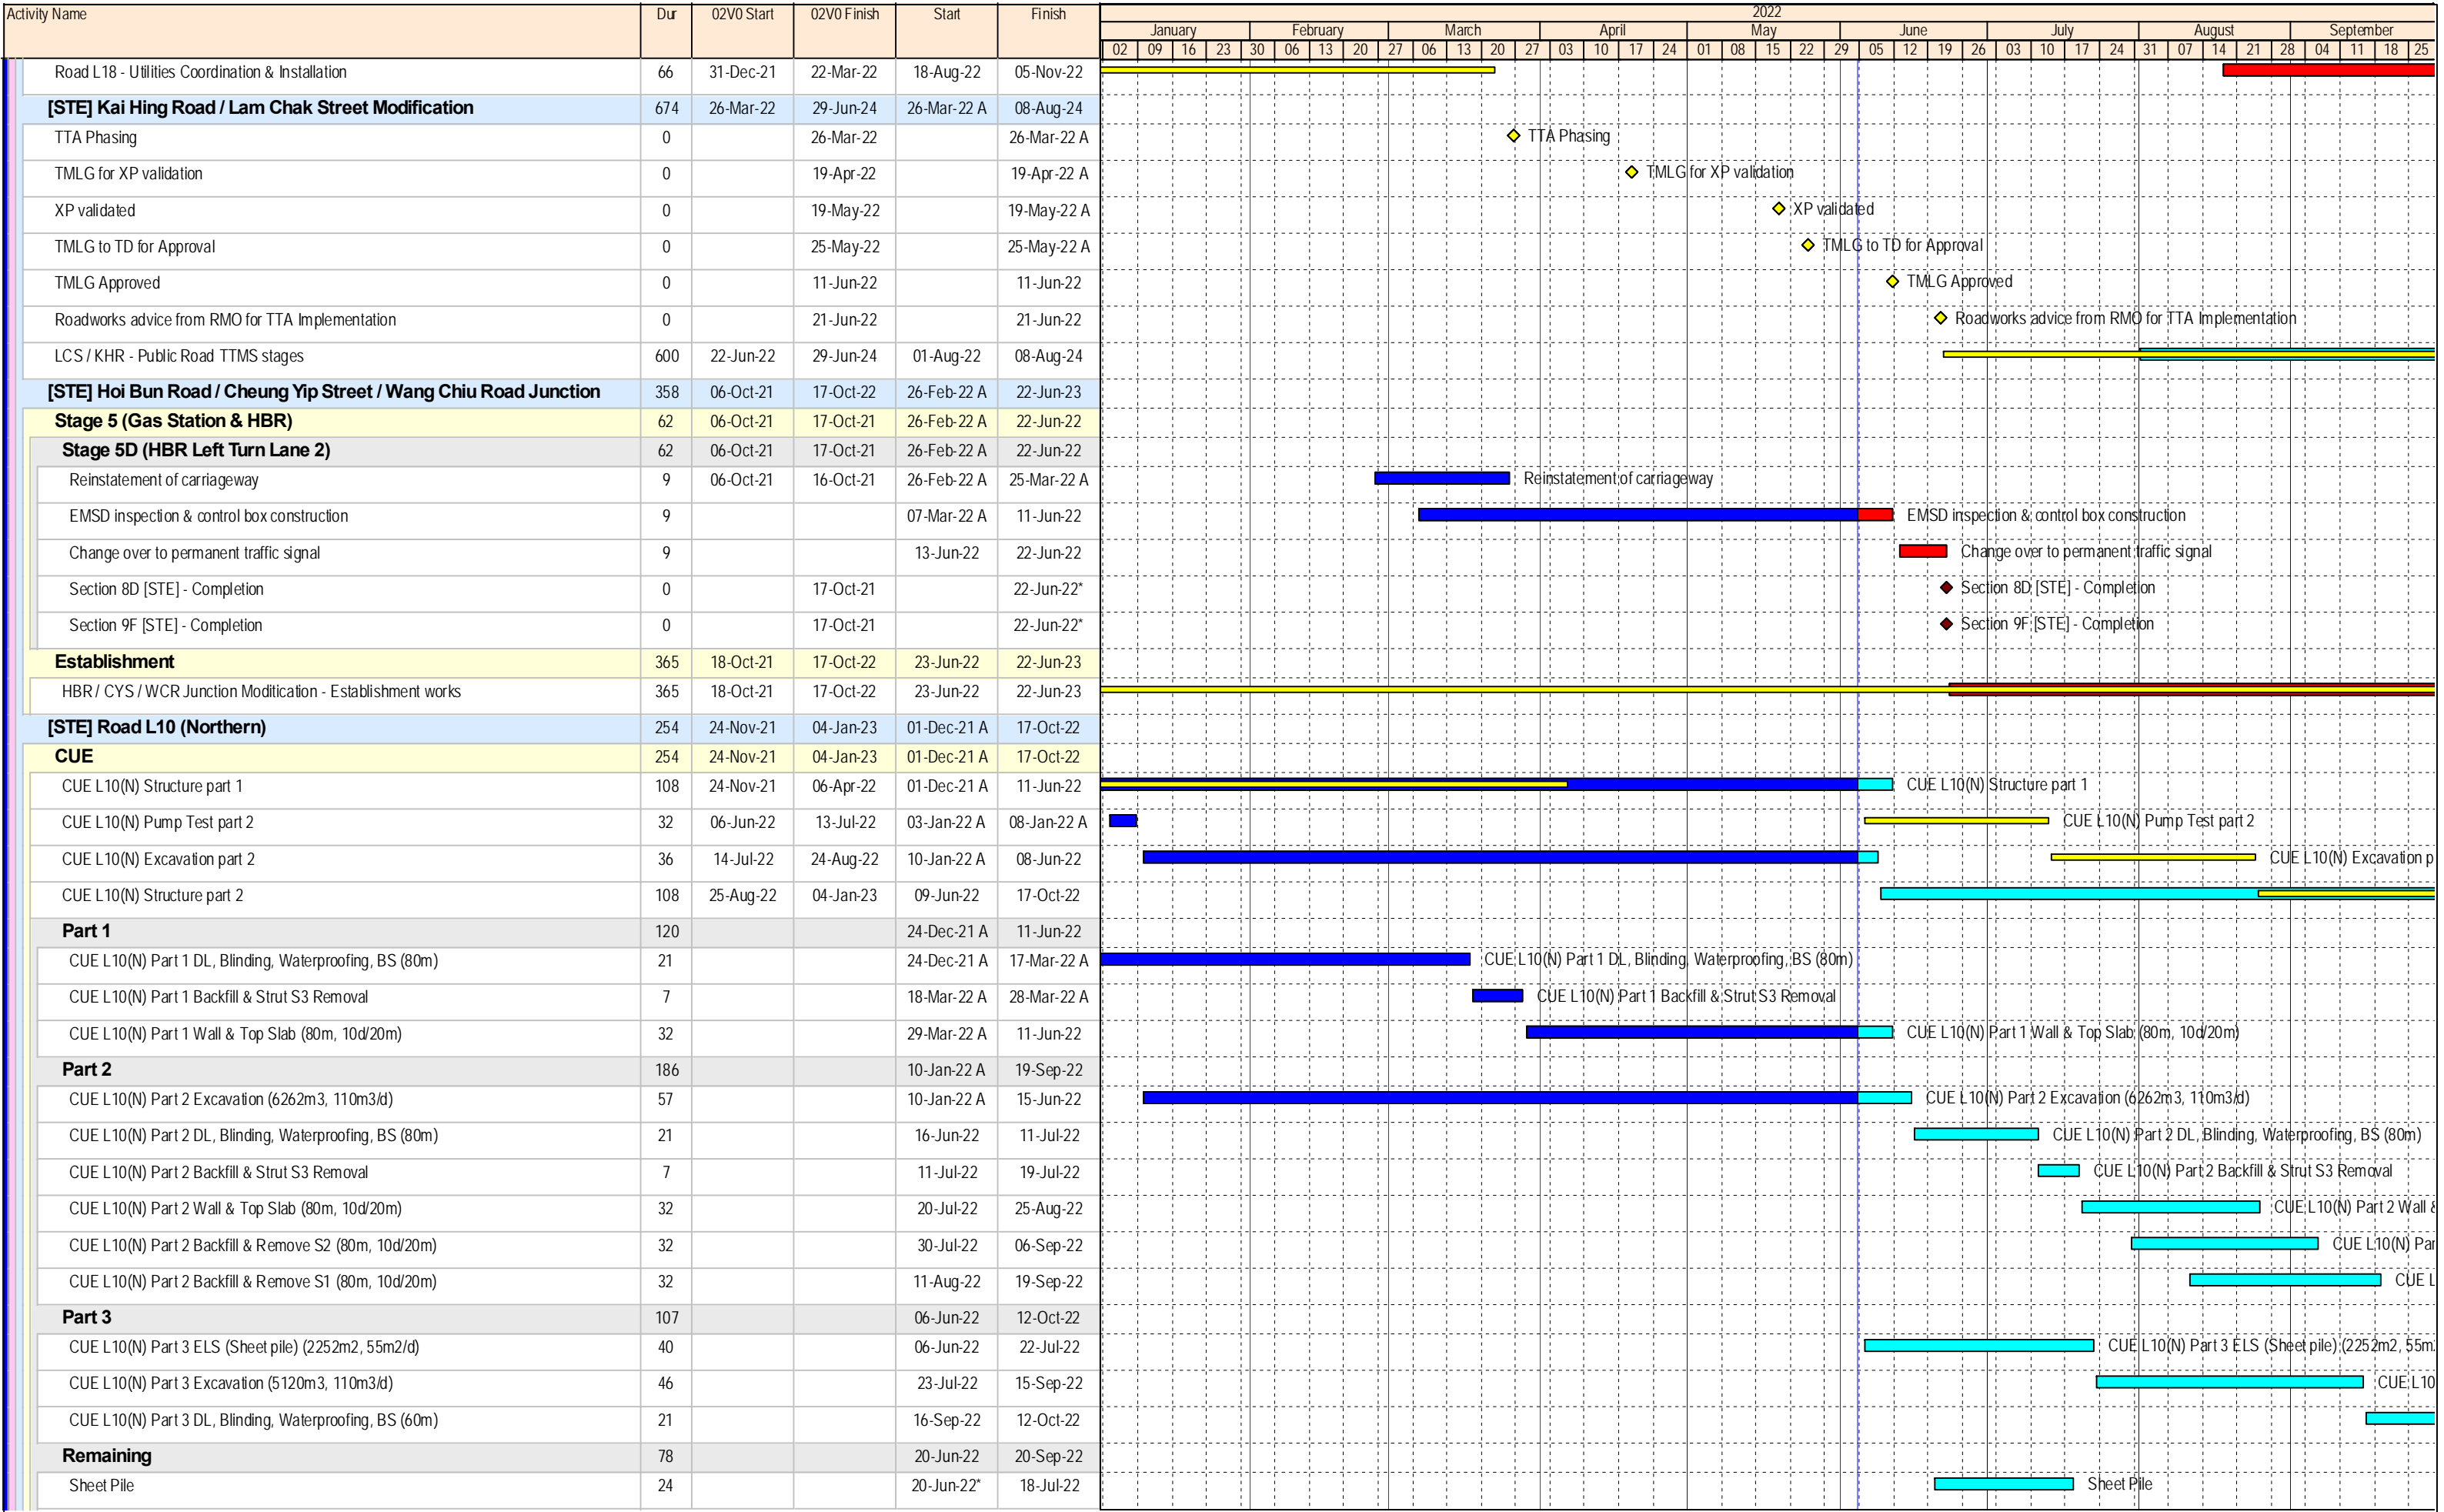


- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

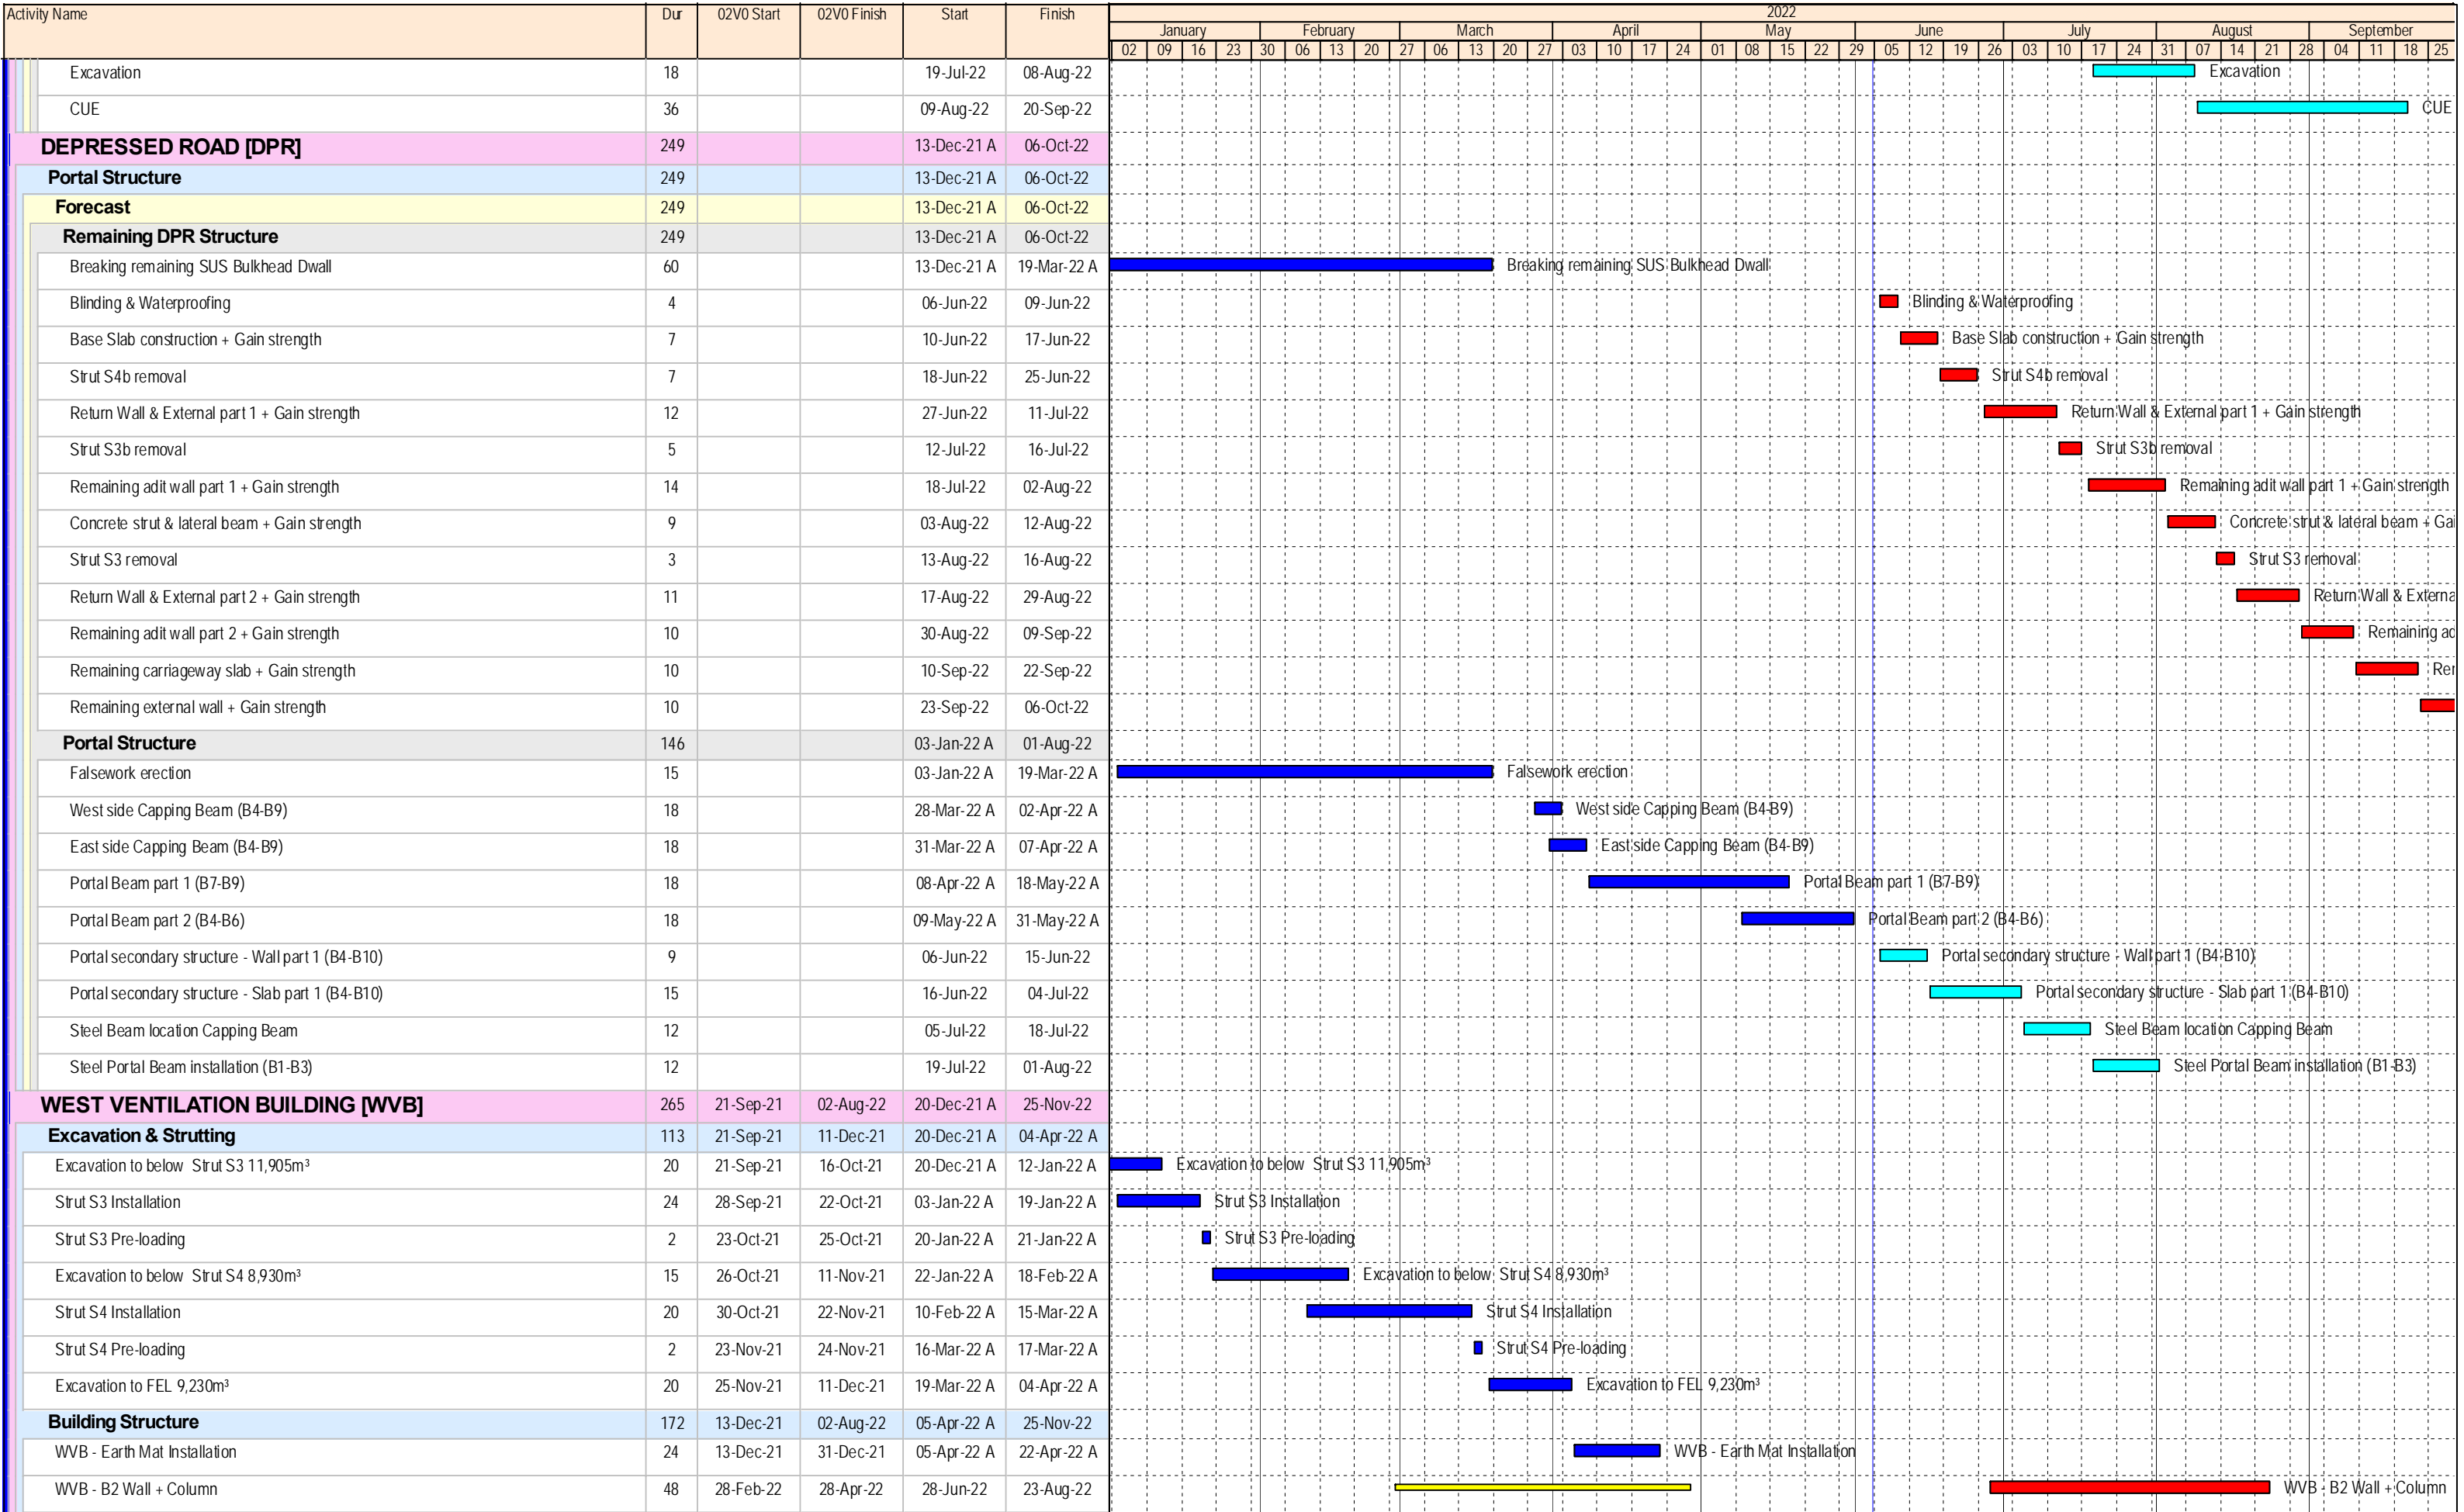


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

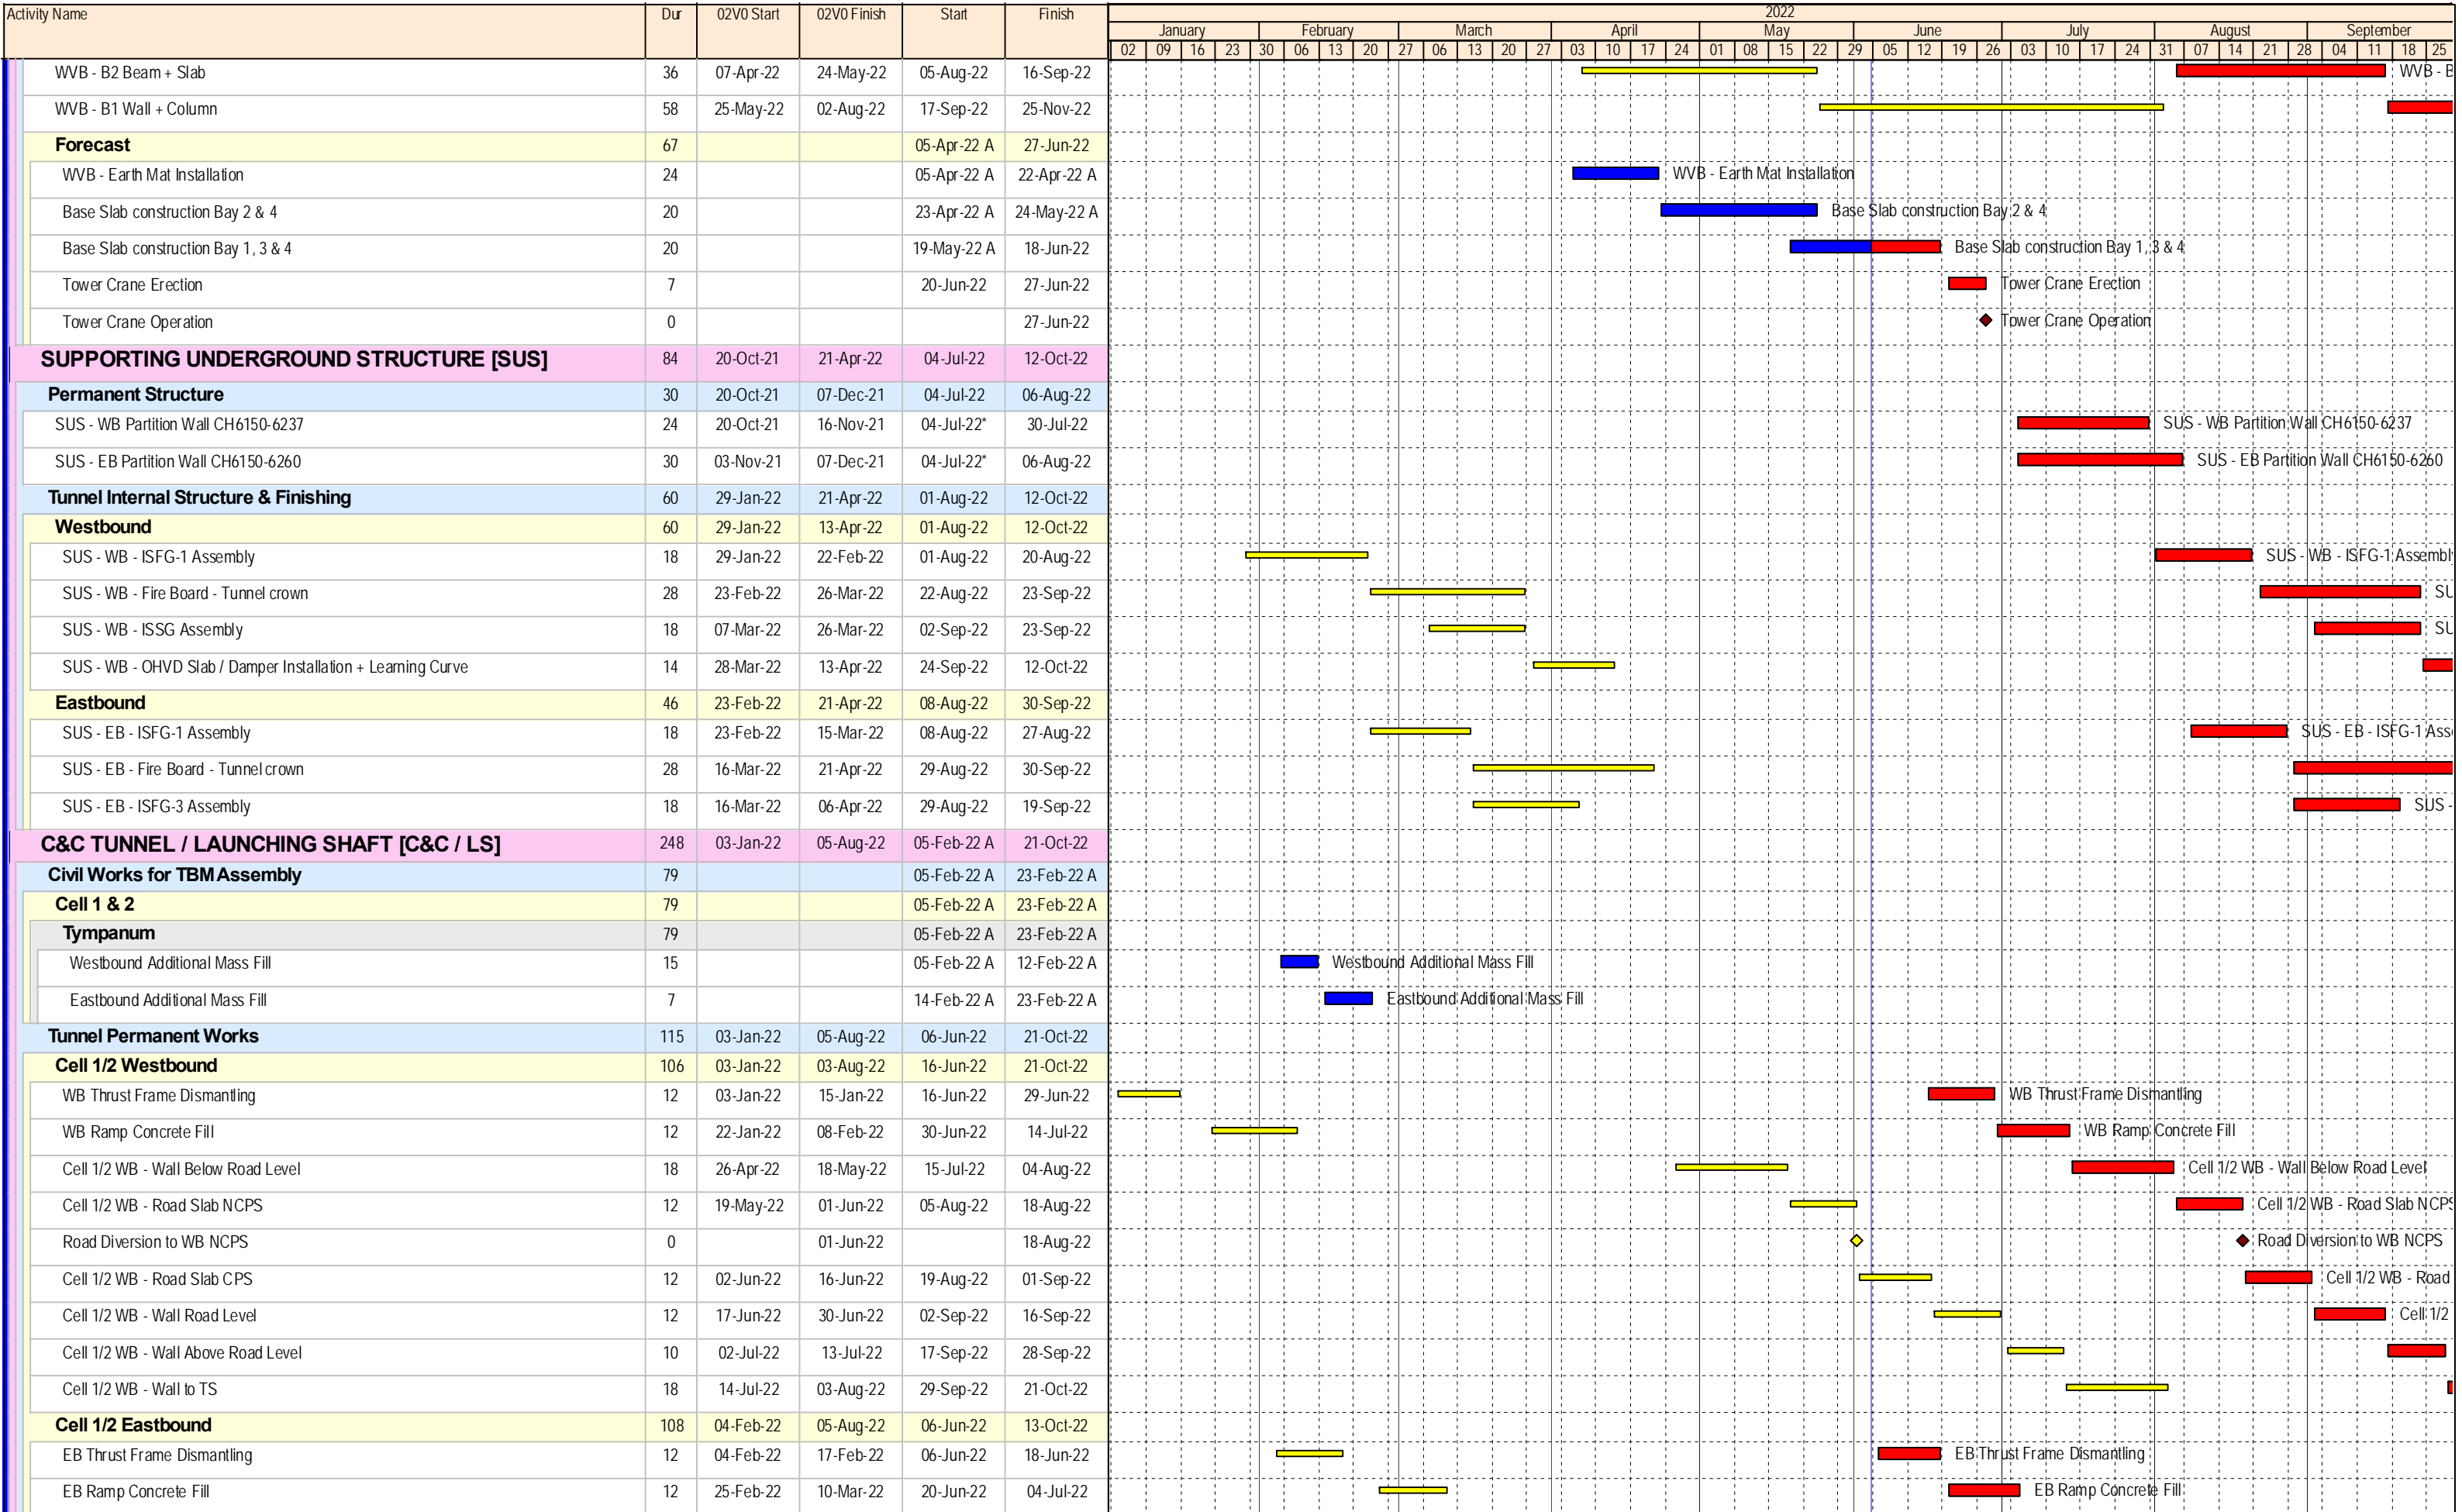


Page 17 of 24
Data Date: 04-Jun-22


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

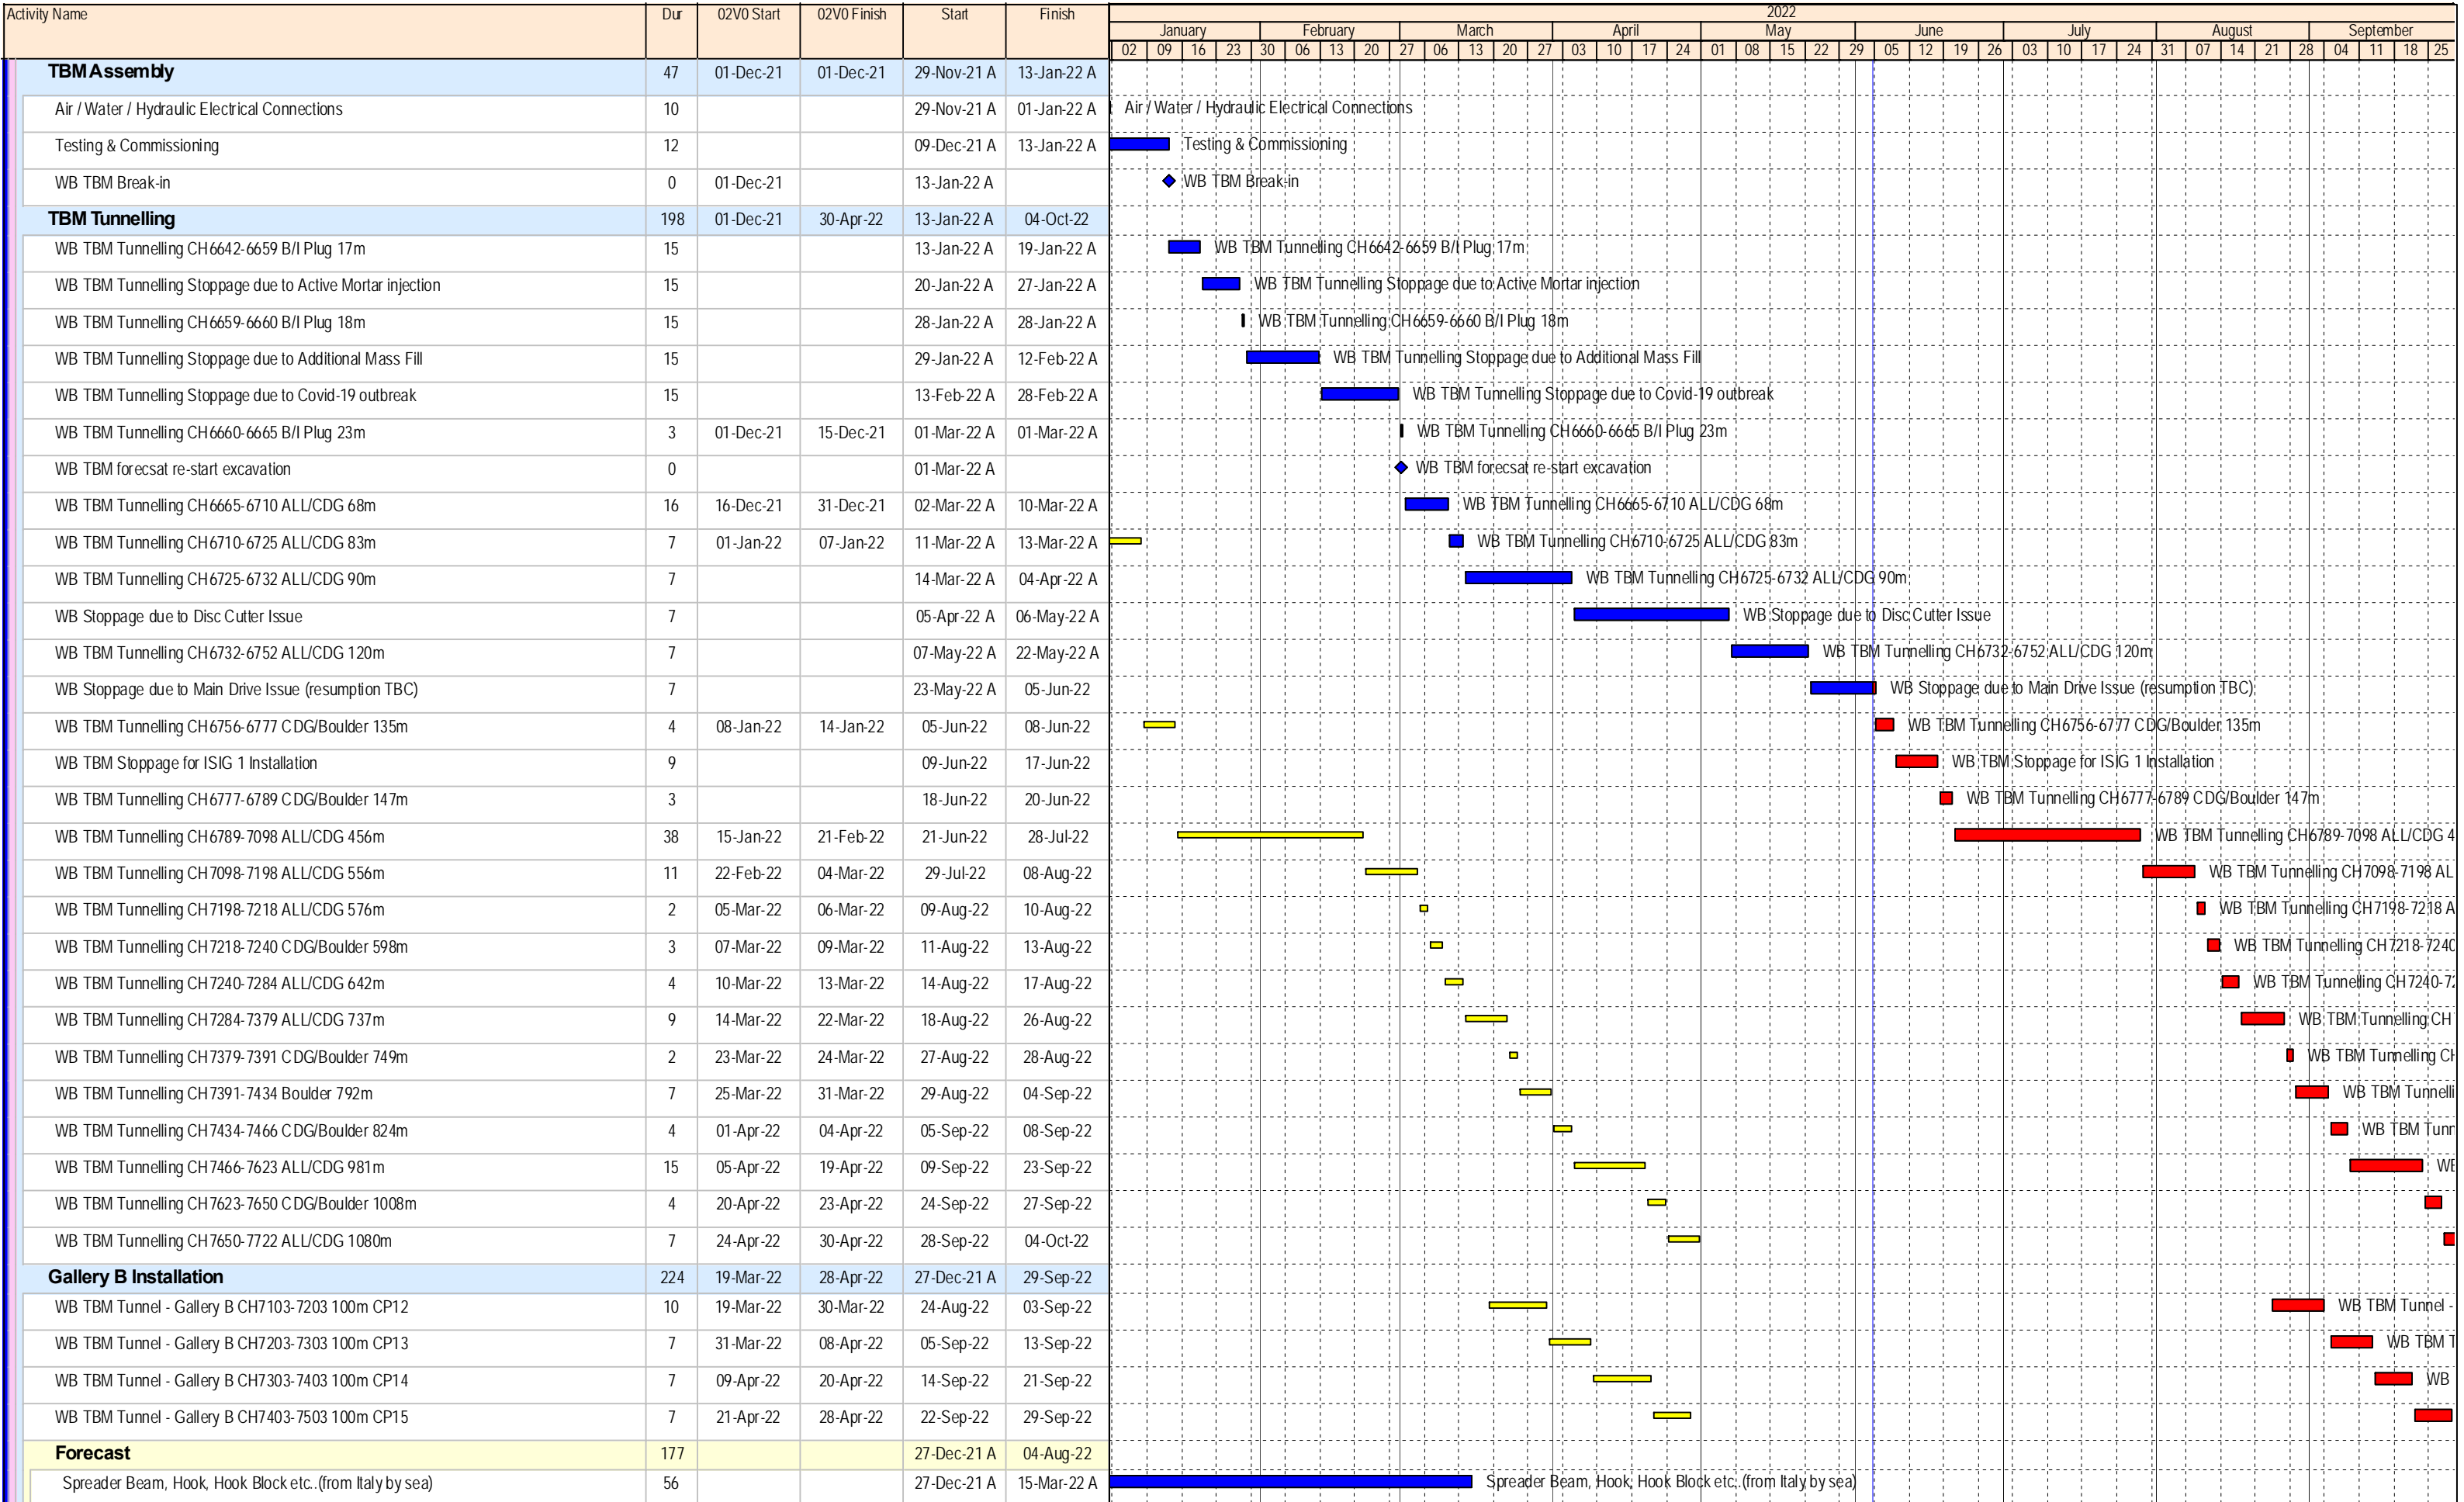


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

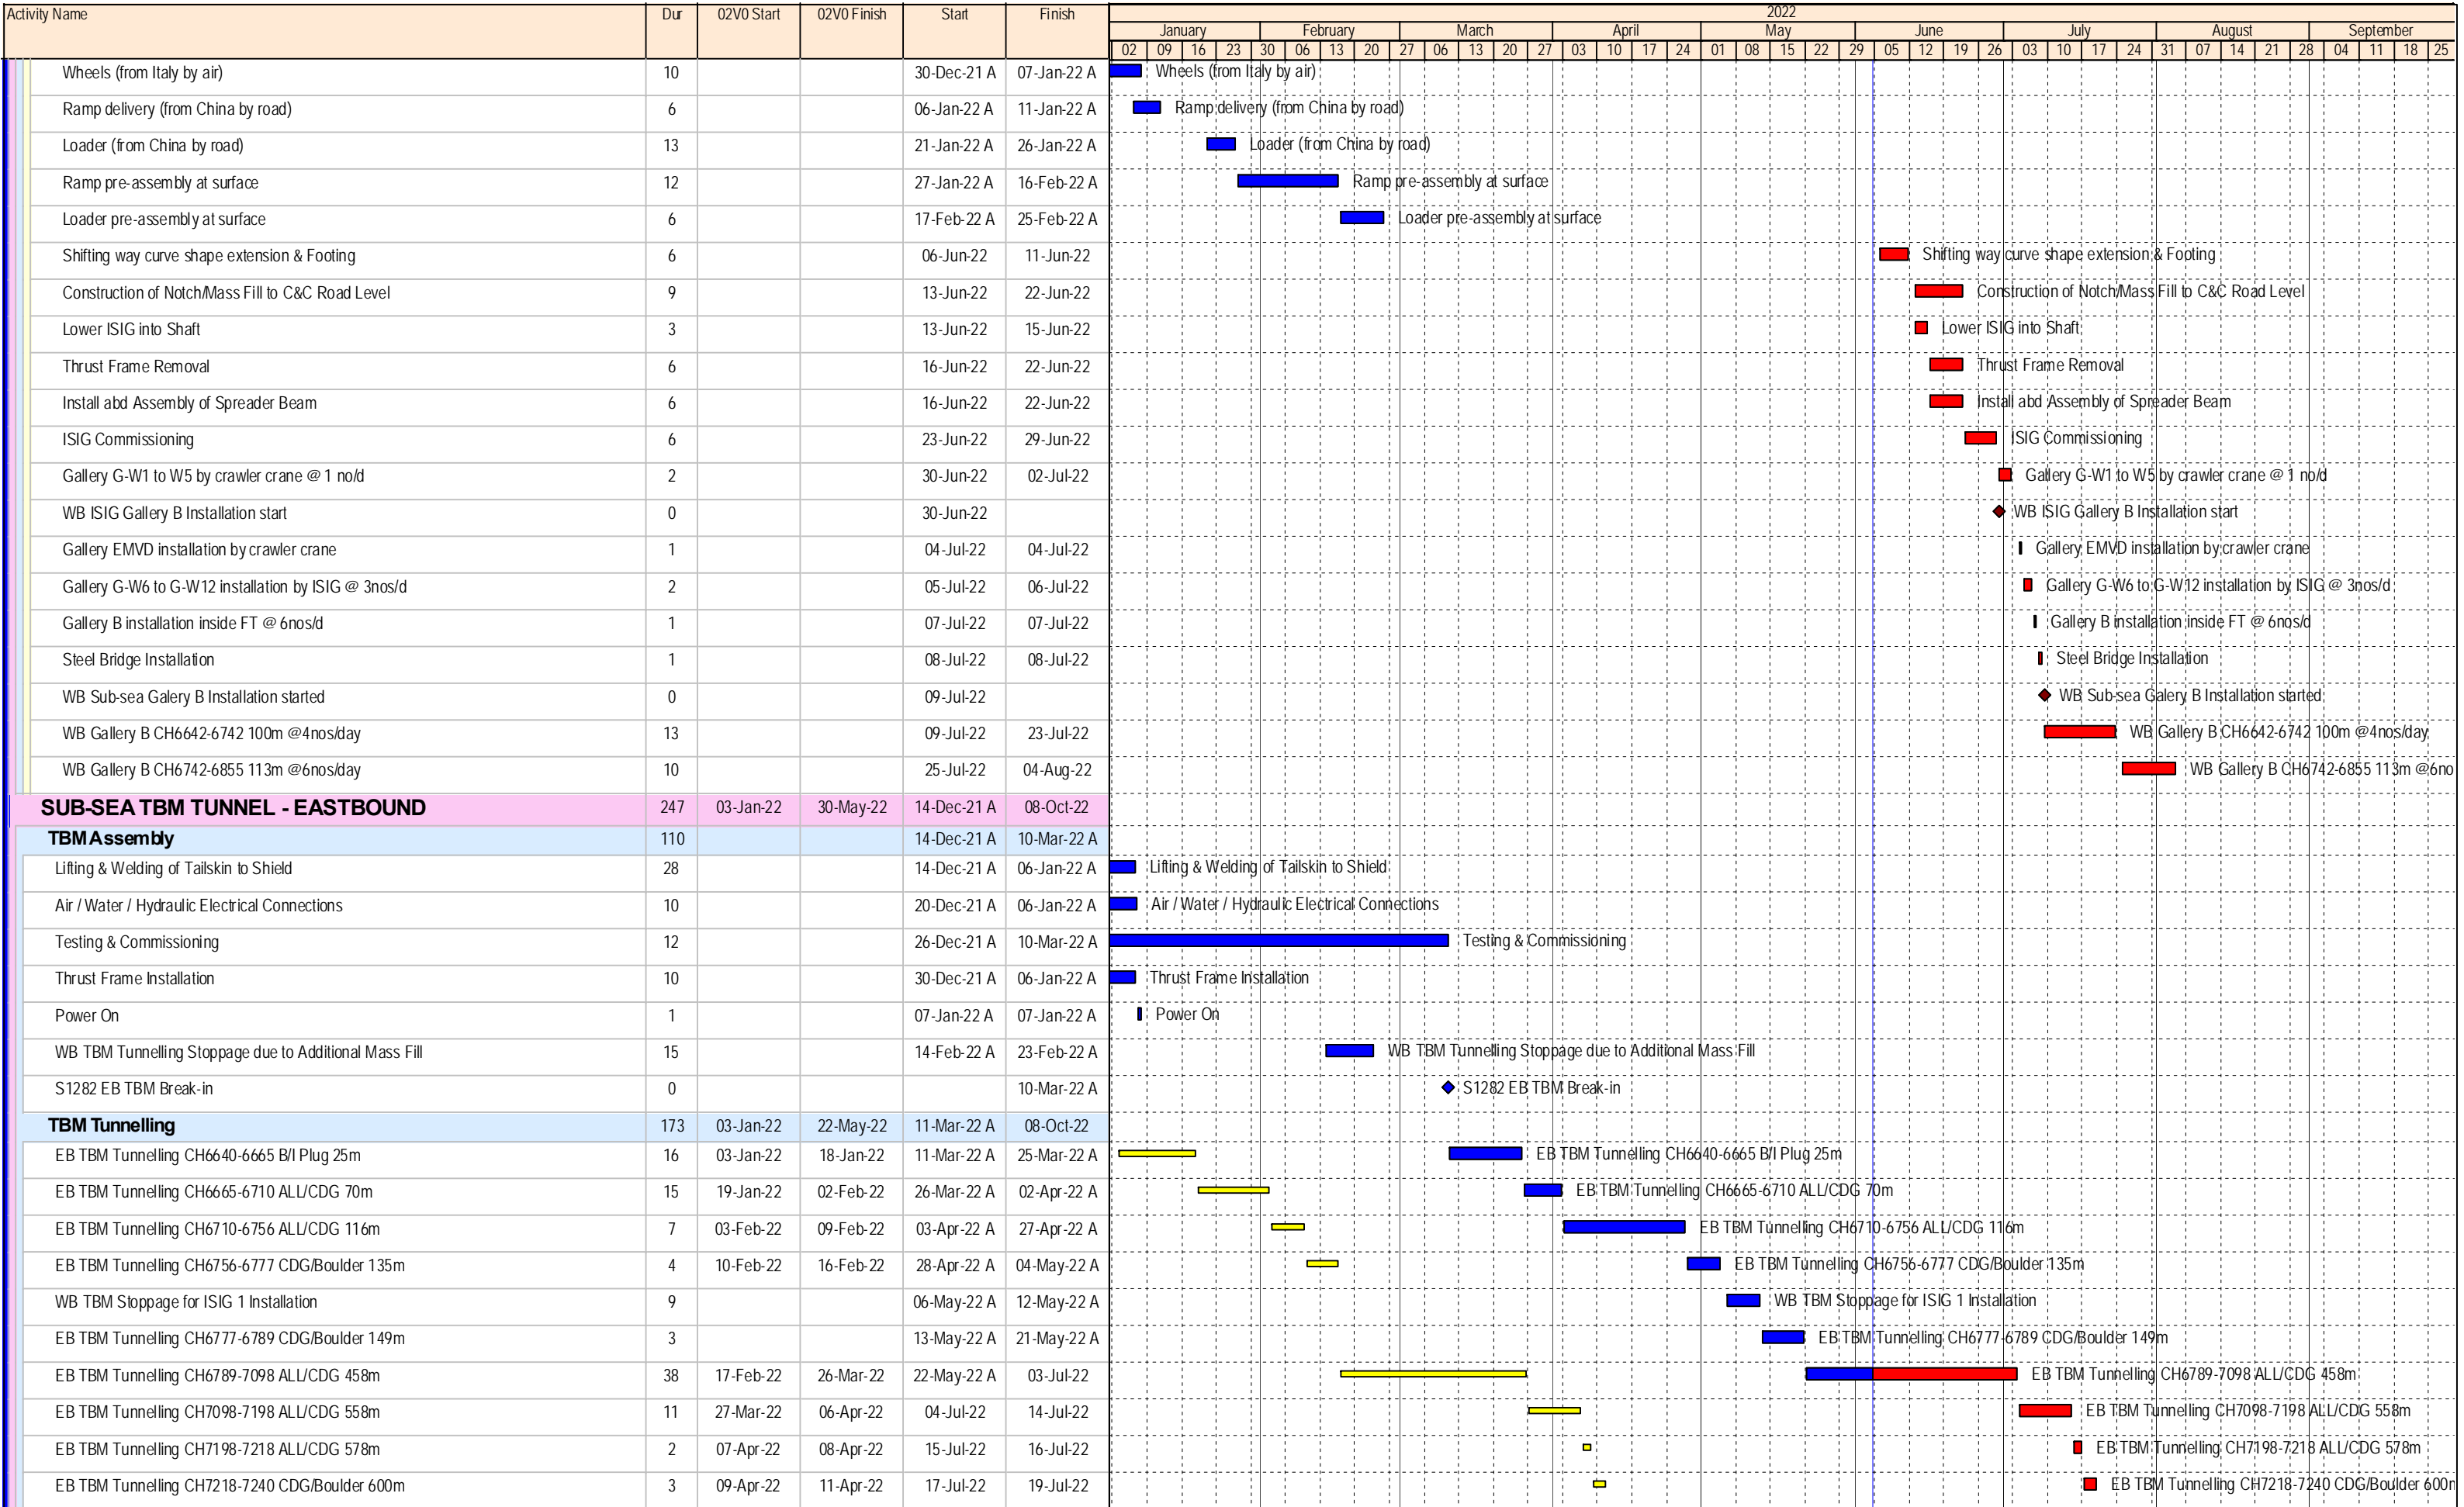


- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

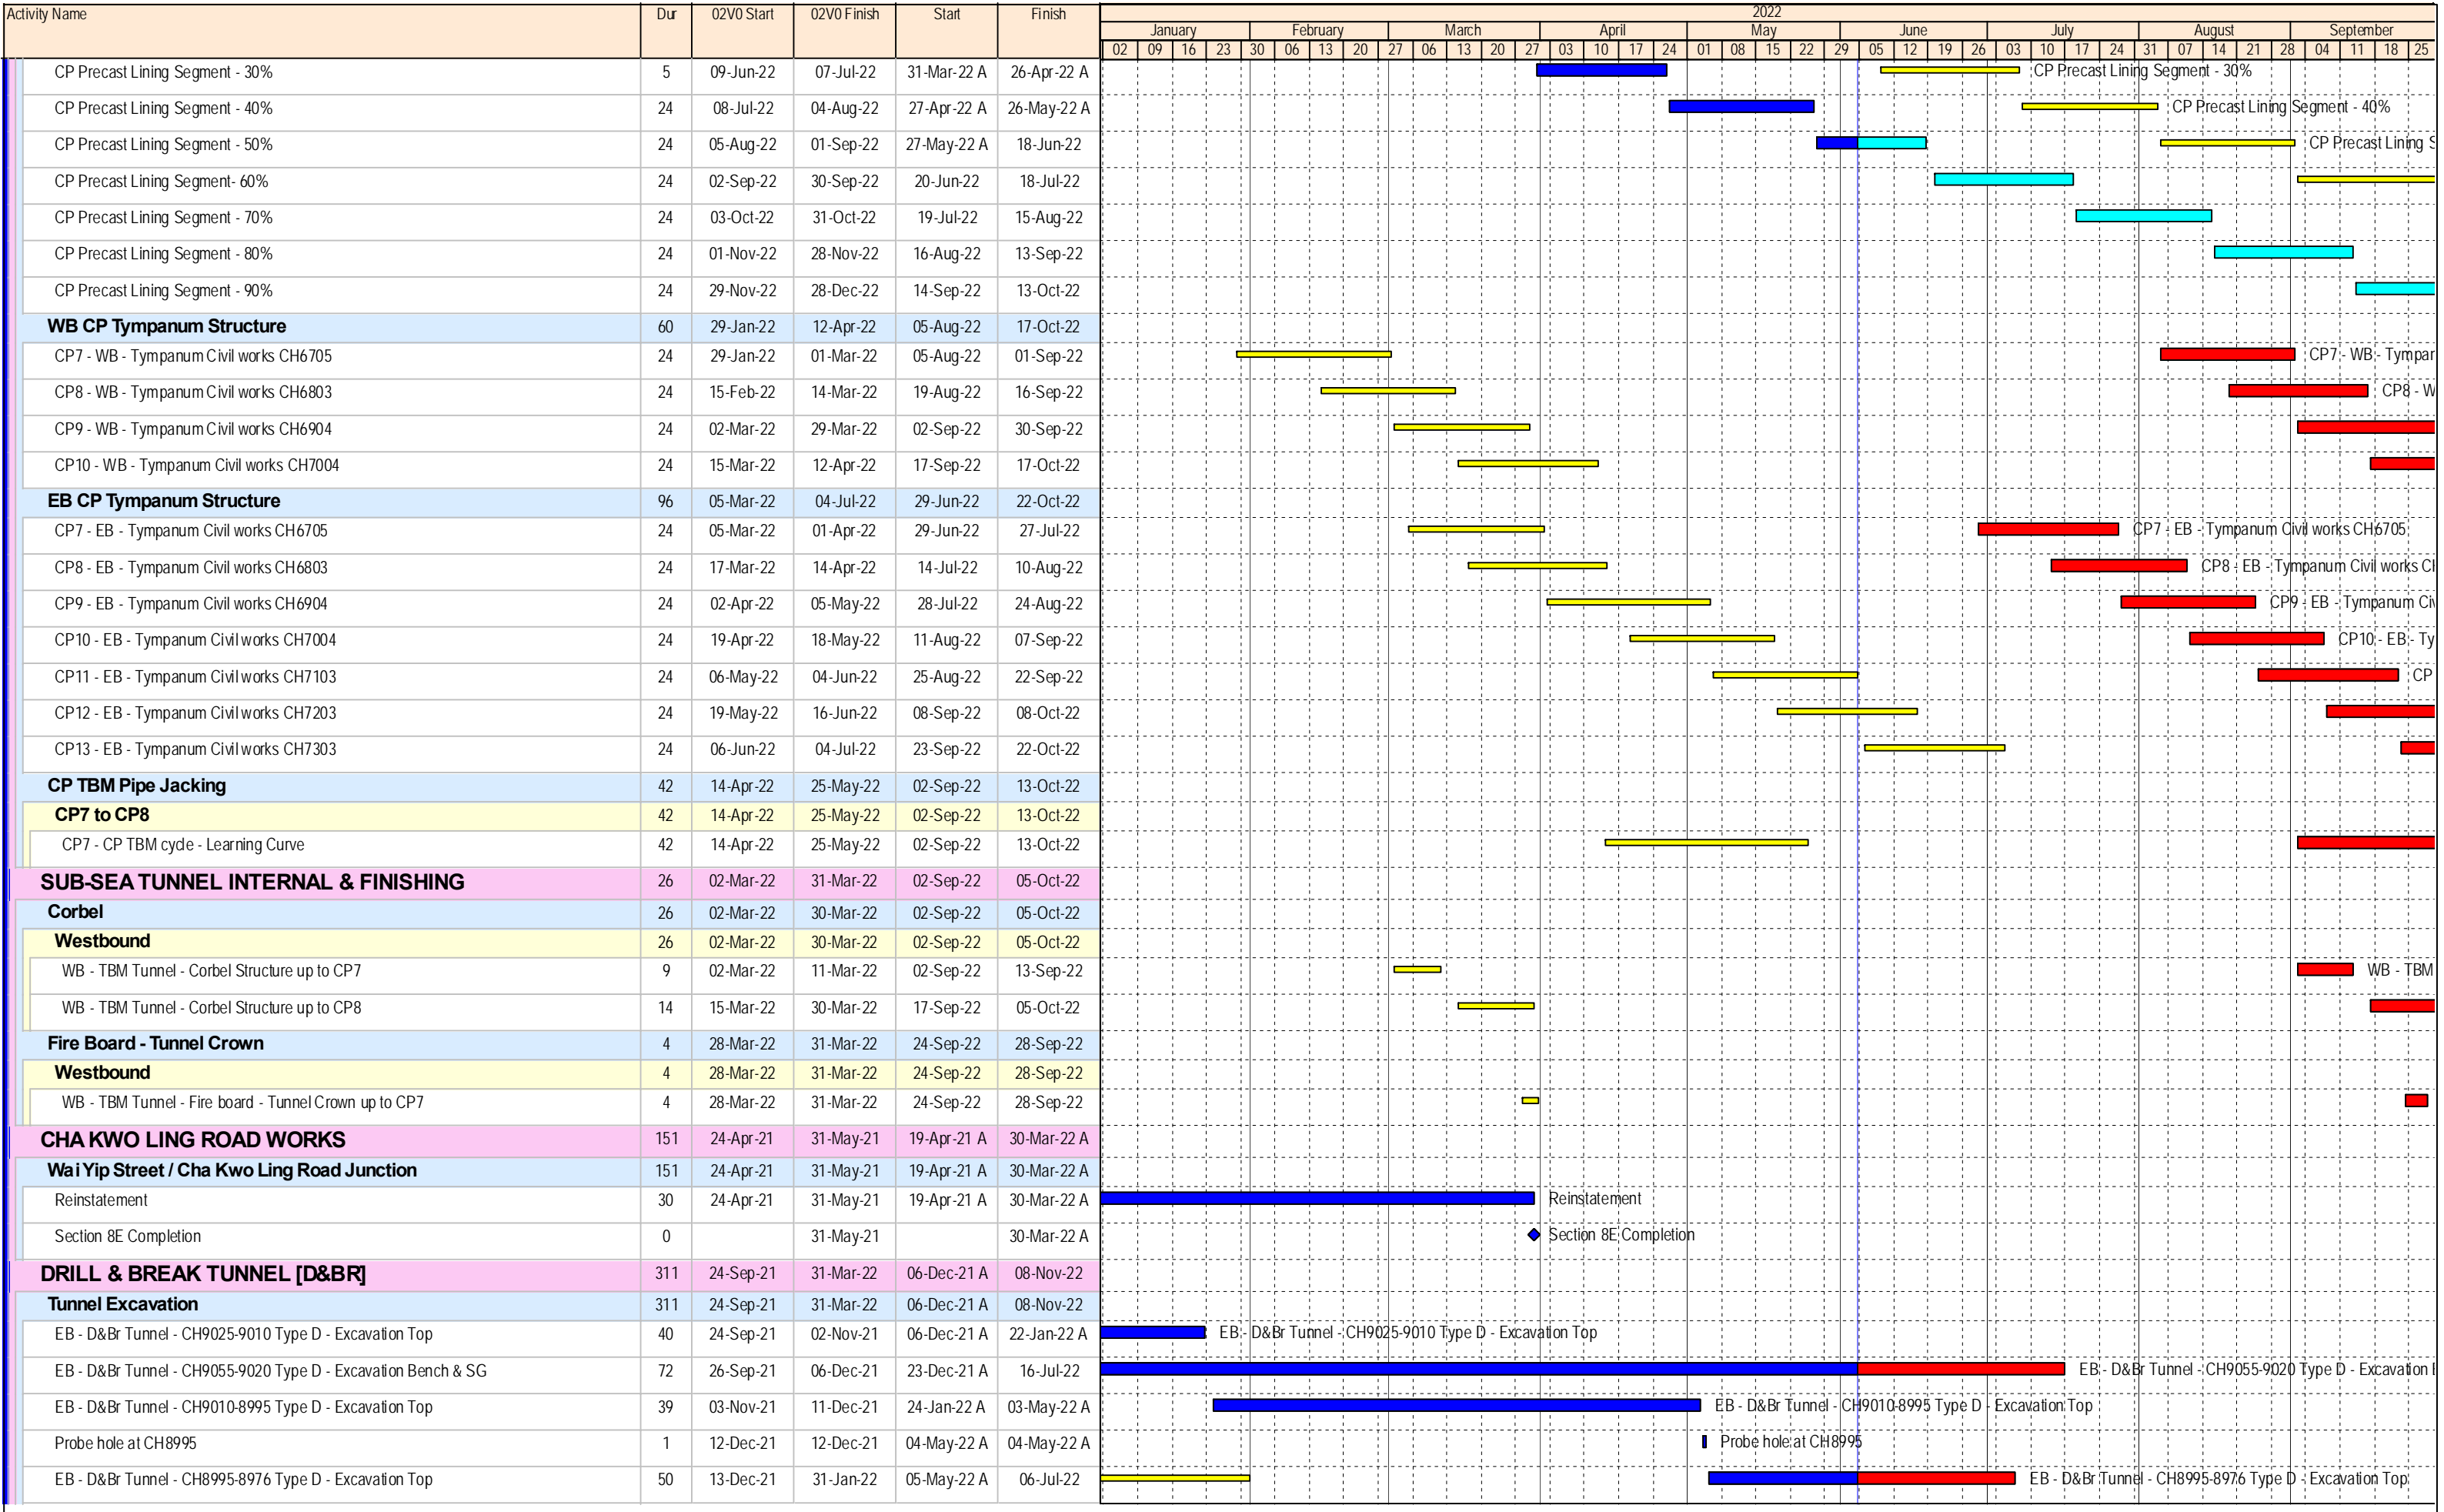


- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

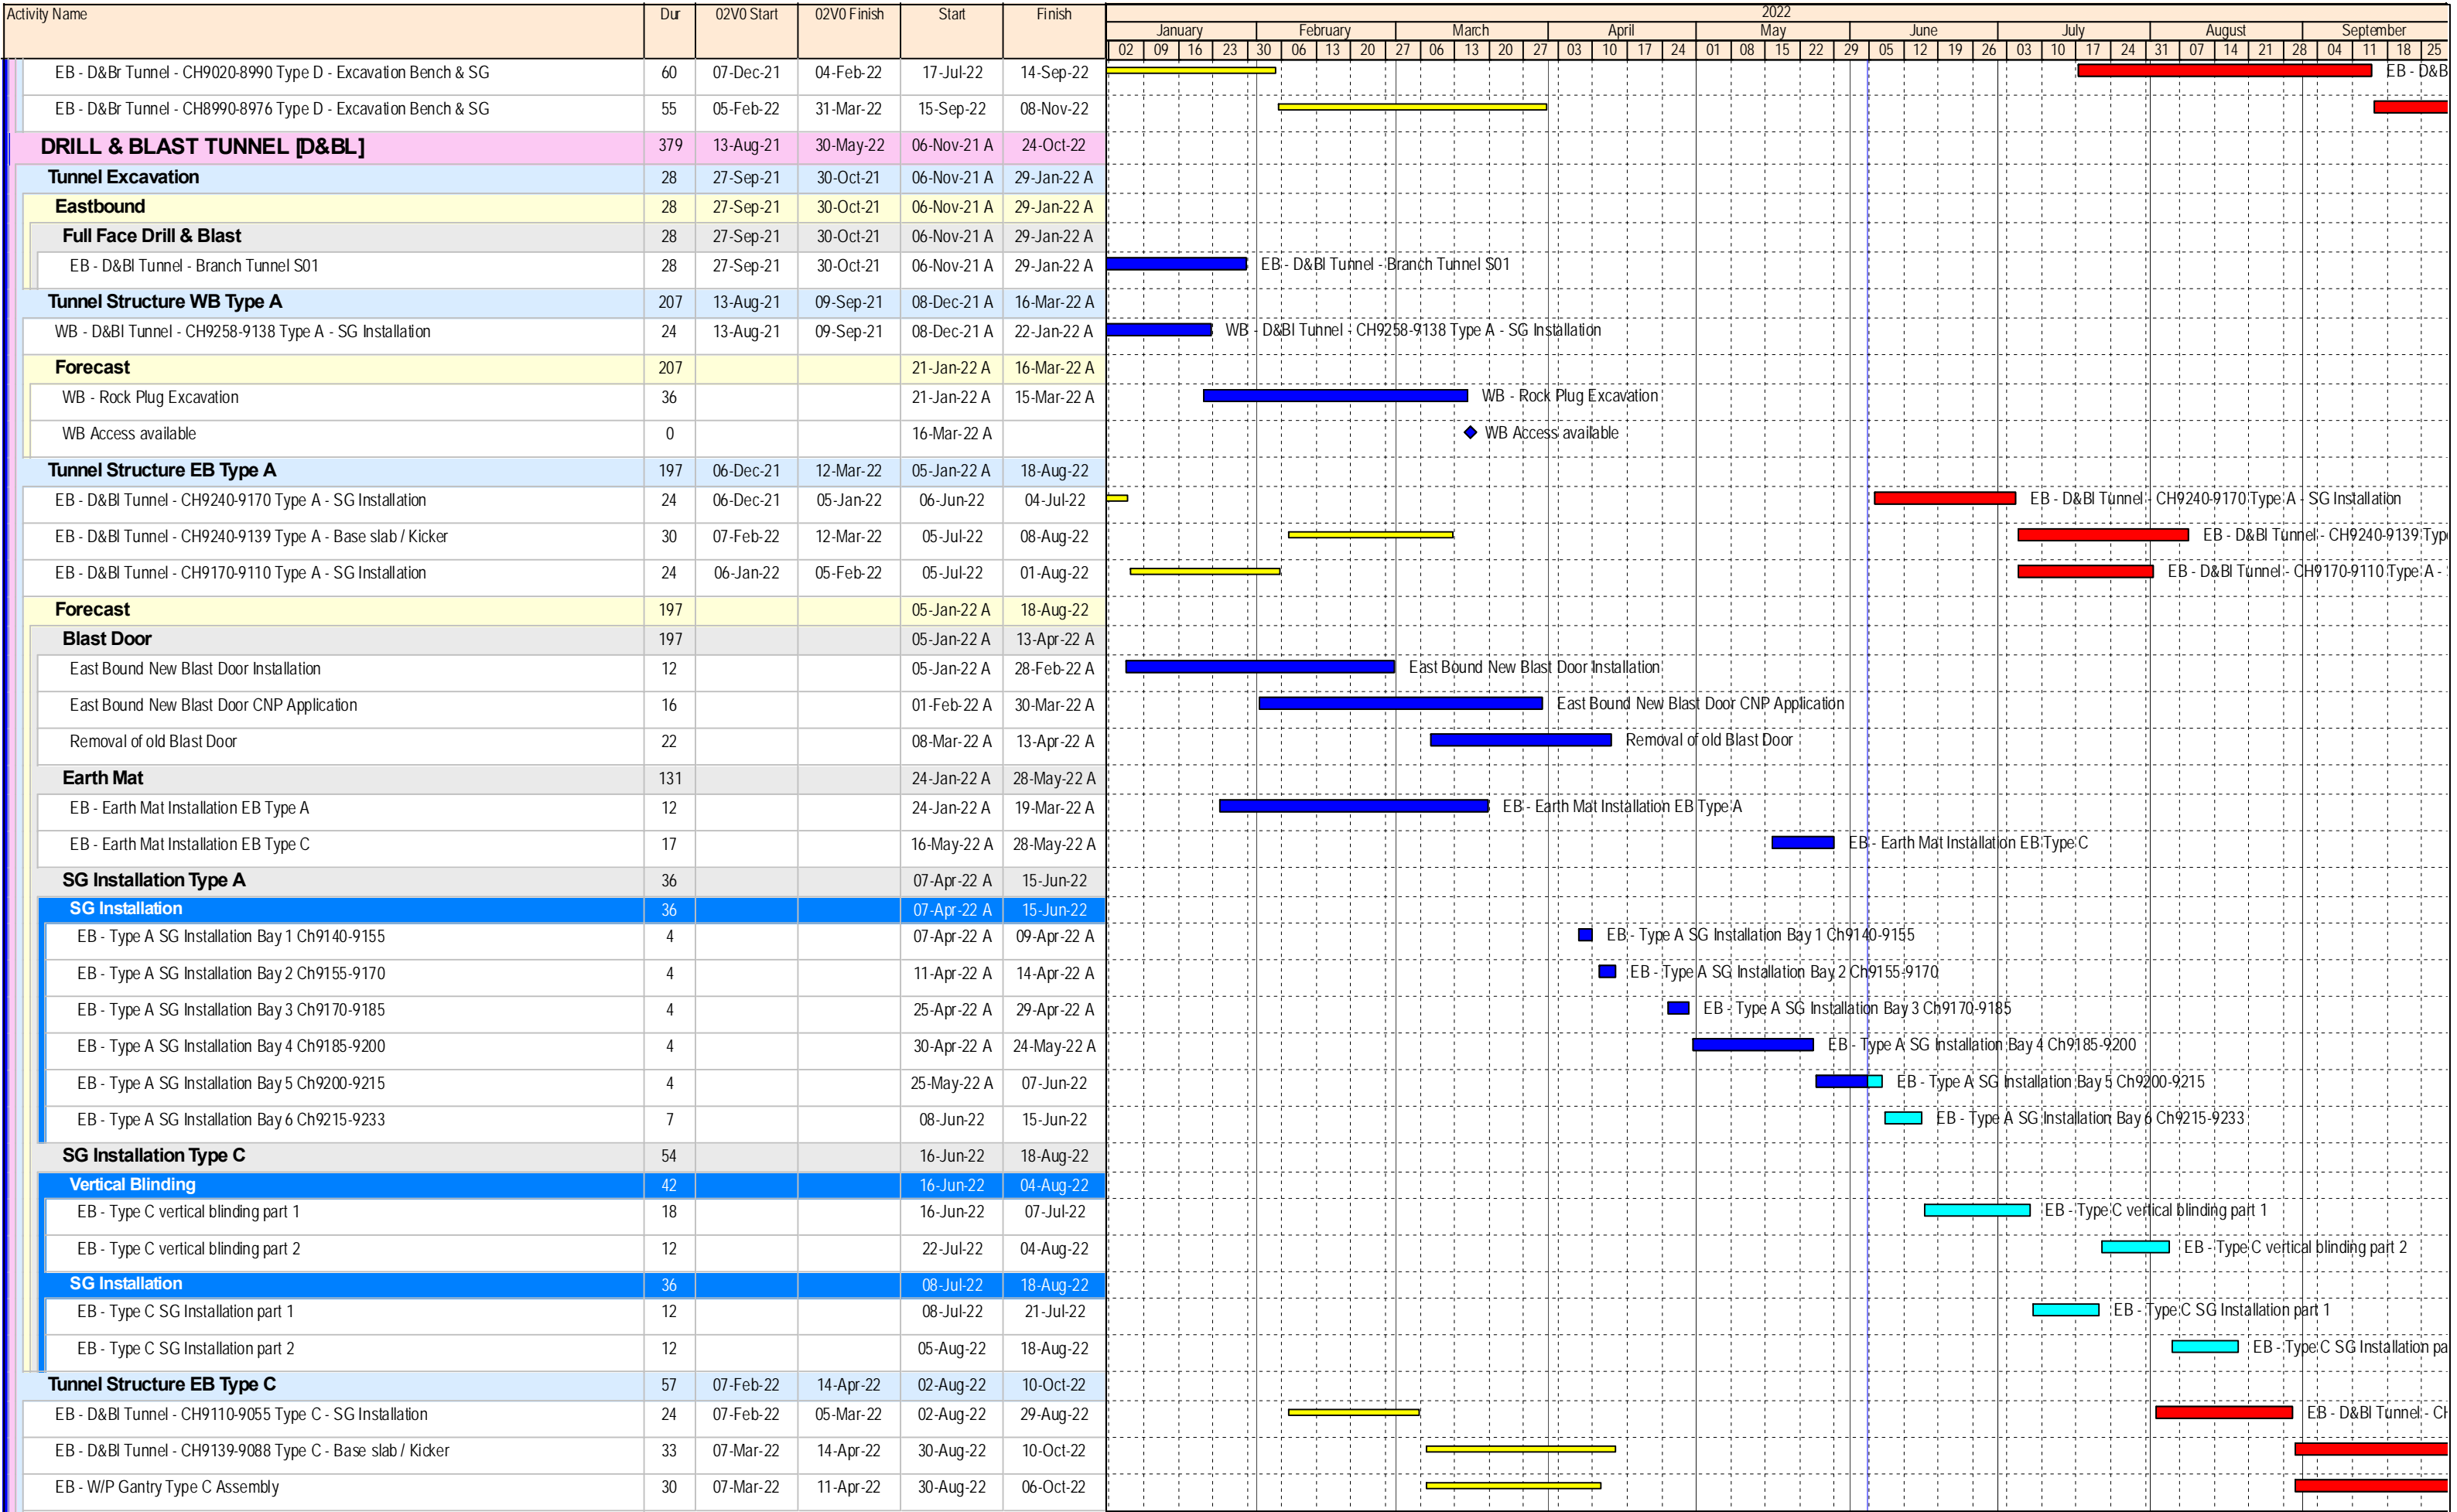

- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

