


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish
DESIGN SUBMISSION & APPROVAL	603	03-Oct-20	17-Oct-22	27-Oct-20 A	13-Nov-22
GENERAL					
Design Memorandum	540	03-Oct-20	01-Aug-22	29-Oct-20 A	02-Apr-22
Design Memorandum - 7th Review	521	06-Oct-20	13-Jul-22	16-Apr-21 A	24-Mar-22
Design Memorandum - Approval	0	06-Oct-20	06-Oct-20	17-May-21 A	07-Jun-21 A
Construction Traffic Impact Assessment - Kai Tak Area	0	06-Oct-20	06-Oct-20	03-May-21 A	06-Sep-21 A
CTIA Kai Tak Area - Resubmission	0	06-Oct-20	06-Oct-20	03-May-21 A	19-Aug-21 A
CTIA Kai Tak Area - 6th Sub	0	06-Oct-20	06-Oct-20	20-Aug-21 A	19-Aug-21 A
CTIA Kai Tak Area - 6th Review	0	06-Oct-20	06-Oct-20	06-Sep-21 A	06-Sep-21 A
CTIA Kai Tak Area - Approval	0	06-Oct-20	06-Oct-20	06-Sep-21 A	06-Sep-21 A
ACABAS- Footbridge FB-02	20	01-Apr-21	29-Apr-21	06-Feb-22	05-Mar-22
DDA - 1st Sub	0	01-Apr-21	01-Apr-21	06-Feb-22	05-Feb-22
DDA - Review by SO	28	02-Apr-21	29-Apr-21	06-Feb-22	05-Mar-22
DDA - Review by IP / DC	28	02-Apr-21	29-Apr-21	06-Feb-22	05-Mar-22
ACABAS- Footbridge FB-03	48	17-May-22	13-Jul-22	25-Jan-22	24-Mar-22
DDA - Draft - Preparation by Designer	48	17-May-22	13-Jul-22	25-Jan-22	24-Mar-22
DAP - WVB	48	13-Sep-21	10-Nov-21	15-Jan-22	15-Mar-22
DDA - Draft - Preparation by Designer	48	13-Sep-21	10-Nov-21	15-Jan-22	15-Mar-22
AIP Roadworks and Street Furniture	0	16-Feb-21	16-Feb-21	29-May-21 A	05-Oct-21 A
AIP - 4th Review by SO	0	16-Feb-21	16-Feb-21	29-May-21 A	29-Jun-21 A
AIP - Further information required by SO	0	16-Feb-21	16-Feb-21	30-Jun-21 A	07-Sep-21 A
AIP - 5th Sub	0	16-Feb-21	16-Feb-21	07-Sep-21 A	07-Sep-21 A
AIP - 5th Review by SO	0	16-Feb-21	16-Feb-21	08-Sep-21 A	05-Oct-21 A
AIP - SO Consent for DDA Submission	0	16-Feb-21	16-Feb-21	05-Oct-21 A	05-Oct-21 A
DDA Roadworks and Street Furniture	124	16-Feb-21	19-Jul-21	06-Oct-21 A	05-Mar-22
DDA - Draft - Preparation by Designer	36	16-Feb-21	29-Mar-21	06-Oct-21 A	17-Nov-21
DDA - Draft - Final Review and prepare for 1st Sub	18	30-Mar-21	23-Apr-21	18-Nov-21	08-Dec-21
DDA - 1st Sub	0	23-Apr-21	23-Apr-21	08-Dec-21	08-Dec-21
DDA - Review by SO	28	24-Apr-21	21-May-21	09-Dec-21	05-Jan-22
DDA - Review by IP / DC	28	24-Apr-21	21-May-21	09-Dec-21	05-Jan-22
DDA - Further information required by SO	24	22-May-21	14-Jun-21	06-Jan-22	29-Jan-22
DDA - 2nd Sub	0	15-Jun-21	15-Jun-21	29-Jan-22	29-Jan-22
DDA - 2nd Review by SO	35	15-Jun-21	19-Jul-21	30-Jan-22	05-Mar-22
DDA Traffic Sign, Road Marking & Sign Gantry	54	19-Oct-21	20-Dec-21	15-May-21 A	23-Nov-21
DDA - Further information required by SO	24	19-Oct-21	15-Nov-21	15-May-21 A	22-Jun-21 A
DDA - 2nd Sub	0	15-Nov-21	15-Nov-21	22-Jun-21 A	22-Jun-21 A
DDA - 2nd Review by SO	35	16-Nov-21	20-Dec-21	23-Jun-21 A	08-Jul-21 A
DDA - Further information required by SO	0	20-Dec-21	20-Dec-21	09-Jul-21 A	23-Oct-21 A
DDA - 3rd Sub	0	23-Oct-21	23-Oct-21	23-Oct-21 A	23-Oct-21 A
DDA - 3rd Review by SO	0	23-Oct-21	23-Oct-21	25-Oct-21 A	23-Nov-21
DDA - SO Consent for Construction	0	20-Dec-21	20-Dec-21	16-Apr-21 A	13-Dec-21
DDA Street Lighting (AGR/ DPR/ S20/ L 10/ L18)	0	22-Jan-21	22-Jan-21	16-Apr-21 A	13-Dec-21
DDA - Further information required by SO	0	16-Apr-21 A	16-Apr-21 A	07-Jun-21 A	07-Jun-21 A
DDA - 4th Sub	0	07-Jun-21 A	07-Jun-21 A	07-Jun-21 A	07-Jun-21 A

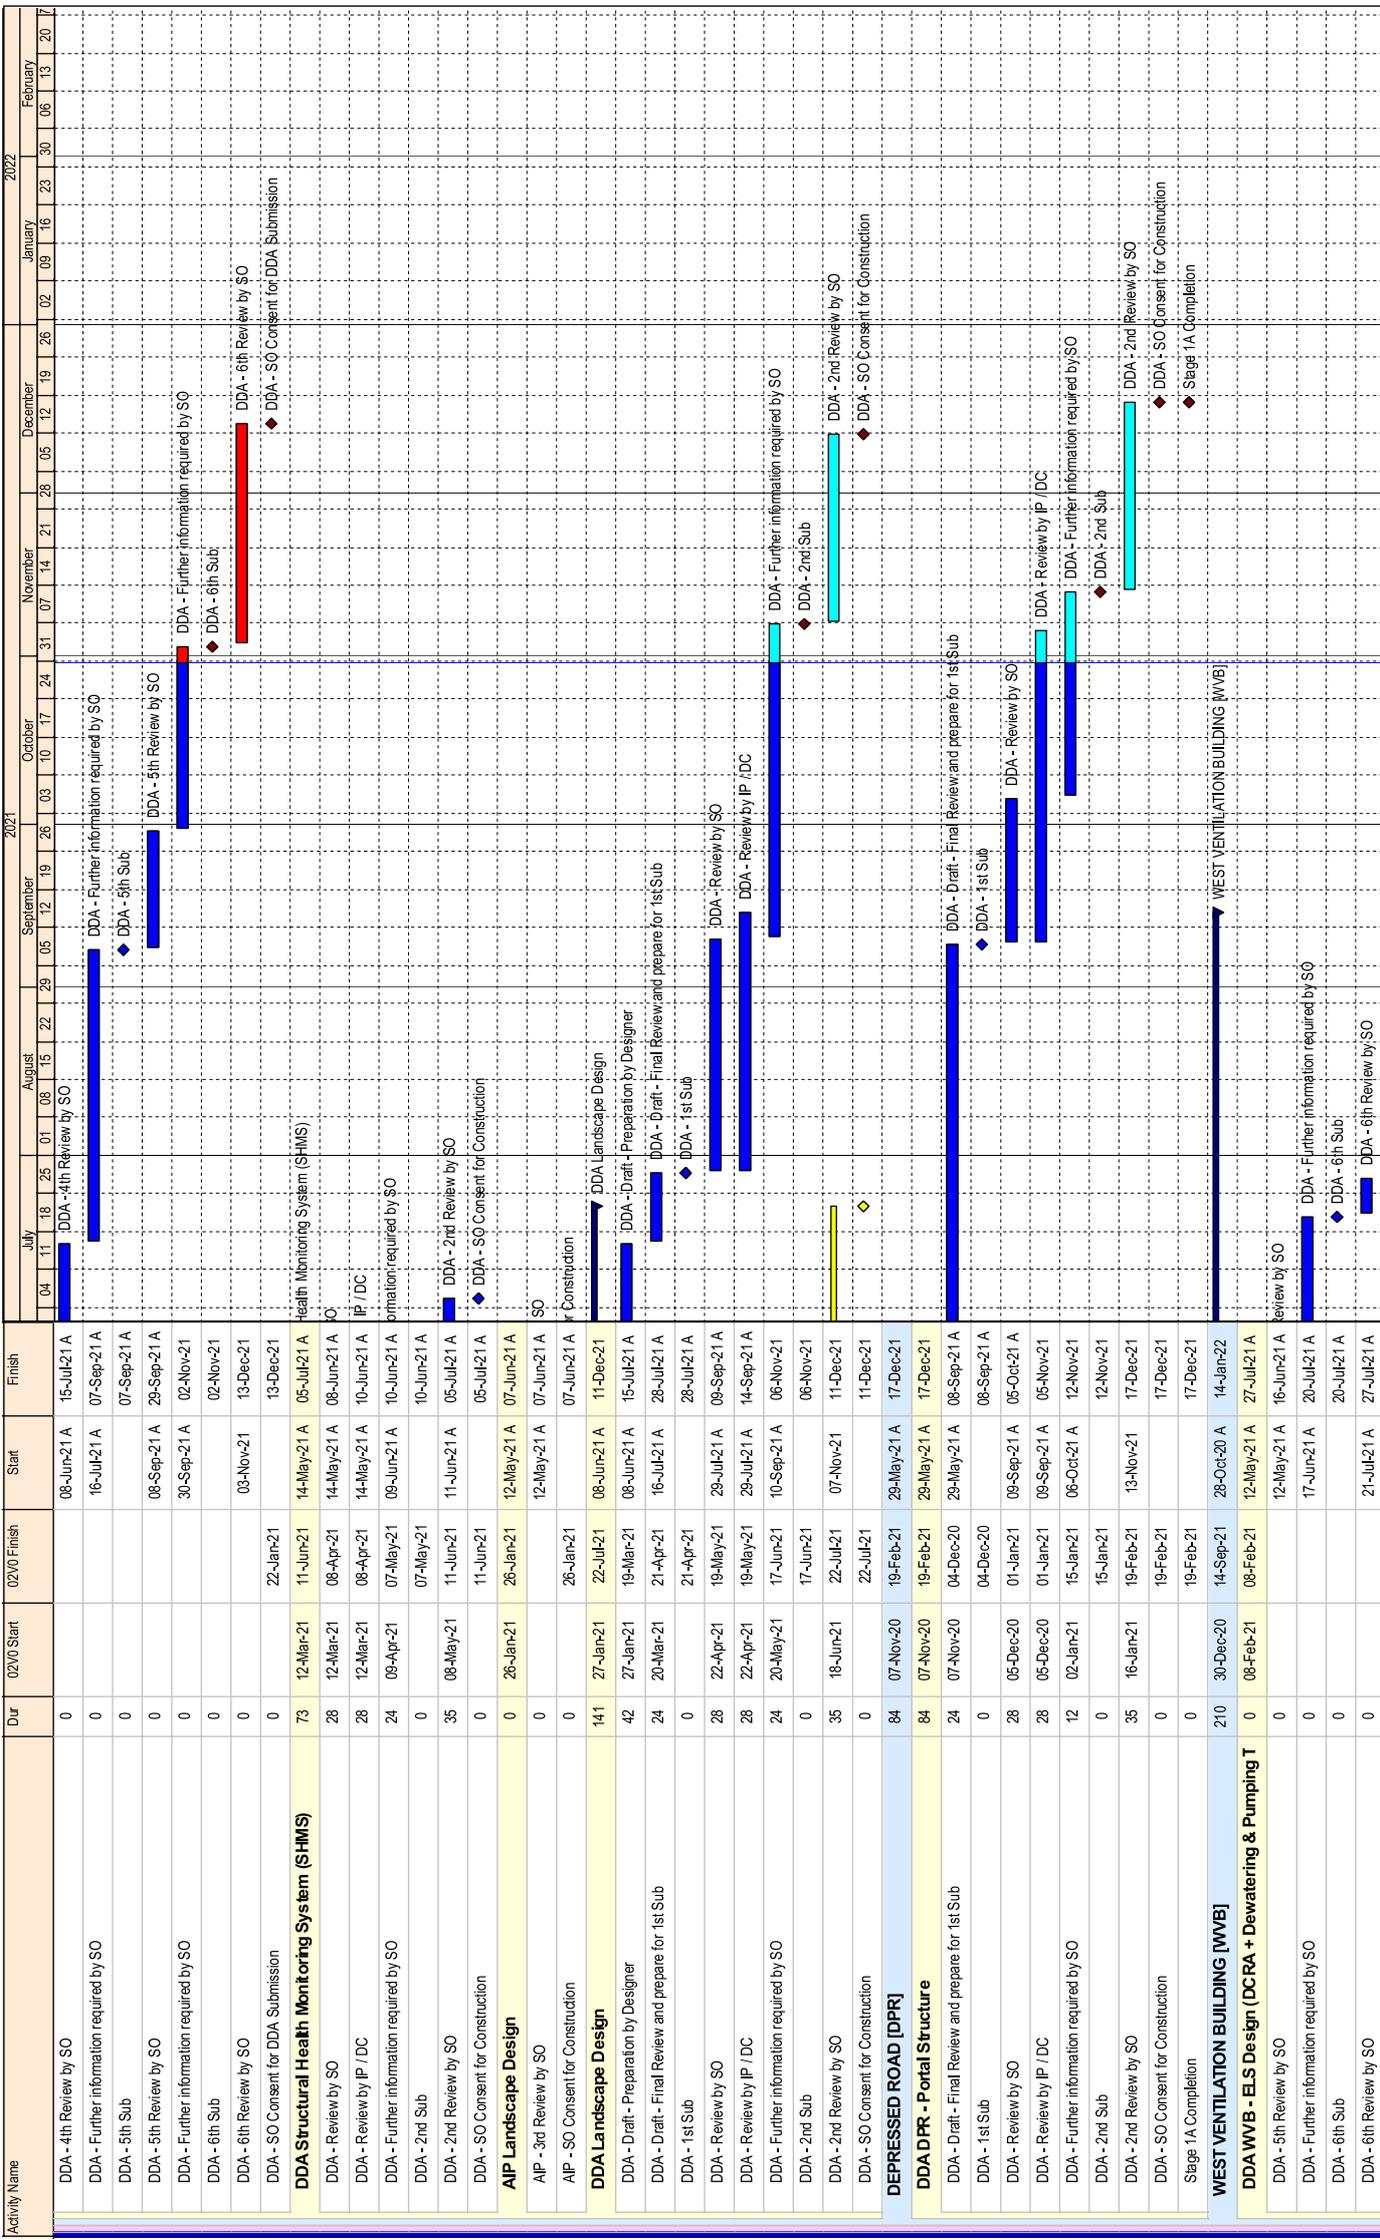


Summary


- Milestone (Diamond)
- Flamed Bar (Red)
- Critical Activity (Blue)
- Actual Milestone (Blue Diamond)
- Actual Work (Blue Bar)
- Baseline Milestone (Yellow Diamond)
- Baseline Bar (Yellow)

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLO	WYu
09-Apr-20	01V1	SPaLLO	WYu
17-Jul-20	01V2	SPaLLO	WYu
09-Oct-20	01V3	SPaLLO	WYu
02-Jul-21	02V0	SPaLLO	WYu

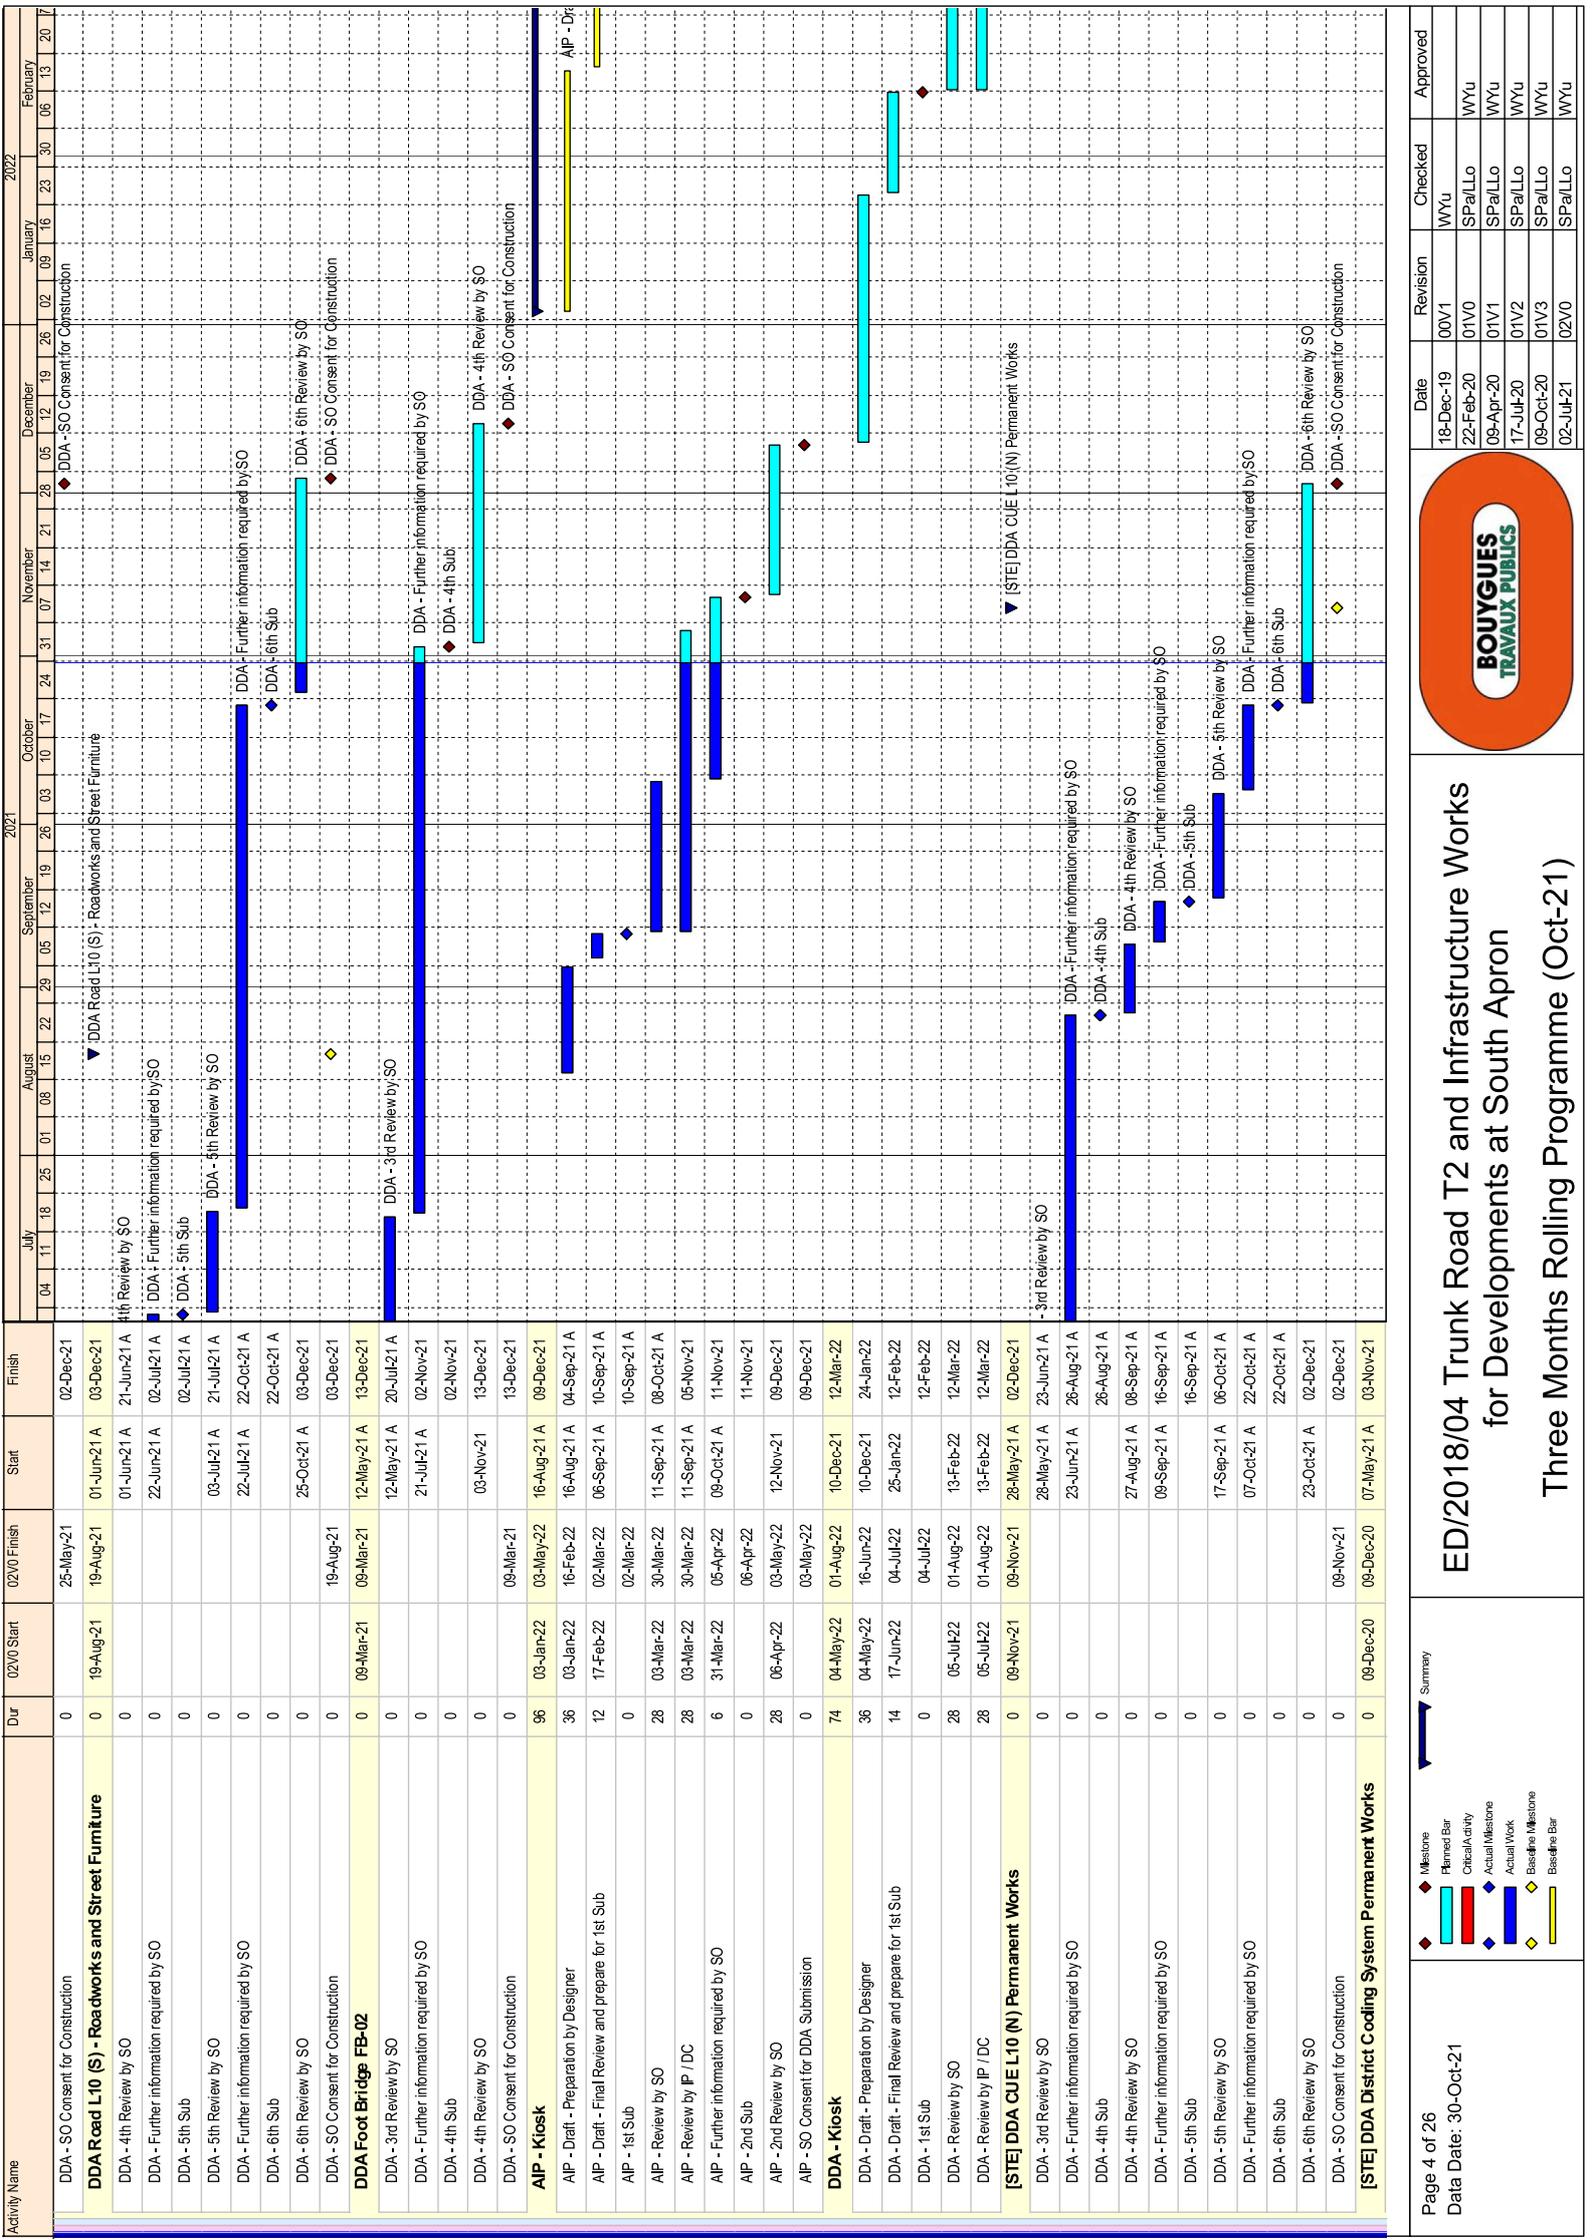

Summary


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu

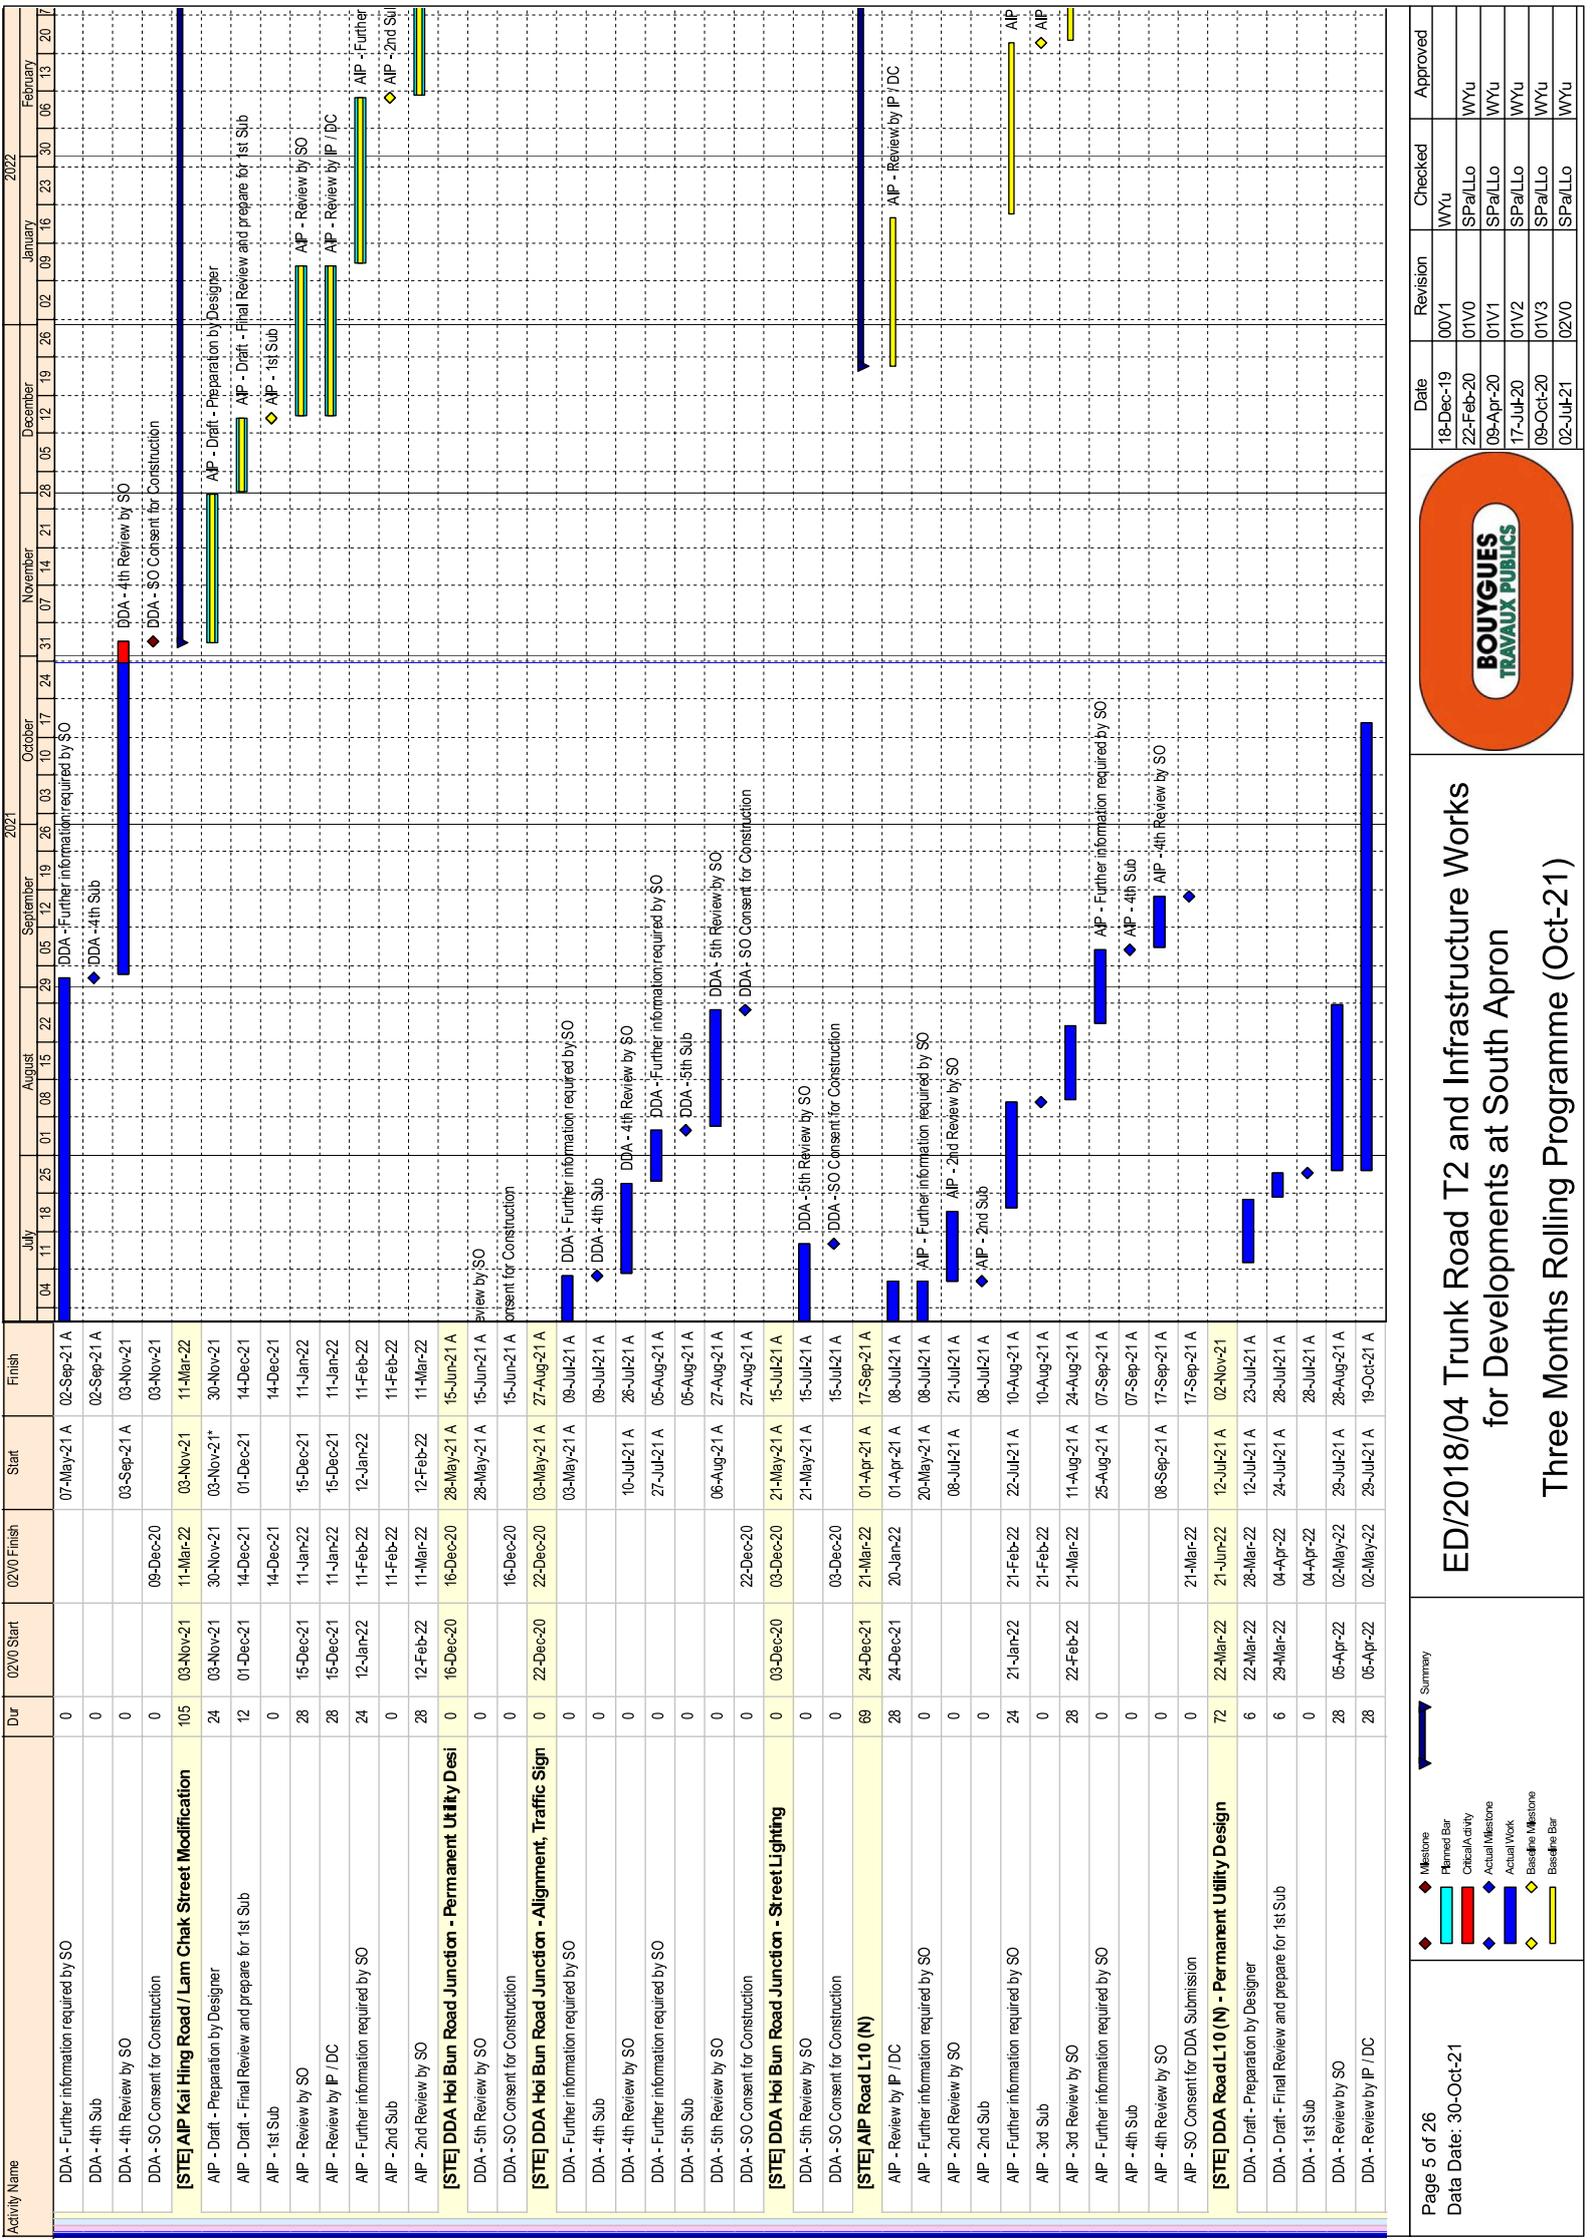


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Oct-21)

Page 5 of 26
Data Date: 30-Oct-21

Summary

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar


Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	WYu
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

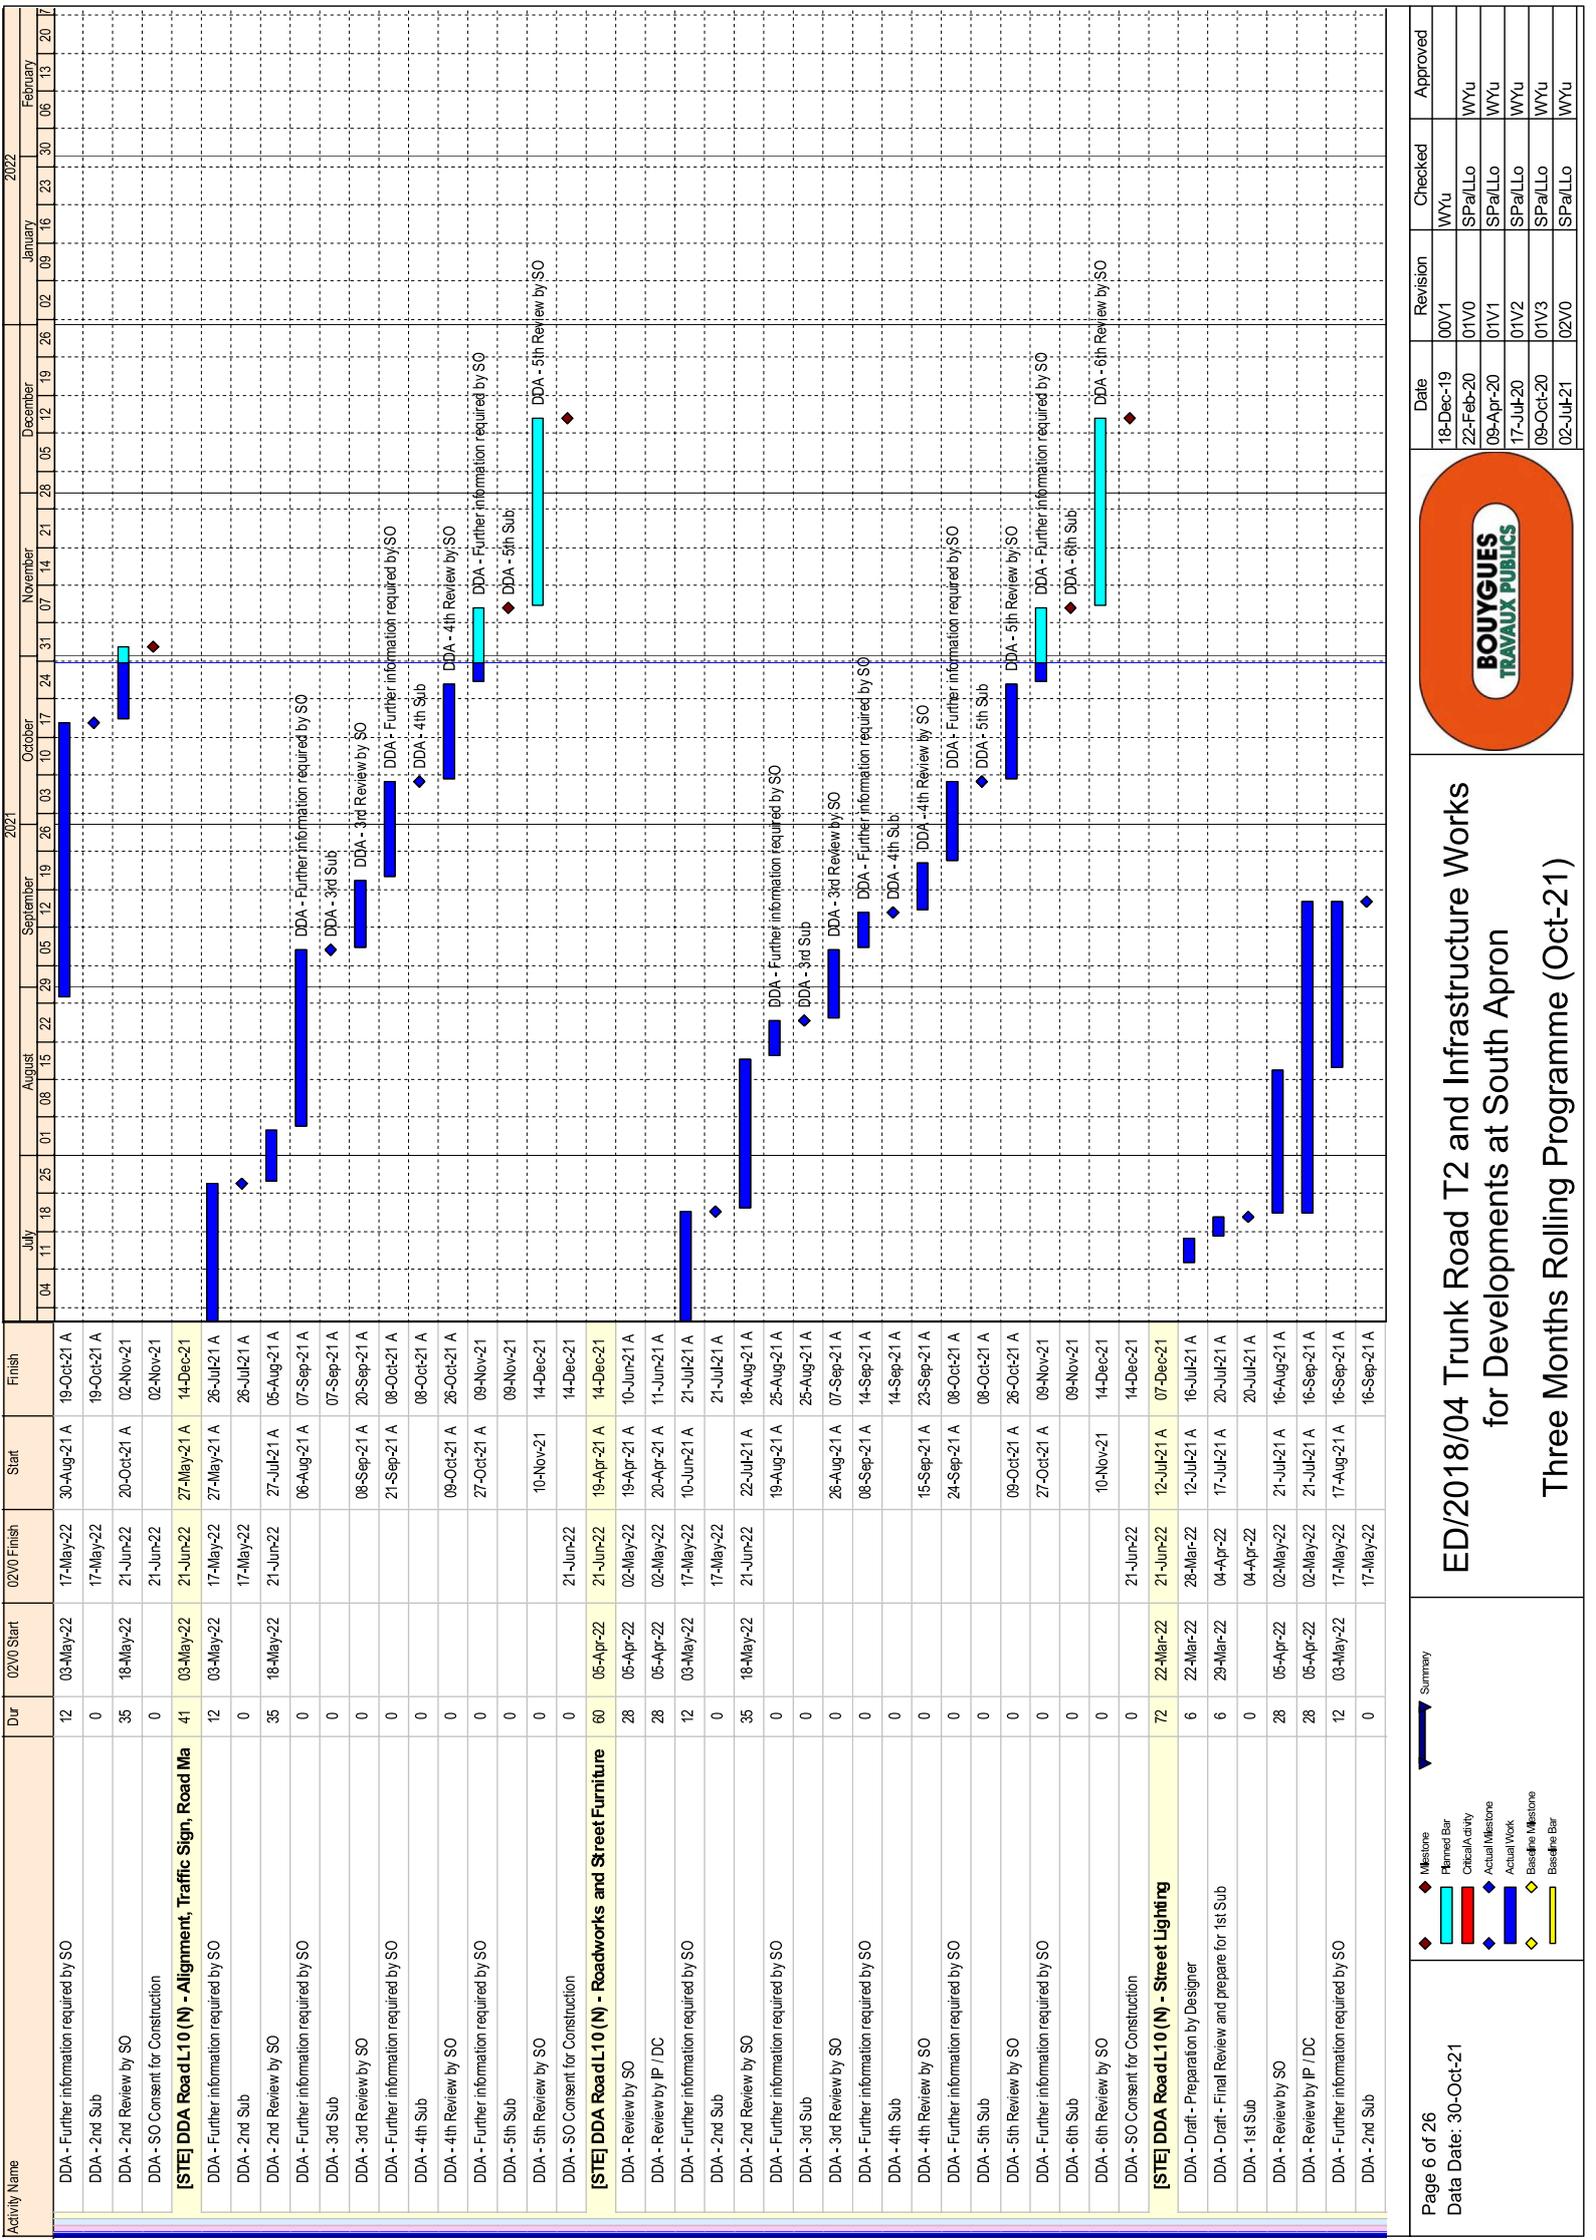


Summary

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

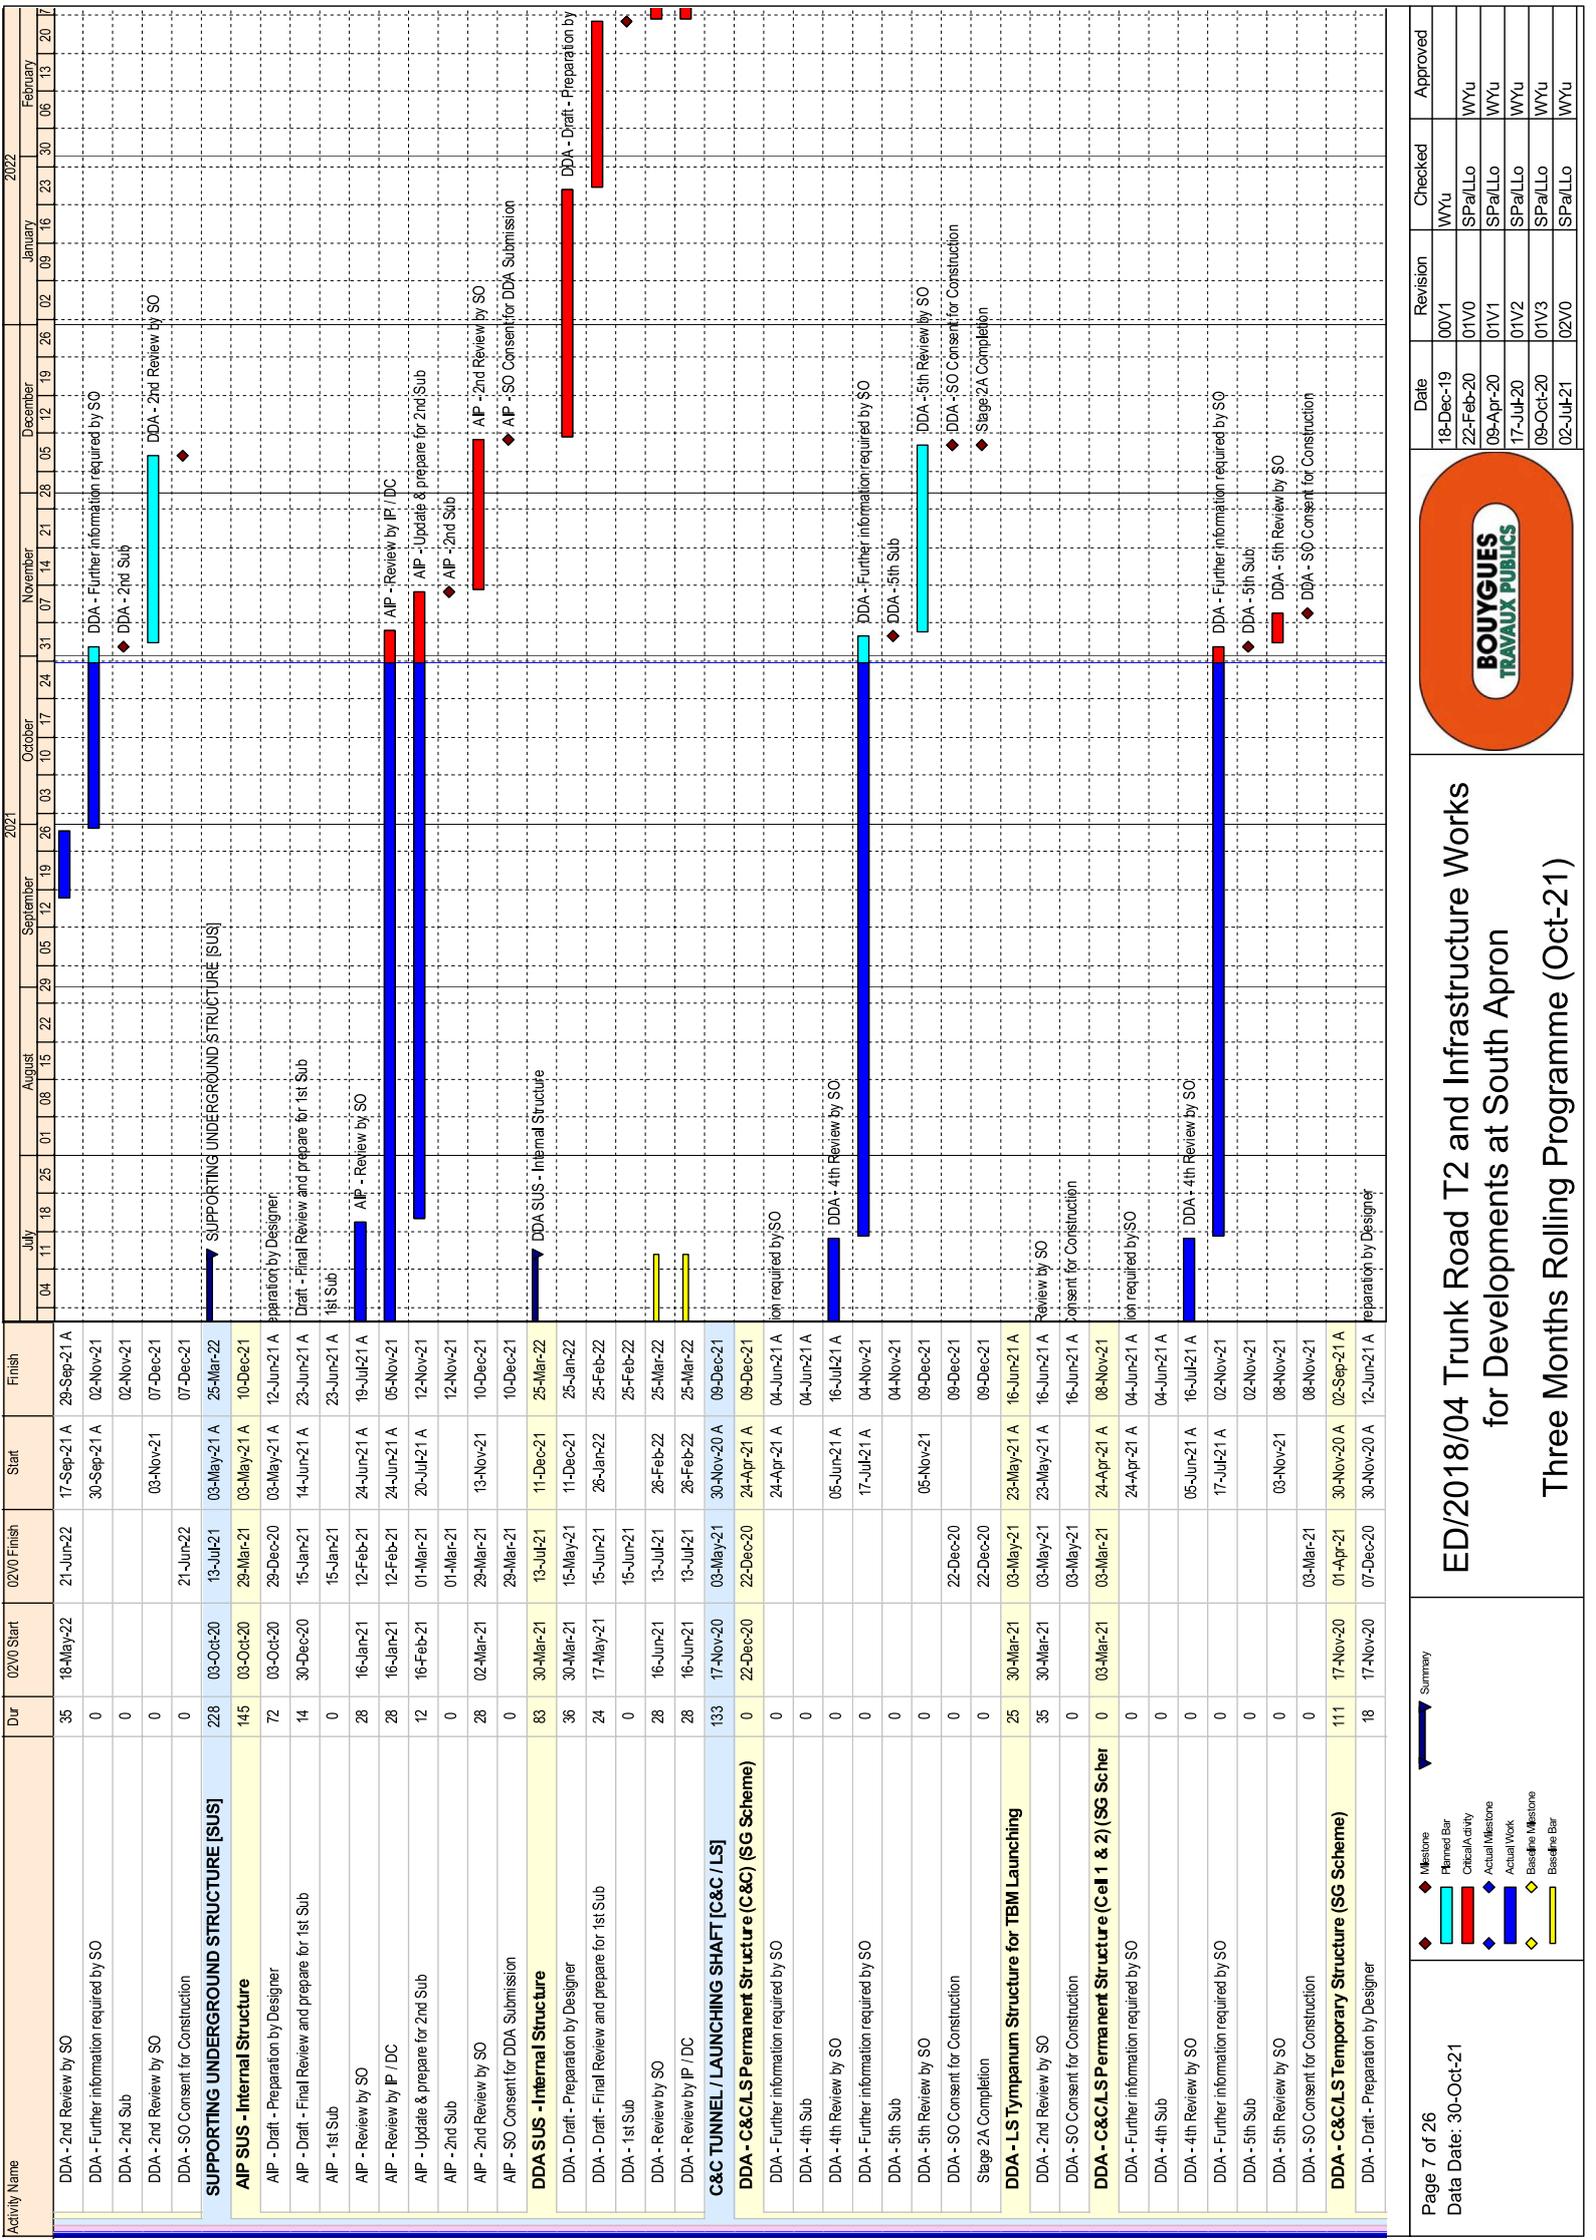


Summary


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

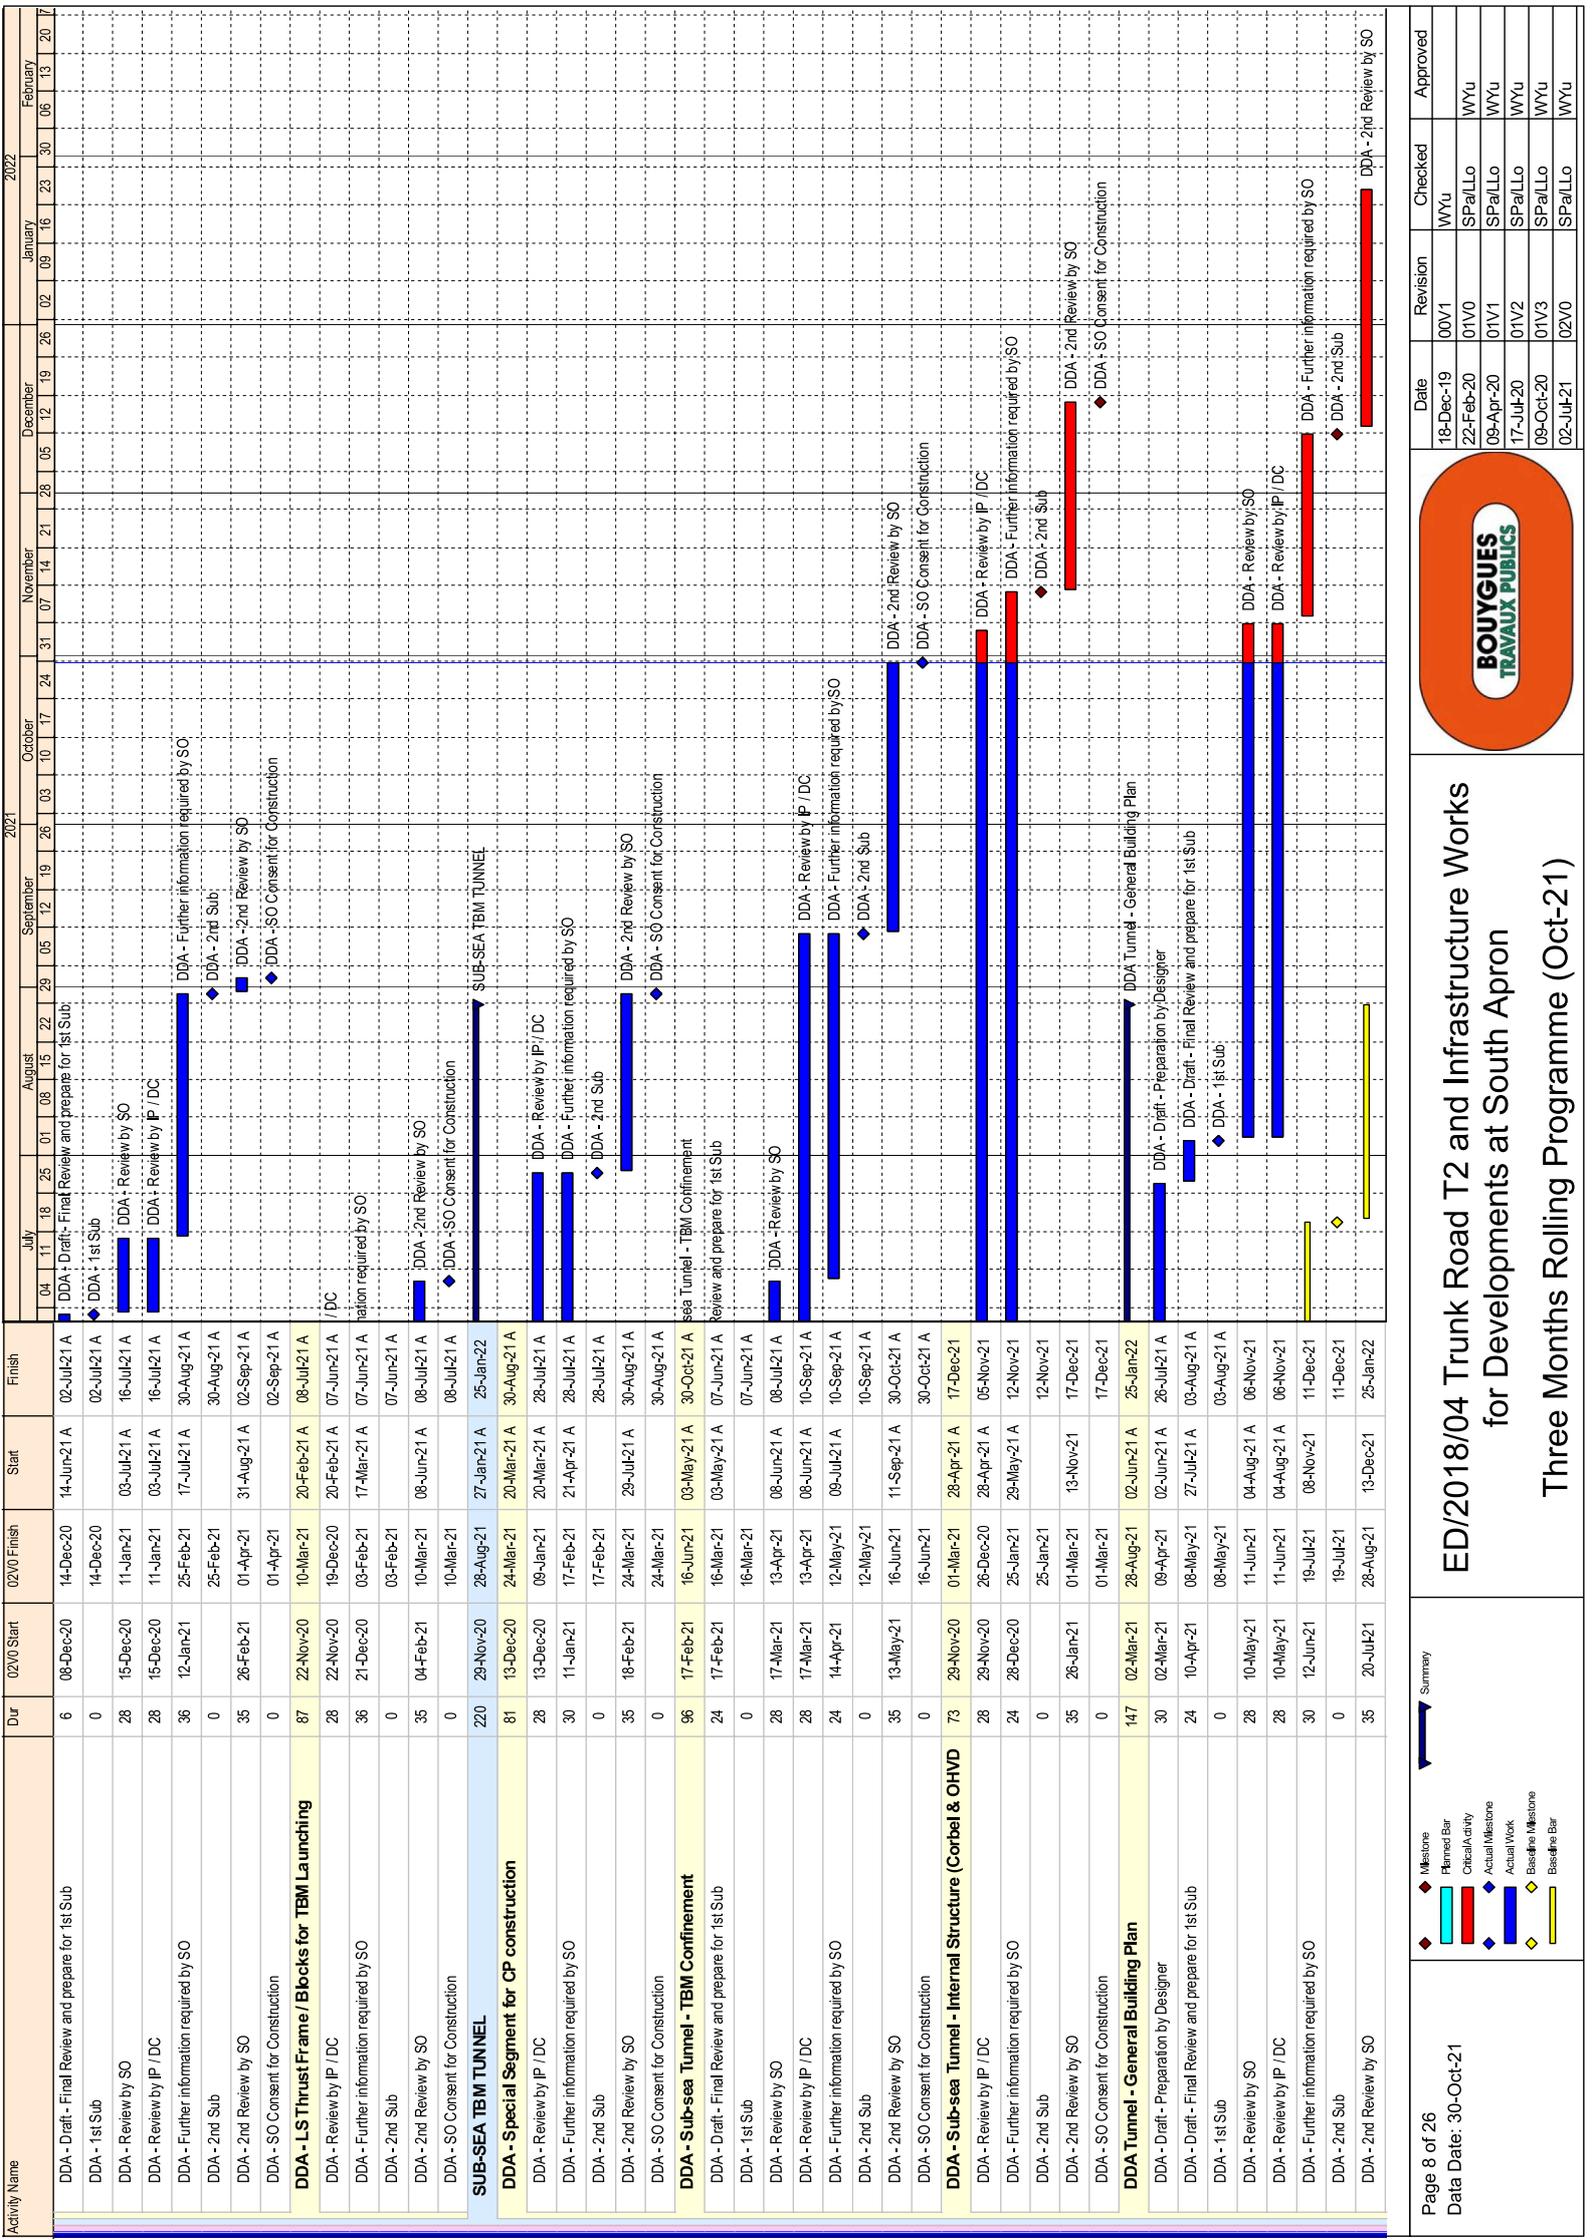


Summary


- Milestone
- Flamed Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu

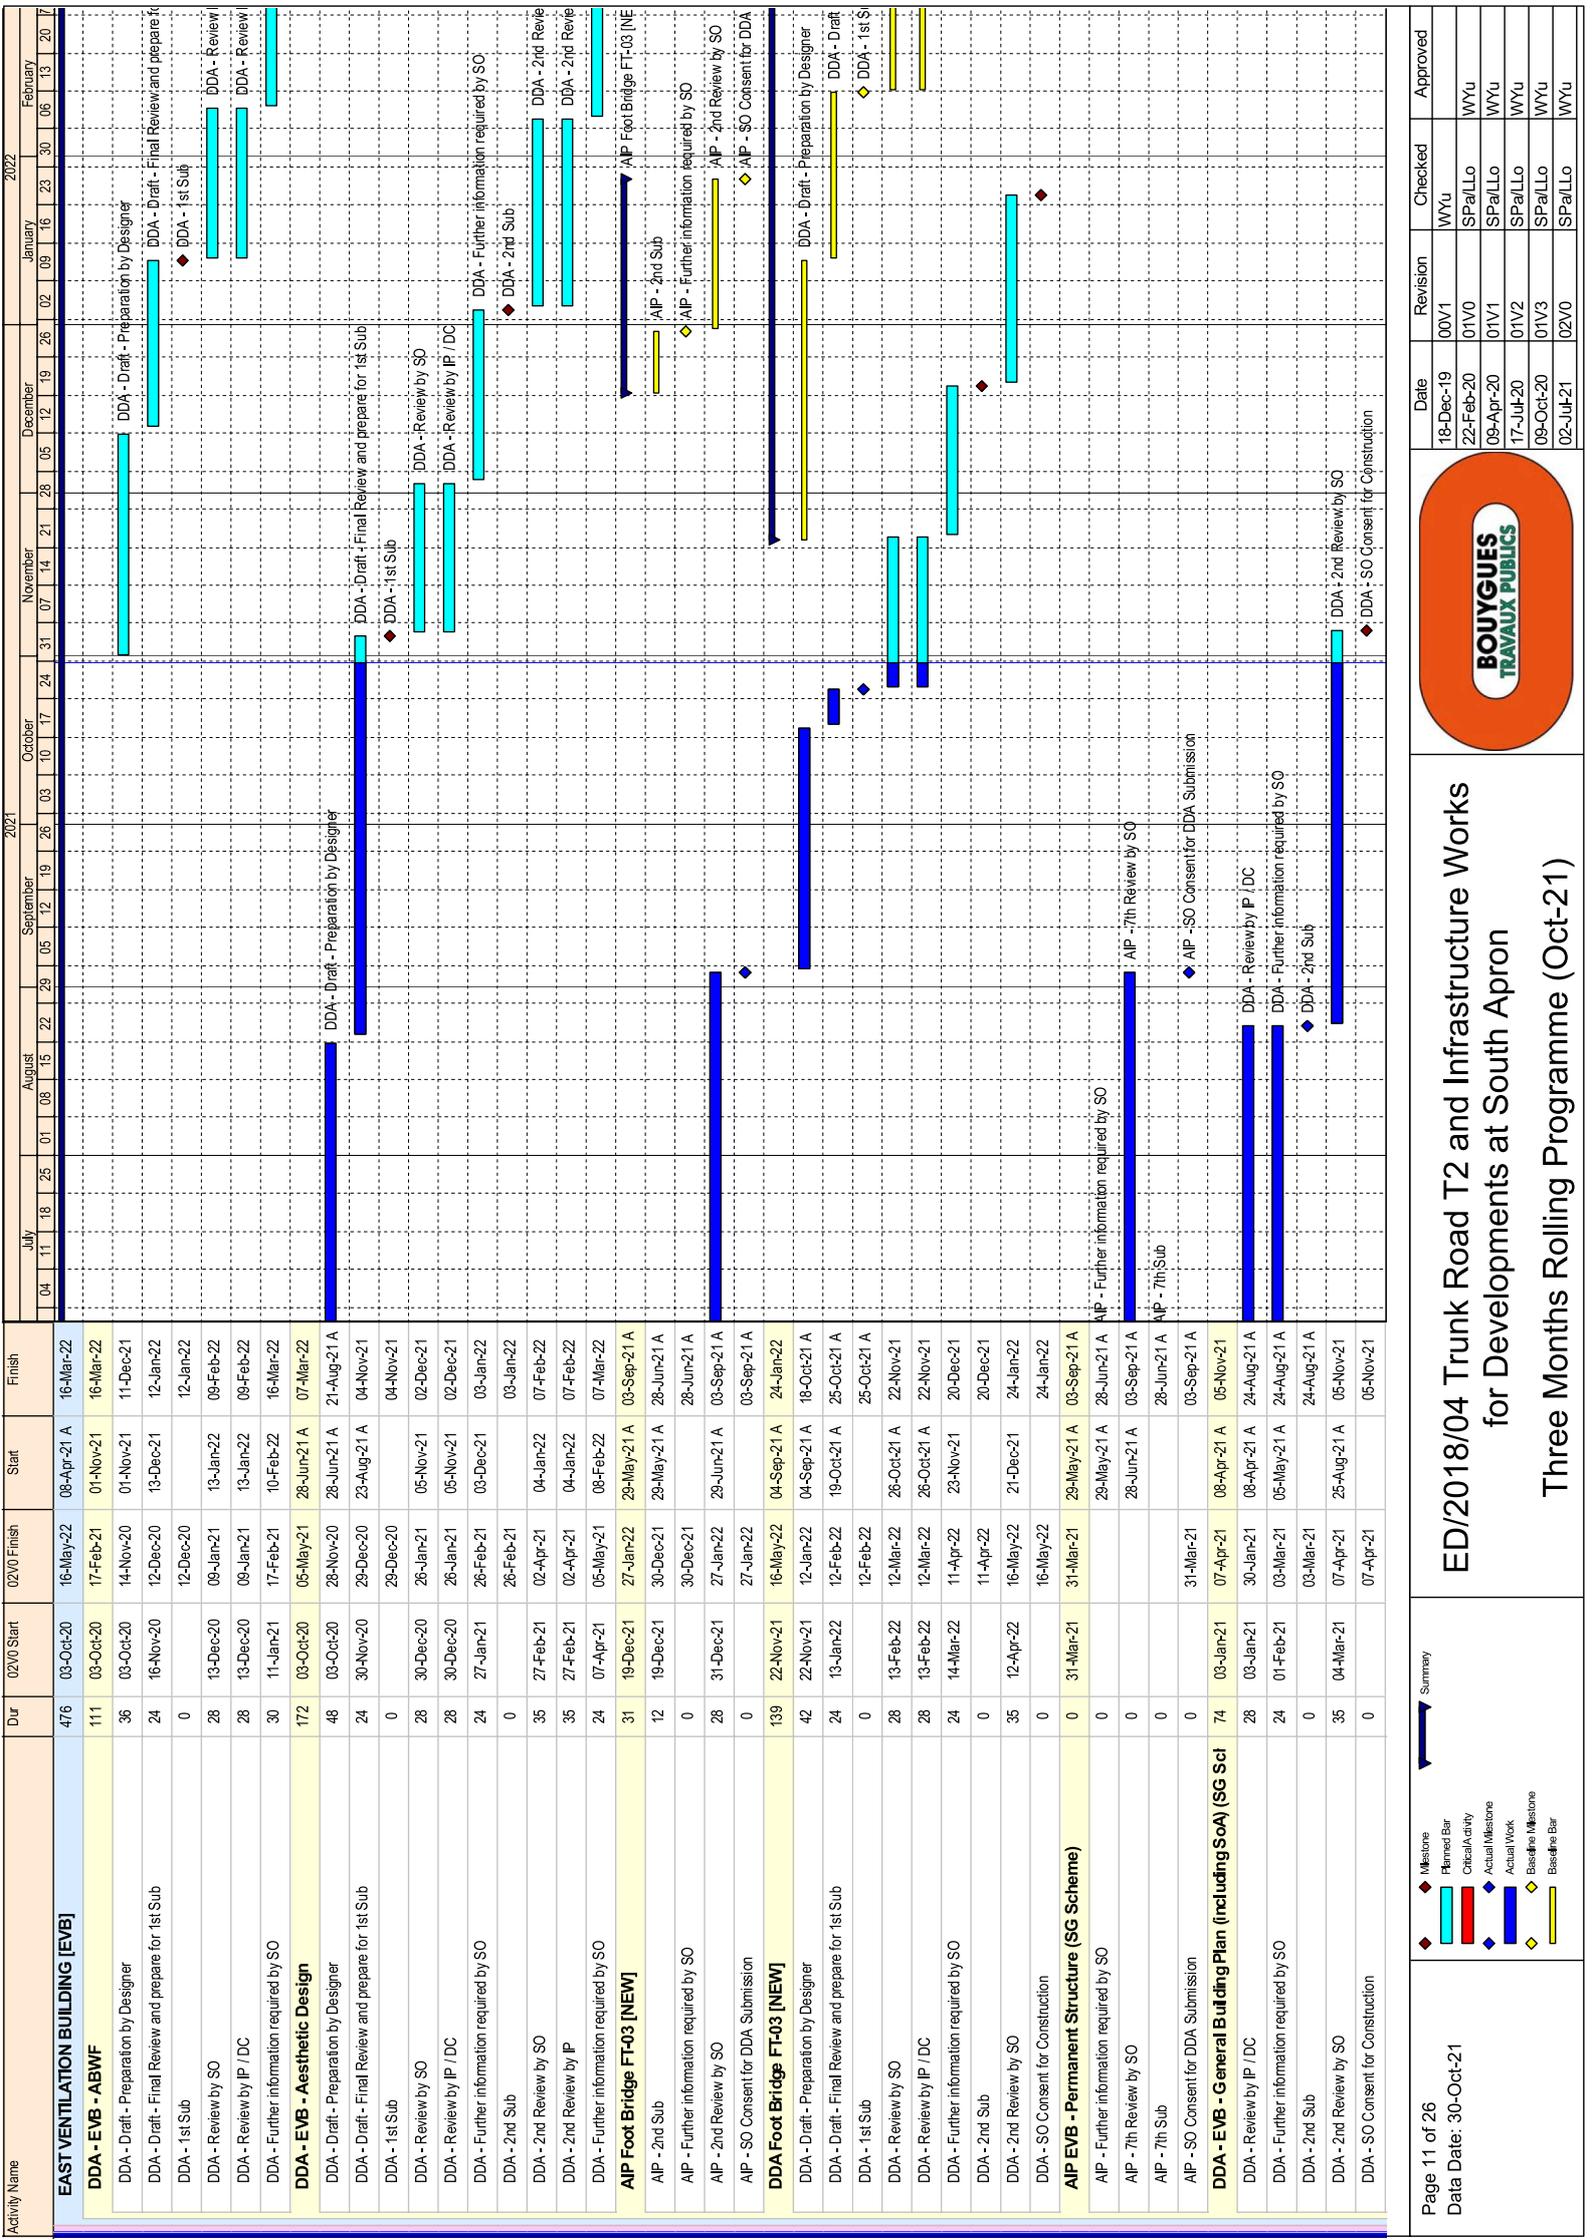

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish
EAST VENTILATION BUILDING [EVB]	476	03-Oct-20	16-Mar-22	08-Apr-21 A	16-Mar-22
DDA - EVB - ABWF	111	03-Oct-20	17-Feb-21	01-Nov-21	16-Mar-22
DDA - Draft - Preparation by Designer	36	03-Oct-20	14-Nov-20	01-Nov-21	11-Dec-21
DDA - Draft - Final Review and prepare for 1st Sub	24	16-Nov-20	12-Dec-20	13-Dec-21	12-Jan-22
DDA - 1st Sub	0		12-Dec-20	12-Jan-22	12-Jan-22
DDA - Review by SO	28	13-Dec-20	09-Jan-21	13-Jan-22	09-Feb-22
DDA - Review by IP / DC	28	13-Dec-20	09-Jan-21	13-Jan-22	09-Feb-22
DDA - Further information required by SO	30	11-Jan-21	17-Feb-21	10-Feb-22	16-Mar-22
DDA - EVB - Aesthetic Design	172	03-Oct-20	05-May-21	28-Jun-21 A	07-Mar-22
DDA - Draft - Preparation by Designer	48	03-Oct-20	28-Nov-20	28-Jun-21 A	21-Aug-21 A
DDA - Draft - Final Review and prepare for 1st Sub	24	30-Nov-20	29-Dec-20	23-Aug-21 A	04-Nov-21
DDA - 1st Sub	0		29-Dec-20	04-Nov-21	04-Nov-21
DDA - Review by SO	28	30-Dec-20	26-Jan-21	05-Nov-21	02-Dec-21
DDA - Review by IP / DC	28	30-Dec-20	26-Jan-21	05-Nov-21	02-Dec-21
DDA - Further information required by SO	24	27-Jan-21	26-Feb-21	03-Dec-21	03-Jan-22
DDA - 2nd Sub	0		26-Feb-21	03-Jan-22	03-Jan-22
DDA - 2nd Review by SO	35	27-Feb-21	02-Apr-21	04-Jan-22	07-Feb-22
DDA - 2nd Review by IP	35	27-Feb-21	02-Apr-21	04-Jan-22	07-Feb-22
DDA - Further information required by SO	24	07-Apr-21	05-May-21	08-Feb-22	07-Mar-22
AIP Foot Bridge FT-03 [NEW]	31	19-Dec-21	27-Jan-22	29-May-21 A	03-Sep-21 A
AIP - 2nd Sub	12	19-Dec-21	30-Dec-21	29-May-21 A	28-Jun-21 A
AIP - Further information required by SO	0		30-Dec-21	29-Jun-21 A	28-Jun-21 A
AIP - 2nd Review by SO	28	31-Dec-21	27-Jan-22	29-Jun-21 A	03-Sep-21 A
AIP - SO Consent for DDA Submission	0		27-Jan-22	03-Sep-21 A	03-Sep-21 A
DDA Foot Bridge FT-03 [NEW]	139	22-Nov-21	16-May-22	04-Sep-21 A	24-Jan-22
DDA - Draft - Preparation by Designer	42	22-Nov-21	12-Jan-22	04-Sep-21 A	18-Oct-21 A
DDA - Draft - Final Review and prepare for 1st Sub	24	13-Jan-22	12-Feb-22	19-Oct-21 A	25-Oct-21 A
DDA - 1st Sub	0		12-Feb-22	25-Oct-21 A	25-Oct-21 A
DDA - Review by SO	28	13-Feb-22	12-Mar-22	26-Oct-21 A	22-Nov-21
DDA - Review by IP / DC	28	13-Feb-22	12-Mar-22	26-Oct-21 A	22-Nov-21
DDA - Further information required by SO	24	14-Mar-22	11-Apr-22	23-Nov-21	20-Dec-21
DDA - 2nd Sub	0		11-Apr-22	20-Dec-21	20-Dec-21
DDA - 2nd Review by SO	35	12-Apr-22	16-May-22	21-Dec-21	24-Jan-22
DDA - SO Consent for Construction	0		16-May-22	24-Jan-22	24-Jan-22
AIP EVB - Permanent Structure (SG Scheme)	0	31-Mar-21	31-Mar-21	29-May-21 A	03-Sep-21 A
AIP - Further information required by SO	0		29-May-21 A	28-Jun-21 A	28-Jun-21 A
AIP - 7th Review by SO	0		28-Jun-21 A	03-Sep-21 A	03-Sep-21 A
AIP - 7th Sub	0		28-Jun-21 A	03-Sep-21 A	03-Sep-21 A
AIP - SO Consent for DDA Submission	0		31-Mar-21	03-Sep-21 A	03-Sep-21 A
DDA - EVB - General Building Plan (including SoA) (SG Sci)	74	03-Jan-21	07-Apr-21	08-Apr-21 A	09-Nov-21
DDA - Review by IP / DC	28	03-Jan-21	30-Jan-21	08-Apr-21 A	24-Aug-21 A
DDA - Further information required by SO	24	01-Feb-21	03-Mar-21	05-May-21 A	24-Aug-21 A
DDA - 2nd Sub	0		03-Mar-21	24-Aug-21 A	24-Aug-21 A
DDA - 2nd Review by SO	35	04-Mar-21	07-Apr-21	25-Aug-21 A	05-Nov-21
DDA - SO Consent for Construction	0		07-Apr-21	05-Nov-21	05-Nov-21

Page 11 of 26
 Data Date: 30-Oct-21

Summary


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

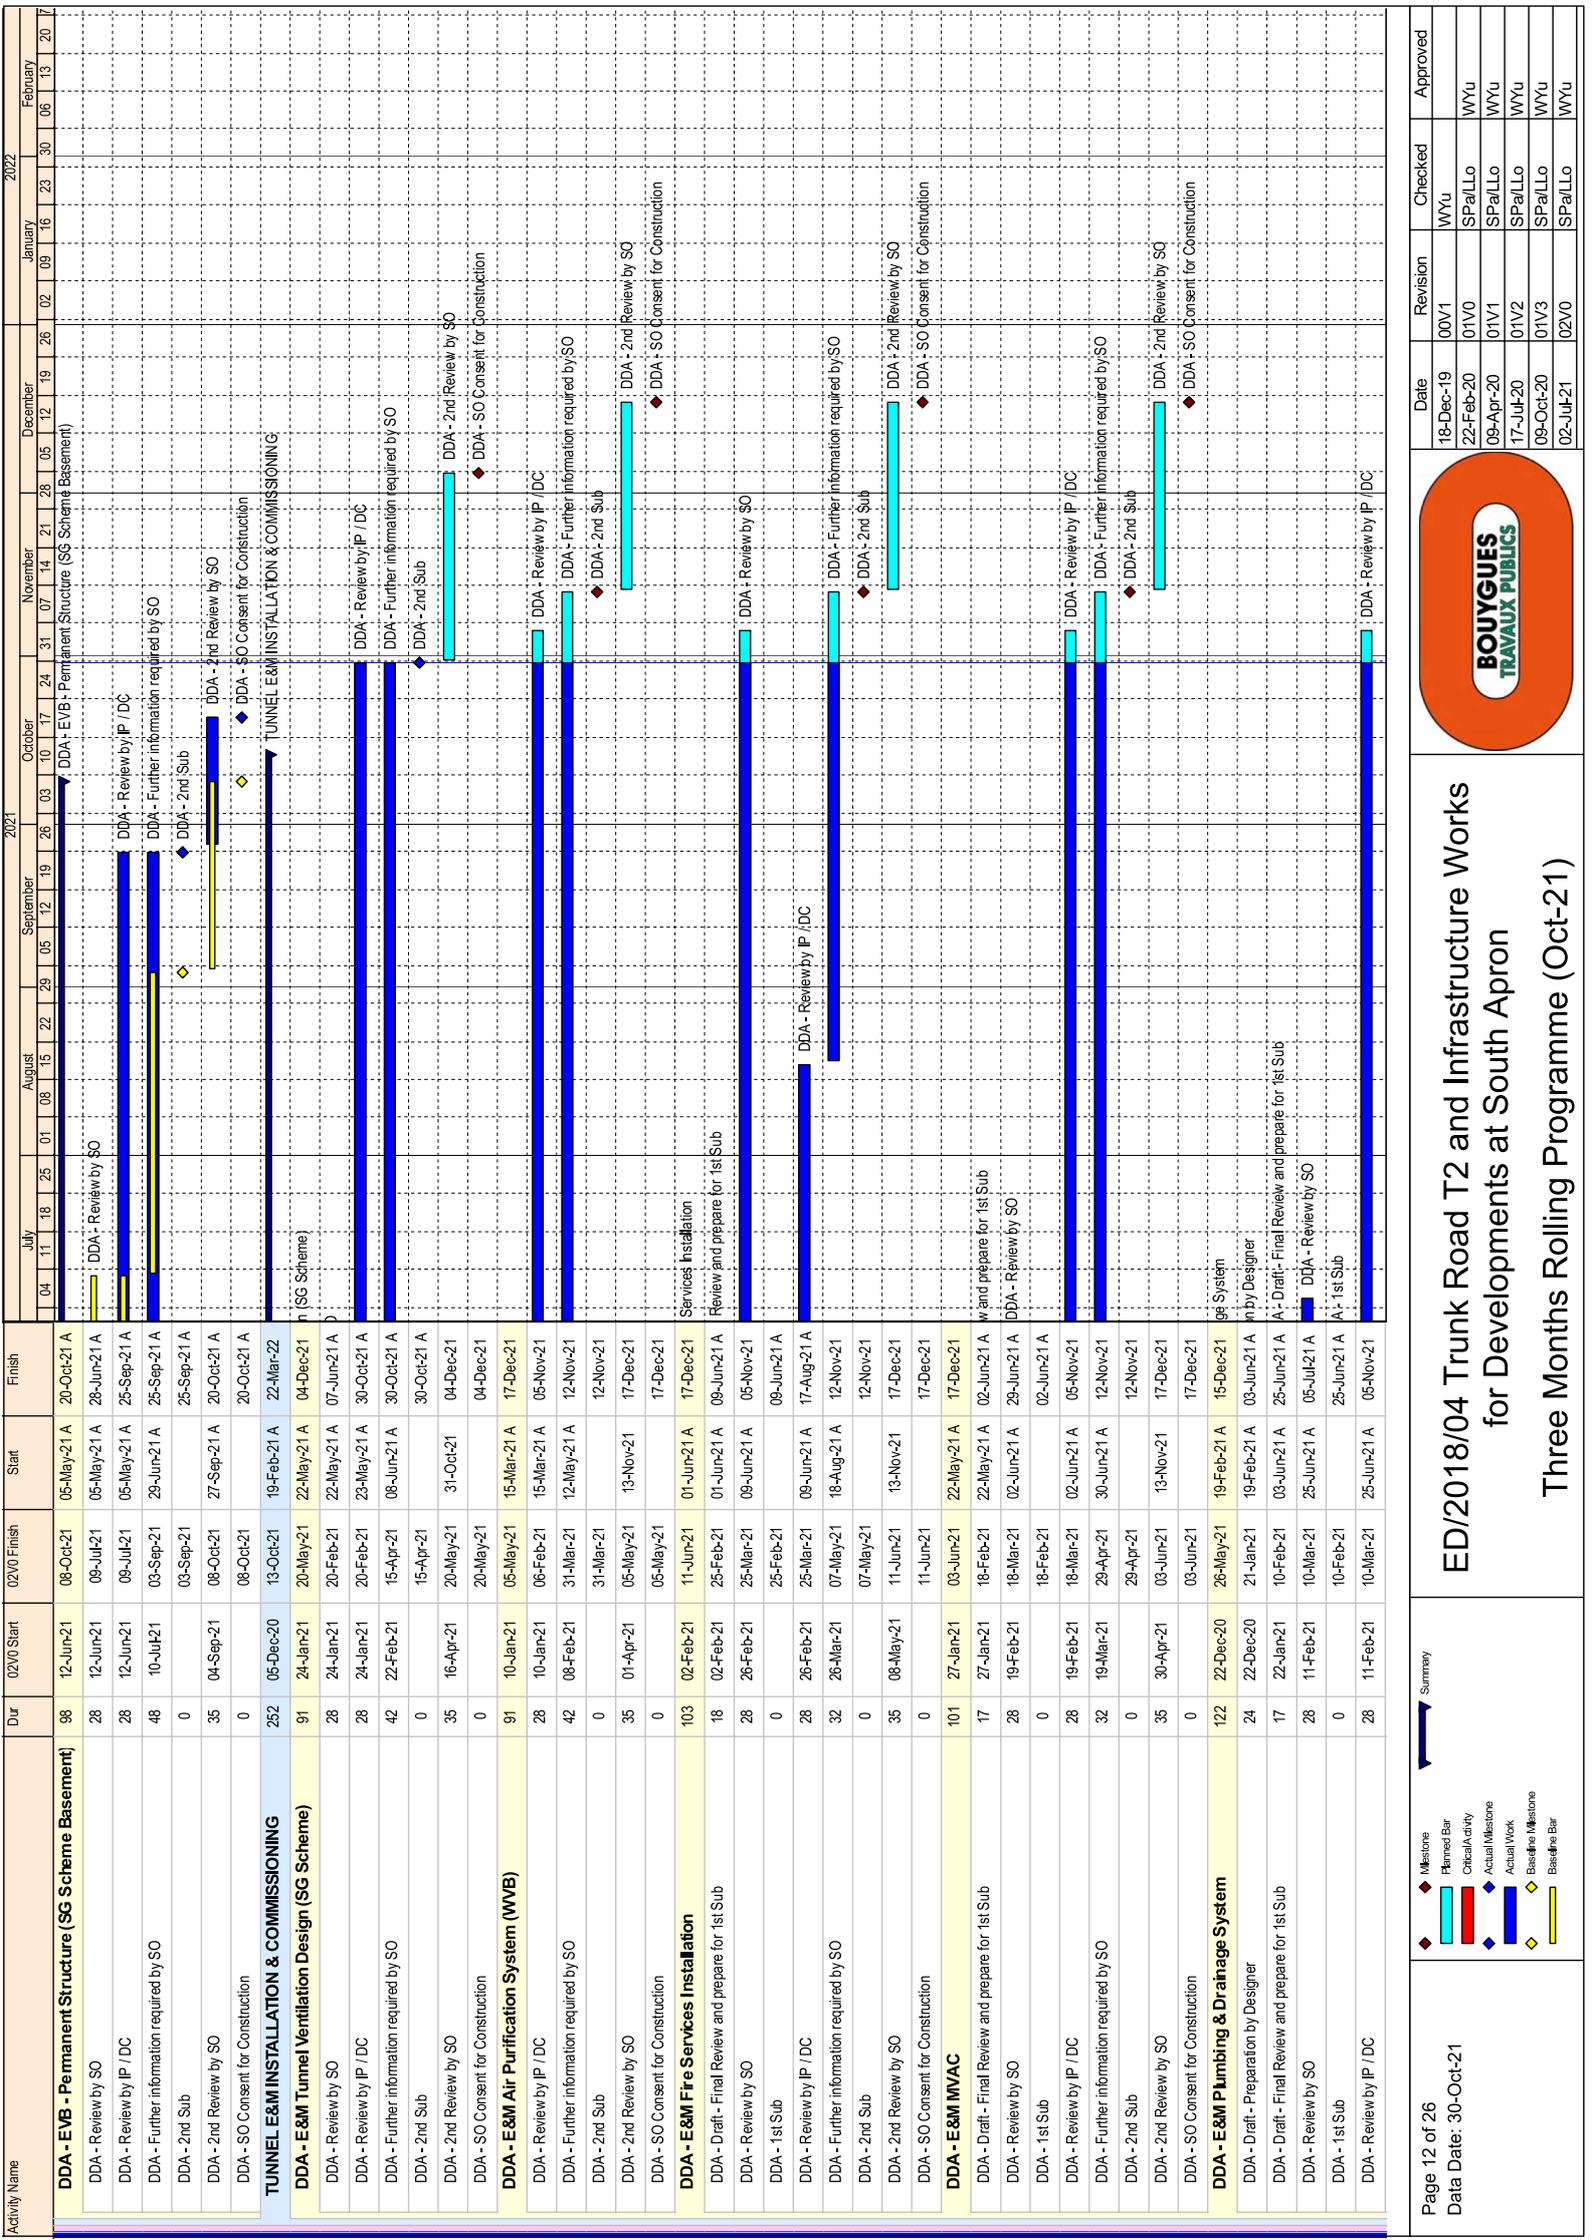

Activity Name	Dur	02/20 Start	02/20 Finish	Start	Finish
DDA - EVB - Permanent Structure (SG Scheme Basement)	98	12-Jun-21	08-Oct-21	05-May-21 A	20-Oct-21 A
DDA - Review by SO	28	12-Jun-21	09-Jul-21	05-May-21 A	28-Jun-21 A
DDA - Review by IP / DC	28	12-Jun-21	09-Jul-21	05-May-21 A	25-Sep-21 A
DDA - Further information required by SO	48	10-Jul-21	03-Sep-21	29-Jun-21 A	25-Sep-21 A
DDA - 2nd Sub	0	03-Sep-21	03-Sep-21	25-Sep-21 A	25-Sep-21 A
DDA - 2nd Review by SO	35	04-Sep-21	08-Oct-21	27-Sep-21 A	20-Oct-21 A
DDA - SO Consent for Construction	0	08-Oct-21	08-Oct-21	20-Oct-21 A	20-Oct-21 A
TUNNEL E&M INSTALLATION & COMMISSIONING	252	05-Dec-20	13-Oct-21	19-Feb-21 A	22-Mar-22
DDA - E&M Tunnel Ventilation Design (SG Scheme)	91	24-Jan-21	20-May-21	22-May-21 A	04-Dec-21
DDA - Review by SO	28	24-Jan-21	20-Feb-21	22-May-21 A	07-Jun-21 A
DDA - Review by IP / DC	28	24-Jan-21	20-Feb-21	23-May-21 A	30-Oct-21 A
DDA - Further information required by SO	42	22-Feb-21	15-Apr-21	08-Jun-21 A	30-Oct-21 A
DDA - 2nd Sub	0	15-Apr-21	15-Apr-21	30-Oct-21 A	30-Oct-21 A
DDA - 2nd Review by SO	35	16-Apr-21	20-May-21	31-Oct-21	04-Dec-21
DDA - SO Consent for Construction	0	20-May-21	20-May-21	04-Dec-21	04-Dec-21
DDA - E&M Air Purification System (WVB)	91	10-Jan-21	05-May-21	15-Mar-21 A	17-Dec-21
DDA - Review by IP / DC	28	10-Jan-21	06-Feb-21	15-Mar-21 A	05-Nov-21
DDA - Further information required by SO	42	08-Feb-21	31-Mar-21	12-May-21 A	12-Nov-21
DDA - 2nd Sub	0	31-Mar-21	31-Mar-21	12-Nov-21	12-Nov-21
DDA - 2nd Review by SO	35	01-Apr-21	05-May-21	13-Nov-21	17-Dec-21
DDA - SO Consent for Construction	0	05-May-21	05-May-21	17-Dec-21	17-Dec-21
DDA - E&M Fire Services Installation	103	02-Feb-21	11-Jun-21	01-Jun-21 A	17-Dec-21
DDA - Draft - Final Review and prepare for 1st Sub	18	02-Feb-21	25-Feb-21	01-Jun-21 A	09-Jun-21 A
DDA - Review by SO	28	26-Feb-21	25-Mar-21	09-Jun-21 A	05-Nov-21
DDA - 1st Sub	0	25-Feb-21	25-Feb-21	09-Jun-21 A	09-Jun-21 A
DDA - Review by IP / DC	28	26-Feb-21	25-Mar-21	09-Jun-21 A	17-Aug-21 A
DDA - Further information required by SO	32	26-Mar-21	07-May-21	18-Aug-21 A	12-Nov-21
DDA - 2nd Sub	0	07-May-21	07-May-21	12-Nov-21	12-Nov-21
DDA - 2nd Review by SO	35	08-May-21	11-Jun-21	13-Nov-21	17-Dec-21
DDA - SO Consent for Construction	0	11-Jun-21	11-Jun-21	17-Dec-21	17-Dec-21
DDA - E&M MVAC	101	27-Jan-21	03-Jun-21	22-May-21 A	17-Dec-21
DDA - Draft - Final Review and prepare for 1st Sub	17	27-Jan-21	18-Feb-21	22-May-21 A	02-Jun-21 A
DDA - Review by SO	28	19-Feb-21	18-Mar-21	02-Jun-21 A	29-Jun-21 A
DDA - 1st Sub	0	18-Feb-21	18-Feb-21	02-Jun-21 A	02-Jun-21 A
DDA - Review by IP / DC	28	19-Feb-21	18-Mar-21	02-Jun-21 A	05-Nov-21
DDA - Further information required by SO	32	19-Mar-21	29-Apr-21	30-Jun-21 A	12-Nov-21
DDA - 2nd Sub	0	29-Apr-21	29-Apr-21	12-Nov-21	12-Nov-21
DDA - 2nd Review by SO	35	30-Apr-21	03-Jun-21	13-Nov-21	17-Dec-21
DDA - SO Consent for Construction	0	03-Jun-21	03-Jun-21	17-Dec-21	17-Dec-21
DDA - E&M Plumbing & Drainage System	122	22-Dec-20	26-May-21	19-Feb-21 A	15-Dec-21
DDA - Draft - Preparation by Designer	24	22-Dec-20	21-Jan-21	19-Feb-21 A	03-Jun-21 A
DDA - Draft - Final Review and prepare for 1st Sub	17	22-Jan-21	10-Feb-21	03-Jun-21 A	25-Jun-21 A
DDA - Review by SO	28	11-Feb-21	10-Mar-21	25-Jun-21 A	05-Jul-21 A
DDA - 1st Sub	0	10-Feb-21	10-Feb-21	25-Jun-21 A	25-Jun-21 A
DDA - Review by IP / DC	28	11-Feb-21	10-Mar-21	25-Jun-21 A	05-Nov-21



Summary

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Oct-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

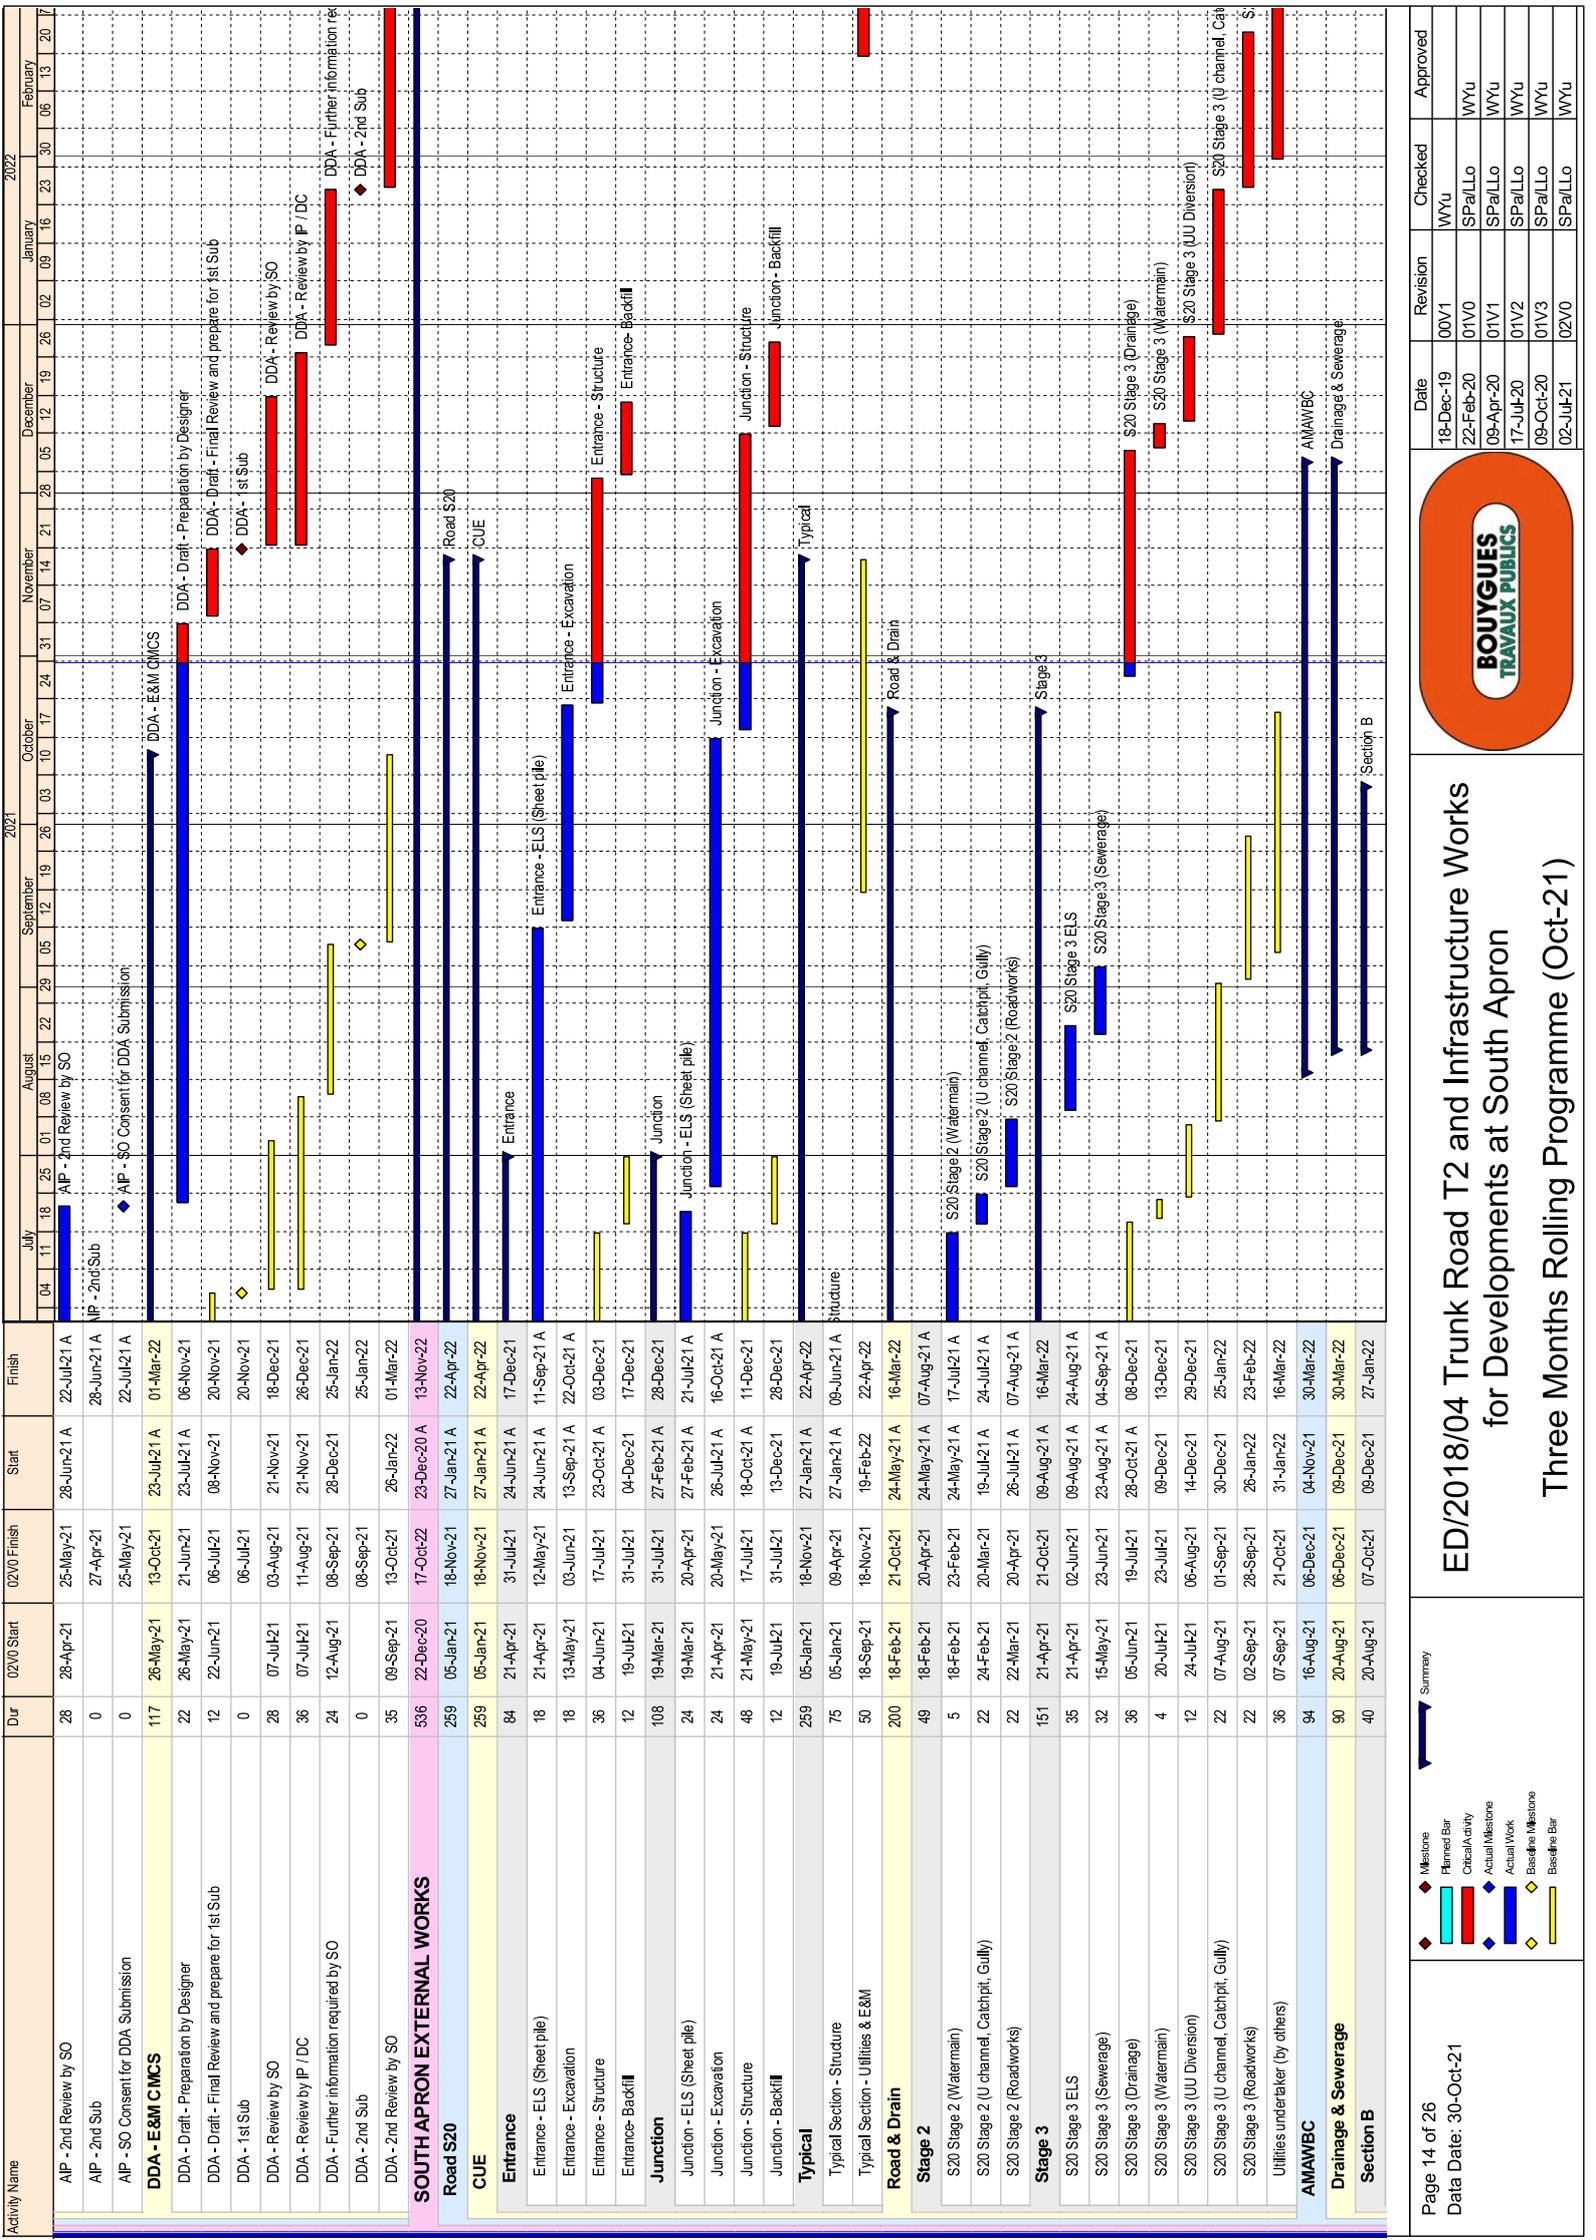


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron


Three Months Rolling Programme (Oct-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLO	WYu
09-Apr-20	01V1	SPaLLO	WYu
17-Jul-20	01V2	SPaLLO	WYu
09-Oct-20	01V3	SPaLLO	WYu
02-Jul-21	02V0	SPaLLO	WYu

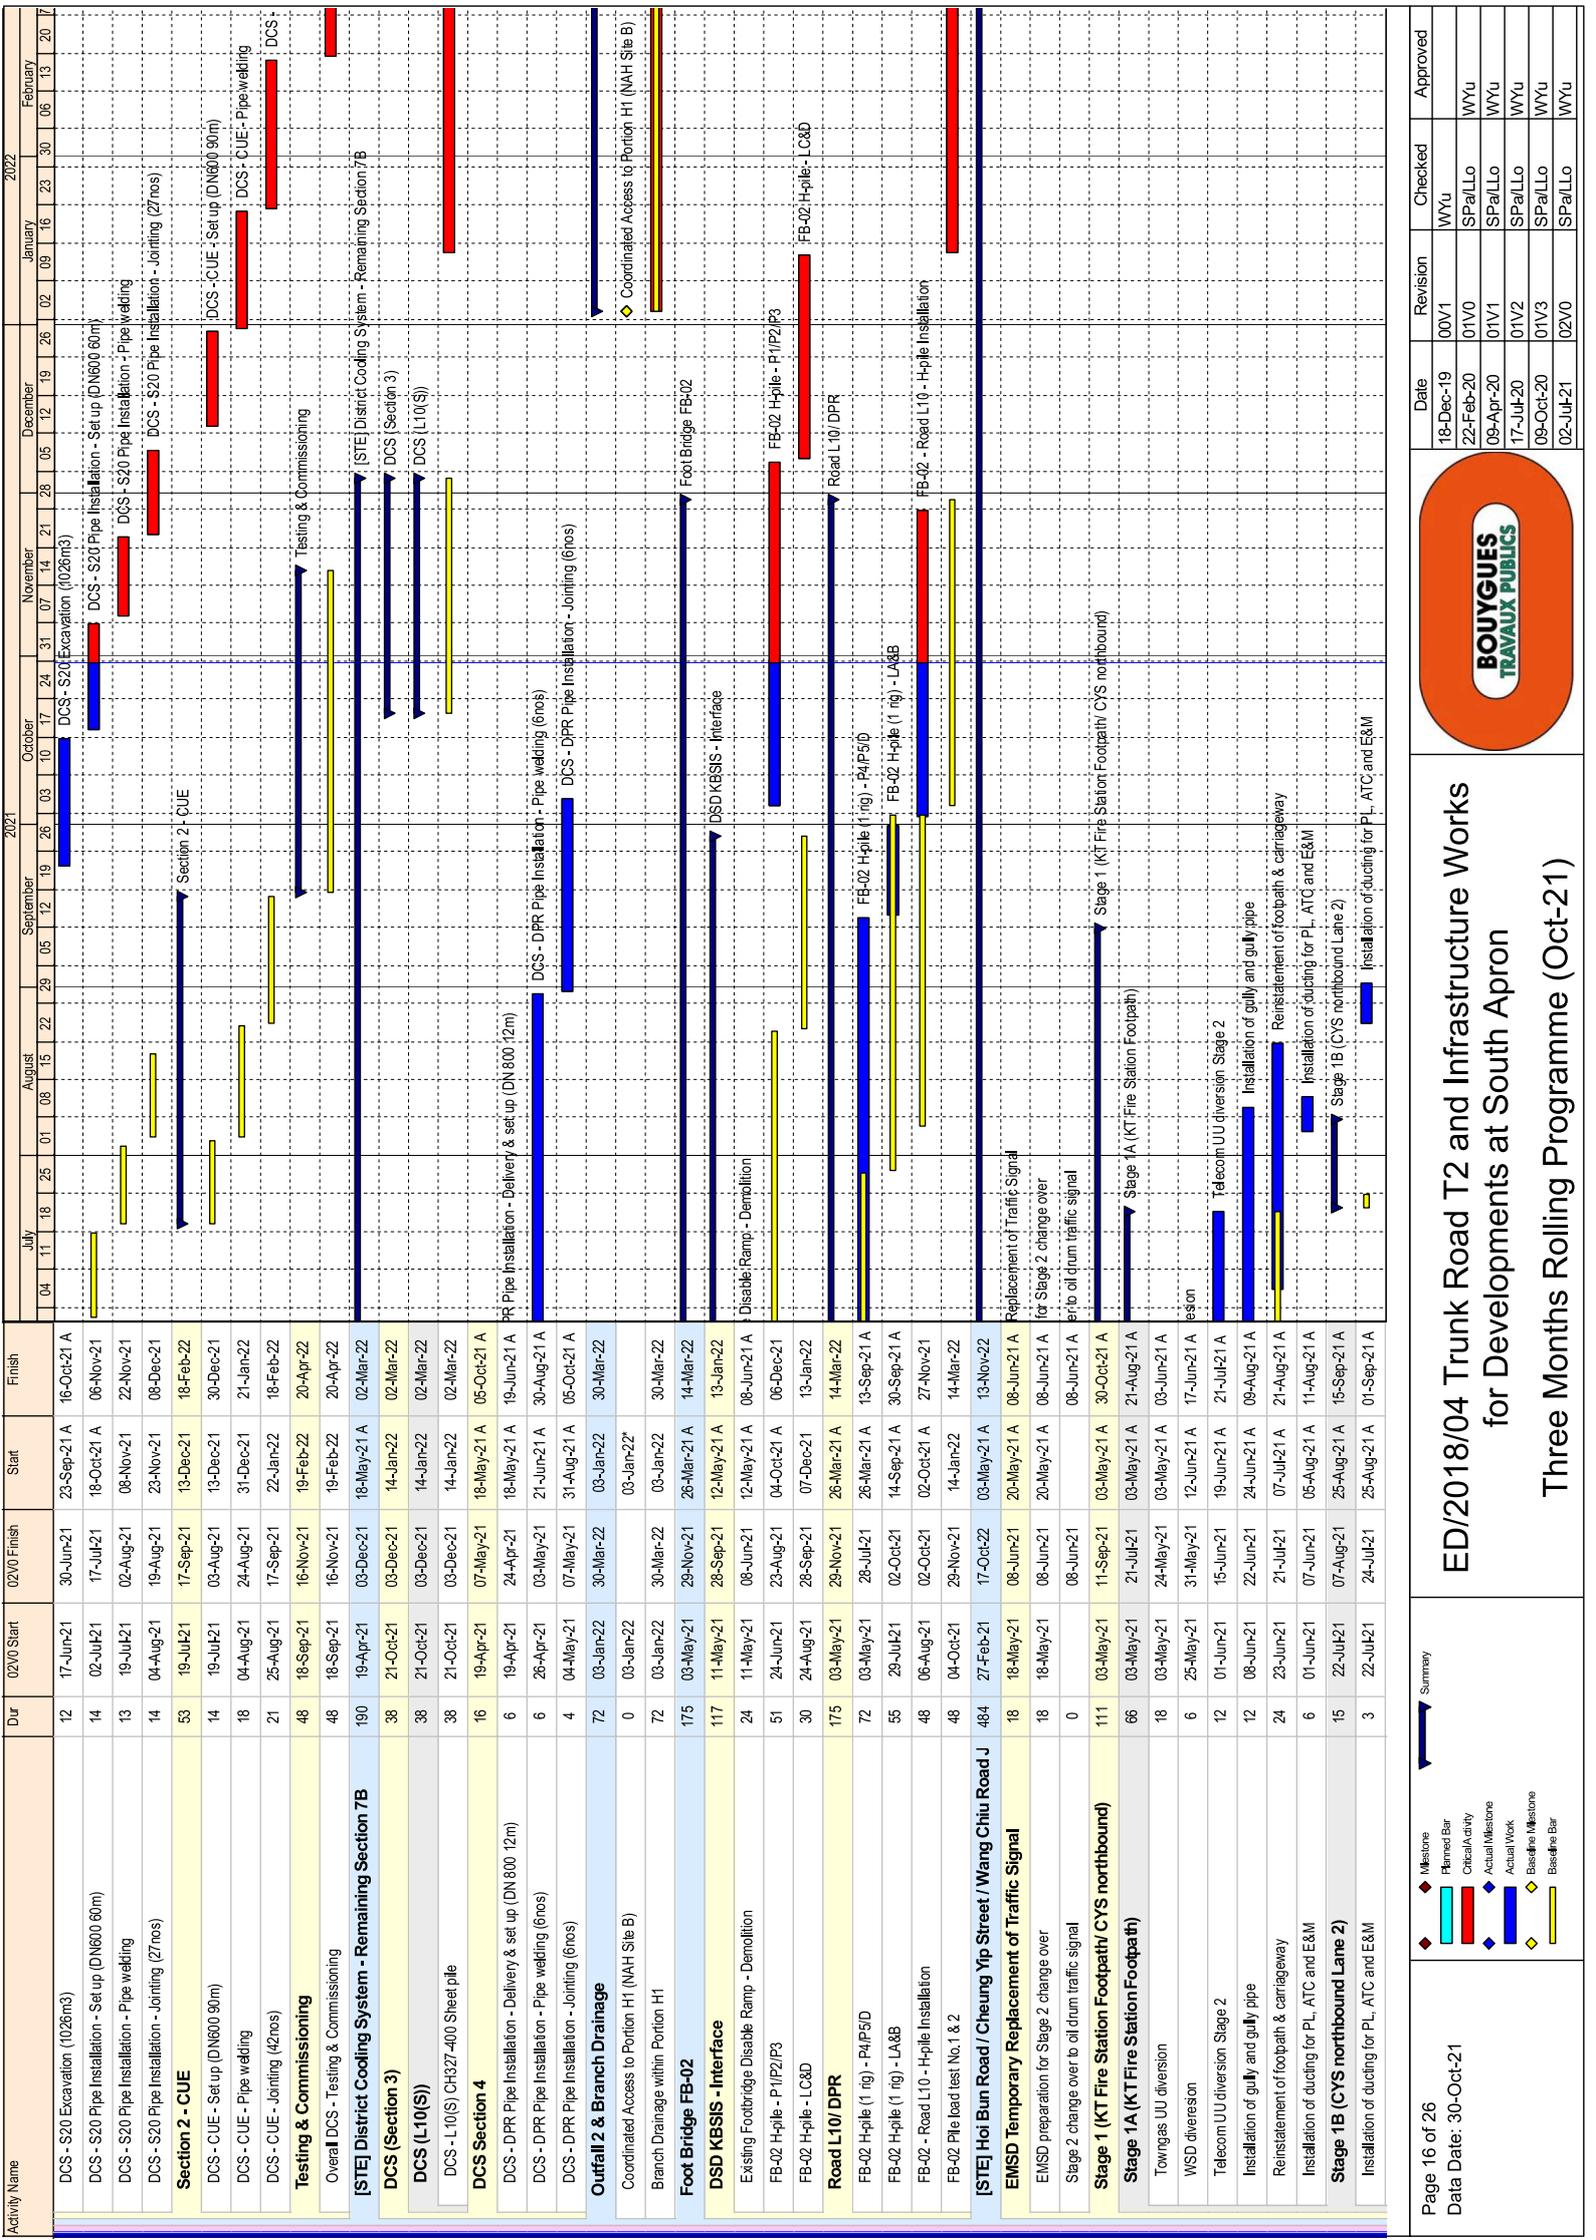

**ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Oct-21)**



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLO	WYu
09-Apr-20	01V1	SPaLLO	WYu
17-Jul-20	01V2	SPaLLO	WYu
09-Oct-20	01V3	SPaLLO	WYu
02-Jul-21	02V0	SPaLLO	WYu

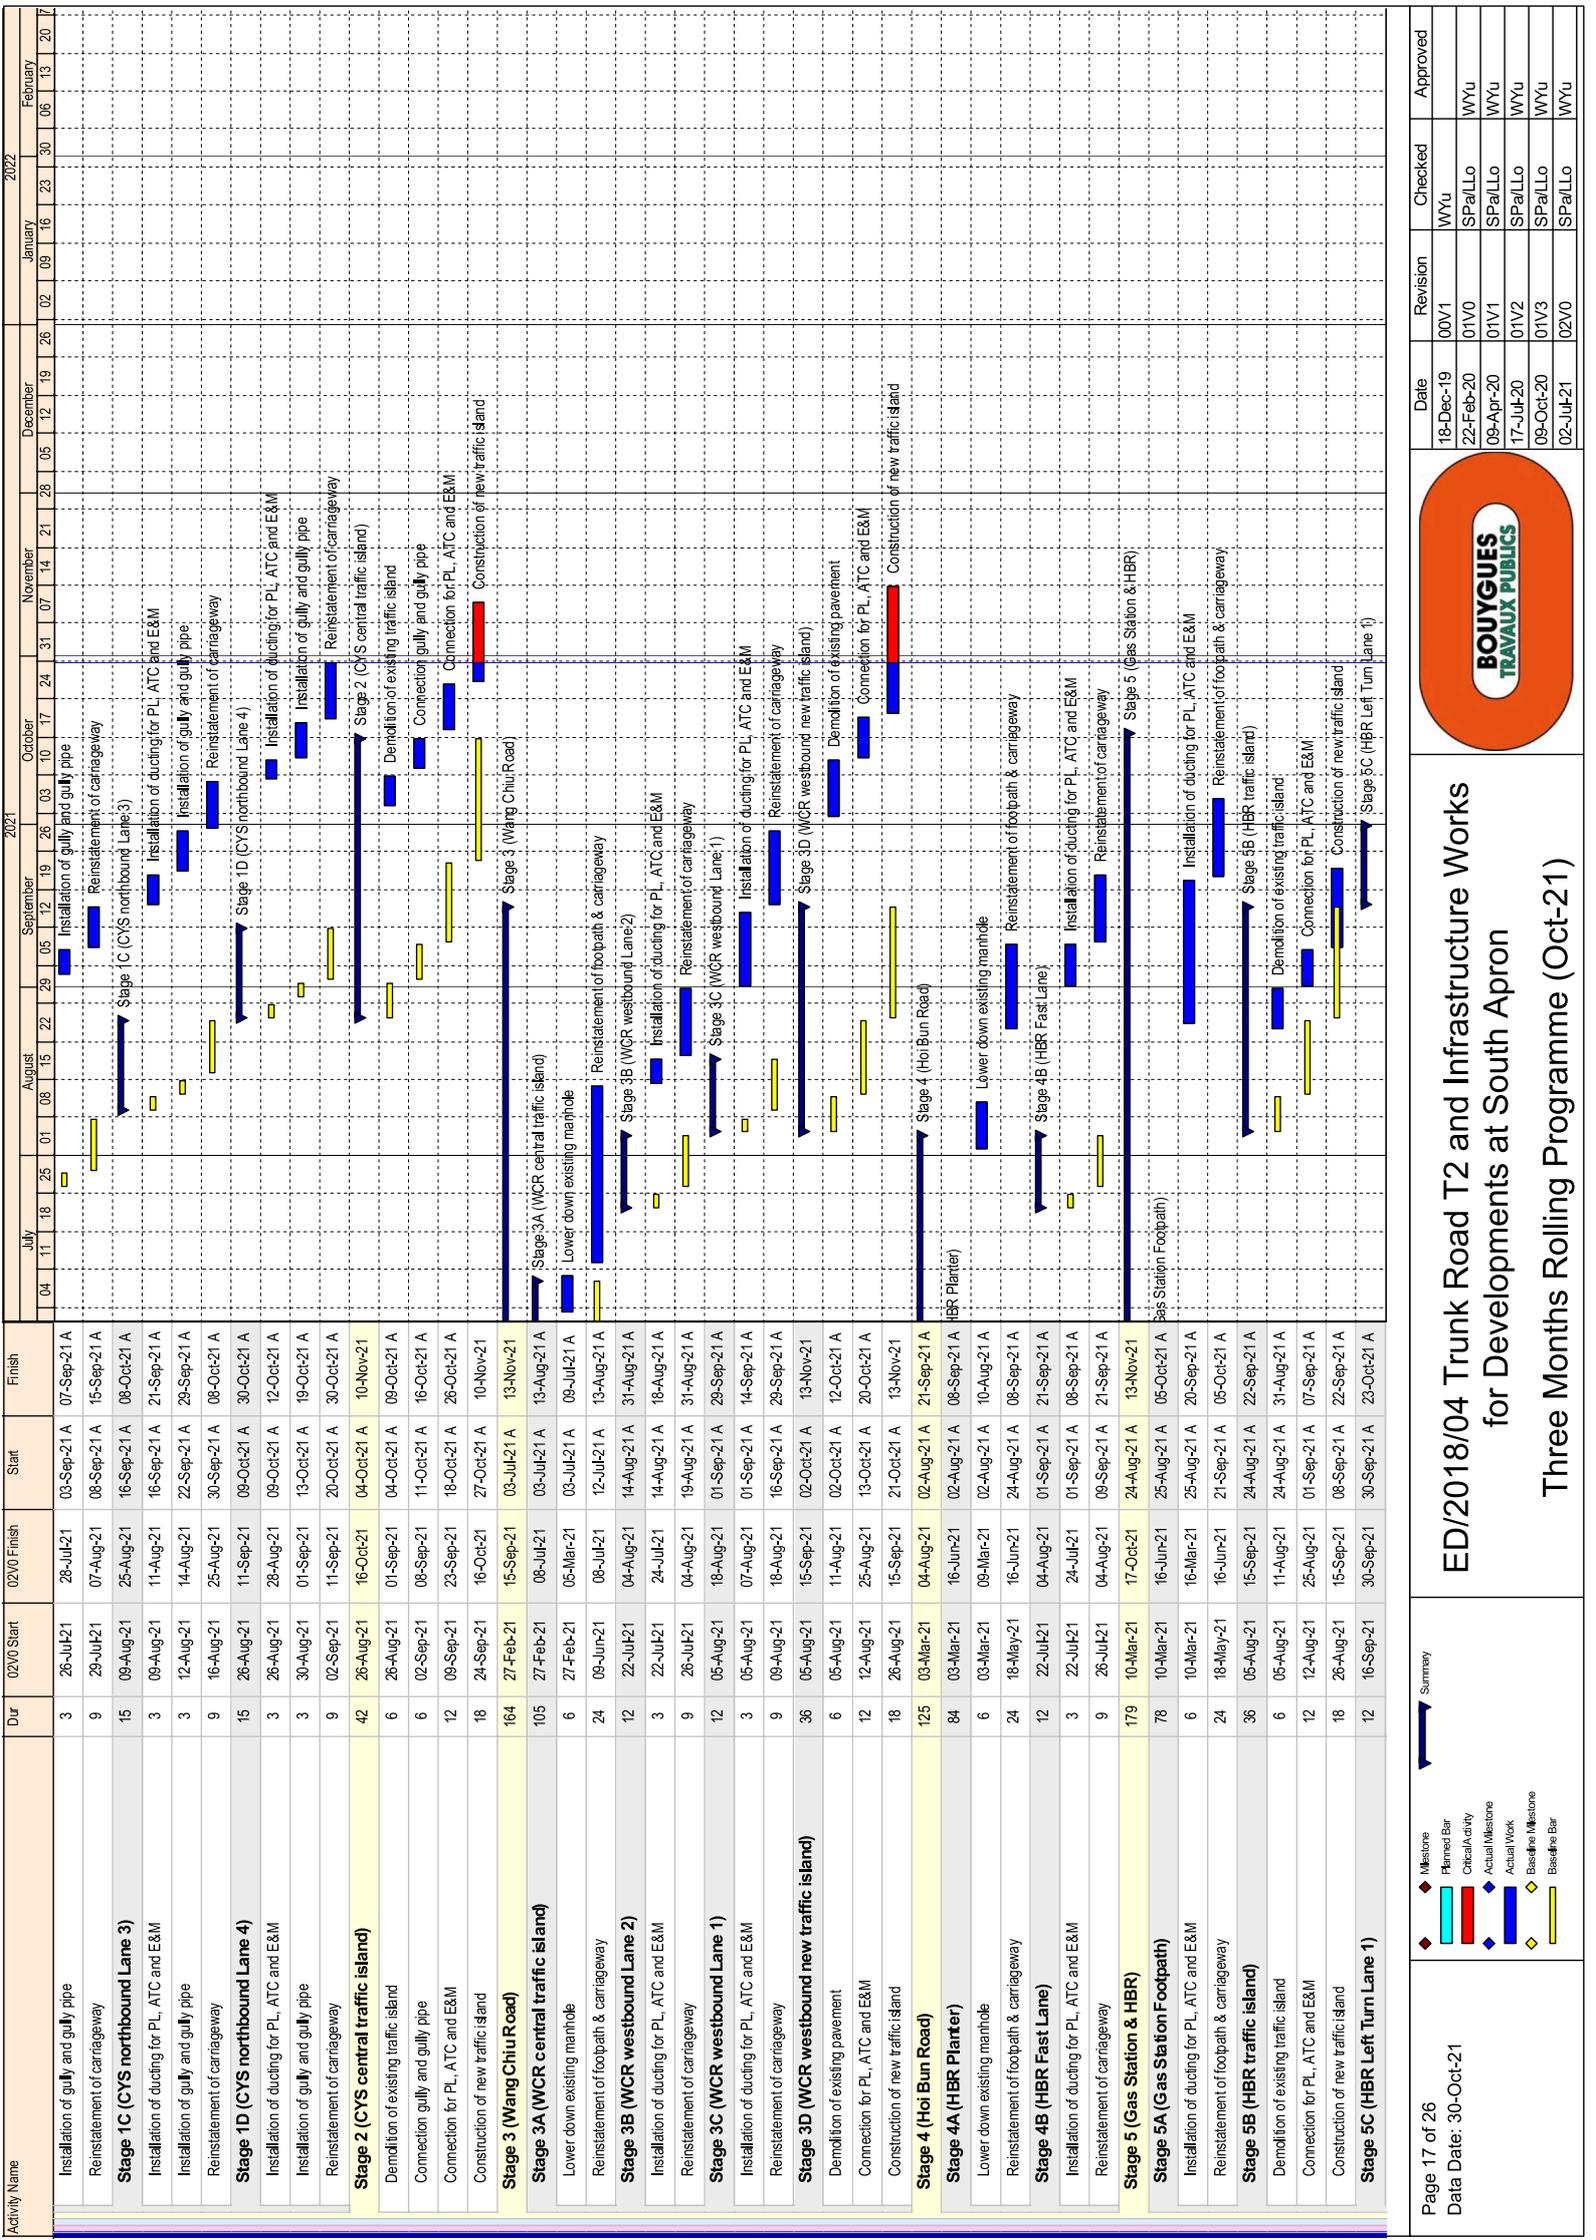


Page 17 of 26
 Data Date: 30-Oct-21

Summary


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

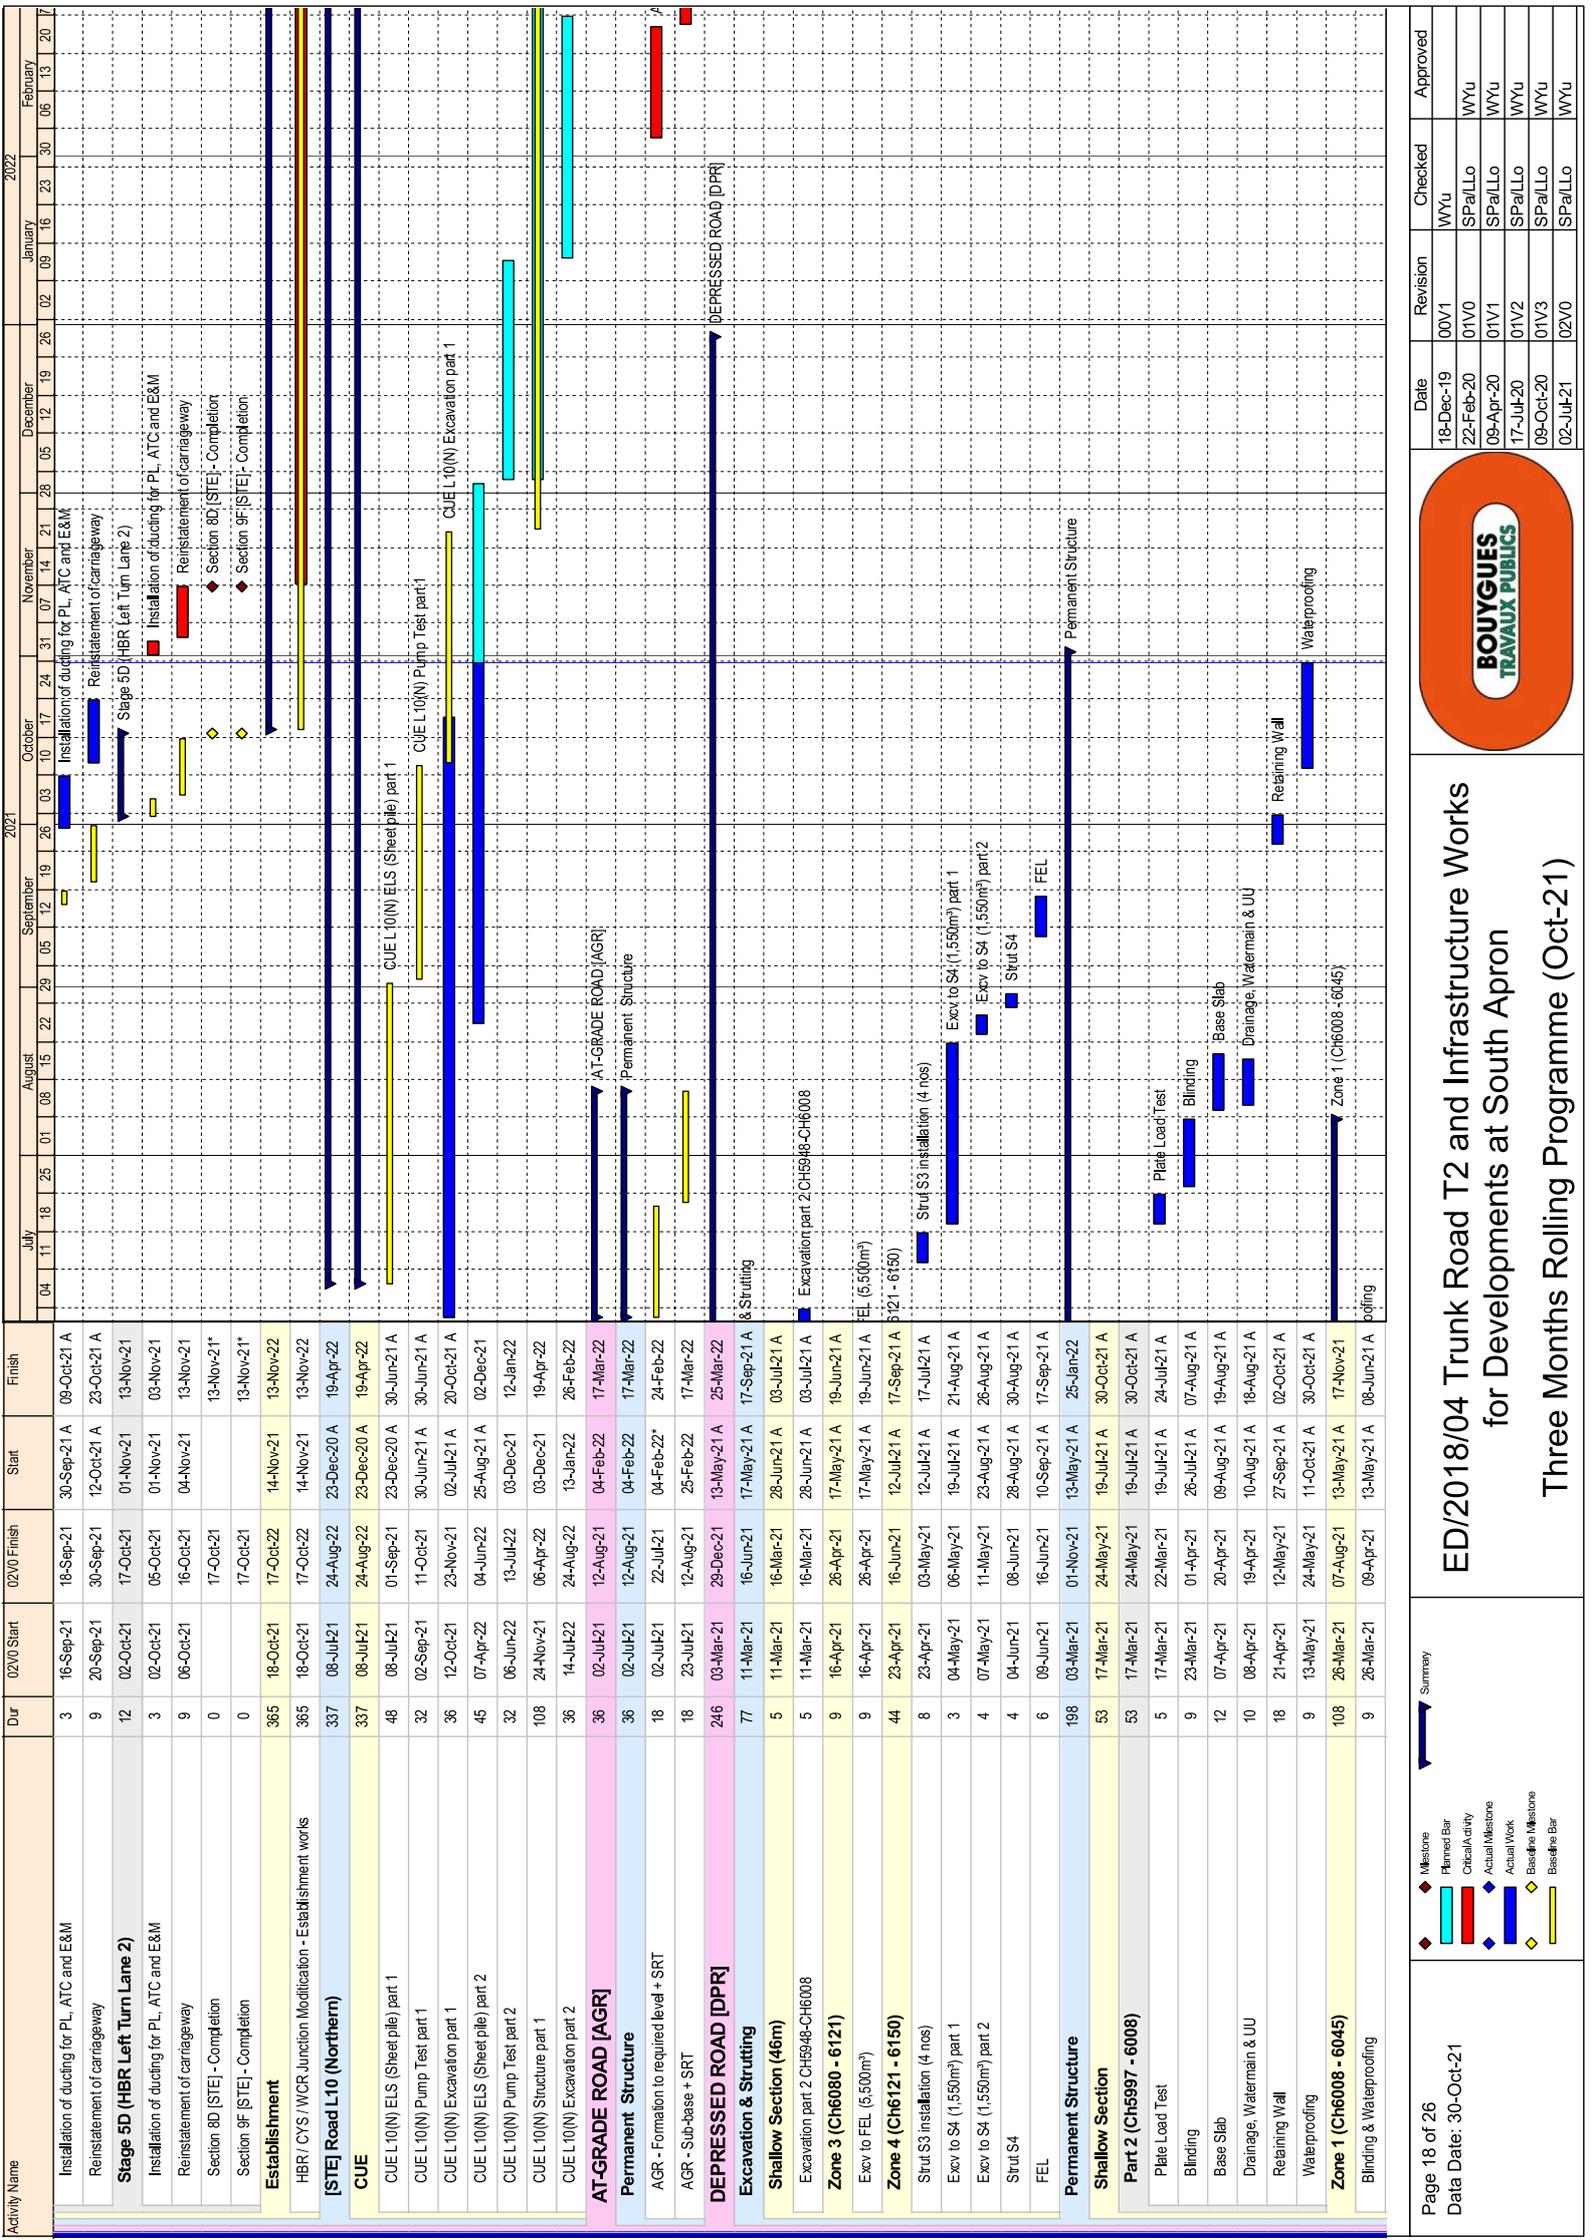

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu




ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)

Page 18 of 26
Data Date: 30-Oct-21

Summary

- Milestone
- Flamed Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

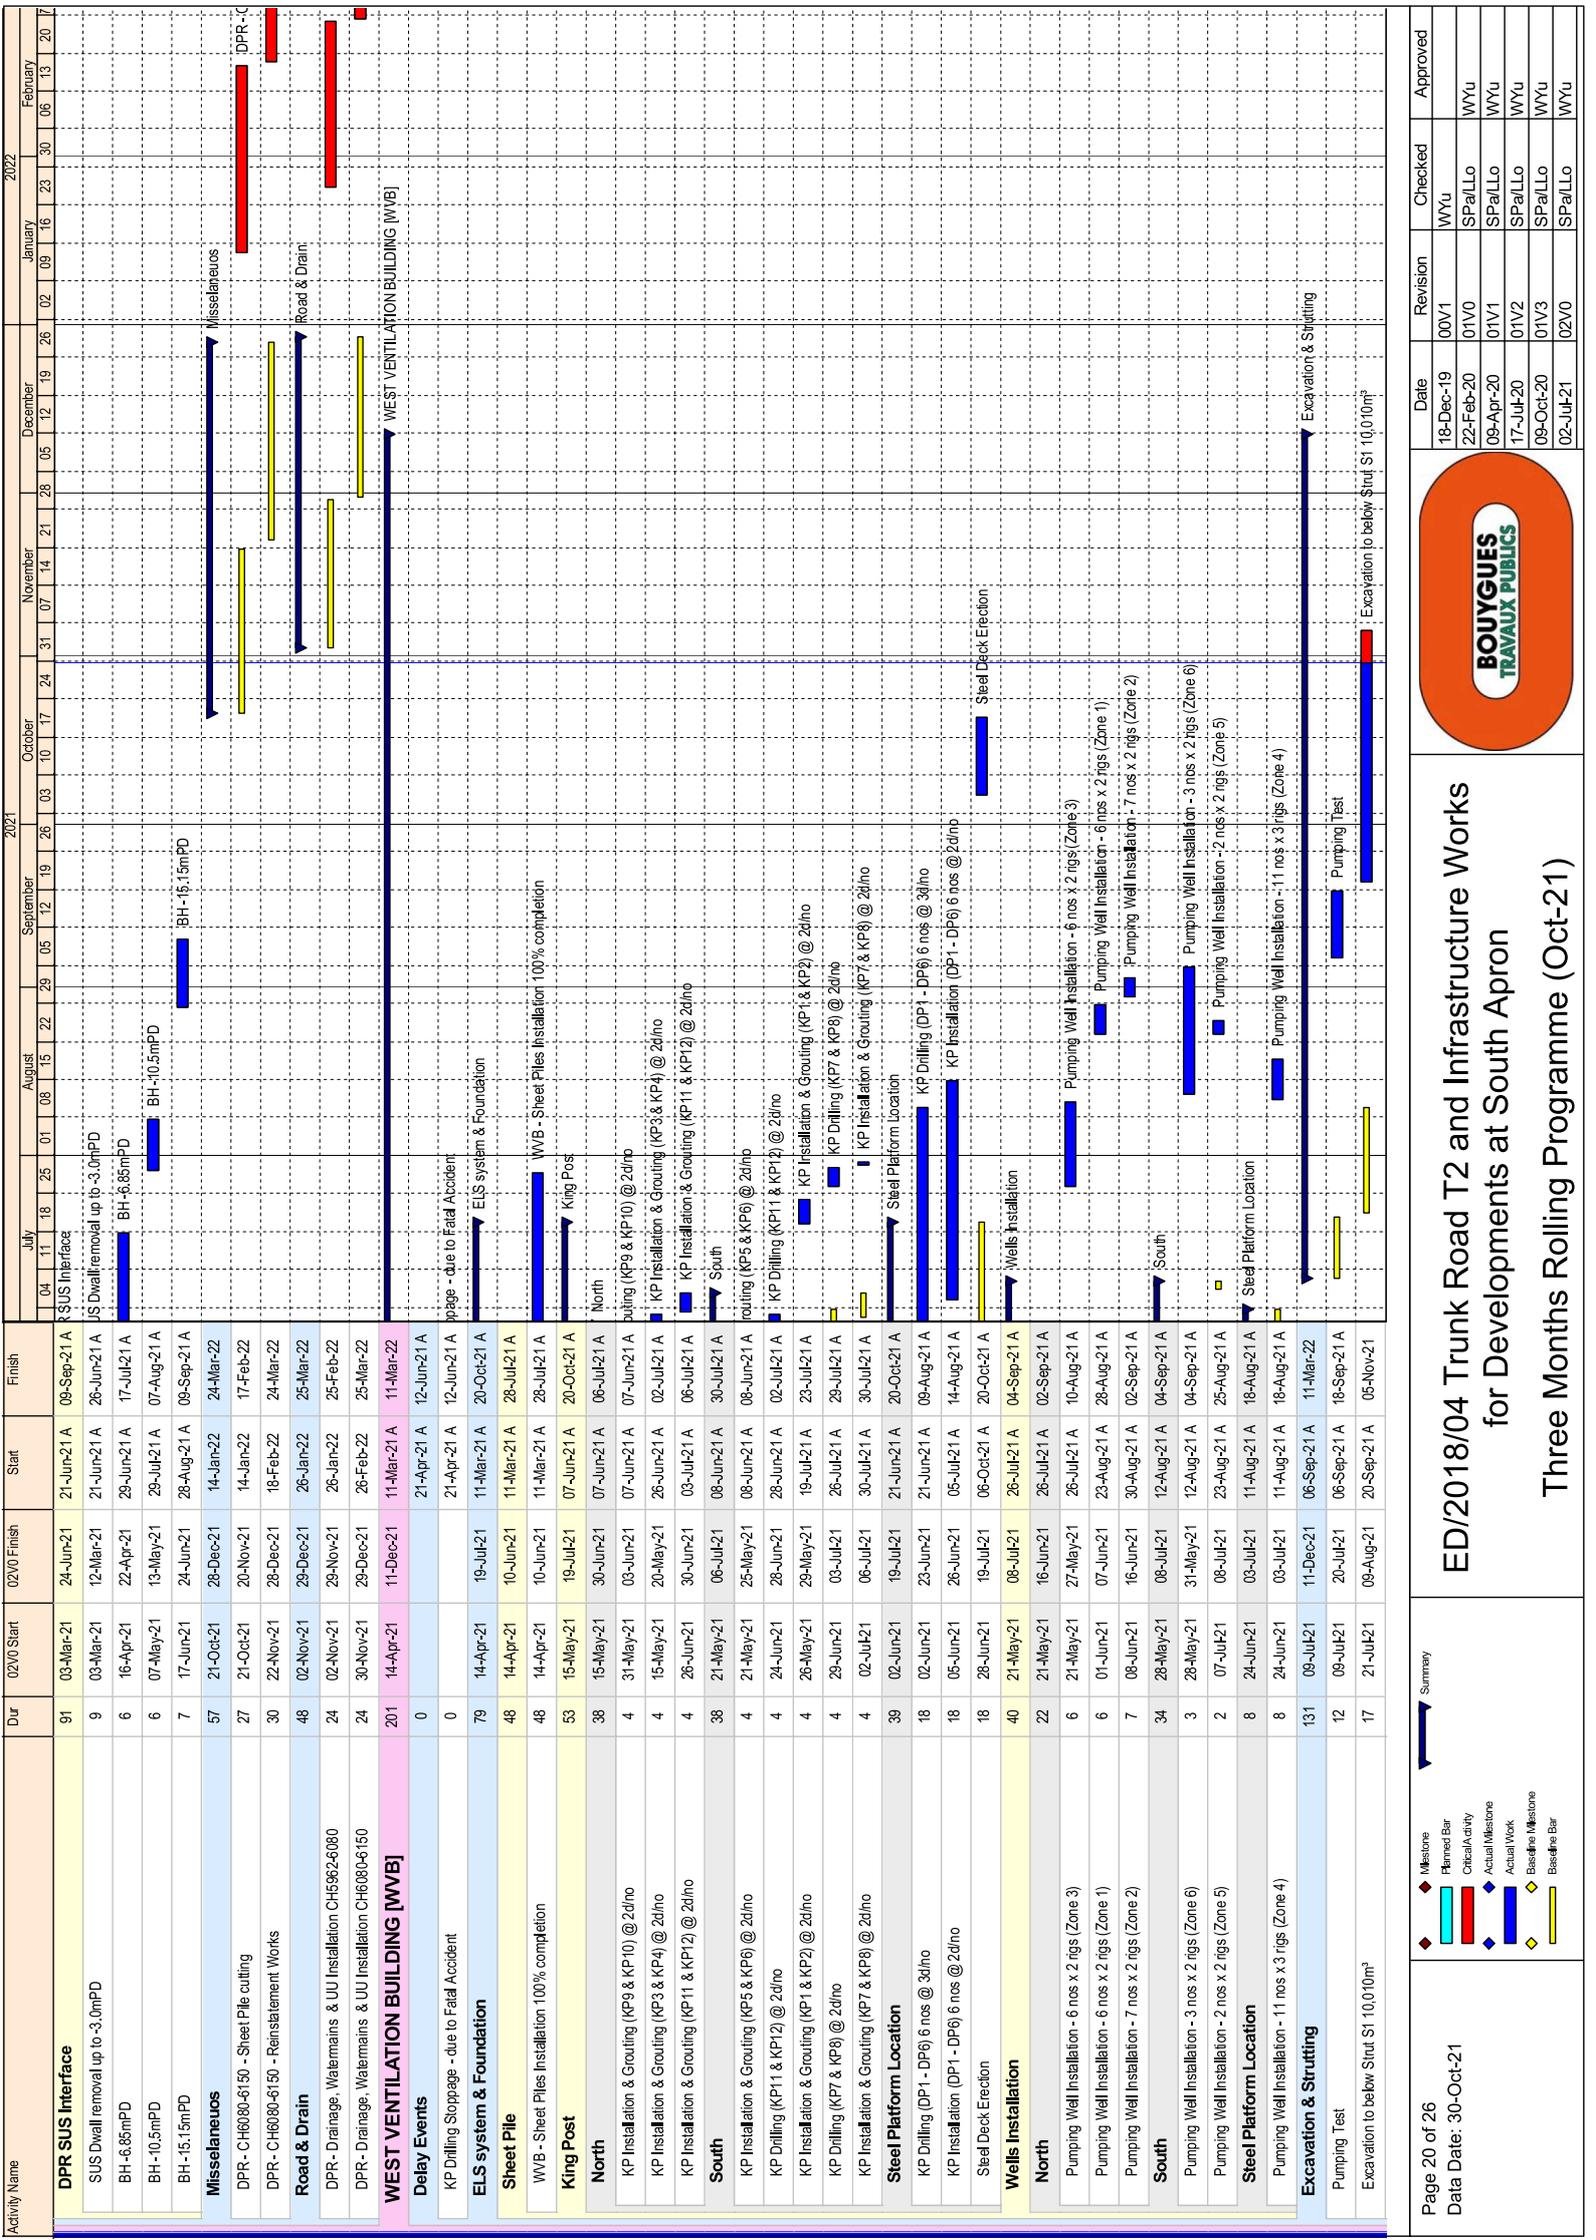

Summary


- Milestone
- Flamed Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLO	WYu
09-Apr-20	01V1	SPaLLO	WYu
17-Jul-20	01V2	SPaLLO	WYu
09-Oct-20	01V3	SPaLLO	WYu
02-Jul-21	02V0	SPaLLO	WYu

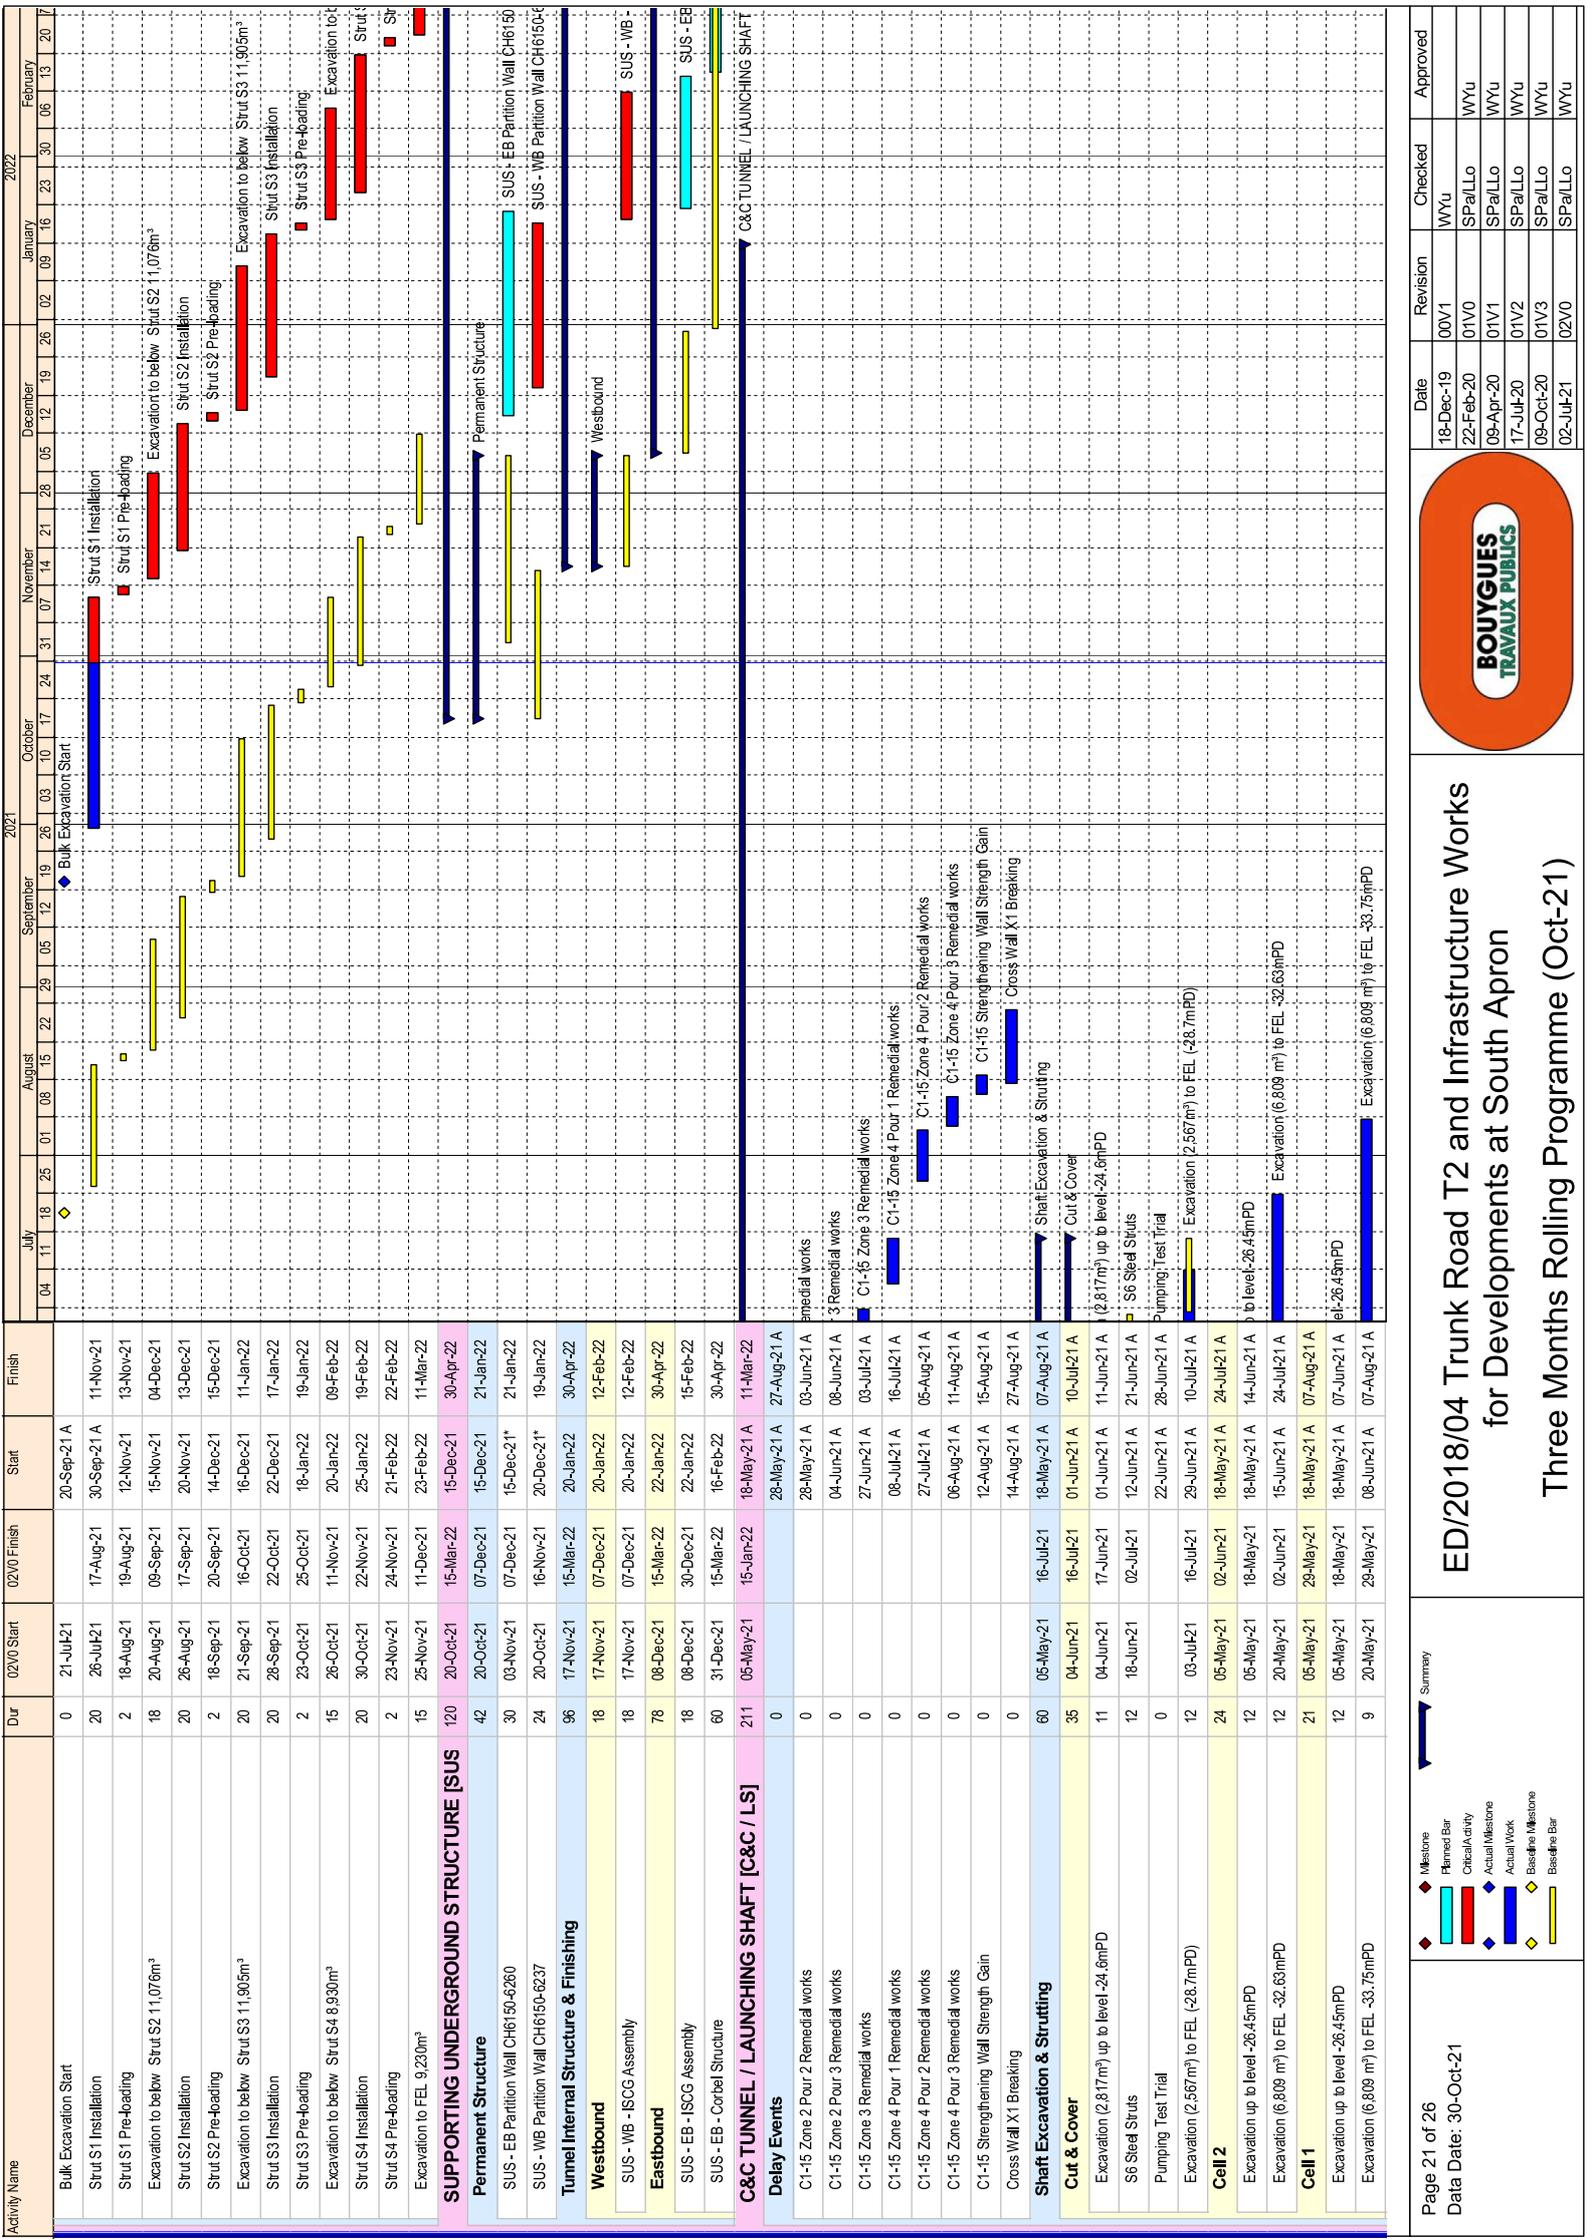

Activity Name	Dur	02/20 Start	02/20 Finish	Start	Finish
Bulk Excavation Start	0	21-Jul-21		20-Sep-21 A	11-Nov-21
Strut S1 Installation	20	26-Jul-21	17-Aug-21	30-Sep-21 A	13-Nov-21
Strut S1 Pre-loading	2	18-Aug-21	19-Aug-21	12-Nov-21	04-Dec-21
Excavation to below Strut S2 11,076m³	18	20-Aug-21	09-Sep-21	15-Nov-21	13-Dec-21
Strut S2 Installation	20	26-Aug-21	17-Sep-21	20-Nov-21	15-Dec-21
Strut S2 Pre-loading	2	18-Sep-21	20-Sep-21	14-Dec-21	11-Jan-22
Excavation to below Strut S3 11,905m³	20	21-Sep-21	16-Oct-21	16-Dec-21	17-Jan-22
Strut S3 Installation	20	28-Sep-21	22-Oct-21	22-Dec-21	19-Jan-22
Strut S3 Pre-loading	2	23-Oct-21	25-Oct-21	18-Jan-22	09-Feb-22
Excavation to below Strut S4 8,930m³	15	26-Oct-21	11-Nov-21	20-Jan-22	19-Feb-22
Strut S4 Installation	20	30-Oct-21	22-Nov-21	25-Jan-22	22-Feb-22
Strut S4 Pre-loading	2	23-Nov-21	24-Nov-21	21-Feb-22	11-Mar-22
Excavation to FEL 9,230m³	15	25-Nov-21	11-Dec-21	23-Feb-22	30-Apr-22
SUPPORTING UNDERGROUND STRUCTURE [SUS]	120	20-Oct-21	15-Dec-21	15-Dec-21	21-Jan-22
Permanent Structure	42	20-Oct-21	07-Dec-21	15-Dec-21	21-Jan-22
SUS - EB Partition Wall CH6150-6260	30	03-Nov-21	07-Dec-21	15-Dec-21*	19-Jan-22
SUS - WB Partition Wall CH6150-6237	24	20-Oct-21	16-Nov-21	20-Dec-21*	30-Apr-22
Tunnel Internal Structure & Finishing	96	17-Nov-21	15-Mar-22	20-Jan-22	12-Feb-22
Westbound	18	17-Nov-21	07-Dec-21	20-Jan-22	12-Feb-22
SUS - WB - ISCG Assembly	18	17-Nov-21	07-Dec-21	20-Jan-22	12-Feb-22
Eastbound	78	08-Dec-21	15-Mar-22	22-Jan-22	15-Feb-22
SUS - EB - ISCG Assembly	18	08-Dec-21	30-Dec-21	22-Jan-22	15-Feb-22
SUS - EB - Corbel Structure	60	31-Dec-21	15-Mar-22	16-Feb-22	30-Apr-22
C&C TUNNEL / LAUNCHING SHAFT [C&C / LS]	211	05-May-21	15-Jan-22	18-May-21 A	11-Mar-22
Delay Events	0			28-May-21 A	27-Aug-21 A
C1-15 Zone 2 Pour 2 Remedial works	0			28-May-21 A	03-Jun-21 A
C1-15 Zone 2 Pour 3 Remedial works	0			04-Jun-21 A	08-Jun-21 A
C1-15 Zone 3 Remedial works	0			27-Jun-21 A	03-Jul-21 A
C1-15 Zone 4 Pour 1 Remedial works	0			08-Jul-21 A	16-Jul-21 A
C1-15 Zone 4 Pour 2 Remedial works	0			27-Jul-21 A	05-Aug-21 A
C1-15 Zone 4 Pour 3 Remedial works	0			06-Aug-21 A	11-Aug-21 A
C1-15 Strengthening Wall Strength Gain	0			12-Aug-21 A	15-Aug-21 A
Cross Wall X1 Breaking	0			14-Aug-21 A	27-Aug-21 A
Shaft Excavation & Strutting	60	05-May-21	16-Jul-21	18-May-21 A	07-Aug-21 A
Cut & Cover	35	04-Jun-21	16-Jul-21	01-Jun-21 A	10-Jul-21 A
Excavation (2,817m³) up to level -24.6mPD	11	04-Jun-21	17-Jun-21	01-Jun-21 A	11-Jun-21 A
S6 Steel Struts	12	18-Jun-21	02-Jul-21	12-Jun-21 A	21-Jun-21 A
Pumping Test Trial	0			22-Jun-21 A	28-Jun-21 A
Excavation (2,567m³) to FEL (-28.7mPD)	12	03-Jul-21	16-Jul-21	29-Jun-21 A	10-Jul-21 A
Cell 2	24	05-May-21	02-Jun-21	18-May-21 A	24-Jul-21 A
Excavation up to level -26.45mPD	12	05-May-21	18-May-21	18-May-21 A	14-Jun-21 A
Excavation (6,809 m³) to FEL -32.63mPD	12	20-May-21	02-Jun-21	15-Jun-21 A	24-Jul-21 A
Cell 1	21	05-May-21	29-May-21	18-May-21 A	07-Aug-21 A
Excavation up to level -26.45mPD	12	05-May-21	18-May-21	18-May-21 A	07-Jun-21 A
Excavation (6,809 m³) to FEL -33.75mPD	9	20-May-21	29-May-21	06-Jun-21 A	07-Aug-21 A


Page 21 of 26
 Data Date: 30-Oct-21

Summary


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

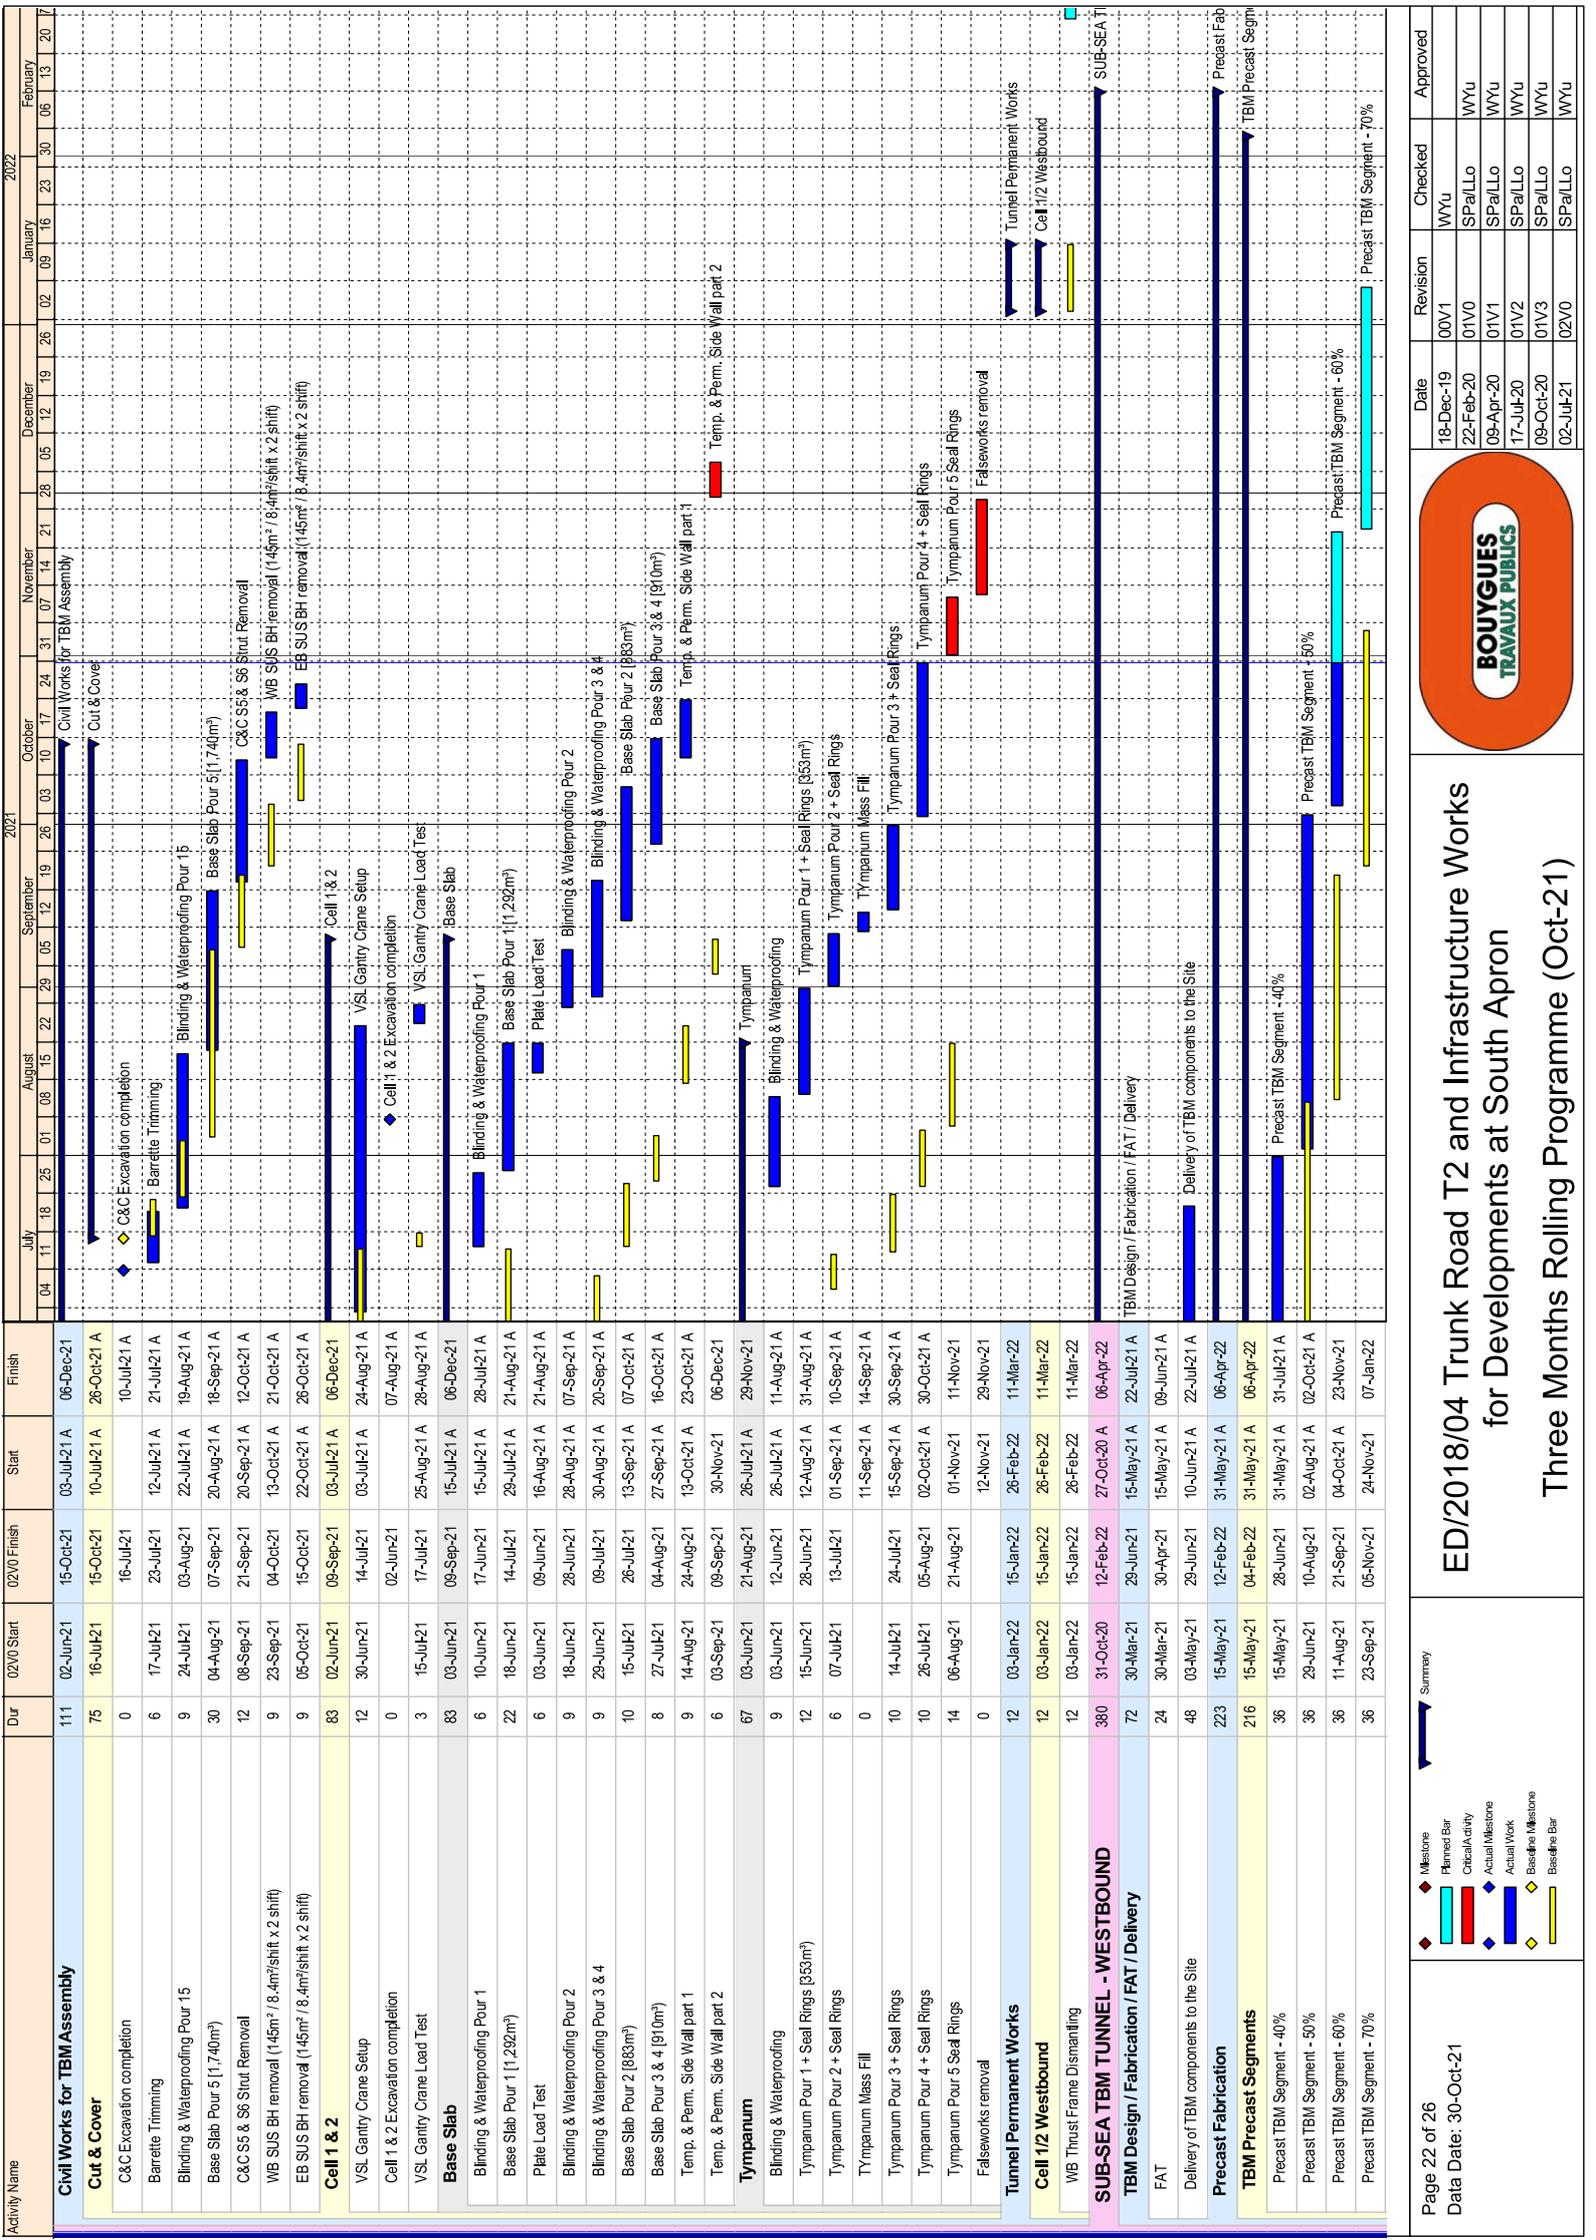


Summary

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Backlogs Milestone
- Backlogs Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaILLo	WYu
09-Apr-20	01V1	SPaILLo	WYu
17-Jul-20	01V2	SPaILLo	WYu
09-Oct-20	01V3	SPaILLo	WYu
02-Jul-21	02V0	SPaILLo	WYu

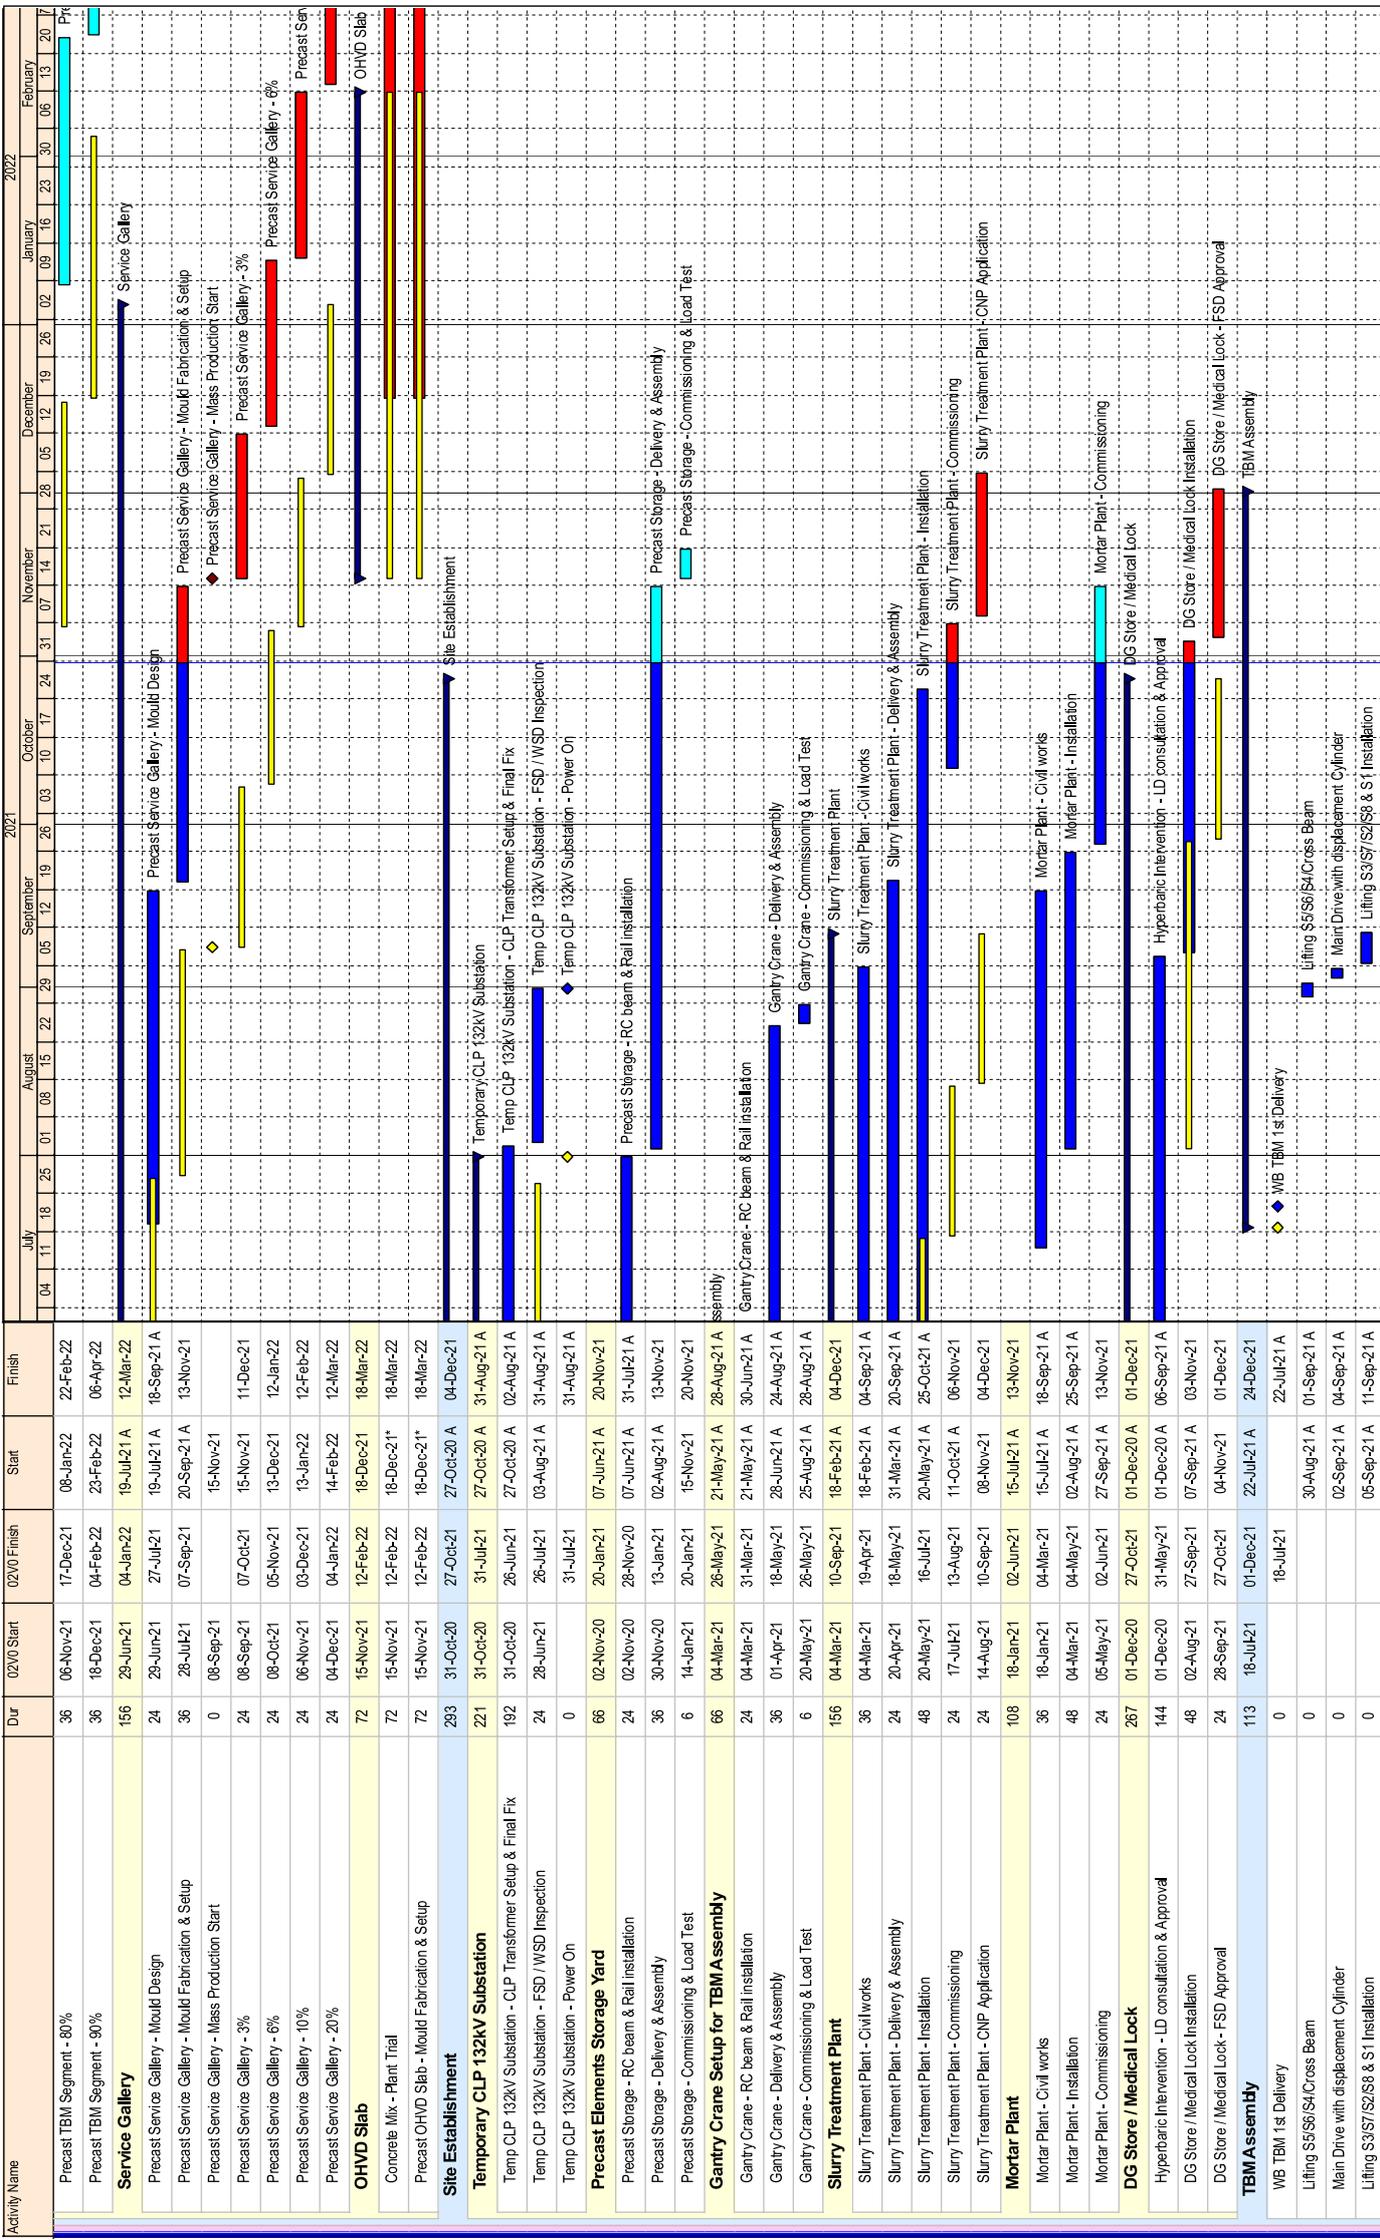

Summary



- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLO	WYu
09-Apr-20	01V1	SPaLLO	WYu
17-Jul-20	01V2	SPaLLO	WYu
09-Oct-20	01V3	SPaLLO	WYu
02-Jul-21	02V0	SPaLLO	WYu

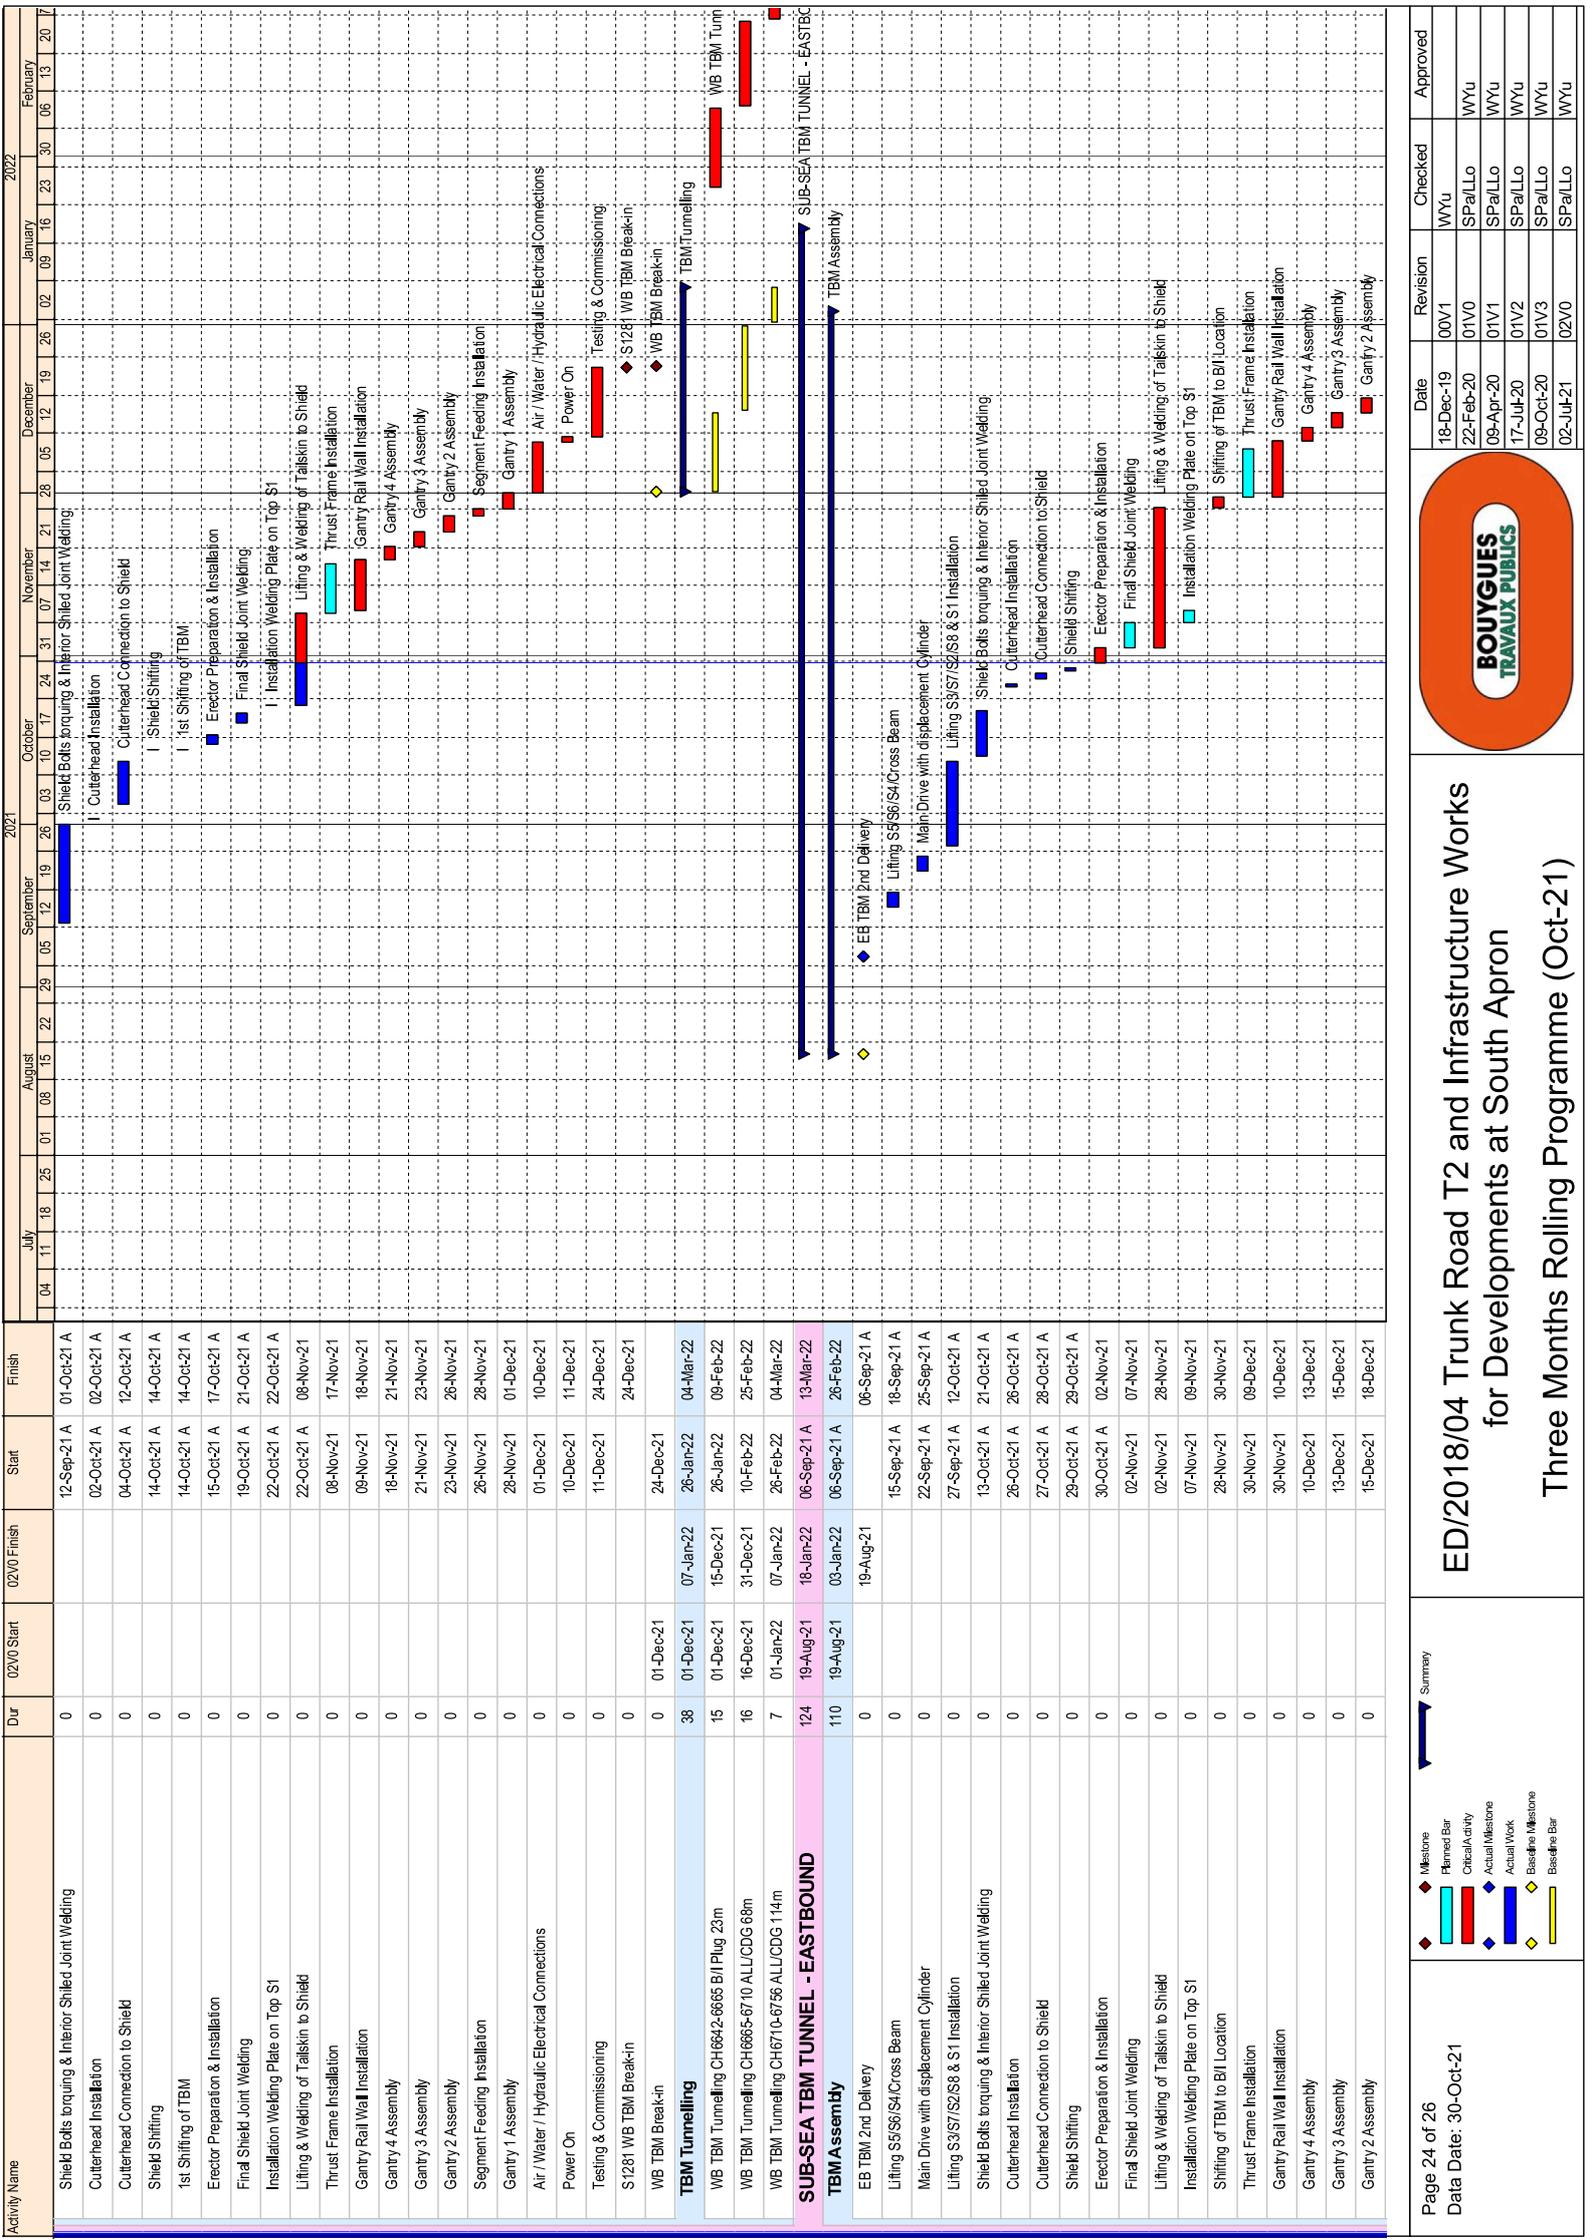

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron



Three Months Rolling Programme (Oct-21)

Page 24 of 26
Data Date: 30-Oct-21


Summary

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu

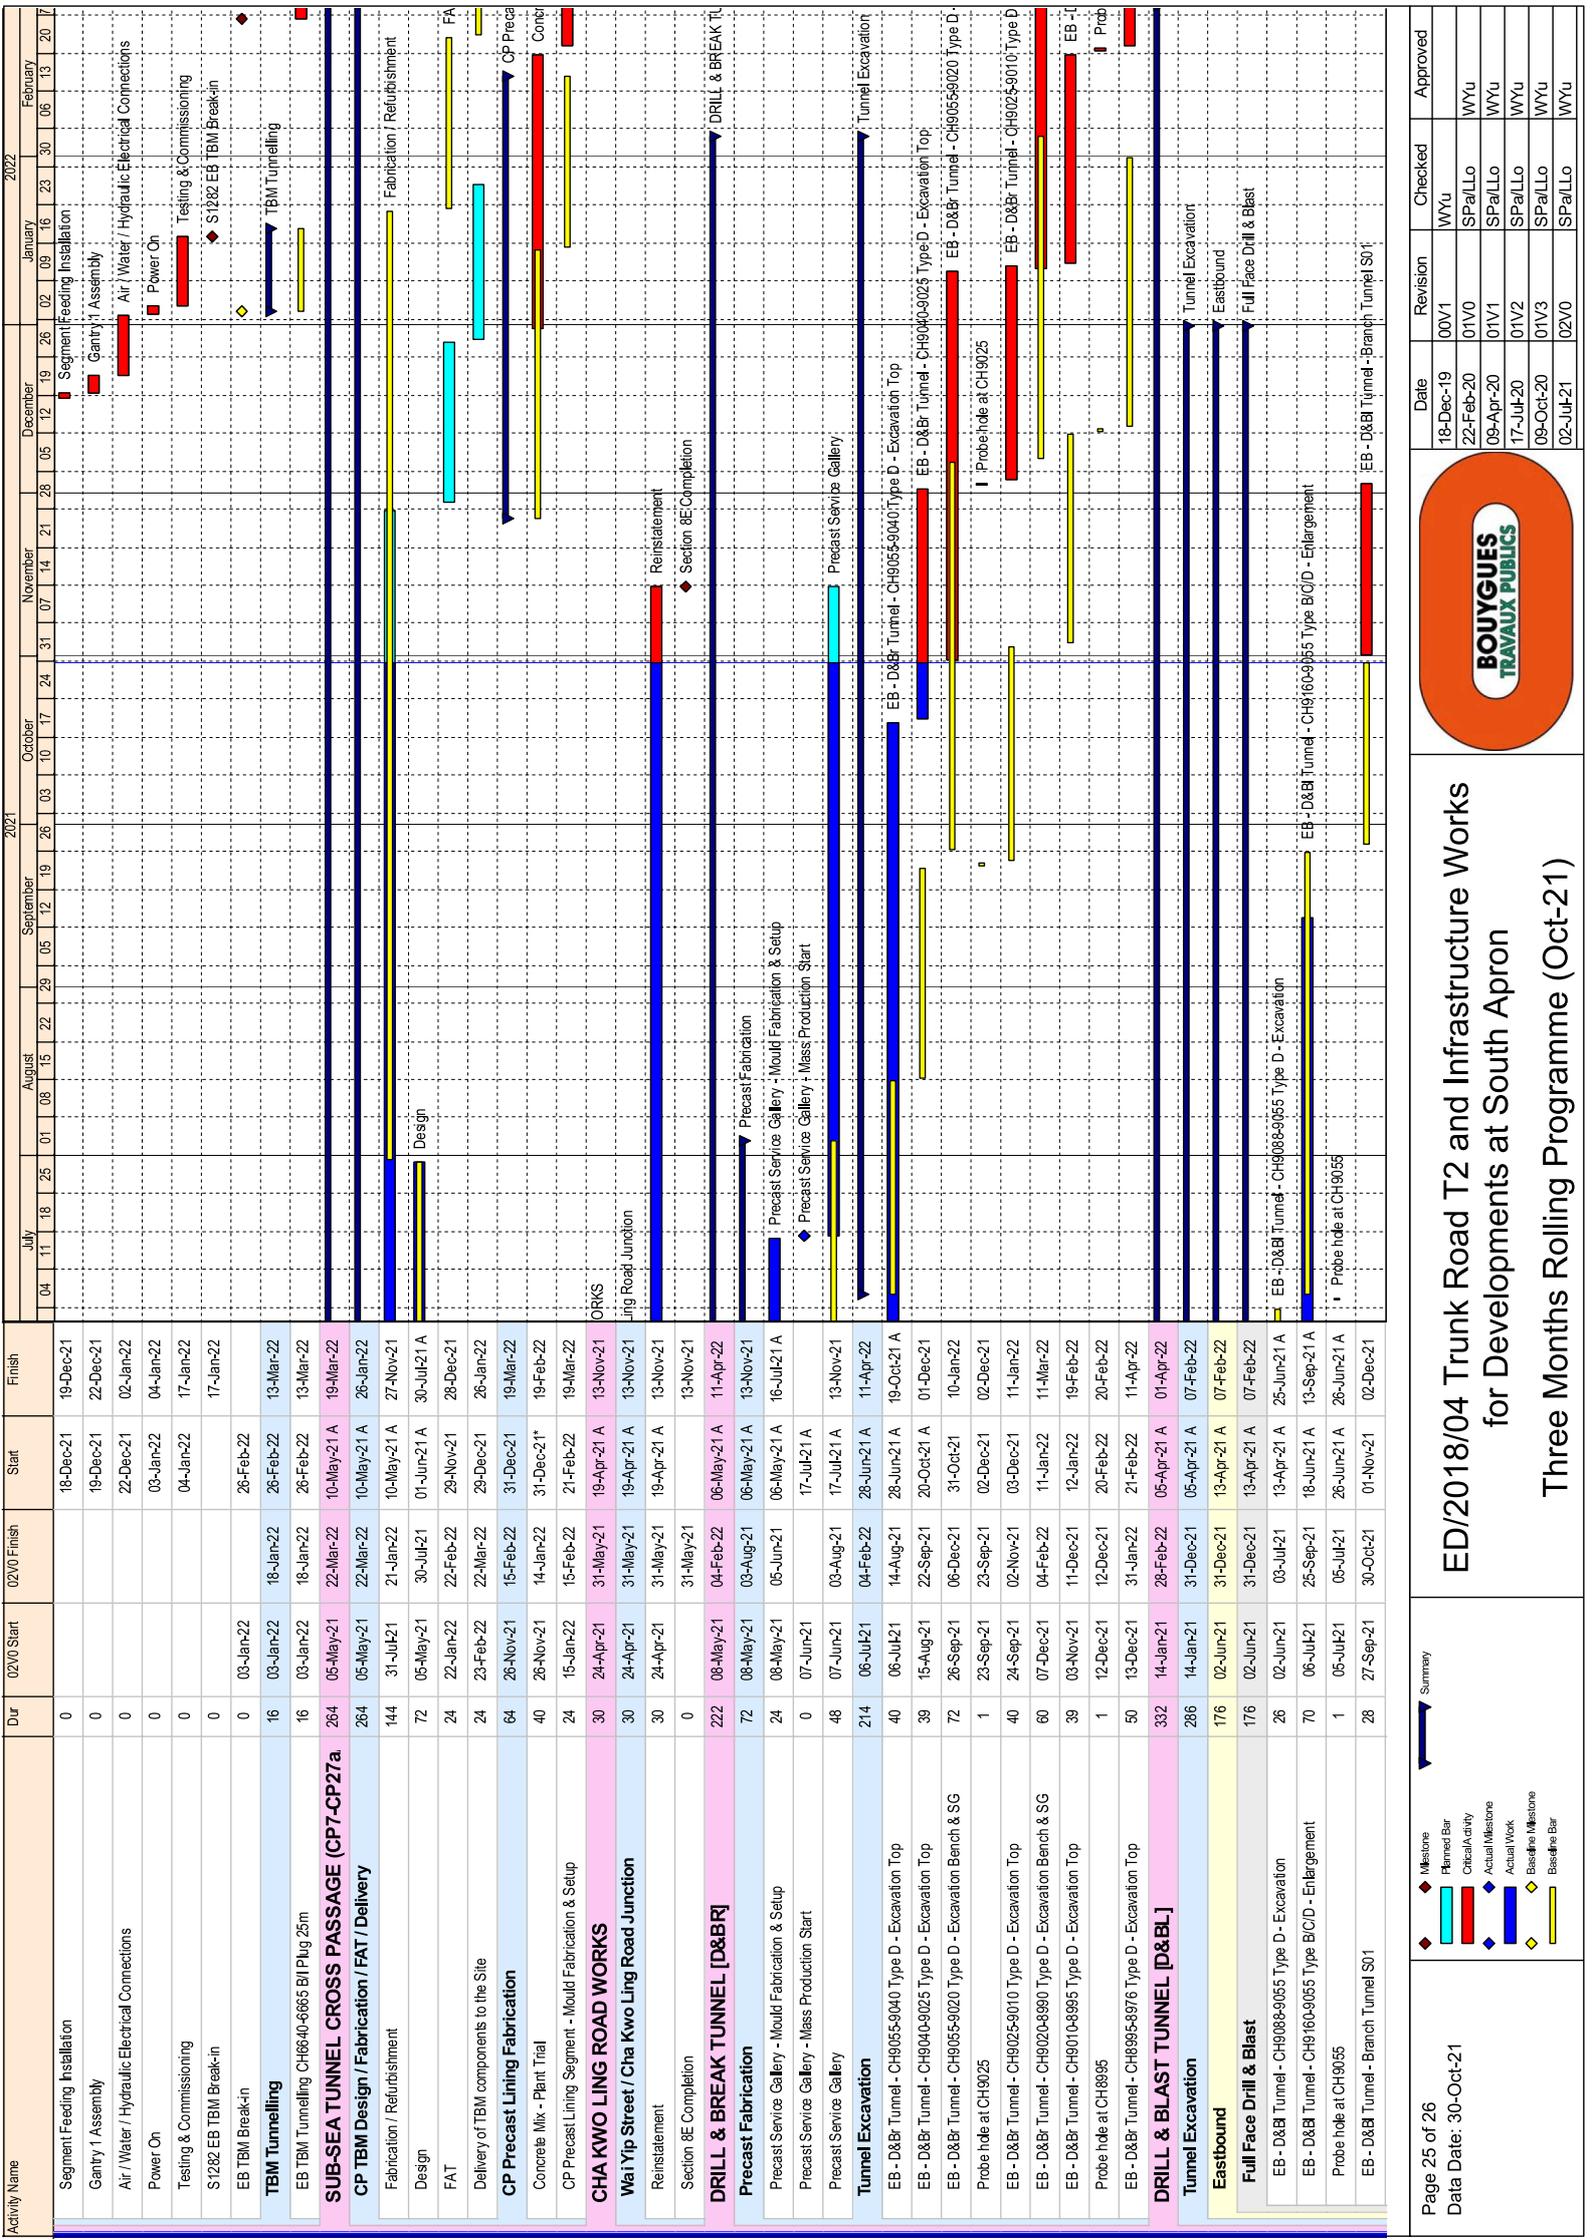

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Oct-21)

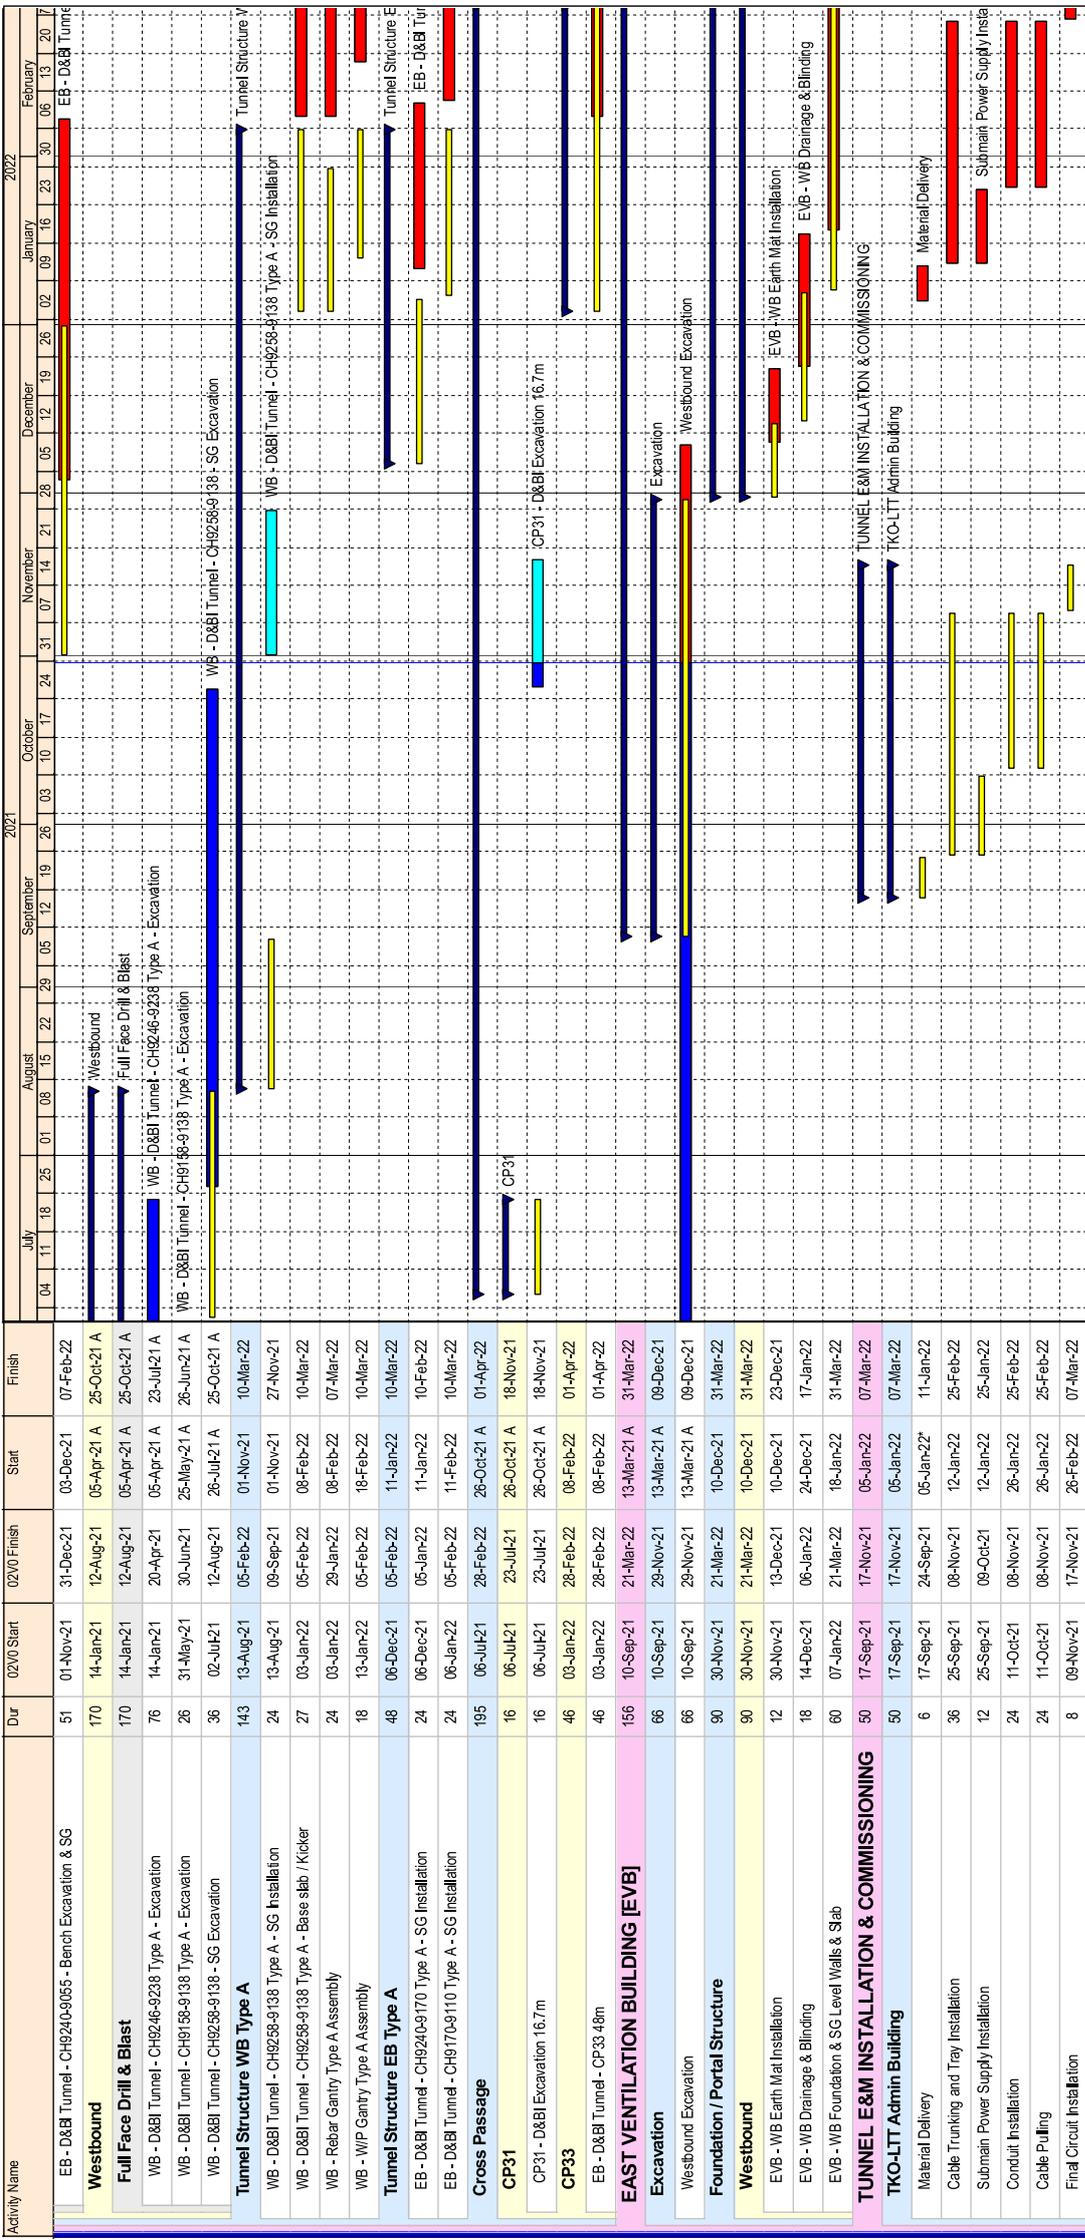


Summary

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Oct-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu
