

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



QUARTERLY EM&A REPORT

September 2018 – November 2018

Client : Civil Engineering and Development
Department, HKSAR

Contract No. : KLN/2015/07

Contract Name : Environmental Monitoring Works for
Contract KL/2014/03 – Kai Tak Development
– Stage 3 Infrastructure Works for Developments
at the Southern Part of the Former Runway

Report No. : 0405/15/ED/1141B


EP-337/2009 New Distributor Roads Serving the Planned Kai Tak
Development Area

EP-339/2009/A Decommissioning of the Remaining Parts (Ex-GFS
Building, Radar Station and Hong Kong Aviation Club)
of the former Kai Tak Airport

EP-451/2013 Trunk Road T2

Prepared by : Toby K. H. Wan

Reviewed by : Alfred Y. S. Lam

Certified by : 
Colin K. L. Yung
Environmental Team Leader
Fugro Technical Services Limited

Ref.: CEDKTDS3EM00_0_0356L.19

11 January 2019

Hyder-Meinhardt Joint Venture
17/F, Two Harbour Square,
180 Wai Yip Street, Kwun Tong
Kowloon, Hong Kong

By Post and Email

Attention: Mr. Wong W K, Chris

Dear Mr. Wong,

Re: Contract No. KL/2014/03 – Kai Tak Development – Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway Quarterly EM&A Report for September 2018 to November 2018

Reference is made to the Environmental Team's submission of the Quarterly EM&A Report for September 2018 to November 2018 (Report No. 0405/15/ED/1141B) we received by e-mail on 11 January 2019.

Please be informed that we have no adverse comment on the captioned report.

Thank you for your attention. Please do not hesitate to contact us should you have any queries.

Yours sincerely,
For and on behalf of
Ramboll Hong Kong Limited



F. C. Tsang
Independent Environmental Checker

c.c. CEDD
Fugro
CRBC

Attn.: Ms. Amy Chu
Attn.: Mr. Colin K. L. Yung
Attn.: Mr. Dickey Yau

Fax: 2369 4980
By email
Fax: 2283 1689

Q:\Projects\CEDKTDS3EM00\02_Proj_Mgt\02_Corr\CEDKTDS3EM00_0_0356L.19.docx

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



TABLE OF CONTENTS

EXECUTIVE SUMMARY	1
1. INTRODUCTION	2
2. SUMMARY OF EM&A REQUIREMENTS AND MONITORING RESULTS	4
3. LANDSCAPE AND VISUAL	6
4. WASTE MANAGEMENT	7
5. SITE INSPECTION	8
6. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	10
7. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	12
8. CONCLUSIONS	13

FIGURES

Figure 1	Project General Layout
Figure 2	Air and Noise Monitoring Locations

LIST OF APPENDICES

Appendix A	Construction Programme
Appendix B	Project Organization Chart
Appendix C	Action and Limit Levels for Air Quality and Noise
Appendix D	Graphical Presentation of Monitoring Data
Appendix E	Waste Flow Table
Appendix F	Environmental Mitigation Implementation Schedule (EMIS)

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EXECUTIVE SUMMARY

- i. The Civil Engineering and Development Department HKSAR has appointed Fugro Technical Services Limited (FTS) to undertake the Environmental Team services for the Project and implement the EM&A works.
- ii. This is the eleventh Quarterly EM&A Report presents the environmental monitoring and audit works for the period between 1 September 2018 and 30 November 2018. As informed by the Contractor, major activities in the reporting period included:

September 2018	October 2018	November 2018
<ul style="list-style-type: none">• Excavation and laying of drainage pipe and manhole;• Construction of tunnel box structure;• Excavation and ELS construction.	<ul style="list-style-type: none">• Excavation and laying of drainage pipe and manhole;• Excavation and ELS construction;• Construction of Supporting Underground Structure; and• Construction of District Cooling System.	<ul style="list-style-type: none">• Excavation and laying of drainage pipe and manhole;• Excavation and ELS construction.• Construction of SUS structure; and• Construction of District Cooling System.

Breaches of the Action and Limit Levels

- iii. No Action and Limit Level exceedance for 24-hr TSP and noise was recorded in the reporting period at all monitoring stations.

Complaint, Notification of Summons and Successful Prosecution

- iv. No environmental complaint and no notification of summons and successful prosecution were received in the reporting period.



1. INTRODUCTION

1.1 Background

1.1.1 The Kai Tak Development is located in the south-eastern part of Kowloon Peninsula of the HKSAR, comprising the apron and runway areas of the former Kai Tak Airport and existing waterfront areas at To Kwa Wan, Ma Tau Kok, Kowloon Bay, Kwun Tong and Cha Kwo Ling.

1.1.2 Contract No. KL/2014/03 is the works package to construct an approximately 420m long supporting underground structure (SUS) underneath Shing Cheong Road and Cheung Yip Street. The EM&A programme under this Contract is governed by three EPs (EP-337/2009, EP-339/2009/A and EP-451/2013) and two EM&A Manuals (AEIAR-130/2009 and AEIAR-174/2013). The Works to be executed under this Contract and corresponding EPs include but not be limited to the following main items:

EP-451/2013 – Trunk Road T2

(i) Construction of approximately 420m long supporting underground structure (SUS) including diaphragm walls, barrettes, piled foundation, top and bottom slabs, end wall and adits underneath Shing Cheong Road and Cheung Yip Street;

EP-337/2009 – New Distributor Roads Serving the Planned Kai Tak Development

- (ii) Widening and re-alignment of Cheung Yip Street of approximately 330m long and associated footpaths;
- (iii) Demolition, reconstruction and widening of Shing Cheong Road of approximately 410m long and associated footpaths;
- (iv) Construction of drainage outfall and modification of existing seawall;
- (v) Construction of ancillary works including surface drainage, sewerage, water, fire fighting, street lighting, street furniture, road marking, road signage, utilities and services, irrigation and landscape works.

EP-339/2009/A – Decommissioning of the Remaining Parts (Ex-GFS Building, Radar Station and Hong Kong Aviation Club) of the former Kai Tak Airport

(vi) Demolition of RADAR Tower and guard house;

Other works not covered by any EP

- (vii) Construction of two subways between Phase II of New Acute Hospital (Site A) and Hong Kong Children's Hospital (Site C), and between Phase I of New Acute Hospital (Site B) and Site C;
- (viii) Construction of District Cooling System (DCS) along Cheung Yip Street and Shing Cheong Road

1.1.3 The location and boundary of the site is shown in **Figure 1**.

1.1.4 This Quarterly EM&A report is required under Section 16.1.2 and 16.7.1 of the EM&A Manual AEIAR-130/2009. It is to report the results and findings of the EM&A programme required in the EM&A Manual.

1.1.5 This is the eleventh Quarterly EM&A Report which summaries the impact monitoring results and audit findings for the Project within the period between 1 September 2018 and 30 November 2018.



1.2 Project Organization

1.2.1 The project proponent was the Civil Engineering and Development Department, HKSAR (CEDD). Hyder Meinhardt Joint Venture (HMJV) was commissioned by CEDD as the Engineer for the Project. Ramboll Hong Kong Limited was commissioned as the Independent Environmental Checker (IEC). China Road and Bridge Corporation (Hong Kong) (CRBC) was appointed as the main contractor for the construction works under the contract KL/2014/03. Fugro Technical Services Limited (FTS) was appointed as the Environmental Team (ET) by CEDD to implement the EM&A programme for the Project.

1.2.2 The organization structure is shown in **Appendix B**. The key personnel contact names and numbers for the Project are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Project Proponent (CEDD)	Co-ordinator	Ms. Amy Chu	3106 3172	2369 4980
Engineer's Representative (HMJV)	Chief Resident Engineer	Mr. W. K., Chris Wong	3742 3803	3742 3899
IEC (Ramboll Hong Kong Limited)	Independent Environmental Checker	Mr. F. C. Tsang	3465 2851	3465 2899
Main Contractor (CRBC)	Site Agent	Mr. Yau Kwok Kiu, Dickey	5699 4503	2283 1689
	Environmental Officer	Mr. Calvin So	9724 6254	2283 1689
ET (FTS)	Environmental Team Leader	Mr. Colin Yung	3565 4114	3565 4160

1.3 Construction Programme and Activities

1.3.1 The construction of the Project commenced in February 2016 and is expected to complete in 2020. The construction programme is shown in **Appendix A**. A summary of the major construction activities undertaken in the reporting period were:

September 2018	October 2018	November 2018
<ul style="list-style-type: none"> • Excavation and laying of drainage pipe and manhole; • Construction of tunnel box structure; • Excavation and ELS construction. 	<ul style="list-style-type: none"> • Excavation and laying of drainage pipe and manhole; • Excavation and ELS construction; • Construction of Supporting Underground Structure; and • Construction of District Cooling System. 	<ul style="list-style-type: none"> • Excavation and laying of drainage pipe and manhole; • Excavation and ELS construction. • Construction of SUS structure; and • Construction of District Cooling System.



2. SUMMARY OF EM&A REQUIREMENTS AND MONITORING RESULTS

2.1 Monitoring Requirement

In accordance with the approved EM&A Manuals, 24-hour Total Suspended Particulates (TSP) level and Leq (30min) at the designated monitoring stations is required. Impact 24-hour TSP monitoring should be carried out at least once every 6 days. In case of complaints, 1-hour TSP monitoring should be carried out at least 3 times per 6 days when the highest dust impacts are likely to occur. Leq (30min) monitoring is conducted for at least once a week during the construction phase between 0700 and 1900 on normal weekdays. The Action and Limit Levels of the air quality monitoring and noise monitoring are given in **Appendix C**

2.2 Monitoring Locations

- 2.2.1 According to the EM&A Manual, three monitoring locations for air quality monitoring and noise monitoring, namely KTD1, KTD2 and KER1, are covered by this Contract within the South Apron Area of Former Kai Tak Airport. The other two air quality monitoring locations and two noise monitoring locations which are identified in Cha Kwo Ling area, are farther than 500m and 300m away from the site boundary respectively and thus not covered by this Contract. The monitoring works in Cha Kwo Ling area are covered by other Contract(s) respectively.
- 2.2.2 According to the approved alternative baseline air quality and noise monitoring locations (EPD reference: () in EP2/K19/A/21 pt.5), the original monitoring locations (KTD1, KTD2 and KER1) are proposed to be replaced by alternative monitoring locations (KTD1a, KTD2a and KER1a).
- 2.2.3 According to the approved relocation of monitoring location KER1a (EPD reference: () in EP2/K19/A/21 pt.5), the monitoring location KER1a are proposed to be relocated by alternative monitoring locations KER1b.
- 2.2.4 According to the approved relocation of monitoring location KTD2a (EPD reference: () in EP2/K19/A/21 Pt.6), the monitoring location KTD2a are proposed to be relocated by alternative monitoring locations KTD2b.
- 2.2.5 The most updated locations are summarized in **Table 2.1** and shown in **Figure 2**.

Table 2.1 Location of Air Quality Monitoring and Noise Monitoring Station

Monitoring Station	Location
KTD1a	Centre of Excellence in Paediatrics (Children's Hospital)
KTD2b	G/IC Zone next to Kwun Tong Bypass (Next to the site of the New Acute Hospital)
KER1b	Site Boundary at Cheung Yip Street

2.3 Results and Observations

- 2.3.1 No Action and Limit Level exceedance for 24-hr TSP was recorded in the reporting period at all monitoring stations.
- 2.3.2 No Action / Limit Level exceedance for construction noise was recorded in the reporting period at all monitoring stations.
- 2.3.3 No raining and wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation.



2.3.4 During the reporting period, major dust sources including loading and unloading of C&D wastes, vehicles movement were observed in the site. Major noise sources including noise emission from plant & PME and some other construction activities, travel of vehicles, loading and unloading of C&D waste were observed in the site. Non-project related construction activities at the nearby construction site and road traffic along Shing Cheong Road, Cheung Yip Street and the Kwun Tong By-pass were observed. The above factors may affect the monitoring results.

2.3.5 Graphical presentation of the monitoring data in the reporting period is presented in **Appendix D**.

2.4 Comparison of Monitoring Results with EIA Predictions

2.4.1 The monitoring data was compared with the EIA predictions as summarized in **Table 2.2** and **Table 2.3**.

Table 2.2 Comparison of 24-hr TSP data with EIA predictions

Monitoring Station	Receiver Reference	Predicted Maximum 24-hour TSP Concentration (µg/m ³)	24-hour TSP concentration in Reporting Period (µg/ m ³)			Average 24-hour TSP concentration in Reporting Period (µg/ m ³)		
			Sep 2018	Oct 2018	Nov 2018	Sep 2018	Oct 2018	Nov 2018
KTD1a	KTD3	126	26 - 68	36 - 81	34 - 132	46	58	77
KTD2b	-	-	39 - 61	27 - 89	50 - 121	51	58	86
KER1b	KTD6	169	51 - 71	33 - 143	37 - 127	62	66	68

Note:

For KTD2b, there was no receiver reference in the EIA report, EIAR-174/2013.

Predicted Maximum TSP Concentration extracted from Table 4.14 of EIA Report, EIAR-174/2013.

Table 2.3 Comparison of Noise Monitoring data with EIA predictions

Monitoring Station	Receiver Reference	Maximum Predicted Mitigated Construction Noise Level, dB(A)	Leq (30min) dB(A) in Reporting Period		
			Sep 2018	Oct 2018	Nov 2018
KTD1a	KTD1	74	69 - 72	65 - 74	65 - 74
KTD2b	KTD2	75	59 - 63	63 - 72	65 - 71
KER1b	KER1	75	66 - 70	64 - 71	64 - 72

Note:

Maximum Predicted Mitigated Construction Noise Level extracted from Table 5.13 of EIA Report, EIAR-174/2013.

2.4.2 The 24-hour TSP monitoring results at KER1b in the reporting months did not exceed the Predicted Maximum 24-hour TSP Concentration in the approved Environmental Impact Assessment (EIA) Report and no Action / Limit Level exceedance was recorded in the reporting period.

2.4.3 The 24-hour TSP monitoring result of KTD1a on 10 November 2018 exceeded the prediction in the approved EIA report. No project related dust source was observed during the site monitoring. The discrepancy between the 24-hour TSP concentration and EIA Prediction in KTD1a is considered due to dust source from the non-project related construction activities near the monitoring station and the road travel along Shing Fung Road.

2.4.4 The noise monitoring results in the reporting months did not exceed the Maximum Predicted Mitigated Construction Noise Level in the approved Environmental Impact Assessment (EIA) Report and no Action / Limit Level exceedance was recorded in the reporting period.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



3. LANDSCAPE AND VISUAL

3.1 Results and Observations

- 3.1.1 To monitor and audit the implementation of landscape and visual mitigation measures, 13 weekly Landscape and Visual Site audits were carried out and 6 of them were carried out by a Registered Landscape Architect. The weekly Landscape and Visual Impact reports were counter-signed by IEC as according to the requirement of EM&A Manual (AEIAR-130/2009).
- 3.1.2 During the site inspection on 26 September 2018, contractor was reminded to check and properly cover all stockpiling after typhoon.
- 3.1.3 During the site audit on 24 October 2018, contractor was reminded that the backfilling material in Zone 1 should be properly covered.
- 3.1.4 No non-compliance was recorded in the weekly Landscape and Visual Site audits in the reporting period.
- 3.1.5 Observations and recommendations during site audits are summarized in **Table 5.1**.



4. WASTE MANAGEMENT

4.1 Results and Observations

- 4.1.1 C&D materials and wastes sorting were carried out on site. Receptacles were available for C&D wastes and general refuse collection.
- 4.1.2 The amount of wastes generated by the site activities in the reporting period is shown in **Appendix E**.
- 4.1.3 The Contractor is advised to properly maintain on site C&D materials and wastes collection, sorting and recording system and maximize reuse / recycle of C&D materials and wastes. The Contractor is reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.
- 4.1.4 The Contractor is reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.



5. SITE INSPECTION

5.1 Site Inspection

- 5.1.1 Site inspections were carried out weekly to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. A summary of the mitigation measures implementation schedule is provided in **Appendix F**.
- 5.1.2 In the reporting quarter, 13 site inspections were carried out. 6 of them were the joint inspections with the IEC, ER, the Contractor and the ET.
- 5.1.3 No outstanding issues were reported during the reporting period.
- 5.1.4 All the follow-up actions requested by Contractor’s ET and IEC during the site inspections were undertaken as reported by the Contractor and confirmed in the following weekly site inspection conducted during the reporting month.
- 5.1.5 Details of observations recorded during the site inspections are presented in **Table 5.1**.

Table 5.1 Observations and Recommendations of Site Audit

Parameters	Date	Observations and Recommendations	Follow-up
Air Quality	5 September 2018	Observation: Contractor should water the dusty material regularly. (Zone 1)	The item was rectified by the Contractor and inspected on 12 September 2018.
	26 September 2018	Reminder: Contractor was reminded to check the sheeting of stockpile after typhoon (Zone 1).	NA
	24 October 2018	Reminder: Backfilling material in Zone 1 should be properly covered.	NA
	14 November 2018	Observation: Dust was observed on the ground. Contractor should clean up the dust. (Portion I)	The item was rectified by the Contractor and inspected on 21 November 2018.
Noise	7 November 2018	Reminder: Contractor was reminded to use acoustic fabric during breaking. (zone 3)	NA
	21 November 2018	Observation: Acoustic fabric should be used during breaking to reduce noise. (zone 3)	The item was rectified by the Contractor and inspected on 28 November 2018.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Parameters	Date	Observations and Recommendations	Follow-up
Water Quality	19 September 2018	Reminder: Contractor was reminded to clear the sediments accumulated in sedimentation tank regularly. (Zone 1)	NA
	21 November 2018	Reminder: Contractor was reminded to clear the sediments in the sedimentation tank regularly. (zone 1)	NA
	28 November 2018	Reminder: Broken water pipe shall be repaired as soon as possible. (zone 1)	NA
Chemical and Waste Management	26 September 2018	Reminder: Contractor was reminded to place chemical containers on drip tray (Zone 3).	NA
	3 October 2018	Observation: Chemical containers were not placed on drip tray (Zone 3). Contractor should provide drip tray to store chemical containers properly.	The item was rectified by the Contractor and inspected on 10 October 2018.
Land Contamination	NA		
Landscape and Visual Impact	26 September 2018	Reminder: Contractor was reminded to check the sheeting of stockpile after typhoon (Zone 1).	NA
	24 October 2018	Reminder: Backfilling material in Zone 1 should be properly covered.	NA
General	NA		



6. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

6.1 Environmental Exceedance

6.1.1 No Action and Limit Level exceedance for 24-hr TSP and noise was recorded in the reporting period at all monitoring stations. Number of exceedance in the reporting period was summarized in **Table 6.1**.

Table 6.1 Summary of Exceedance in Reporting Period

Monitoring Station		Number of exceedance in the reporting period						Total
		24hr TSP µg/m ³			Leq (30min) dB(A)			
		Sep 2018	Oct 2018	Nov 2018	Sep 2018	Oct 2018	Nov 2018	
KTD1a	AL	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0
KTD2b	AL	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0
KER1b	AL	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0
Total	AL	0	0	0	0	0	0	0
	LL	0	0	0	0	0	0	0

6.2 Complaints, Notification of Summons and Prosecution

6.2.1 No inspection notice, notification of summons or prosecution was received in this reporting period. Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Table 6.2, 6.3 and 6.4**.

Table 6.2 Environmental Complaints Log

Reference No.	Date of Complaint Received	Received From	Received By	Nature of Complaint	Date of Investigation	Outcome	Date of Reply
20161207_complaint_c	7 Dec 2016	EPD	Andy Choy (CRBC)	Air	13 Feb 2017	Project-related	13 Feb 2017
20170209_complaint_c	9 Feb 2017	EPD	Andy Choy (CRBC)	Air	22 Feb 2017	Not Project-related	7 Mar 2017
20170502_complaint_c	2 May 2017	CEDD	Andy Choy (CRBC)	Noise	4 May 2017	Not Valid	22 May 2017
20170716_complaint_a	16 Jul 2017	CEDD	HMJV	Water Quality	4 Aug 2017	Not Project-related	4 Aug 2017
20180530_complaint	30 May 2018	EPD	CRBC	Air	9 June 2018	Not Valid	20 Jun 2018



Table 6.3 Cumulative Statistics on Complaints

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints in the Reporting Period			Cumulative Project-to-Date
		September 2018	October 2018	November 2018	
Air	3	0	0	0	3
Noise	1	0	0	0	1
Water	1	0	0	0	1
Waste	0	0	0	0	0
Total	0	0	0	0	0

Table 6.4 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Complaints This Reporting Period			Cumulative Project-to-Date
		September 2018	October 2018	November 2018	
Air	0	0	0	0	0
Noise	0	0	0	0	0
Water	0	0	0	0	0
Waste	0	0	0	0	0
Total	0	0	0	0	0

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



7. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

7.1 Implementation Status

7.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting period is summarized in **Appendix F**.



8. CONCLUSIONS

- 8.1.1 No Action and Limit Level exceedance for 24-hr TSP and noise was recorded in the reporting period at all monitoring stations.
- 8.1.2 No complaint of air quality was received. Therefore, no impact 1-hour TSP monitoring was conducted in the reporting period.
- 8.1.3 13 weekly environmental site inspections were carried out in the reporting period. Recommendations on mitigation measures on air quality, noise quality, water quality, chemical and waste management, landscape and visual impact were given to the Contractor for remediating the deficiencies identified during the site inspections.
- 8.1.4 13 weekly Landscape and Visual Site audits were carried out on in the reporting period and 6 of them were carried out by a Registered Landscape Architect in the reporting period. The weekly Landscape and Visual Impact reports were counter-signed by IEC as according to the requirement of EM&A Manual (AEIAR-130/2009). No non-compliance was recorded in the weekly Landscape and Visual Site audits in the reporting period.
- 8.1.5 Referring to the Contractor's information, no notification of summons and successful prosecution was received in the reporting period.

8.2 Comment and Recommendations

- 8.2.1 The recommended environmental mitigation measures, as proposed in the EIA reports and EM&A Manuals shall be effectively implemented to minimize the potential environmental impacts from the Project. The EM&A programme would effectively monitor the environmental impacts generated from the construction activities and ensure the proper implementation of mitigation measures.
- 8.2.2 According to the environmental audit performed in the reporting period, the following recommendations were made:

Air Quality Impact

- Watering on dusty materials should be carried out regularly for dust suppression.
- The sheeting of stockpile should be check after typhoon weather.
- Backfilling materials should be properly covered.
- Dust was observed on the ground. Contractor should clean up the dust.

Construction Noise Impact

- Contractor was reminded to use acoustic fabric during breaking.

Water Quality Impact

- Sediments inside the sedimentation tank should be removed regularly.
- Contractor was reminded to clear the sediments in the sedimentation tank regularly.
- Broken water pipe shall be repaired as soon as possible.

Chemical and Waste Management

- Chemical containers should be placed in drip tray.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Land Contamination

- No specific observation was identified in the reporting period.

Landscape and Visual Impact

- Check and properly cover all stockpiling after typhoon.
- Backfilling materials should be properly covered.

General Condition

- No specific observation was identified in the reporting period.

Permit / Licenses

- No specific observation was identified in the reporting period.


FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 1 Project General Layout

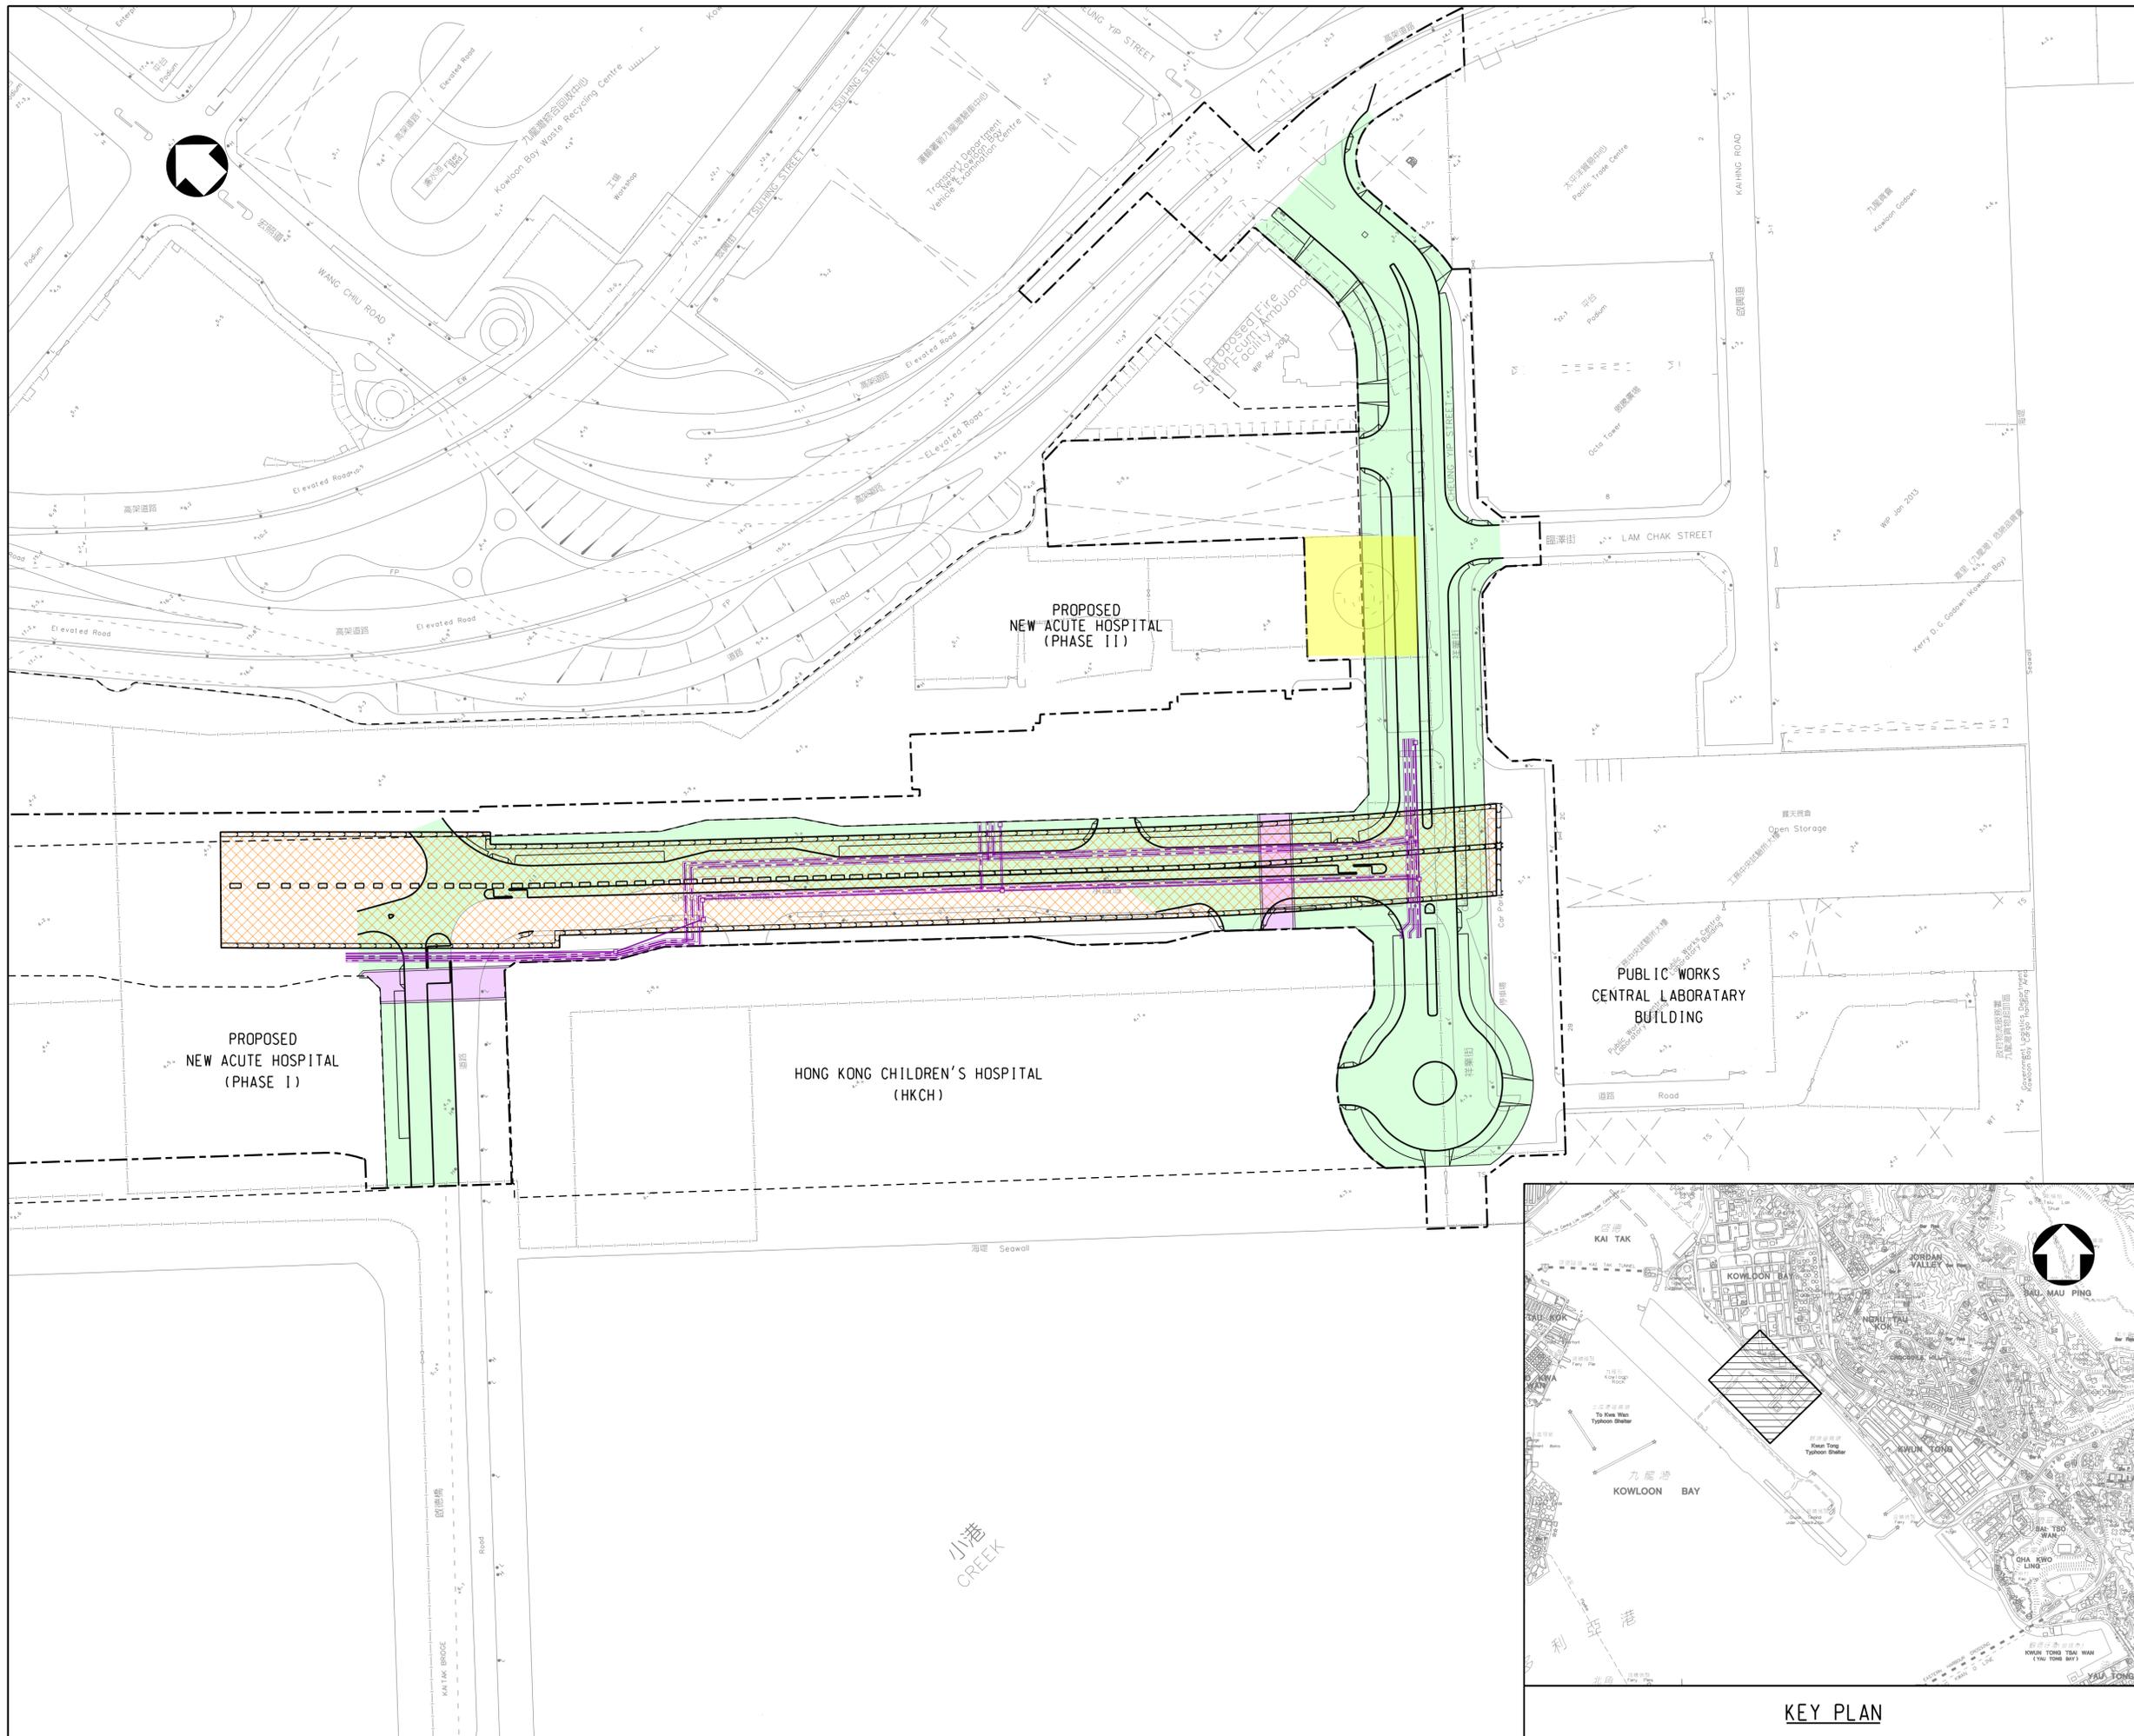

- LEGENDS:**
- SITE BOUNDARY
 - HOSPITAL SITE BOUNDARY
 - PROPOSED SUPPORTING UNDERGROUND STRUCTURE
 - PROPOSED SUBWAYS
 - PROPOSED ROADWORKS
 - PROPOSED DISTRICT COOLING SYSTEM
 - DEMOLITION OF RADAR TOWER

Rev.	Date	Drawn	Description	Checked	Approved



CLIENT



土木工程拓展署
Civil Engineering and
Development Department
九龍拓展處
Kowloon Development Office

PROJECT

CONTRACT NO. KL/2014/03
KAI TAK DEVELOPMENT - STAGE 3
INFRASTRUCTURE WORKS FOR
DEVELOPMENTS AT THE SOUTHERN PART OF
THE FORMER RUNWAY


TITLE

GENERAL LAYOUT PLAN

DESIGNED		ENG. CHECK	
DRAWN		COORDINATION	
DWG. CHECK		APPROVED	
SCALE AT A1	STATUS	REV	
1 : 1000		A	

Drawing No. **FIGURE 1.0**

© Copyright reserved

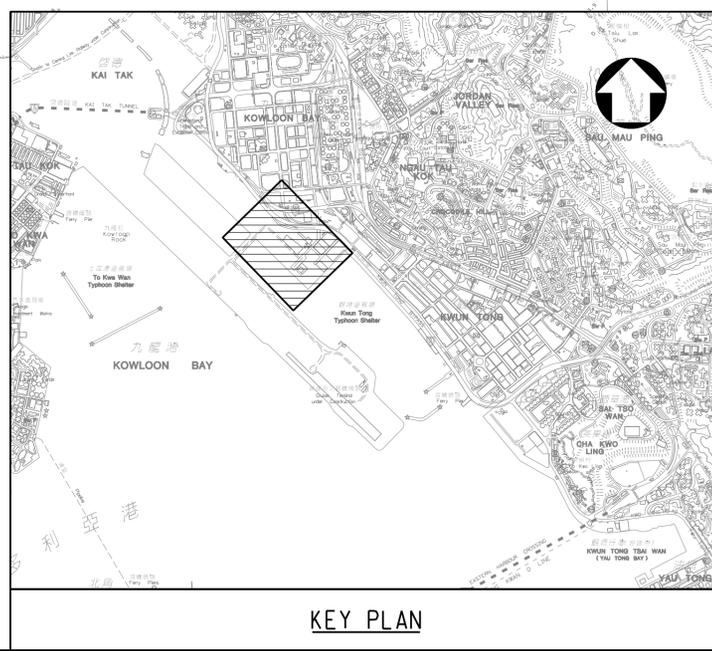

KEY PLAN

PRINTED BY: kitchan 18/2/2015 13:00:43
FILENAME: K:\91164 Trunk Road T2\Tender Drawing (Contract I)\Figure 1.dgn

FUGRO TECHNICAL SERVICES LIMITED


Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Figure 2

Air and Noise Monitoring Locations

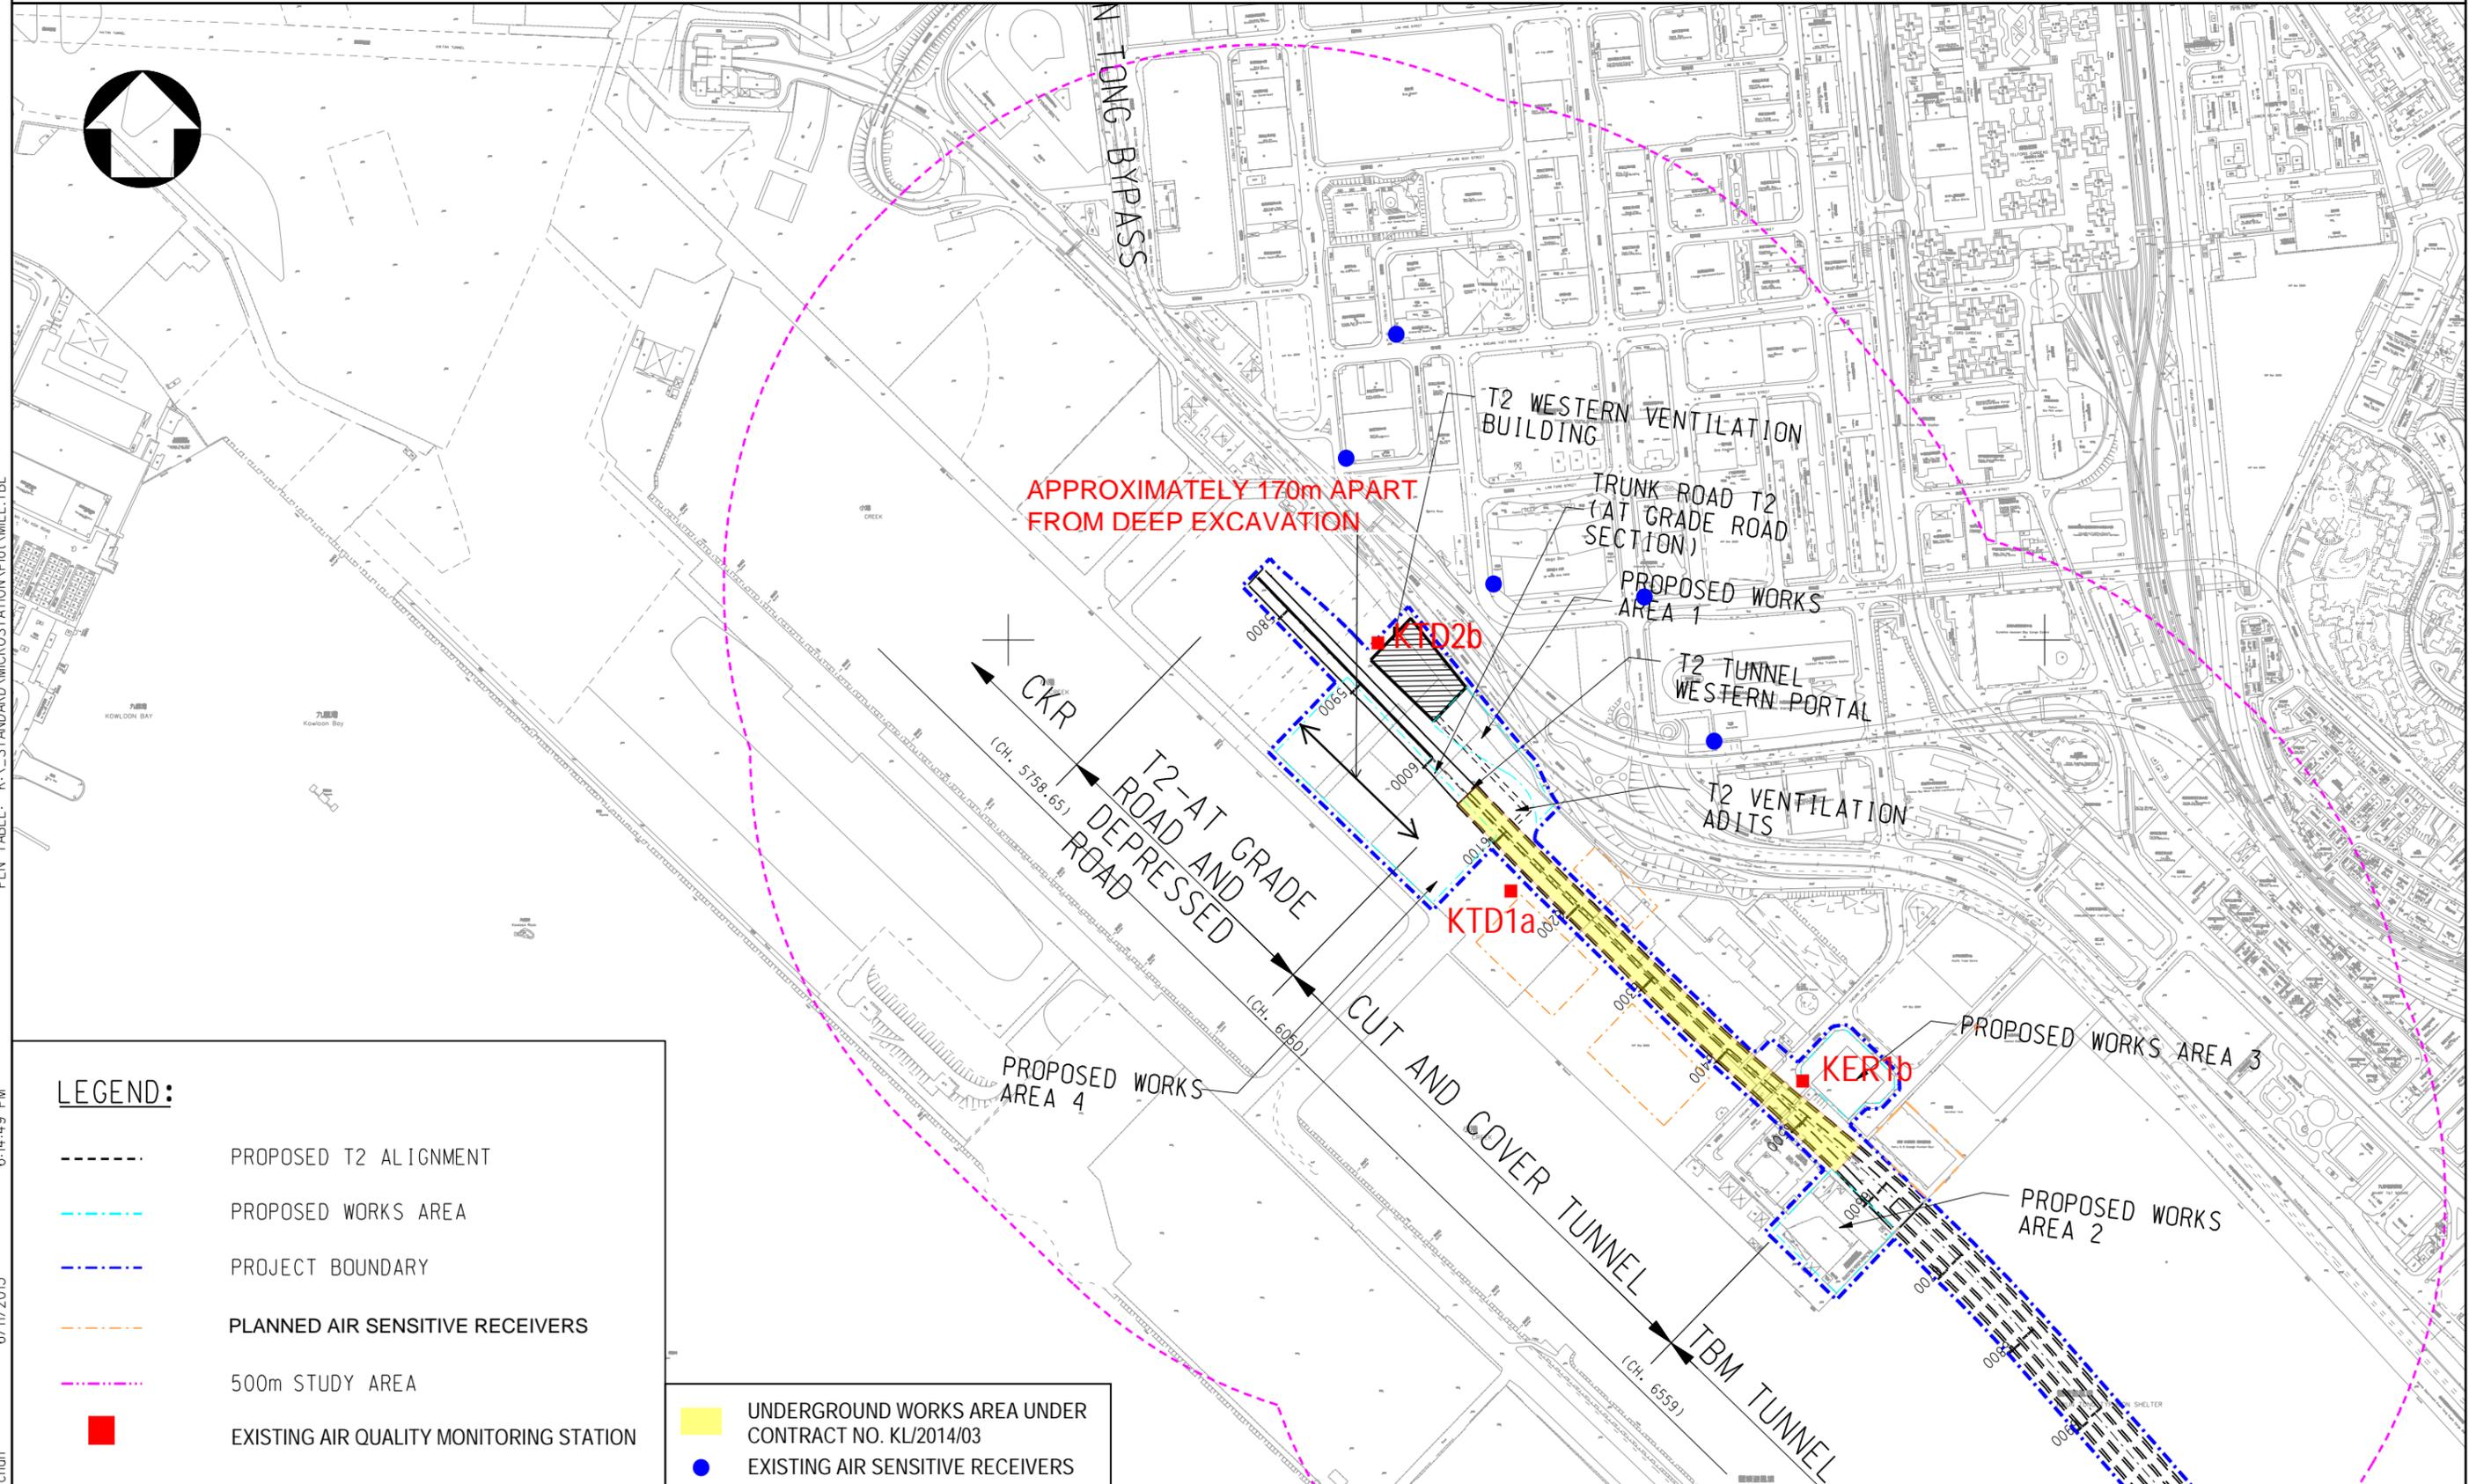

LEGEND:

- - - - PROPOSED T2 ALIGNMENT
- - - - PROPOSED WORKS AREA
- - - - PROJECT BOUNDARY
- - - - PLANNED AIR SENSITIVE RECEIVERS
- - - - 500m STUDY AREA
- EXISTING AIR QUALITY MONITORING STATION
- UNDERGROUND WORKS AREA UNDER CONTRACT NO. KL/2014/03
- EXISTING AIR SENSITIVE RECEIVERS

Drawing title

IDENTIFIED DUST MONITORING STATIONS AT SOUTH APRON OF FORMER KAI TAK AIRPORT

Original Size

A3

Scale 1 : 6000

Date 30/01/2012

File name


© Copyright reserved

Drawing No.

FIGURE 2.1a(revised)

Rev.

--

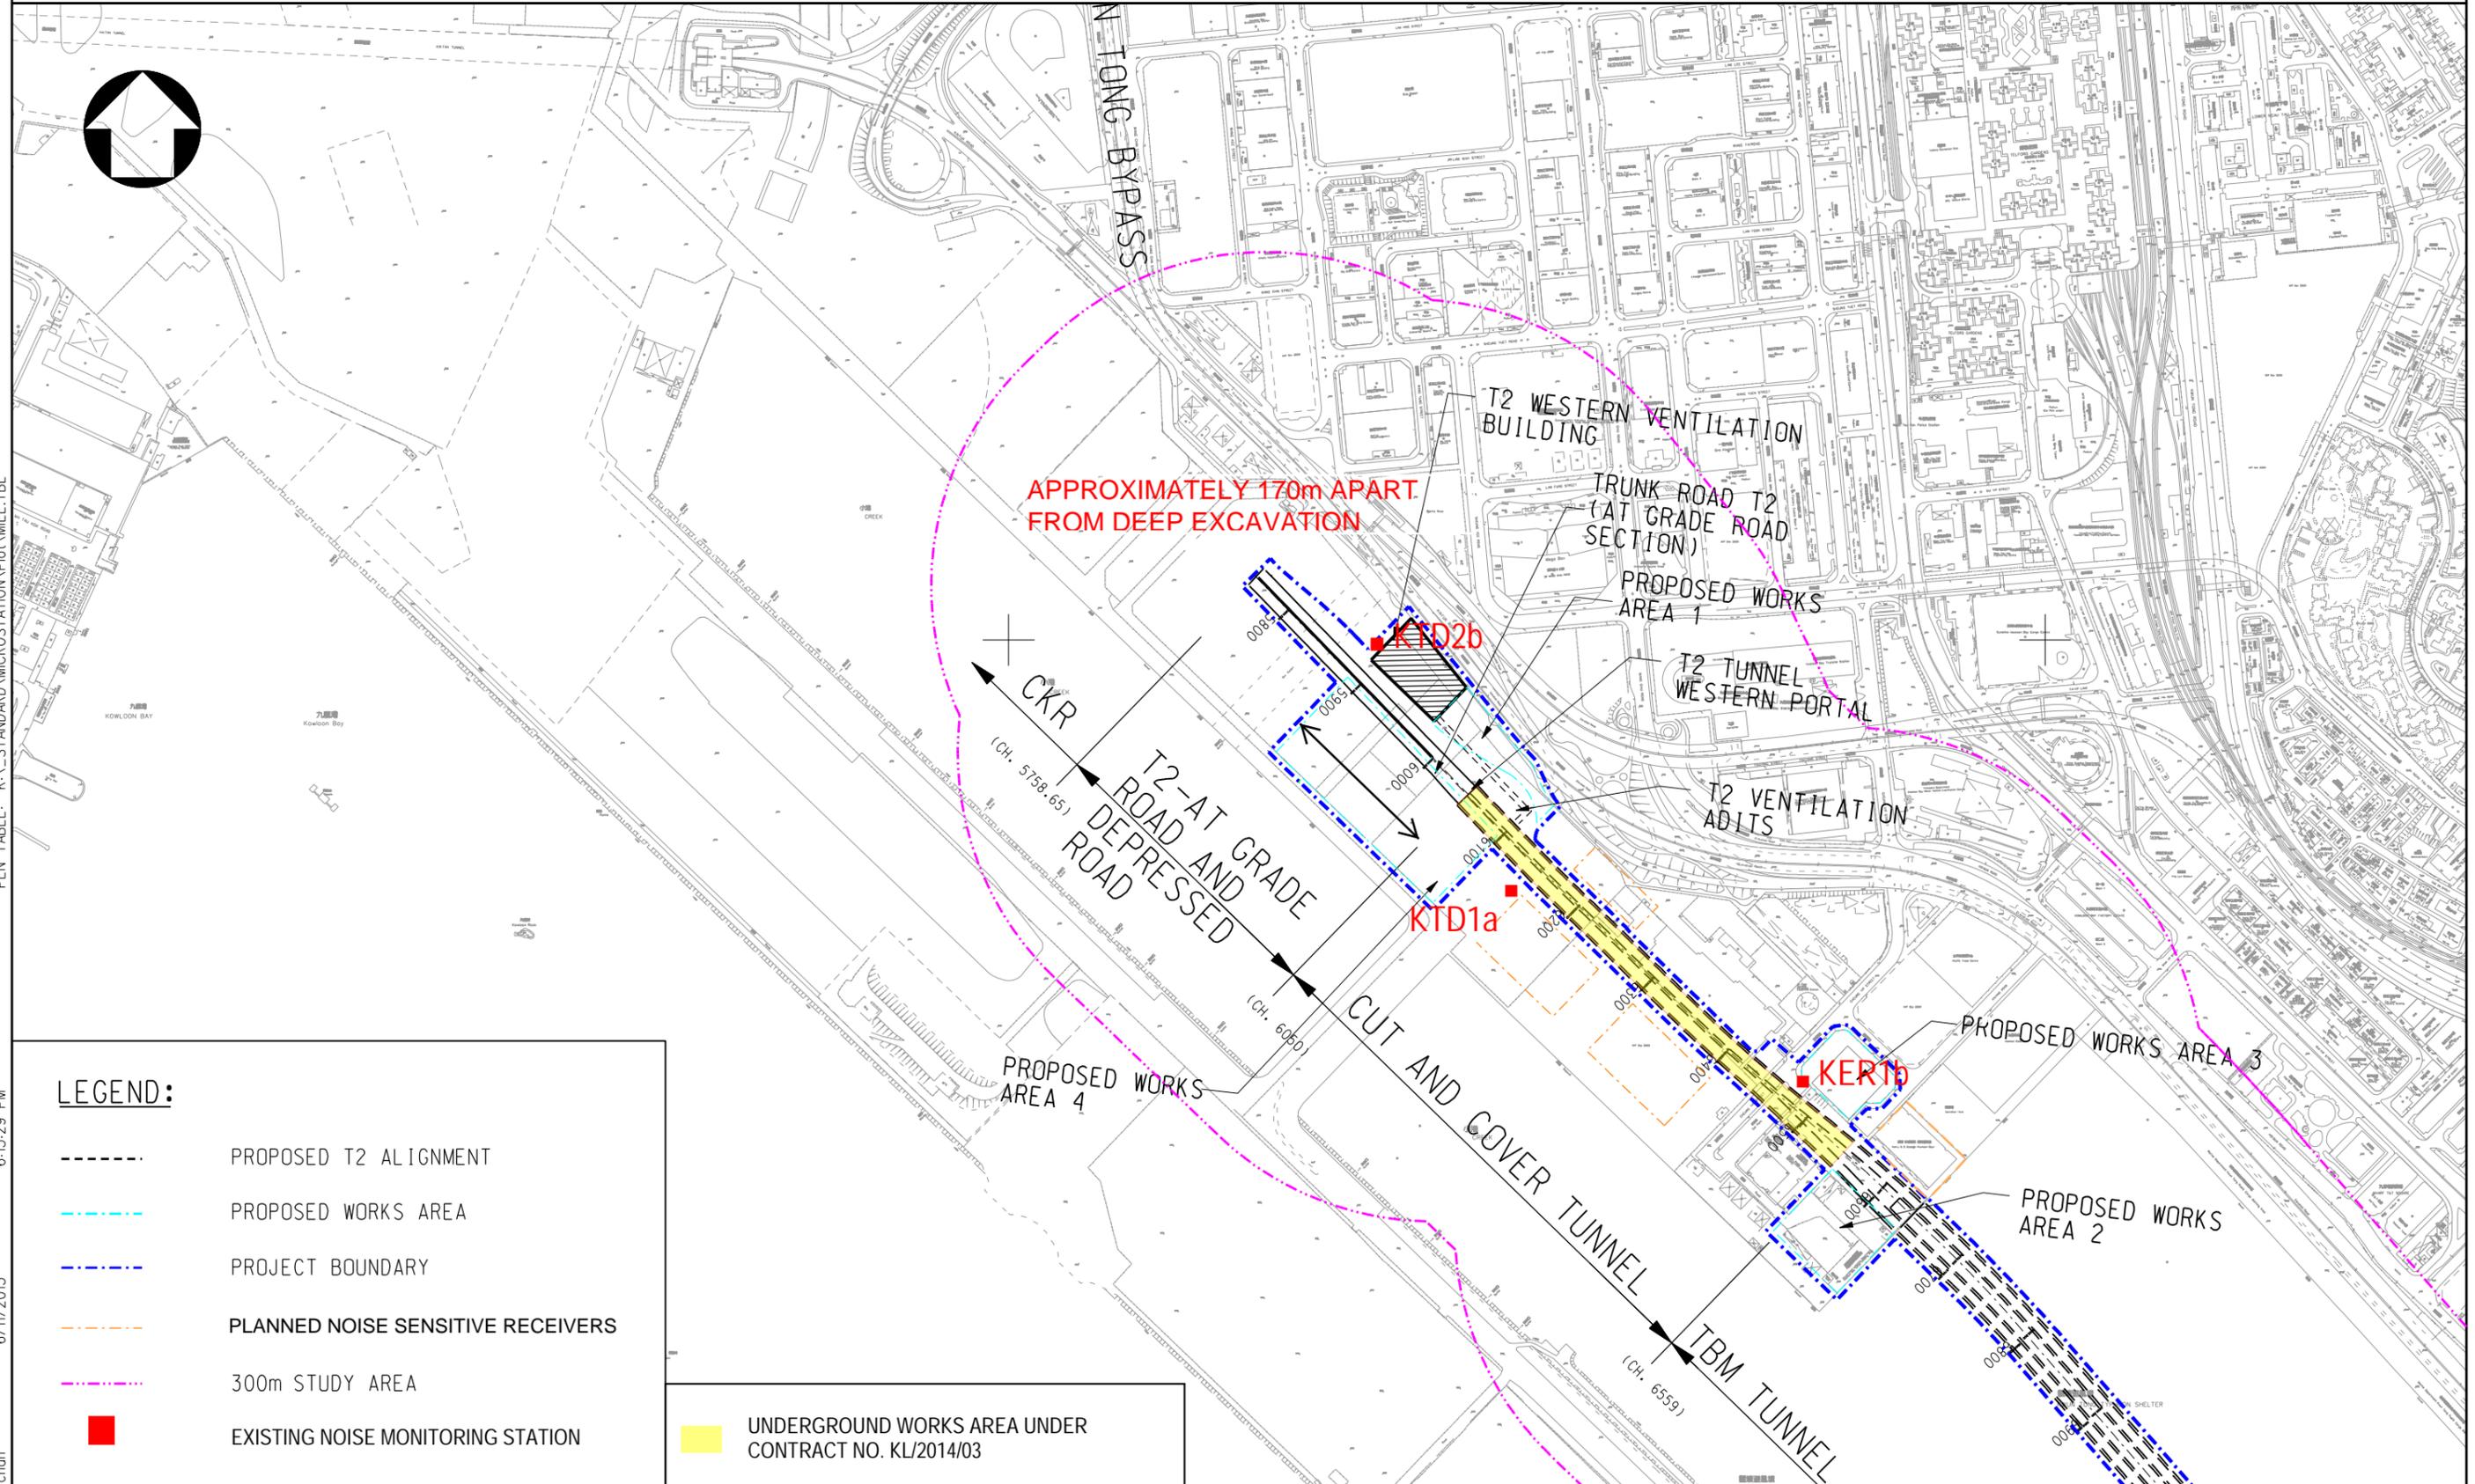

LEGEND:

-  PROPOSED T2 ALIGNMENT
-  PROPOSED WORKS AREA
-  PROJECT BOUNDARY
-  PLANNED NOISE SENSITIVE RECEIVERS
-  300m STUDY AREA
-  EXISTING NOISE MONITORING STATION

 UNDERGROUND WORKS AREA UNDER CONTRACT NO. KL/2014/03

Drawing title

IDENTIFIED NOISE MONITORING STATIONS AT
 SOUTH APRON OF FORMER KAI TAK AIRPORT

Original Size

A3

Scale 1 : 6000

Date 30/01/2012

File name

© Copyright reserved

Drawing No.

FIGURE 2.2 a (revised)

Rev.

--

Rev.	Description	Date

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix A

Construction Programme

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September				October				November				Index
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	
SUS updated + SCR for SUS calendar days Zone 3 stage 2 Time Compression delete Section 1 CSR																						
Project Key Dates																						
Site Handover Date																						
K-PK-SHD-1100	Portion B	0		31-Aug-18*																		
K-PK-SHD-1200	Portion B1	0		31-Aug-18*																		
K-PK-SHD-1500	Portion E	0		31-Aug-18*																		
K-PK-SHD-1600	Portion F	0		06-Sep-18*																		
K-PK-SHD-1700	Portion H	0		31-Aug-18*																		
K-PK-SHD-2300	Portion P	0		31-Aug-18*																		
K-PK-SHD-2500	Portion R	0		31-Aug-18*																		
General Submission																						
Major Temporary Works Design																						
K-PA-GSP-6840	ELS design for construction of subway A (Bay 1&5)	32	28-Feb-18 A	01-Oct-18																		
K-PA-GSP-7010	ELS design for construction of DCS - Stage 2	35	13-Sep-18	17-Oct-18																		
Major Construction Works Method Statement																						
K-PA-GSP-7455	Engineer's comments and approval	8	23-Oct-17 A	07-Sep-18																		
K-PA-GSP-7460	Method statement for Construction of subway A (Bay 1&5)	28	31-Aug-18	27-Sep-18																		
K-PA-GSP-7465	Engineer's comments and approval	28	28-Sep-18	25-Oct-18																		
Temporary Traffic Management																						
Temp Traffic Arrangement Schemes																						
K-PA-TTA-8950	Submission and approval of TTA schemes-TTA stage 4 for re-construction of Shing Cheong Road	90	31-Aug-18	28-Nov-18																		
Implementation of Temporary Traffic Arrangement																						
K-PA-TTA-4400	TTA stage 4 - Road diversion for Handover of Portion N	0		29-Nov-18																		
Materials Procurement (Major Materials)																						
Water Works																						
K-PA-MP-1050	Manufacturing & delivery to site	81	31-Aug-18	19-Nov-18																		
ELS struct / waling																						
K-PA-MP-1150	Manufacturing & delivery to site	9	10-Jun-16 A	08-Sep-18																		
Chilled Water Pipes - DCS																						
K-PA-MP-1350	Manufacturing & delivery to site	185	06-Feb-17 A	03-Mar-19																		
Preliminaries																						

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September					October					November				
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	
K-DR-PRE-1800	Submission of time-lapsed photographs and video	459	20-Feb-16 A	03-Dec-19																				
Barge Loading Facilities																								
K-DR-PRE-1480	Operation of temporary barging point	80	21-Jun-17 A	05-Dec-18																				
Instrumentation and Monitoring																								
Tilt Monitoring Tile Plates																								
K-IM-TMT-1000	Tilt Monitoring near PWCL	166	25-Apr-16 A	12-Feb-19																				
Section 1 of the Works-Remainder of the Works																								
Roadwork and Drainage Works																								
Road D4-3 (Ching Shung Road)																								
<i>Zone 2 R & D Works (Stage 1) CH410-CH340</i>																								
SCR1000	SUS	0	06-Sep-18*							◆ SUS														
SCR1020	Trim westside Dwall	0		07-Nov-18																◆ Trim westside Dwall				
SCR1040	DN250 sewerage (HKCH - FMH24-1E - FMH24-1G)	18	17-Nov-18*	07-Dec-18																				
SCR1120	DN250 sewerage (FMH24-1G - FMH24-1F)	3	07-Nov-18*	09-Nov-18																				
SCR1130	DN350x3 Rising main (from Subway B - FMH24-1B) phase 1 near EB Dwall	6	10-Nov-18*	16-Nov-18																				
SCR1140	Proposed drainage M112 to M110 (eastbound)	18	10-Nov-18*	30-Nov-18																				
SCR1150	Lay fresh watermain (eastbound)	24	17-Nov-18*	14-Dec-18																				
SCR1210	Construct and divert temporary footpath	12	17-Nov-18*	30-Nov-18																				
<i>Shing Fung Road R & D Works (Stage 1)</i>																								
SCR1260	DCS at Zone 2 Bay 1 (CH20 - CH35)	62	15-Sep-18*	29-Nov-18																				
<i>Zone 3 R & D Works (Stage 1) CH340 to CH270 - For shifting of gate no. 1</i>																								
SCR1490	Demolition of Dwall (105mL) for Bay 5 - 7	0		18-Oct-18																◆ Demolition of Dwall (105mL) for Bay 5 - 7				
SCR1510	Drainage (westbound) SMH14-9A to SMH14-8	12	26-Oct-18*	08-Nov-18																				
SCR1520	Gully Construction	6	09-Nov-18*	15-Nov-18																				
SCR1530	Lay 300mm dia. salt watermain (westbound)	6	16-Nov-18*	22-Nov-18																				
SCR1540	Removal of temporary crane platform	6	23-Nov-18*	29-Nov-18																				
SCR1550	Proposed drainage M109 to M108 (eastbound)	18	04-Oct-18*	25-Oct-18																				
SCR1560	Proposed drainage M109c to M109 (eastbound)	12	26-Oct-18*	08-Nov-18																				
SCR1570	Gully Construction	6	09-Nov-18*	15-Nov-18																				
SCR1580	Proposed drainage M108a to M108b (eastbound)	11	26-Oct-18*	07-Nov-18																				
SCR1590	Gully Construction	6	08-Nov-18*	14-Nov-18																				

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September				October				November				Number			
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18		25	02	
SCR1600	Lay 600mm dia. fresh watermain (eastbound)	6	15-Nov-18*	21-Nov-18																					Lay 600mm dia. fresh watermain (eastbound)
SCR1610	Construct temporary access road (permanent pavement) to gate no. 1 and divert access road	30	23-Nov-18*	29-Dec-18																					
Cheung Yip Street Cul de Sac																									
SCR2182	Storm drainage M103 to M105/M104 to M201/M104a to M104	48	20-Nov-18*	17-Jan-19																					
SCR2183	Trim formation, lay subbase and kerb (half of cul de sac)	18	20-Nov-18	10-Dec-18																					
Road D4-4 (Cheung Yip Street)																									
CH220 - CH420 Northbound																									
Temporary Traffic Arrangement																									
K-01-RWS-9450	Implementation of TTA stage 3 - phase 1	0	31-Jul-18 A																						Implementation of TTA stage 3 - phase 1
CH220 - CH420 Southbound																									
Part 1																									
Sewerage Works																									
K-01-RWS-9471	Excavation of Sewerage Pipe and FMH23-16A to FMH23-17A (Part 2)	0	03-Aug-18 A	29-Aug-18 A																					Excavation of Sewerage Pipe and FMH23-16A to FMH23-17A (Part 2)
K-01-RWS-9472	Laying Sewerage Pipe and Construction of FMH23-16A /FMH23-17A (Part 2)	12	30-Aug-18 A	13-Sep-18																					Laying Sewerage Pipe and Construction of FMH23-16A /FMH23-17A (Part 2)
K-01-RWS-9473	Backfilling Sewerage Pipe and FMH23-16A /FMH23-17A (Part 2)	12	14-Sep-18	28-Sep-18																					Backfilling Sewerage Pipe and FMH23-16A /FMH23-17A (Part 2)
K-01-RWS-9474	Excavation of Sewerage Pipe FMH23-15A (Part 2)	0	03-Aug-18 A	17-Aug-18 A																					Excavation of Sewerage Pipe FMH23-15A (Part 2)
K-01-RWS-9475	Laying Sewerage Pipe aFMH23-15A (Part 2)	12	31-Aug-18	13-Sep-18																					Laying Sewerage Pipe aFMH23-15A (Part 2)
K-01-RWS-9476	Backfilling Sewerage Pipe FMH23-15A (Part 2)	12	14-Sep-18	28-Sep-18																					Backfilling Sewerage Pipe FMH23-15A (Part 2)
K-01-RWS-9477	Relocation of Underground Utilities under Center Median	7	29-Sep-18	08-Oct-18																					Relocation of Underground Utilities under Center Median
Laying of Drainage Pipe and Construction of Manhole (M301 to M306)																									
K-01-RWS-9485	Excavation of Drainage Pipe and Manhole (M301 to M306)	10	04-Sep-18	14-Sep-18																					Excavation of Drainage Pipe and Manhole (M301 to M306)
K-01-RWS-9490	Laying Drainage Pipe and Construction of Manhole (M301 to M306)	25	10-Sep-18	10-Oct-18																					Laying Drainage Pipe and Construction of Manhole (M301 to M306)
K-01-RWS-9500	Backfilling Drainage Pipe and Manhole (M301 to M306)	9	11-Oct-18	22-Oct-18																					Backfilling Drainage Pipe and Manhole (M301 to M306)
K-01-RWS-9502	Construction of Gully and other drainage works along M301 to M306	10	09-Oct-18	20-Oct-18																					Construction of Gully and other drainage works along M301 to M306
Water Works																									
K-01-RWS-9580	Laying of Fresh Watermain Pipe	5	23-Oct-18	27-Oct-18																					Laying of Fresh Watermain Pipe
K-01-RWS-9604	Laying of Salt Watermain Pipe	5	23-Oct-18	27-Oct-18																					Laying of Salt Watermain Pipe
Road Works																									
K-01-RWS-1075	Construction of Subgrade Works and Subbase Works	5	29-Oct-18	02-Nov-18																					Construction of Subgrade Works and Subbase Works
K-01-RWS-1076	Road Base and Pavement Works	3	03-Nov-18	06-Nov-18																					Road Base and Pavement Works
K-01-RWS-1077	Temporary Road Construction for TTA stage 3 - phase 2	5	05-Nov-18	09-Nov-18																					Temporary Road Construction for TTA stage 3 - phase 2

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September				October				November				Index		
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18		25	02
Part 2																								
Laying of Drainage Pipe and Construction of Manhole (SMH4048691, SHM4048692 and M401)																								
K-01-RWS-1050	Excavation of Drainage Pipe and Manhole (M401)	0	03-Aug-18 A	17-Aug-18 A	█ Excavation of Drainage Pipe and Manhole (M401)																			
K-01-RWS-1050	Laying Drainage Pipe and Construction Manhole (M401)	0	18-Aug-18 A	27-Aug-18 A	█ Laying Drainage Pipe and Construction Manhole (M401)																			
K-01-RWS-1051	Backfilling Drainage Pipe and Manhole (M401)	0	28-Aug-18 A	31-Aug-18 A	█ Backfilling Drainage Pipe and Manhole (M401)																			
K-01-RWS-1052	Excavation of Drainage Pipe and Manhole (SMH4048691-92)	6	10-Nov-18	16-Nov-18	█ Excavation of Drainage Pipe and Manhole (SMH4048691-92)																			
K-01-RWS-1052	Laying Drainage Pipe and Construction Manhole (SMH4048691-92)	18	14-Nov-18	04-Dec-18	█ Laying Drainage Pipe and Construction Manhole (SMH4048691-92)																			
K-01-RWS-1095	Relocation of Underground Utilities under Center Median	7	10-Nov-18	17-Nov-18	█ Relocation of Underground Utilities under Center Median																			
Section 1A of the Works -Construction of Supporting Underground Structure																								
SUS and Ventilation Adits from CH6+150 to CH6+220 in Zone 1																								
Construction of Tunnel Box Structure																								
SUS Bay 1 (Ch6150-Ch6167.5)																								
K-1A-SV1-8425	Breaking and Removal D-wall to +2.5mPD	0	22-May-18 A	31-Aug-18	█ Breaking and Removal D-wall to +2.5mPD																			
SUS Bay 4 (Ch6202.5-Ch6220)																								
K-1A-SV1-8650	Breaking and Removal of D-wall to +2.5mPD	0	22-May-18 A	11-Sep-18 A	█ Breaking and Removal of D-wall to +2.5mPD																			
Backfilling Works																								
K-1A-SV1-6900	Backfilling (bay 1 to bay 2) (to +3.7m)	6	31-Aug-18	06-Sep-18	█ Backfilling (bay 1 to bay 2) (to +3.7m)																			
SUS and Ventilation Adits from CH6+220 to CH6+291 in Zone 2																								
Construction of SUS Structure at Zone 2																								
VA2																								
A1510	Base Slab _VA2	0	14-Aug-18 A	17-Aug-18 A	█ Base Slab _VA2																			
A1530	Dismantling Struts	0	21-Aug-18 A	24-Aug-18 A	█ Dismantling Struts																			
A1540	Wall Stem	9	27-Aug-18 A	08-Sep-18	█ Wall Stem																			
A1560	Re-prop	3	11-Sep-18	13-Sep-18	█ Re-prop																			
A1610	Dismantling Struts _SV1__Bay 2	1	14-Sep-18	14-Sep-18	█ Dismantling Struts _SV1__Bay 2																			
A1620	Erect Scaffolding_Base Slab 1A & B	2	15-Sep-18	16-Sep-18	█ Erect Scaffolding_Base Slab 1A & B																			
A1630	Soffit formworks_Base Slab 1A & B	1	17-Sep-18	17-Sep-18	█ Soffit formworks_Base Slab 1A & B																			
Scaffolding / Falseworks																								
Bay 1																								
A1642	Base Slab _Bay 1B	6	16-Sep-18	21-Sep-18	█ Base Slab _Bay 1B																			
A1662	RSB_Bay 1EB	0	10-Aug-18 A	15-Aug-18 A	█ RSB_Bay 1EB																			

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September					October					November				
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	
A1665	Top Slab _1A	15	17-Aug-18 A	14-Sep-18																				
A1668	RSB_Bay 1WB	6	23-Sep-18	28-Sep-18																				
A1710	Top Slab _1B	12	23-Sep-18	04-Oct-18																				
A2500	Dismantling of Struts_S1B - 1 to 5	3	08-Oct-18	10-Oct-18																				
A2510	Waterproofing Works (1440 m2) and Screeding Works (108 m3)	5	11-Oct-18	15-Oct-18																				
A2520	Demolition of Dwall (96mL)	10	16-Oct-18	25-Oct-18																				
A2530	Backfilling Works for Bay 1 to +2mPD (950m3)	5	26-Oct-18	30-Oct-18																				
Bay 2																								
A1738	Metal Scaffolds_Soffit and Working Platform_2nd Pour	0	31-Jul-18 A	24-Aug-18 A																				
A1740	Wall_Bay 2_2nd pour	0	17-Aug-18 A	22-Aug-18 A																				
A1750	RSB_Bay 2	0	08-Aug-18 A	15-Aug-18 A																				
A1760	Top Slab _2	6	27-Aug-18 A	05-Sep-18																				
A2540	Dismantling of Struts_S1B - 1 to 5	5	09-Sep-18	13-Sep-18																				
A2550	Waterproofing Works (1440 m2) and Screeding Works (108 m3)	6	14-Sep-18	19-Sep-18																				
A2552	Backfilling Works to S1B (950m3)	18	20-Sep-18	07-Oct-18																				
A2555	Dismantling of Struts_S1B - 6 to 9, S1A - 1 to 6	7	08-Oct-18	14-Oct-18																				
A2560	Demolition of Dwall (142mL)	15	23-Oct-18	06-Nov-18																				
Bay 3																								
A1810	Wall_Bay 3_2nd pour	0	03-Aug-18 A	10-Aug-18 A																				
A1820	RSB_Bay 3	0	31-Jul-18 A	07-Aug-18 A																				
A1830	Top Slab _3	0	13-Aug-18 A	19-Aug-18 A																				
SUS Structure from CH6+291 to 6+467 in Zone 3																								
Construction of SUS Structure at Zone 3																								
<i>Scaffolding / Falseworks - Bay 4</i>																								
A1870	Top Slab _4	0	14-Aug-18 A	26-Aug-18 A																				
<i>System Formworks - SUS Construction Works at Zone 3</i>																								
Bay 5 to 7																								
A2140	Top slab_SF_Bay 7	0	13-Aug-18 A	30-Aug-18 A																				
A2570	Dismantling of Struts_S4 - 1 to 7	6	01-Sep-18	06-Sep-18																				
A2580	Waterproofing Works (1440 m2) and Screeding Works (105 m3)	5	07-Sep-18	11-Sep-18																				
A2590	Backfilling Works to S1A (6850m3)	18	12-Sep-18	29-Sep-18																				

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September					October					November					Order					
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02							
A2380	RSB_Bay 12	8	05-Sep-18	12-Sep-18																										
A2390	Top slab_SF_Bay 12	13	20-Sep-18	02-Oct-18																										
A2400	Base Slab_Bay 13	0	17-Aug-18 A	24-Aug-18 A																										
A2410	Dismantling of Struts_Bay 13	0	27-Aug-18 A	30-Aug-18 A																										
A2420	Wall_Bay 13	8	17-Sep-18	25-Sep-18																										
A2430	RSB_Bay 13	8	13-Sep-18	20-Sep-18																										
A2670	Top slab_SF_Bay 13	13	30-Sep-18	12-Oct-18																										
A2680	Dismantling of Struts_S4 - 16 to 25	10	15-Oct-18	24-Oct-18																										
A2700	Waterproofing Works (1900 m2)	4	25-Oct-18	28-Oct-18																										
A2710	Screeding Works (145 m3)	3	29-Oct-18	31-Oct-18																										
A2720	Backfilling Works to S3 (8760m3) @400m3 (C)	22	01-Nov-18	22-Nov-18																										
A2730	Dismantling of Struts_S3 - 1 to 10	10	23-Nov-18	02-Dec-18																										
Bay 14 to 15 (Top Slab)																														
A2440	Base Slab_bay 14	8	17-Sep-18	25-Sep-18																										
A2450	Dismantling of Struts_Bay 14	7	29-Sep-18	06-Oct-18																										
A2460	Wall_Bay 14	8	06-Oct-18	14-Oct-18																										
A2470	Top slab_Bay14	15	21-Oct-18	05-Nov-18																										
A2490	Top slab_Bay 15	15	05-Nov-18	20-Nov-18																										
A2770	Dismantling of Struts_S4 - 26 to 28 & DS1-4	7	22-Nov-18	29-Nov-18																										
A2780	Waterproofing Works (1350 m2)	3	29-Nov-18	02-Dec-18																										
Section 3 of the Works- Construction of District Cooling System (Subject to Excision)																														
Construction of District Cooling System																														
Construction of DCS Works at Zone 2																														
SCR1030	DCS at Zone 2 Bay 2 to Bay 4 (CH35 - CH110)	24	10-Nov-18*	07-Dec-18																										
Construction of DCS Works at Zone 3																														
SCR1500	Zone 3 DCS (3 x 900) south of Gate 1 bridge (CH140 - CH190)	18	04-Oct-18*	25-Oct-18																										
Construction of DCS Works at Zone 4																														
K-03-DCS-7800	Construction of DCS Valve Pit	95	10-Aug-18 A	22-Dec-18																										
K-03-DCS-7810	ELS for DCS (Outside of SUS)	48	20-Nov-18*	17-Jan-19																										
Section 4A of the Works-Construction of Subway A (Subject to Excision)																														
K-4A-BAY-1900	ELS for Subway A Bay 1 (west of D-wall)	48	17-Sep-18*	14-Nov-18																										

Activity ID	Activity Name	Rem Dur	Start	Finish	August					September				October				November				Order			
					29	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18		25	02	
K-4A-BAY-1930	ELS for Subway A Bay 3 (east of D-wall)	48	06-Oct-18	01-Dec-18																					
Section 4B of the Works- Construction of Subway B (Subject to Excision)																									
Bay 1 & 2																									
K-4B-BAY-3100	Handover of Portion B	0		31-Aug-18*																					
Bay 3 & 4																									
K-4B-BAY-3290	Construction of Base Slab at Bay 3	0	01-Aug-18 A	09-Aug-18 A																					
K-4B-BAY-3300	Construction of Wall and Top Slab at Bay 3	0	10-Aug-18 A	31-Aug-18 A																					
K-4B-BAY-3310	Backfilling Works (Bay 3)	12	01-Sep-18	14-Sep-18																					
K-4B-BAY-3330	Excavation and Lateral Support works for Bay 4	21	24-Sep-18	20-Oct-18																					
K-4B-BAY-3340	Casting Blinding Layer for Bay 4	5	22-Oct-18	26-Oct-18																					
K-4B-BAY-3350	Construction of Base Slab at Bay 4	12	27-Oct-18	09-Nov-18																					
K-4B-BAY-3360	Construction of Wall and Top Slab at Bay 4	30	10-Nov-18	14-Dec-18																					
Section 5 of the Works-Completion of All Landscape Softworks																									
K-05-LCS-1000	Procurement of plant species	90	31-Aug-18	28-Nov-18																					
Section 7 of the Works-Preservation and Protection of Existing Trees																									
K-07-001-1000	Section 7 of the Works-Preservation and Protection of Existing Trees	420	04-Jan-16 A	24-Oct-19																					

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com





Appendix B

Project Organization Chart

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com

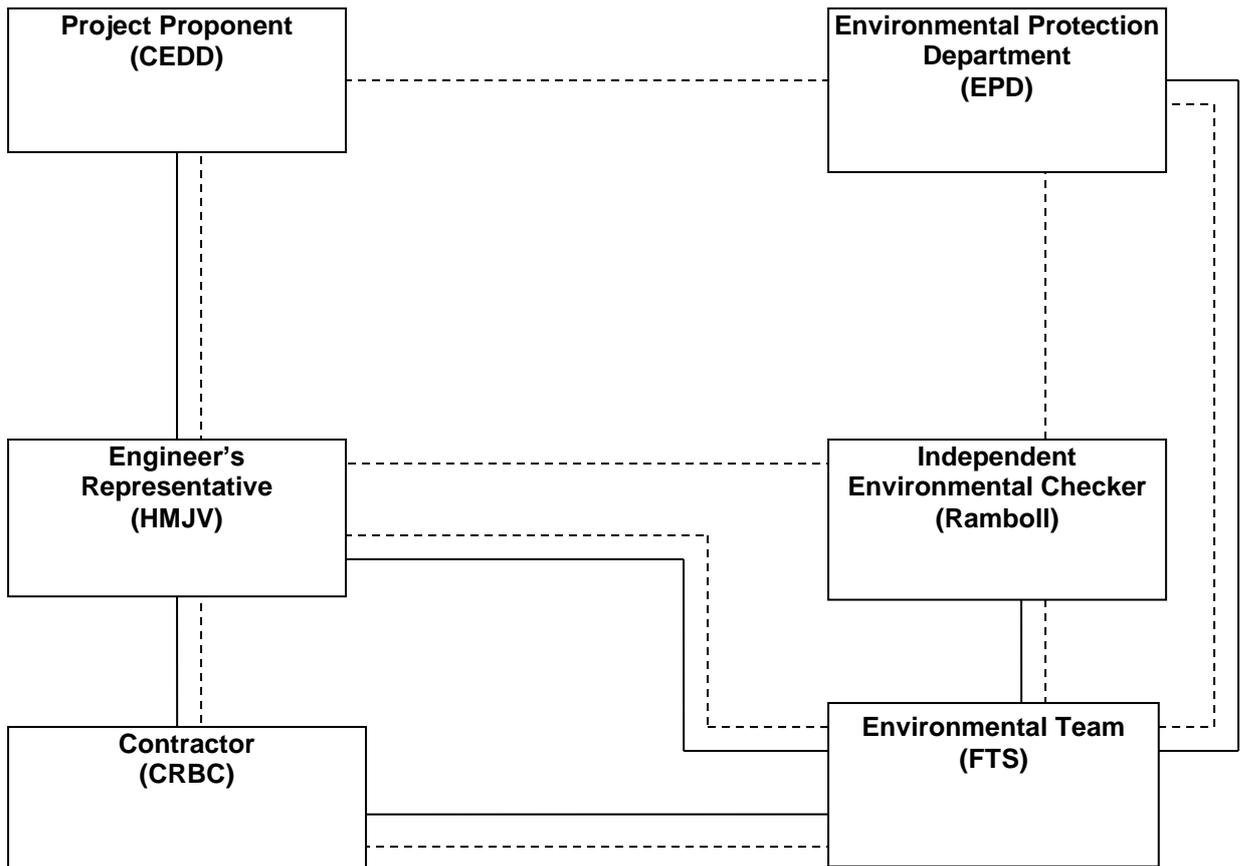

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix C

Action and Limit Levels for Air Quality and Noise

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Action and Limit Levels for 24-hr TSP and 1-hr TSP

Parameter	Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)	Limit Level ($\mu\text{g}/\text{m}^3$)
24-hr TSP ($\mu\text{g}/\text{m}^3$)	KTD1a	177	260
	KTD2b	157	
	KER1b	172	
*1-hr TSP ($\mu\text{g}/\text{m}^3$)	KTD1a	285	500
	KTD2b	279	
	KER1b	295	

Note:

1-hr TSP monitoring should be required in case of complaints.

Action and Limit Levels for Construction Noise, Leq (30min), dB(A)

Time Period	Location	Action	Limit
0700-1900 hrs on normal weekdays	KTD1a KTD2b KER1b	When one documented complaint is received	75 dB(A)

FUGRO TECHNICAL SERVICES LIMITED




Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com






Appendix D

Graphical Presentation of Monitoring Data

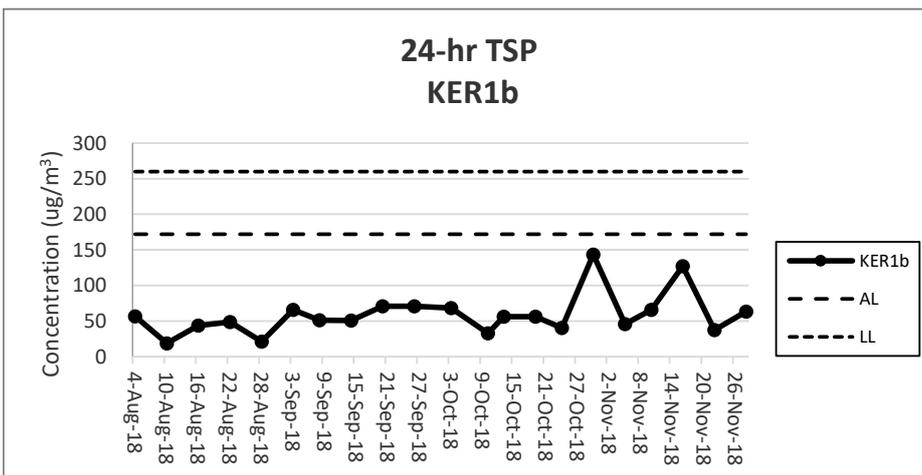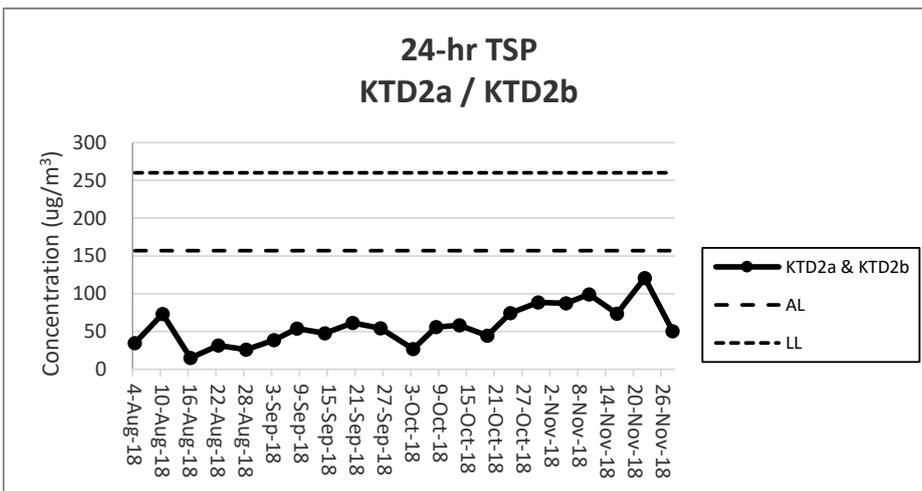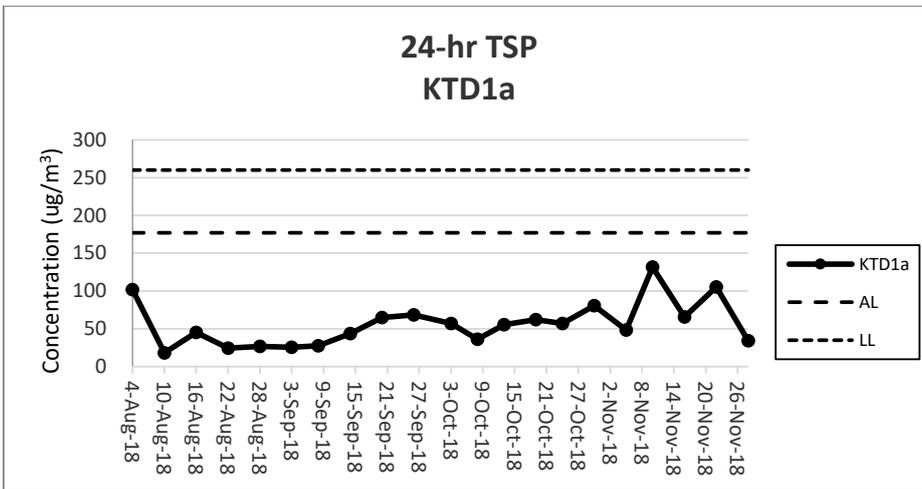

Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.1.
- 2) The weather conditions during monitoring in the reporting period was range from cloudy and fine.
- 3) Any other factors which might affect the monitoing results can be referred to Section 2.3.4.
- 4) KTD2a was relocated to KTD2b on 9 August 2018
- 5)Power supply of high volume sampler at KER1b was suspended on 8 October 2018 due to the damage of the cable, TSP monitoring was resumed at 10 October 2018.

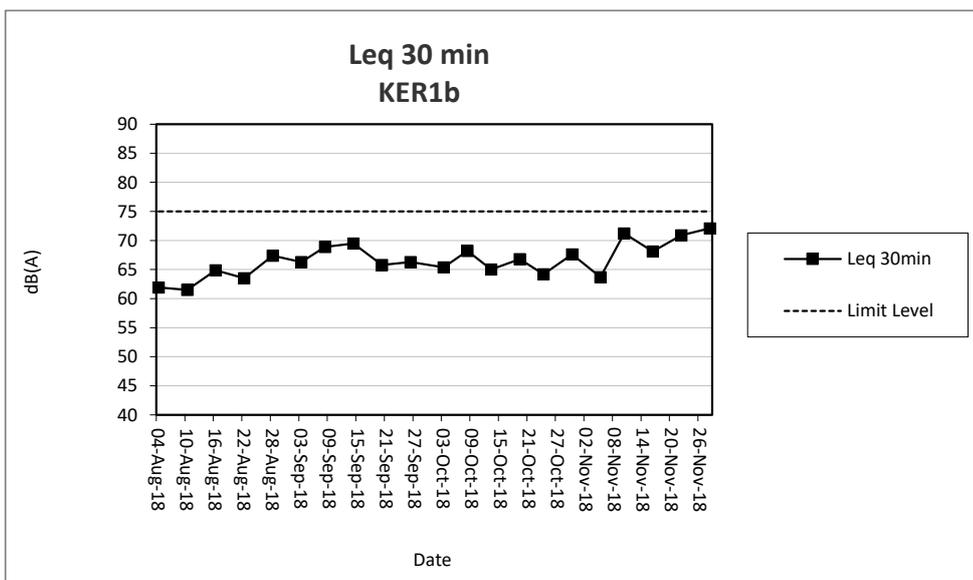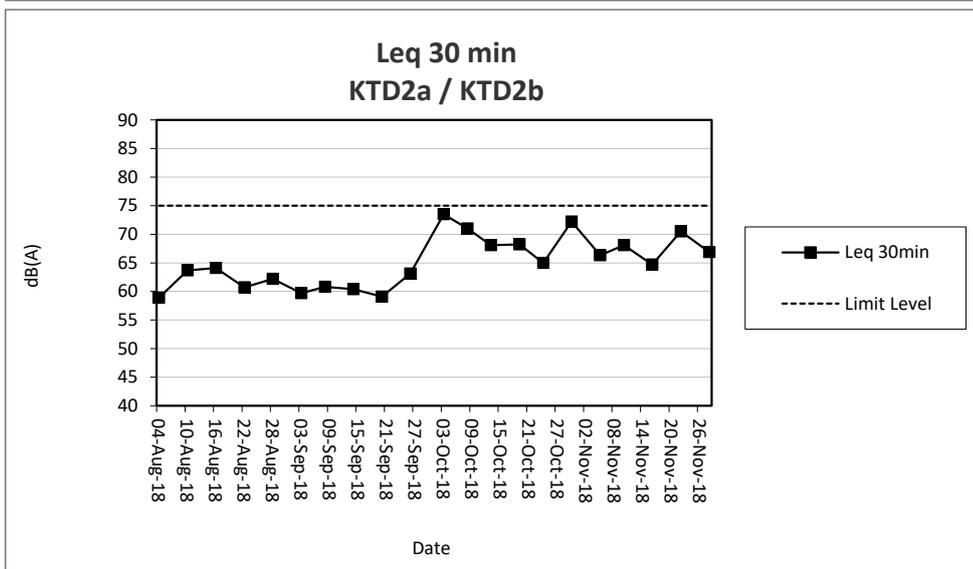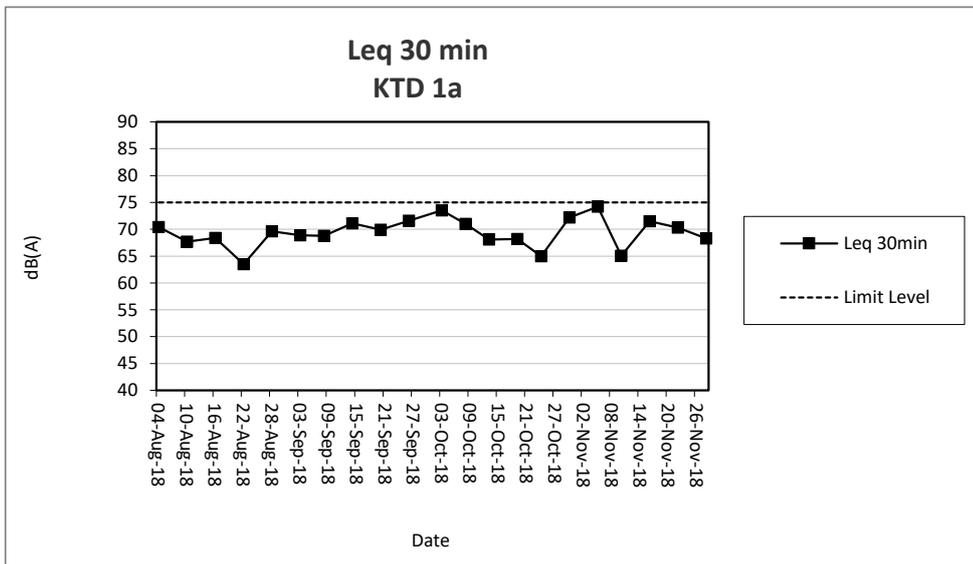

Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.1.
- 2) The weather conditions during monitoring in the reporting period was ranged from cloudy and fine.
No raining or wind with speed over 5 m/s was observed during monitoring in the reporting period.
- 3) Any other factors which might affect the monitoring results can be referred to Section 2.3.4.
- 4) KTD2a was relocated to KTD2b on 9 August 2018

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix E

Waste Flow Table

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2016											
Months	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2016 Jan	0.159	0.101	0.058	Nil	Nil	Nil	Nil	0.023	0.00002	0.0158	0.0335
2016 Feb	0.291	0.050	0.241	Nil	Nil	Nil	1.34	0.023	0.00002	0.0158	0.0335
2016 Mar	2.7389	0.0407	0.0662	Nil	2.632	Nil	5.92	0.023	0.00002	0.0158	0.0571
2016 Apr	4.1718	0.0578	0.462	Nil	3.652	Nil	12.5	0.023	0.00002	0.0158	0.0426
2016 May	3.592	Nil	0.299	Nil	3.293	Nil	5.23	0.023	0.00002	0.0158	0.0621
2016 June	4.6035	Nil	0.8555	Nil	3.748	Nil	Nil	0.023	0.00002	0.0158	0.0619
2016 July	6.155	0.153	0.015	Nil	5.987	Nil	7.84	0.023	0.00002	0.0158	0.0433
2016 Aug	5.1155	Nil	Nil	Nil	5.1155	Nil	19.93	0.023	Nil	Nil	0.0147
2016 Sept	7.2267	Nil	Nil	Nil	7.2267	Nil	33.65	0.023	Nil	Nil	0.0103
2016 Oct	4.6448	Nil	Nil	Nil	4.6448	Nil	13.30	0.023	Nil	Nil	0.0385
2016 Nov	6.1626	Nil	Nil	Nil	6.1626	Nil	27.06	0.023	Nil	Nil	0.0192
2016 Dec	6.3522	Nil	Nil	Nil	6.3522	Nil	13.30	0.023	Nil	Nil	0.0121
Total	51.213	0.4025	1.9967	Nil	48.8138	Nil	140.07	0.276	0.00014	0.1106	0.4288

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2017

Months	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2017 Jan	4.2300	Nil	Nil	Nil	4.2300	Nil	0.015	0.023	Nil	Nil	0.0109
2017 Feb	3.2128	Nil	Nil	Nil	3.2128	Nil	0.015	0.023	Nil	Nil	0.0096
2017 Mar	9.4759	Nil	Nil	Nil	9.4759	Nil	0.034	0.023	Nil	Nil	0.0162
2017 Apr	4.8827	Nil	Nil	Nil	4.8827	Nil	0.016	0.023	Nil	Nil	0.0062
2017 May	3.0366	Nil	Nil	Nil	3.0366	Nil	0.022	0.023	Nil	Nil	0.0282
2017 Jun	2.5656	Nil	Nil	Nil	2.5656	Nil	41.25	Nil	Nil	Nil	0.0357
2017 Jul	5.5267	Nil	0.7851	Nil	4.7416	Nil	4.01	0.4515	Nil	0.25	0.0364
2017 Aug	11.4734	Nil	0.0276	Nil	11.4458	Nil	7.4	Nil	Nil	Nil	0.0196
2017 Sep	23.9373	Nil	2.6167	Nil	21.3206	Nil	3.52	Nil	Nil	Nil	0.0333
2017 Oct	17.8261	Nil	0.4069	Nil	17.4192	Nil	Nil	Nil	Nil	Nil	0.0156
2017 Nov	5.8834	Nil	0.6664	Nil	5.217	Nil	Nil	Nil	Nil	Nil	0.023
2017 Dec	21.3554	Nil	0.4763	Nil	20.8791	Nil	29.13	Nil	Nil	Nil	0.022
Total	113.4059	Nil	4.9790	Nil	108.4269	Nil	85.412	0.5665	Nil	0.25	0.2567

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Waste Flow Table for Year 2018

Months	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non-inert C&D Wastes Generated Monthly				
	Total Quantity Generated (Inert C&D)	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
2018 Jan	10.2340	Nil	Nil	Nil	10.2340	Nil	32.39	Nil	Nil	Nil	0.0161
2018 Feb	6.5256	Nil	Nil	Nil	6.5256	Nil	Nil	Nil	Nil	Nil	0.0235
2018 Mar	28.1995	Nil	Nil	Nil	28.1995	Nil	54.54	Nil	Nil	Nil	0.0190
2018 Apr	11.2165	Nil	Nil	Nil	11.2165	Nil	Nil	Nil	Nil	Nil	0.0270
2018 May	5.6011	Nil	Nil	Nil	5.6011	Nil	Nil	Nil	Nil	Nil	0.0140
2018 Jun	5.8072	Nil	Nil	Nil	5.8072	Nil	93.3	Nil	Nil	Nil	0.0235
2018 Jul	7.4206	Nil	Nil	Nil	7.4206	Nil	Nil	Nil	Nil	Nil	0.0383
2018 Aug	2.0815	Nil	Nil	Nil	2.0815	Nil	Nil	Nil	Nil	Nil	0.0665
2018 Sep											
2018 Oct											
2018 Nov											
2018 Dec											
Total	77.0860	Nil	Nil	Nil	77.0860	Nil	180.23	Nil	Nil	Nil	0.2280

Note:

- 1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



Appendix F

Environmental Mitigation Implementation Schedule (EMIS)

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
<u>Air Quality Measures</u>					
New Distributor Roads Serving the Planned KTD					
AEIAR-130/2009 S3.2	AEIAR 130/2009 EM&A Manual S2.2	8 times daily watering of the work site with active dust emitting activities.	Contractor	All relevant worksites	Partially Implemented
Decommissioning of the Radar Station of the former Kai Tak Airport					
AEIAR-130/2009 S5.2.19	AEIAR 130/2009 EM&A Manual S4.2.4	The excavation area should be limited to as small in size as possible and backfilled with clean and/or treated soil shortly after excavation work. The exposed excavated area should be covered by the tarpaulin during night time. The top layer soils should be sprayed with fine misting of water immediately before the excavation.	Contractor	All relevant worksites	Not Applicable
Trunk Road T2					
AEIAR-174/2013 S4.9.2.1	AEIAR-174/2013 EM&A Manual S2.3.1.1	Watering of the construction areas 12 times per day to reduce dust emissions by 91.7%, with reference to the "Control of Open Fugitive Dust Sources" (USEPA AP-42). The amount of water to be applied would be 0.91L/m ² for the respective watering frequency.	Contractor	All relevant worksites	Implemented
		Dust enclosures with watering would be provided along the loading ramps and conveyor belts for unloading the C&D materials to the barge for dust suppression.	Contractor	All relevant worksites	Not Applicable
		8 km per hour is the recommended limit of the speed for vehicles on unpaved site roads.	Contractor	All relevant worksites	Implemented
<u>Good Site Practices</u>					
AEIAR-130/2009 S3.2, S5.2.19, AEIAR-174/2013 S4.9.2.2	AEIAR 130/2009 EM&A Manual S2.2, S4.2, AEIAR 174/2013 EM&A Manual S2.3.1.2	Stockpiling site(s) should be lined with impermeable sheeting and banded. Stockpiles should be fully covered by impermeable sheeting to reduce dust emission.	Contractor	All relevant worksites	Partially Implemented
		Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather. Use of frequent watering for particularly dusty construction areas and areas close to ASRs.	Contractor	All relevant worksites	Partially Implemented
		Misting for the dusty material should be carried out before being loaded into the vehicle. Any vehicle with an open load carrying area should have properly fitted side and tail boards.	Contractor	All relevant worksites	Implemented
		Material having the potential to create dust should not be loaded from a level higher than the side and tail boards and should be dampened and covered by a clean tarpaulin.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations; The tarpaulin should be properly secured and should extent at least 300 mm over the edges of the sides and tailboards. The material should also be dampened if necessary before transportation.	Contractor	All relevant worksites	Implemented
		The vehicles should be restricted to maximum speed of 10 km per hour. Confined haulage and delivery vehicle to designated roadways inside the site. Onsite unpaved roads should be compacted and kept free of loose materials.	Contractor	All relevant worksites	Implemented
		Vehicle washing facilities should be provided at every vehicle exit point. Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites. The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	Contractor	All relevant worksites	Implemented
		Every main haul road should be sealed with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet.	Contractor	All relevant worksites	Implemented
		Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.	Contractor	All relevant worksites	Implemented
		Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed.	Contractor	All relevant worksites	Implemented
		Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.	Contractor	All relevant worksites	Implemented
		Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.	Contractor	All relevant worksites	Implemented
		Open stockpiles shall be avoided or covered. Prevent placing dusty material storage piles near ASRs.	Contractor	All relevant worksites	Implemented
		Routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs.	Contractor	All relevant worksites	Implemented
		<u>Dark smoke</u>			
		Dark smoke emission shall be control in accordance with the Air Pollution Control (Smoke)	Contractor	All relevant	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		Regulation and ETWB TCW 19/2005.		worksites	
		Plant and equipment should be well maintained to prevent dark smoke emission.	Contractor	All relevant worksites	Implemented
Noise Measures					
Trunk Road T2					
AEIAR-174/2013 S5.9.2.1	AEIAR-174/2013 EM&A Manual S3.4.1.1	The use of quieter plant, including Quality Powered Mechanical Equipment (QPME) is specified for the list of equipment: <ul style="list-style-type: none"> • Concrete lorry mixer • Dump Truck, 5.5 tonne < gross vehicle weight <= 38 tonne • Generator, Super Silenced, 70 dB(A) at 7m • Poker, vibratory, Hand-held (electric) • Water Pump, Submersible (Electric) • Mobile Crane - KOBELCO CKS900 • Excavator, wheeled/tracked - HYUNDAI R80CR-9 	Contractor	All relevant worksites	Implemented
		Use of temporary or fixed noise barriers with a surface density of at least 10kg/m ² to screen noise from movable and stationary plant.	Contractor	All relevant worksites	Implemented
		Use of enclosures with covers at top and three sides and a surface density of at least 10kg/m ² to screen noise from generally static noisy plant such as air compressors.	Contractor	All relevant worksites	Implemented
		Use of acoustic fabric for the silent piling system, drill rigs, rock drills etc.	Contractor	All relevant worksites	Partially Implemented
<u>Good Site Practices</u>					
AEIAR-130/2009 S3.3, S5.3.10, AEIAR-174/2013 S5.9.2.1	AEIAR 130/2009 EM&A Manual S2.3, S4.3.2, AEIAR-174/2013 EM&A Manual S3.4.1.1	Only well-maintained plant should be operated on-site and plant shall be serviced regularly during the construction/ decommissioning program.	Contractor	All relevant worksites	Implemented
		Silencers or mufflers on construction equipment should be utilized and shall be properly maintained during the construction/ decommissioning program.	Contractor	All relevant worksites	Implemented
		Mobile plant, if any, should be sited as far away from NSRs as possible.	Contractor	All relevant worksites	Implemented
		Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or should be throttled down to a minimum.	Contractor	All relevant worksites	Implemented
		Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.	Contractor	All relevant worksites	Implemented
Material stockpiles and other structures should be effectively utilized, wherever practicable, in	Contractor	All relevant	Implemented		

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		screening noise from on-site construction/ decommissioning activities.		worksites	
		Use of site hoarding as a noise barrier to screen noise at low level NSRs.	Contractor	All relevant worksites	Implemented
		For the use of hand held percussive breakers (with mass of above 10kg) and portable air compressors (supply air at 500 kPa or above), the noise level of such PME shall comply with a stringent noise emission standard and a noise emission label shall be obtained from the DEP before use at any time in construction site.	Contractor	All relevant worksites	Implemented
		Quiet powered mechanical equipment (PME) shall be used for the construction of the Project.	Contractor	All relevant worksites	Implemented
		Full enclosures shall be used to screen noise from relatively static PMEs (including air compressor, bar bender, concrete pump, generator and water pump) from sensitive receiver(s).	Contractor	All relevant worksites	Implemented
		Movable cantilevered noise barriers shall be used to screen noise from mobile PMEs (including asphalt paver, breaker, excavator and hand-held breaker) from sensitive receiver(s). These movable cantilevered noise barriers shall be located close to the mobile PMEs and shall be moved/adjusted iteratively in step with each movement of the corresponding mobile PMEs in order to maximize their noise reduction effects.	Contractor	All relevant worksites	Implemented
		Only approved or exempted Non-road Mobile Machineries (NRMMS) including regulated machines and non-road vehicles with proper labels are allowed to be used in specified activities on-site.	Contractor	All relevant worksites	Implemented
Water Quality Measures					
Trunk Road T2					
		Accidental Spillage			
AEIAR-174/2013 S6.4.8.5	AEIAR-174/2013 EM&A Manual S4.2.1.1	All bentonite slurry should be stored in a container that resistant to corrosion, maintained in good conditions and securely closed; The container should be labelled in English and Chinese and note that the container is for storage of bentonite slurry only.	Contractor	All relevant worksites	Implemented
		The storage container should be placed on an area of impermeable flooring and bunded with capacity to accommodate 110% of the volume of the container size or 20% by volume stored in the area and enclosed with at least 3 sides.	Contractor	All relevant worksites	Implemented
		The storage container should be sufficiently covered to prevent rainfall entering the container or bunded area (water collected within the bund must be tested and disposed of as chemical waste, if necessary). An emergency clean up kit shall be readily available where bentonite fluid will be stored or used.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		The handling and disposal of bentonite slurries should be undertaken in accordance within ProPECC PN 1/94. Surplus bentonite slurries used in construction works shall be reconditioned and reused wherever practicable. Residual bentonite slurry shall be disposed of from the site as soon as possible as stipulated in Clause 8.56 of the General Specification for Civil Engineering Works. The Contractor should explore alternative disposal outlets for the residual bentonite slurry (dewatered bentonite slurry to be disposed to a public filling area and liquid bentonite slurry, if mixed with inert fill material, to be disposed to a public filling area) and disposal at landfill should be the last resort.	Contractor	All relevant worksites	Implemented
AEIAR-174/2013 S6.4.8.8	AEIAR-174/2013 EM&A Manual S4.2.1.1	In order to protect against impacts to the surrounding marine waters of the KTTS and Victoria Harbour in the event of an accidental spillage of fuel or oil, the Contractor will be required to prepare a spill response plan to the satisfaction of AFCD, EPD, FSD, Police, TD and WSD to define procedures for the control, containment and clean-up of any spillage that could occur on the construction site.	Contractor	All relevant worksites	Implemented
		<u>Dredging, Reclamation and Filling</u>			
		No dredging, reclamation or filling in the marine environment shall be carried out.	Contractor	All relevant worksites	Implemented
Decommissioning of the Radar Station of the former Kai Tak Airport					
		<u>Building Demolition</u>			
AEIAR-130/2009 S5.4	AEIAR 130/2009 EM&A Manual S4.4	The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" should be followed as far as practicable in order to minimise surface runoff and the chance of erosion.	Contractor	All relevant worksites	Not Applicable
		There is a need to apply to EPD for a discharge licence under the WPCO for discharging effluent from the construction site. The discharge quality is required to meet the requirements specified in the discharge licence. All the runoff, wastewater or extracted groundwater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. It is anticipated that the wastewater generated from the works areas would be of small quantity. Monitoring of the treated effluent quality from the works areas should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD.	Contractor	All relevant worksites	Not Applicable
		<u>General Construction Works</u>			
		<u>Construction Runoff</u>			
AEIAR-130/2009 S3.4,	AEIAR 130/2009 EM&A Manual	Exposed soil areas should be minimised to reduce the potential for increased siltation, contamination of runoff, and erosion. Construction runoff related impacts associated with the	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
S5.4/ AEIAR-174/2013 S6.4.8.1	S2.4, S4.4/ AEIAR-174/2013 EM&A Manual S4.2.1.1	above ground construction activities can be readily controlled through the use of appropriate mitigation measures which include the use of sediment traps and adequate maintenance of drainage systems to prevent flooding and overflow.			
		Construction site should be provided with adequately designed perimeter channel and pre-treatment facilities and proper maintenance. The boundaries of critical areas of earthworks should be marked and surrounded by dykes or embankments for flood protection. Temporary ditches should be provided to facilitate runoff discharge into the appropriate watercourses, via a silt retention pond. Permanent drainage channels should incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94.	Contractor	All relevant worksites	Implemented
		Ideally, construction works should be programmed to minimise surface excavation works during the rainy season (April to September). All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.	Contractor	All relevant worksites	Implemented
		Sediment tanks of sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m ³ capacity, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity is flexible and able to handle multiple inputs from a variety of sources and particularly suited to applications where the influent is pumped.	Contractor	All relevant worksites	Partially Implemented
		Open stockpiles of construction materials (for examples, aggregates, sand and fill material) of more than 50 m ³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.	Contractor	All relevant worksites	Implemented
		Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.	Contractor	All relevant worksites	Implemented
		Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecast, and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		Oil interceptors should be provided in the drainage system and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain.	Contractor	All relevant worksites	Implemented
		An adequately designed and located wheel washing bay should be provided at every site exit, and wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.	Contractor	All relevant worksites	Implemented
		<u>Drainage</u>			
		It is recommended that on-site drainage system should be installed prior to the commencement of other construction activities. Sediment traps should be installed in order to minimise the sediment loading of the effluent prior to discharge into foul sewers. There should be no direct discharge of effluent from the site into the sea.	Contractor	All relevant worksites	Implemented
		All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment control measures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage should be reinstated to its original condition when the construction work has finished or the temporary diversion is no longer required.	Contractor	All relevant worksites	Implemented
		<u>Stormwater Discharges</u>			
		Minimum distances of 100 m should be maintained between the existing or planned stormwater discharges and the existing or planned seawater intakes.	Contractor	All relevant worksites	Implemented
		<u>Sewage Effluent</u>			
		Construction work force sewage discharges on site are expected to be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage may need to be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets should be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor should also be responsible for waste disposal and maintenance practices.	Contractor	All relevant worksites	Implemented
		<u>Debris and Litter</u>			
		In order to maintain water quality in acceptable conditions with regard to aesthetic quality,	Contractor	All relevant	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		contractors should be required, under conditions of contract, to ensure that site management is optimised and that disposal of any solid materials, litter or wastes to marine waters does not occur. Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering into the adjacent harbour waters. Stockpiles of cement and other construction materials should be kept covered when not being used.		worksites	
		<u>Accidental Spillage</u> Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to the nearby harbour waters, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour WCZ. The bund should be drained of rainwater after a rain event.	Contractor	All relevant worksites	Partially Implemented
<u>Waste Management Measures</u>					
		<u>Waste Management Plan</u>			
AEIAR-174/2013 S11.4.8.1	AEIAR-174/2013 EM&A Manual S9.2.1.2	Contractor should be requested to submit an outline Waste Management Plan (WMP) prior to the commencement of construction work, in accordance with the ETWB TC(W) No.19/2005 so as to provide an overall framework of waste management and reduction.	Contractor	All relevant worksites	Implemented
		<u>Good Site Practices</u>			
AEIAR-130/2009 S3.5, S5.5	AEIAR 130/2009 EM&A Manual S2.5, S4.5	Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	Contractor	All relevant worksites	Implemented
		Training of site personnel in proper waste management and chemical waste handling procedures.	Contractor	All relevant worksites	Implemented
		Provision of sufficient waste disposal points and regular collection for disposal.	Contractor	All relevant worksites	Implemented
		Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	Contractor	All relevant worksites	Implemented
		A recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	Contractor	All relevant worksites	Implemented
		<u>Waste Reduction Measures</u>			
		Sort C&D waste from demolition of the remaining structures to recover recyclable portions such as metals.	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase
					Implementation Status
		Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.	Contractor	All relevant worksites	Implemented
		Encourage collection of aluminum cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force.	Contractor	All relevant worksites	Implemented
		Any unused chemicals or those with remaining functional capacity should be recycled.	Contractor	All relevant worksites	Implemented
		Proper storage and site practices to minimize the potential for damage or contamination of construction materials.	Contractor	All relevant worksites	Implemented
		<u>Construction and Demolition Materials</u>			
		Where it is unavoidable to have transient stockpiles of C&D material within the work site pending collection for disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as possible.	Contractor	All relevant worksites	Implemented
		Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric.	Contractor	All relevant worksites	Implemented
		Skip hoist for material transport should be totally enclosed by impervious sheeting.	Contractor	All relevant worksites	Implemented
		Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site.	Contractor	All relevant worksites	Implemented
		The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.	Contractor	All relevant worksites	Implemented
		The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle.	Contractor	All relevant worksites	Implemented
		All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.	Contractor	All relevant worksites	Implemented
		The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.	Contractor	All relevant worksites	Implemented
		When delivering inert C&D material to public fill reception facilities, the material should consist entirely of inert construction waste and of size less than 250mm or other sizes as agreed with the Secretary of the Public Fill Committee. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system as stipulated in the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction	Contractor	All relevant worksites	Implemented

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		and Demolition Materials” should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.			
		<u>Chemical Waste</u>			
		After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals should be collected by a licensed collector for disposal at the CWTF or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Contractor	All relevant worksites	Implemented
		<u>General Refuse</u>			
		General refuse should be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Effective collection and storage methods (including enclosed and covered area) of site wastes would be required to prevent waste materials from being blown around by wind, wastewater discharge by flushing or leaching into the marine environment, or creating odour nuisance or pest and vermin problem.	Contractor	All relevant worksites	Implemented
Land Contamination Measures					
		For any excavation works conducted at Radar Station			
AEIAR-130/2009 S3.6.57	AEIAR 130/2009 EM&A Manual S4.6	As the risk due to dermal contact with groundwater by site workers is uncertain, it is recommended that personnel protective equipment (PPE) be used by site workers as a mitigation measure.	Contractor	All relevant worksites	Not Applicable
Landscape and Visual Impact					
New Distributor Roads Serving the Planned KTD					
		<u>Construction Phase</u>			
AEIAR-130/2009 S3.8.12	AEIAR 130/2009 EM&A Manual S2.8	All existing trees should be carefully protected during construction.	Contractor	All relevant worksites	Not Applicable
		Trees unavoidably affected by the works should be transplanted where practical. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with ETWBC 2/2004 and 3/2006. Final locations of transplanted trees should be agreed prior to commencement of the work.	Contractor	All relevant worksites	Not Applicable
		Control of night-time lighting.	Contractor	All relevant	Not Applicable

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,
5 Lok Yi Street, Tai Lam,
Tuen Mun, N.T.,
Hong Kong.

Tel : +852 2450 8233
Fax : +852 2450 6138
E-mail : matlab@fugro.com
Website : www.fugro.com



EIA Ref	EM&A Ref	Environmental Protection Measures / Mitigation Measures	Who to implement the measure	Location / Timing	Construction Phase Implementation Status
		Erection of decorative screen hoarding.	Contractor	worksites All relevant worksites	Implemented
Trunk Road T2					
		<u>Construction Phase</u>			
AEIAR-174/2013 S9.9.1.1	AEIAR-174/2013 EM&A Manual S7.2.1.2	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	Contractor	All relevant worksites	Not Applicable
		Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	Contractor	All relevant worksites	Not Applicable
		Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	Contractor	All relevant worksites	Partially Implemented
		Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance.	Contractor	All relevant worksites	Implemented
		Erection of decorative screen hoarding should be designed to be compatible with the existing urban context.	Contractor	All relevant worksites	Implemented
		All lighting in construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC user. The contractor shall consider other security measures, which shall minimize the visual impacts.	Contractor	All relevant worksites	Not Applicable
General Condition					
		The Permit Holder shall display conspicuously a copy of this Permit on the Project site(s) at all vehicular site entrances/exits or at a convenient location for public's information at all times. The Permit Holder shall ensure that the most updated information about the Permit, including any amended Permit, is displayed at such locations. If the Permit Holder surrenders a part or the whole of the Permit, the notice he sends to the Director shall also be displayed at the same locations as the original Permit. The suspended, varied or cancelled Permit shall be removed from display at the Project site(s).	Contractor	All relevant worksites	Implemented

Implementation status: Implemented / Partially Implemented / Not Implemented / Not Applicable
