

**Noise Impact Monitoring Result for
Kai Tak Development - Stage 3 Infrastructure Works for
Developments at the Southern Part of the Former Runway**

KTD 1a: Centre of Excellence in Paediatrics (Children's Hospital)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
02-Jul-19	09:46	60	62	56	0.0	Cloudy
08-Jul-19	10:38	70	74	66	0.2	Cloudy
13-Jul-19	09:19	69	73	67	0.1	Fine
19-Jul-19	10:32	70	74	65	0.1	Fine
25-Jul-19	08:30	68	70	65	0.0	Fine
31-Jul-19	09:32	69	73	66	1.4	Cloudy
Max		70				
Min		60				
Limit Level		75				

KTD 2b: G/I/C Zone next to Kwun Tong Bypass (Next to the site of the New Acute Hospital)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
02-Jul-19	10:43	72	75	59	0.7	Cloudy
08-Jul-19	11:14	75	76	71	0.2	Cloudy
13-Jul-19	10:07	74	77	73	0.1	Fine
19-Jul-19	11:40	74	79	68	0.0	Fine
25-Jul-19	10:24	73	74	72	0.0	Fine
31-Jul-19	10:13	72	78	69	2.1	Cloudy
Max		75				
Min		72				
Limit Level		75				

KER 1b: Site Boundary at Cheung Yip Street




Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
02-Jul-19	09:02	63	65	60	0.9	Cloudy
08-Jul-19	10:00	71	73	67	0.0	Cloudy
13-Jul-19	08:30	70	74	68	0.2	Fine
19-Jul-19	09:47	69	74	66	0.1	Fine
25-Jul-19	09:33	70	72	67	0.0	Fine
31-Jul-19	10:55	75	79	72	2.5	Cloudy
Max		75				
Min		63				
Limit Level		75				

Note:

KTD1a: Façade Measurement

KTD2b & KER1b: Free-field measurement (+3dB(A) correction has been applied)

No raining or wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation.

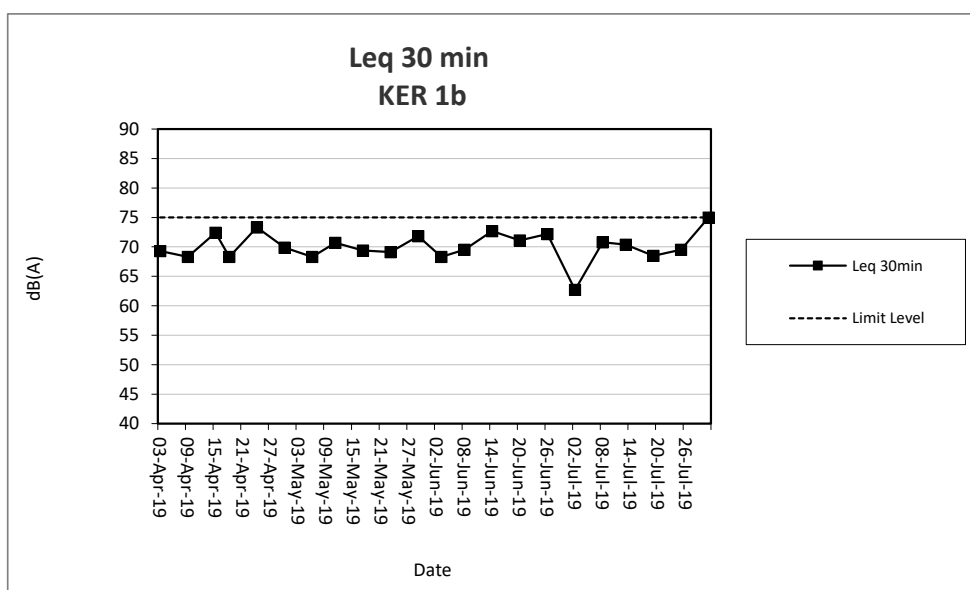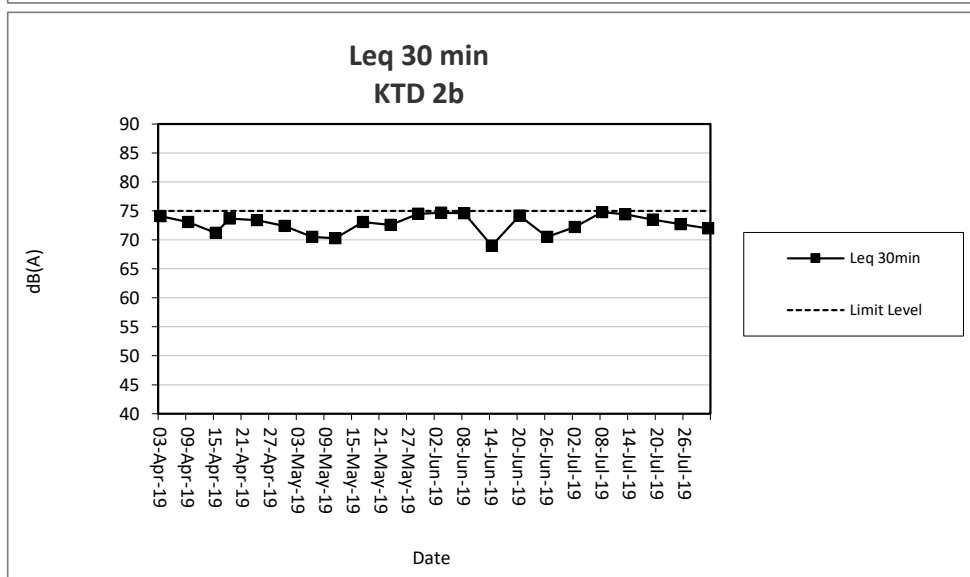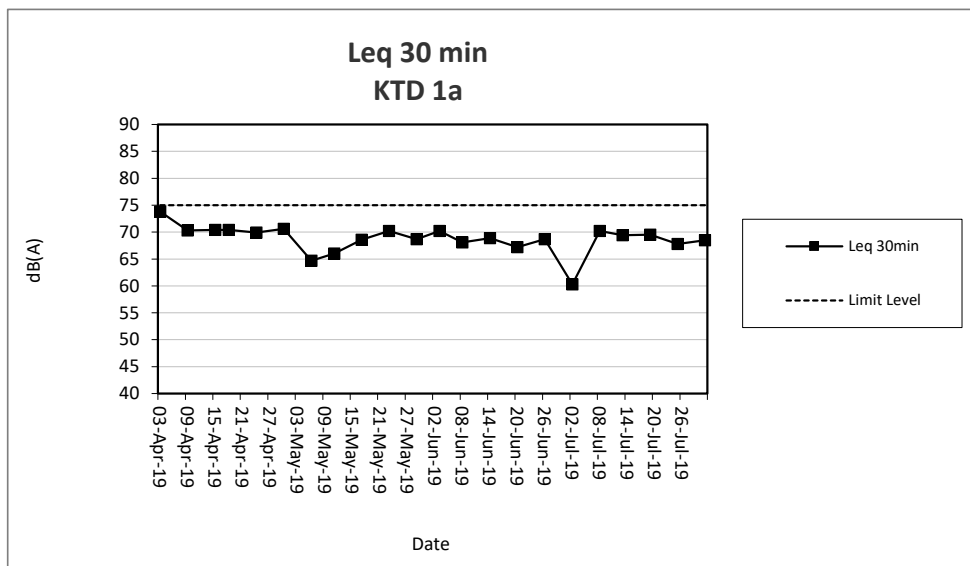

Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.2.
- 2) The weather conditions during the reporting period can be referred to Appendix K.
- 3) Any other factors which might affect the monitoring results can be referred to Section 3.7.2.
- 4) QA/QC results, calibration results and detection limits can be referred to Appendix D.
