

**Noise Impact Monitoring Result for
Kai Tak Development - Stage 3 Infrastructure Works for
Developments at the Southern Part of the Former Runway**

KTD 1a: Centre of Excellence in Paediatrics (Children's Hospital)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
1-Jun-20	09:42	67	68	64	0.2	Fine
6-Jun-20	08:31	70	71	67	0.6	Cloudy
12-Jun-20	09:00	67	70	65	0.0	Fine
18-Jun-20	08:34	67	69	64	0.2	Fine
24-Jun-20	08:45	68	70	66	0.3	Fine
30-Jun-20	08:30	68	70	65	0.5	Fine
Max		70				
Min		67				
Limit Level		75				

KTD 2c: G/I/C Zone next to Kwun Tong Bypass (Next to the Kowloon Bay Sewage Interception Station)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
1-Jun-20	10:29	75	79	71	0.2	Fine
6-Jun-20	09:11	74	76	72	0.5	Cloudy
12-Jun-20	09:39	74	79	73	0.0	Fine
18-Jun-20	09:13	75	76	74	0.4	Fine
24-Jun-20	09:26	74	75	72	0.2	Fine
30-Jun-20	09:12	74	74	73	0.7	Fine
Max		75				
Min		74				
Limit Level		75				

KER 1b: Site Boundary at Cheung Yip Street




Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
1-Jun-20	09:00	74	74	73	0.4	Fine
6-Jun-20	09:52	72	73	71	0.4	Cloudy
12-Jun-20	10:22	75	82	73	0.5	Fine
18-Jun-20	09:56	74	75	73	0.0	Fine
24-Jun-20	10:07	71	72	70	0.4	Fine
30-Jun-20	09:58	72	73	71	0.5	Fine
Max		75				
Min		71				
Limit Level		75				

Note:

KTD1a: Façade Measurement

KTD2c & KER1b: Free-field measurement (+3dB(A) correction has been applied)

No raining or wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation.

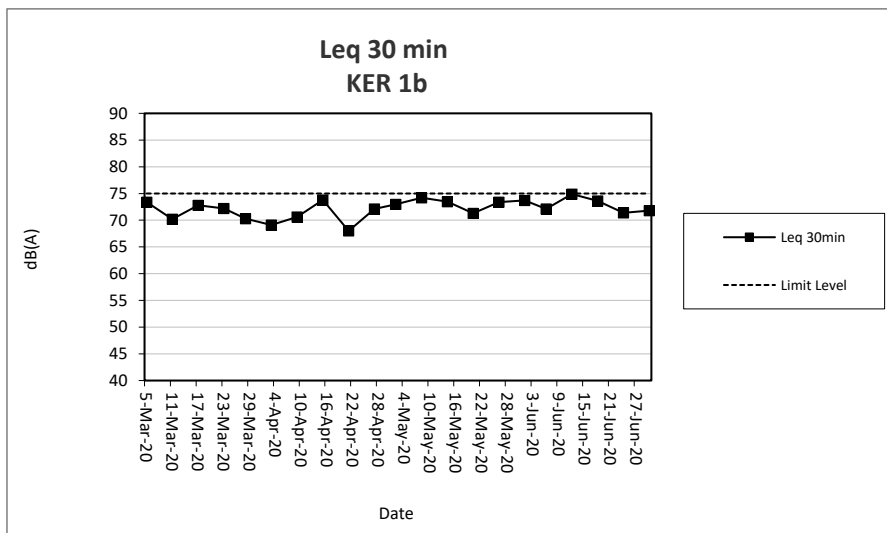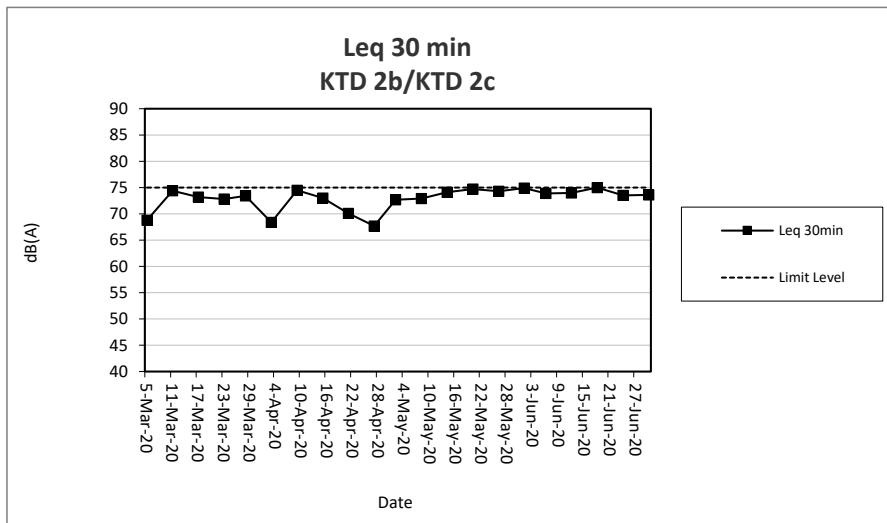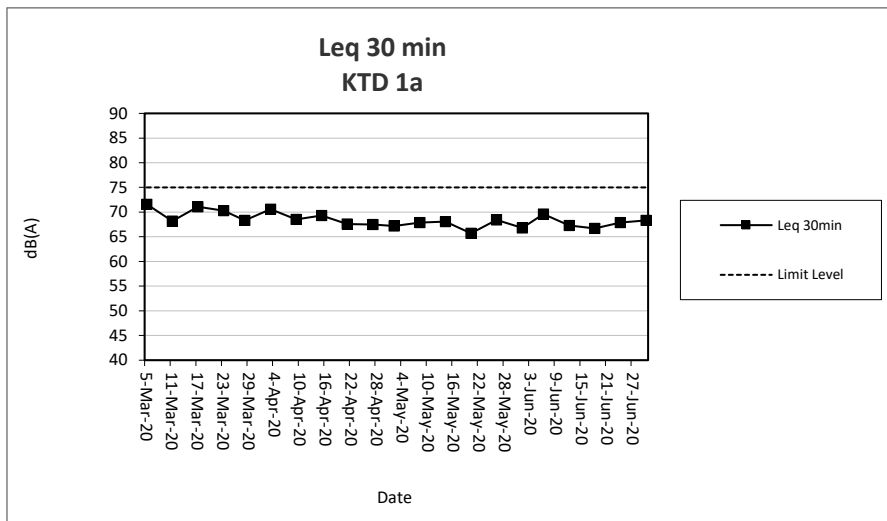

Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.2.
- 2) The weather conditions during the reporting period can be referred to Appendix K.
- 3) Any other factors which might affect the monitoring results can be referred to Section 3.7.2.
- 4) QA/QC results, calibration results and detection limits can be referred to Appendix D.
- 5) KTD 2b was relocated to KTD 2c on 8 April 2020
