Hyder - Meinhardt JV

# KL/2014/03 Kai Tak Development - Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

CEDD 土木工程拓展署 Civil Engineering and Development Department 九龍拓展處 Kowloon Development Office

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish |
|---|---|---|---|---|---|
| **KL/2014/03-Stage 3 Infrastructure Works for Developments at the Southern Par** | | 1200 | 660 | 04-Jan-16 A | 21-Jul-19 |
| **Project Key Dates** | | 1190 | 630 | 01-Feb-16 A | 21-Jun-19 |
| **Project Completion Date** | | 0 | 0 | 26-Oct-17 | 26-Oct-17 |
| K-PK-PCD-1200 | Section 2 - Demolition of Radar Tower and Guard House within Portions X and P of the Site | 0 | 0 | | 26-Oct-17* |
| **Site Handover Date** | | 91 | 91 | 30-Sep-17 | 29-Dec-17 |
| K-PK-SHD-1100 | Portion B | 0 | 0 | | 30-Sep-17* |
| K-PK-SHD-1500 | Portion E | 0 | 0 | | 29-Dec-17* |
| K-PK-SHD-2500 | Portion R | 0 | 0 | | 29-Dec-17* |
| **General Submission** | | 375 | 102 | 15-Dec-16 A | 09-Jan-18 |
| **Alternative Design Submission and Approval** | | 84 | 84 | 30-Sep-17 | 22-Dec-17 |
| ***Package B06 : SUS Top & base slab and intermediate wall from (CH6+220 to CH6+568)*** | | 84 | 84 | 30-Sep-17 | 22-Dec-17 |
| K-PA-ADS-1420 | Revise & resubmit DDA drawing (SUS Top & Base slab and Intermediate wall from CH6+220 to CH6+568) | 28 | 28 | 30-Sep-17 | 27-Oct-17 |
| K-PA-ADS-1430 | Engineer's review and approval | 56 | 56 | 28-Oct-17 | 22-Dec-17 |
| **Major Temporary Works Design** | | 127 | 102 | 05-Sep-17 A | 09-Jan-18 |
| K-PA-GSP-6820 | ELS design for construction of SUS from CH6+220 to CH6+291 in Zone 2 - horizontal members | 56 | 46 | 05-Sep-17 A | 14-Nov-17 |
| K-PA-GSP-6840 | ELS design for construction of subway A (Bay 1&5) | 56 | 56 | 12-Nov-17 | 06-Jan-18 |
| K-PA-GSP-6900 | Falsework design for construction of top slab of SUS structure | 56 | 56 | 15-Nov-17 | 09-Jan-18 |
| **Major Construction Works Method Statement** | | 372 | 99 | 15-Dec-16 A | 06-Jan-18 |
| K-PA-GSP-7160 | Method statement of Excavation and ELS for SUS Construction for Zone 4 | 28 | 8 | 12-Aug-17 A | 07-Oct-17 |
| K-PA-GSP-7165 | Engineer's comments and approval | 28 | 28 | 08-Oct-17 | 04-Nov-17 |
| K-PA-GSP-7170 | Method statement of Excavation and ELS for SUS Construction for Zone 2 | 28 | 19 | 20-Sep-17 A | 18-Oct-17 |
| K-PA-GSP-7175 | Engineer's comments and approval | 28 | 28 | 19-Oct-17 | 15-Nov-17 |
| K-PA-GSP-7450 | Method statement for Construction of top slab and base slab of SUS | 28 | 28 | 19-Oct-17 | 15-Nov-17 |
| K-PA-GSP-7455 | Engineer's comments and approval | 28 | 28 | 16-Nov-17 | 13-Dec-17 |
| K-PA-GSP-7460 | Method statement for Construction of subway A (Bay 1&5) | 28 | 28 | 12-Nov-17 | 09-Dec-17 |
| K-PA-GSP-7465 | Engineer's comments and approval | 28 | 28 | 10-Dec-17 | 06-Jan-18 |
| K-PA-GSP-7490 | Method statement for Erection and Removal of the temporary vehicular and pedestrian access for HKCH | 28 | 0 | 15-Dec-16 A | 09-May-17 A |
| K-PA-GSP-7495 | Engineer's comments and approval | 28 | 14 | 10-May-17 A | 13-Oct-17 |
| **Materials Procurement (Major Materials)** | | 901 | 350 | 01-Feb-16 A | 14-Sep-18 |
| **ELS struct / waling** | | 360 | 65 | 10-Jun-16 A | 03-Dec-17 |
| K-PA-MP-1150 | Manufacturing & delivery to site | 360 | 65 | 10-Jun-16 A | 03-Dec-17 |

中國路橋工程有限責任公司 CHINA ROAD AND BRIDGE CORPORATION

◆ Milestone
Critical Activity
Non-Critical Activity
Remaining Level of Effort
Actual Work

## 3 MRP Oct 2017 - Dec 2017



Project ID :22 3MPR Oct - Dec 17
Layout : KL201403 3MRP


3 Months Rolling Programme

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 30-Sep-17 | Oct 17 - Dec 17 | | |

Hyder - Meinhardt JV

# KL/2014/03 Kai Tak Development - Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

CEDD 土木工程拓展署 Civil Engineering and Development Department 九龍拓展處 Kowloon Development Office

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish |
|---|---|---|---|---|---|
| **Water Works** | | 150 | 150 | 30-Sep-17 | 26-Feb-18 |
| K-PA-MP-1050 | Manufacturing & delivery to site | 150 | 150 | 30-Sep-17 | 26-Feb-18 |
| **Steel H-Pile** | | 420 | 15 | 01-Feb-16 A | 14-Oct-17 |
| K-PA-MP-1250 | Manufacturing & delivery to site | 420 | 15 | 01-Feb-16 A | 14-Oct-17 |
| **Chilled Water Pipes - DCS** | | 550 | 350 | 06-Feb-17 A | 14-Sep-18 |
| K-PA-MP-1350 | Manufacturing & delivery to site | 550 | 350 | 06-Feb-17 A | 14-Sep-18 |
| **Prelimiaries** | | 1190 | 630 | 11-Mar-16 A | 21-Jun-19 |
| K-DR-PRE-1800 | Submission of time-lapsed photographs and video | 1190 | 630 | 11-Mar-16 A | 21-Jun-19 |
| **Barge Loading Facilities** | | 430 | 328 | 21-Jun-17 A | 09-Nov-18 |
| K-DR-PRE-1480 | Operation of temporary barging point | 430 | 328 | 21-Jun-17 A | 09-Nov-18 |
| **Instrumentation and Monitoring** | | 443 | 319 | 25-Apr-16 A | 14-Aug-18 |
| **Eastbound Instrumentation and Monitoring** | | 30 | 30 | 12-Oct-17 | 16-Nov-17 |
| ***Inclinometer (INC)*** | | 30 | 30 | 12-Oct-17 | 16-Nov-17 |
| K-IM-INC-1320 | Installation of INC at Zone 2 | 10 | 10 | 06-Nov-17 | 16-Nov-17 |
| K-IM-INC-1335 | Installation of INC at Zone 4 (CH6+467 to CH6+540) | 10 | 10 | 12-Oct-17 | 23-Oct-17 |
| K-IM-INC-1340 | Installation of INC at Zone 4 (CH6+540 to CH6+568) | 10 | 10 | 12-Oct-17 | 23-Oct-17 |
| **Westbound Instrumentation and Monitoring** | | 38 | 38 | 30-Sep-17 | 16-Nov-17 |
| ***Piezometer/Standpipe (PZR)*** | | 10 | 10 | 30-Sep-17 | 13-Oct-17 |
| K-IM-PZR-1360 | Installation of PZR at Zone 2 | 10 | 10 | 30-Sep-17 | 13-Oct-17 |
| ***Inclinometer (INC)*** | | 30 | 30 | 12-Oct-17 | 16-Nov-17 |
| K-IM-INC-1360 | Installation of INC at Zone 2 | 10 | 10 | 06-Nov-17 | 16-Nov-17 |
| K-IM-INC-1375 | Installation of INC at Zone 4 (CH6+467 to CH6+540) | 10 | 10 | 12-Oct-17 | 23-Oct-17 |
| K-IM-INC-1380 | Installation of INC at Zone 4 (CH6+540 to CH6+568) | 10 | 10 | 12-Oct-17 | 23-Oct-17 |
| **Tilt Monitoring Tile Plates** | | 310 | 319 | 25-Apr-16 A | 14-Aug-18 |
| K-IM-TMT-1000 | Tilt Monitoring near PWCL | 310 | 319 | 25-Apr-16 A | 14-Aug-18 |
| **Section 1 of the Works-Remainder of the Works** | | 185 | 124 | 17-Aug-17 A | 31-Jan-18 |
| **Roadwork and Drainage Works** | | 185 | 124 | 17-Aug-17 A | 31-Jan-18 |
| **Road D4-4 (Cheung Yip Street)** | | 185 | 124 | 17-Aug-17 A | 31-Jan-18 |
| ***CH240 - CH400 Northbound*** | | 153 | 100 | 17-Aug-17 A | 31-Jan-18 |
| **Sewerage Works** | | 40 | 40 | 26-Oct-17 | 12-Dec-17 |
| K-01-RWS-9815 | Excavation of Sewerage Pipe and Manhole (Site 3C1-1) | 6 | 6 | 26-Oct-17 | 02-Nov-17 |

中國路橋工程有限責任公司 CHINA ROAD AND BRIDGE CORPORATION

◆ Milestone
Critical Activity
Non-Critical Activity
Remaining Level of Effort
Actual Work

## 3 MRP Oct 2017 - Dec 2017



Project ID :22 3MPR Oct - Dec 17
Layout : KL201403 3MRP


3 Months Rolling Programme

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 30-Sep-17 | Oct 17 - Dec 17 | | |

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish |
|---|---|---|---|---|---|
| K-01-RWS-9820 | Laying Sewerage Pipe and Manhole (Site 3C1-1) | 22 | 22 | 03-Nov-17 | 28-Nov-17 |
| K-01-RWS-9830 | Backfilling Sewerage Pipe and Manhole (Site 3C1-1) | 12 | 12 | 29-Nov-17 | 12-Dec-17 |
| **Laying of Drainage Pipe and Construction of Manhole (M206 to M213)** | | 67 | 55 | 17-Aug-17 A | 06-Dec-17 |
| K-01-RWS-9340 | Excavation of Drainage Pipe and Manhole (M209 to M213) | 8 | 20 | 19-Sep-17 A | 25-Oct-17 |
| K-01-RWS-9350 | Laying Drainage Pipe and Construction Manhole (M209 to M213) | 30 | 35 | 28-Sep-17 A | 22-Nov-17 |
| K-01-RWS-9410 | Backfilling Drainage Pipe and Manhole (M209 to M213) | 12 | 12 | 17-Aug-17 A | 06-Dec-17 |
| **Road Works** | | 40 | 40 | 13-Dec-17 | 31-Jan-18 |
| K-01-RWS-9440 | Construction of Road Base and Road Pavement | 40 | 40 | 13-Dec-17 | 31-Jan-18 |
| ***Seawall Modification Works*** | | 41 | 41 | 24-Oct-17 | 03-Dec-17 |
| K-01-RWS-9710 | Concreting for Haunching | 15 | 15 | 24-Oct-17 | 10-Nov-17 |
| K-01-RWS-9712 | Removal of Existing Concrete coping | 5 | 5 | 11-Nov-17 | 16-Nov-17 |
| K-01-RWS-9714 | Installation of Last DN2100 Drainage Pipe | 7 | 7 | 17-Nov-17 | 24-Nov-17 |
| K-01-RWS-9750 | Erection of Formwork and Concreting for the Seawall | 5 | 5 | 24-Nov-17 | 29-Nov-17 |
| K-01-RWS-9770 | AI test and CCTV test for drainage pipe | 1 | 1 | 29-Nov-17 | 30-Nov-17 |
| K-01-RWS-9780 | Beakfilling of Drianage pipe near seawall | 1 | 1 | 30-Nov-17 | 01-Dec-17 |
| K-01-RWS-9790 | Maintance department handover inspection | 1 | 1 | 01-Dec-17 | 02-Dec-17 |
| K-01-RWS-9800 | Removal of stop log | 1 | 1 | 02-Dec-17 | 03-Dec-17 |
| **Section 1A of the Works -Construction of Supporting Underground Structure (Alternati** | | 298 | 119 | 15-Oct-16 A | 26-Feb-18 |
| **SUS and Ventilation Adits from CH6+150 to CH6+220 in Zone 1** | | 221 | 89 | 05-Sep-17 A | 18-Jan-18 |
| **Construction of Tunnel Box Structure** | | 221 | 89 | 05-Sep-17 A | 18-Jan-18 |
| ***SUS Bay 1 (Ch6150-Ch6167.5)*** | | 62 | 62 | 12-Oct-17 | 23-Dec-17 |
| K-1A-SV1-8250 | Installation of Re-porp Struct inside VA1, VA2, VA3 and SA | 4 | 4 | 14-Oct-17 | 18-Oct-17 |
| K-1A-SV1-8260 | Backfilling with Sand and Casting Mass Concrete between VA1, VA2 and SA | 5 | 5 | 12-Oct-17 | 17-Oct-17 |
| K-1A-SV1-8270 | Removal of Strut S4 | 4 | 4 | 19-Oct-17 | 23-Oct-17 |
| K-1A-SV1-8290 | Erection of Scaffold and Formwork for Base Slab Construction (inside VA1 and VA3) | 7 | 7 | 24-Oct-17 | 01-Nov-17 |
| K-1A-SV1-8300 | Backfilling with Sand to Formation Level | 6 | 6 | 02-Nov-17 | 08-Nov-17 |
| K-1A-SV1-8320 | Construction of Base Slab | 12 | 12 | 09-Nov-17 | 22-Nov-17 |
| K-1A-SV1-8330 | Removal of Strut S3 | 4 | 4 | 23-Nov-17 | 27-Nov-17 |
| K-1A-SV1-8350 | Side Wall and Intermediate Wall Construction | 10 | 10 | 28-Nov-17 | 08-Dec-17 |
| K-1A-SV1-8360 | Erection of Scaffold and Installation of Re-prop Struct inside W/B and E/B | 8 | 8 | 09-Dec-17 | 18-Dec-17 |
| K-1A-SV1-8370 | Removal of Strut S2 | 5 | 5 | 19-Dec-17 | 23-Dec-17 |



Hyder - Meinhardt JV

# KL/2014/03 Kai Tak Development - Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

CEDD 土木工程拓展署 Civil Engineering and Development Department 九龍拓展處 Kowloon Development Office

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish |
|---|---|---|---|---|---|
| ***SUS Bay 4 (Ch6202.5-Ch6220)*** | | 201 | 30 | 05-Sep-17 A | 07-Nov-17 |
| K-1A-SV1-9105 | Construction of VA2 Wall Structure | 10 | 20 | 05-Sep-17 A | 25-Oct-17 |
| K-1A-SV1-9115 | Strip Formwork and Remedial Works for Waterproofing | 10 | 10 | 26-Oct-17 | 07-Nov-17 |
| ***SUS Bay 3 (Ch6185-Ch6202.5)*** | | 201 | 30 | 05-Sep-17 A | 07-Nov-17 |
| K-1A-SV1-9165 | Construction of VA2 Wall Structure | 10 | 20 | 05-Sep-17 A | 25-Oct-17 |
| K-1A-SV1-9175 | Strip Formwork and Remedial Works for Waterproofing | 10 | 10 | 26-Oct-17 | 07-Nov-17 |
| ***SUS Bay 2 (Ch6167.5-Ch6185)*** | | 89 | 89 | 25-Sep-17 A | 18-Jan-18 |
| K-1A-SV1-8870 | Construction of VA2 Wall Structure | 8 | 17 | 25-Sep-17 A | 21-Oct-17 |
| K-1A-SV1-8880 | Strip Formwork and Remedial Works for Waterproofing | 3 | 3 | 23-Oct-17 | 25-Oct-17 |
| K-1A-SV1-8890 | Backfilling with Sand and Removal part of SV1 | 4 | 4 | 27-Oct-17 | 01-Nov-17 |
| K-1A-SV1-8900 | Installation of Precast Concrete Slab for Base Slab Constrcution | 2 | 2 | 02-Nov-17 | 03-Nov-17 |
| K-1A-SV1-8910 | Casting Blinding Layer (No-Fine) and Laying Waterproofing Works | 4 | 4 | 04-Nov-17 | 08-Nov-17 |
| K-1A-SV1-8920 | Construction of Base Slab | 12 | 12 | 09-Nov-17 | 22-Nov-17 |
| K-1A-SV1-8930 | Removal of Strut S3 | 4 | 4 | 23-Nov-17 | 27-Nov-17 |
| K-1A-SV1-8950 | Construction of Side Wall Construction | 10 | 10 | 28-Nov-17 | 08-Dec-17 |
| K-1A-SV1-8960 | Erection of Scaffold and Installation of Re-prop Struct inside W/B and E/B | 8 | 8 | 09-Dec-17 | 18-Dec-17 |
| K-1A-SV1-8970 | Removal of Strut S2 | 4 | 4 | 19-Dec-17 | 22-Dec-17 |
| K-1A-SV1-8990 | Constrcution of Top Slab | 20 | 20 | 23-Dec-17 | 18-Jan-18 |
| **SUS and Ventilation Adits from CH6+220 to CH6+291 in Zone 2** | | 180 | 119 | 15-Oct-16 A | 26-Feb-18 |
| **E/B Construction of D-Wall** | | 96 | 35 | 15-Oct-16 A | 13-Nov-17 |
| K-1A-SV2-2750 | Testing of D-wall (Sonic test and IC) | 20 | 20 | 15-Oct-16 A | 25-Oct-17 |
| K-1A-SV2-2800 | Toe Grouting Works | 20 | 18 | 26-Sep-17 A | 13-Nov-17 |
| **Construction of Socketed H-Pile** | | 58 | 58 | 06-Oct-17 | 13-Dec-17 |
| K-1A-SV2-3300 | Installation of Socketted H-piles (CH6+220 to CH6+248) | 25 | 25 | 06-Oct-17 | 04-Nov-17 |
| K-1A-SV2-3310 | Implementation of stage 1A Shing Cheong Road diversion | 5 | 5 | 06-Nov-17 | 10-Nov-17 |
| K-1A-SV2-3320 | Excavation and trim Dwall for construction of temporary decking | 9 | 9 | 11-Nov-17 | 21-Nov-17 |
| K-1A-SV2-3330 | Installation of first layer of strut | 5 | 5 | 22-Nov-17 | 27-Nov-17 |
| K-1A-SV2-3340 | Construction of temporary decking at Zone 2 | 11 | 11 | 28-Nov-17 | 09-Dec-17 |
| K-1A-SV2-3350 | Implementation of stage 2A Shing Cheong Road diversion | 3 | 3 | 11-Dec-17 | 13-Dec-17 |
| K-1A-SV2-3400 | Installation of Socketted H-piles (CH6+248 to CH6+265) | 20 | 20 | 06-Nov-17 | 28-Nov-17 |
| K-1A-SV2-3500 | Loading test for Socketted H-Piles | 10 | 10 | 11-Nov-17 | 22-Nov-17 |

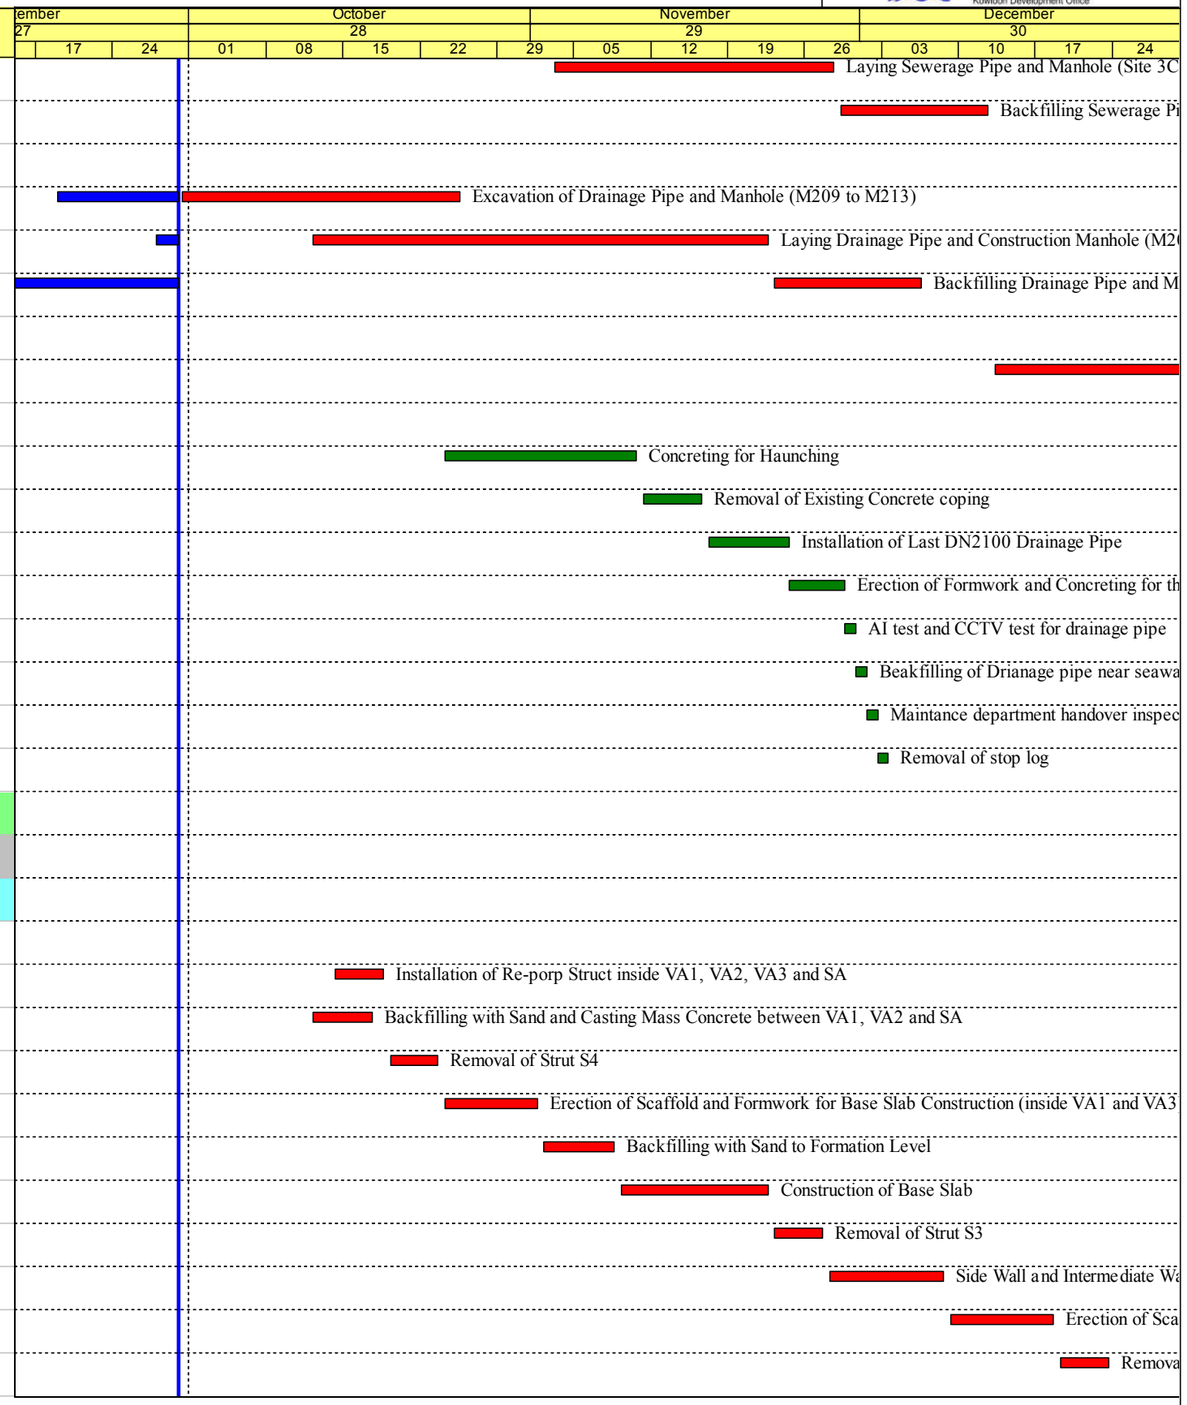


中國路橋工程有限責任公司 CHINA ROAD AND BRIDGE CORPORATION

◆ Milestone
Critical Activity
Non-Critical Activity
Remaining Level of Effort
Actual Work

## 3 MRP Oct 2017 - Dec 2017

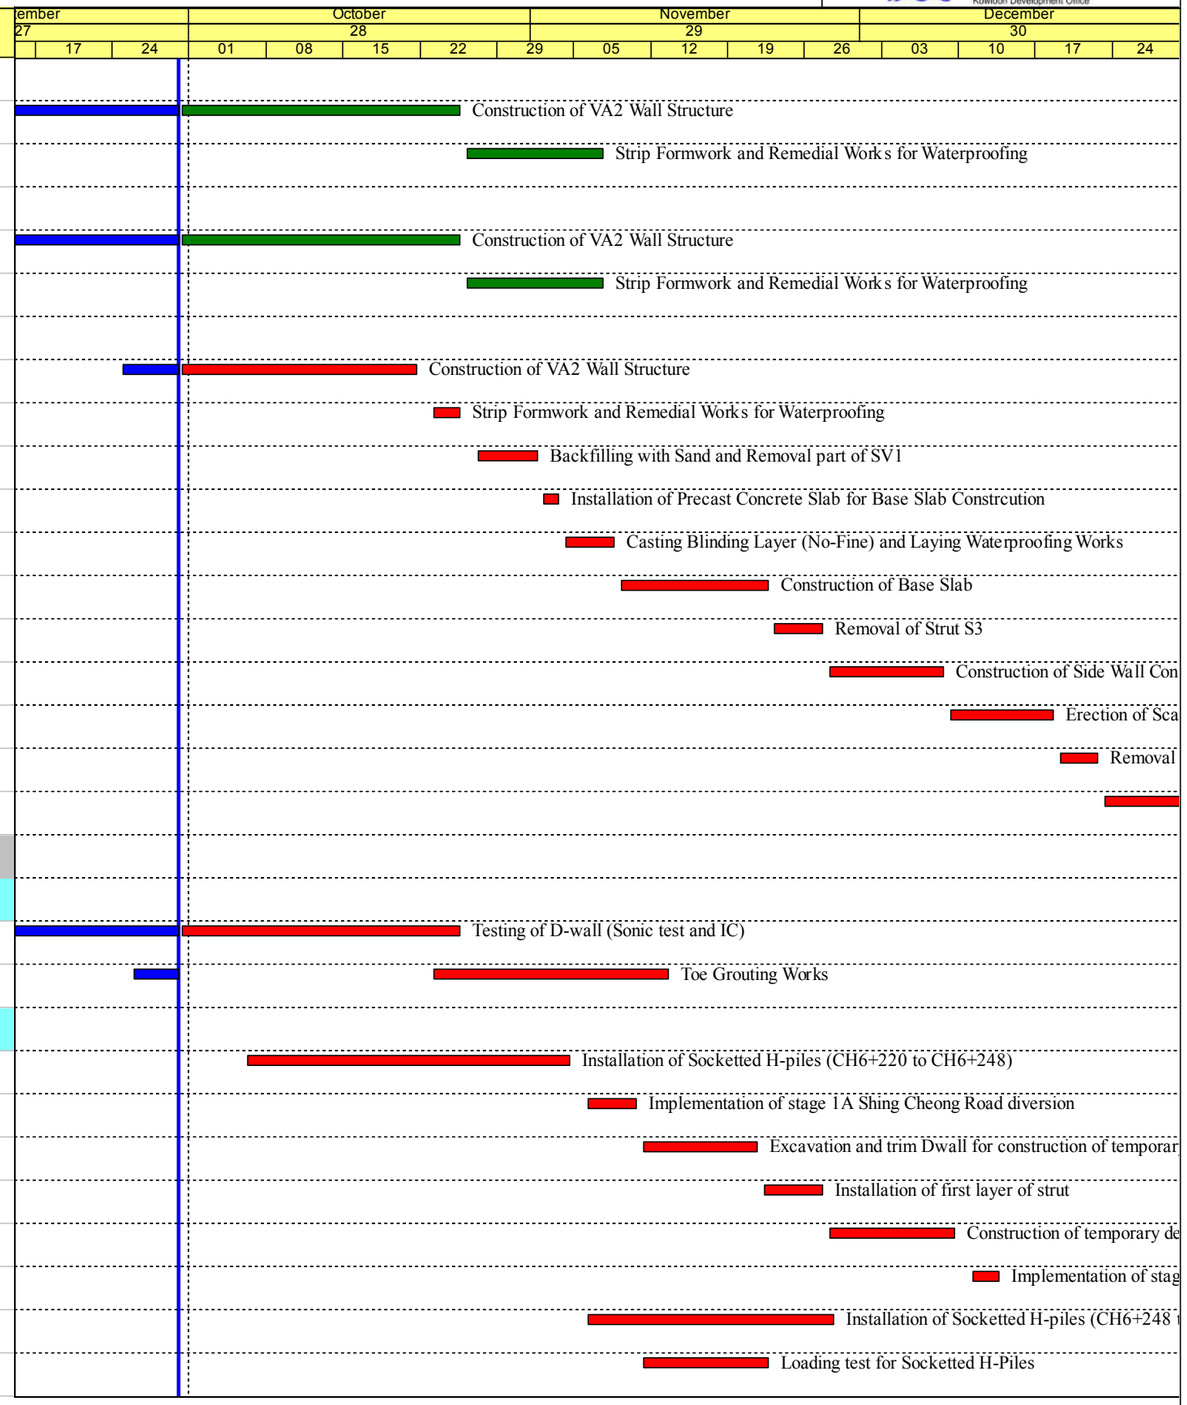

Project ID :22 3MPR Oct - Dec 17
Layout : KL201403 3MRP


3 Months Rolling Programme

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 30-Sep-17 | Oct 17 - Dec 17 | | |

Hyder - Meinhardt JV

# KL/2014/03 Kai Tak Development - Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

CEDD 土木工程拓展署 Civil Engineering and Development Department 九龍拓展處 Kowloon Development Office

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish |
|---|---|---|---|---|---|
| **W/B Construction of D-Wall in TTA Stage 2** | | 38 | 38 | 19-Sep-17 A | 16-Nov-17 |
| K-1A-SV2-4600 | Testing of D-wall (Sonic test and IC) | 28 | 28 | 30-Sep-17 | 04-Nov-17 |
| K-1A-SV2-4700 | Toe Grouting Works | 30 | 18 | 19-Sep-17 A | 16-Nov-17 |
| **Pumping Test** | | 30 | 30 | 06-Nov-17 | 09-Dec-17 |
| K-1A-SV2-6000 | Installation of Dewatering Well, Observation Well and Recharging Well in Zone 2 | 15 | 15 | 06-Nov-17 | 23-Nov-17 |
| K-1A-SV2-6100 | Initial Dewatering to verify the Discharge Rates of Wells for Pumping Test for Excavation in Zone 2 | 1 | 1 | 23-Nov-17 | 23-Nov-17 |
| K-1A-SV2-6110 | Dewatering to Required Levels and Maintained for 48 Hours for Pumping Test for Excavation in Zone 2 | 3 | 3 | 24-Nov-17 | 27-Nov-17 |
| K-1A-SV2-6120 | Ground Water Recovery Stage for Pumping Test for Excavation in Zone 2 | 3 | 3 | 28-Nov-17 | 30-Nov-17 |
| K-1A-SV2-6130 | Review stage for Pumping test for excavation in Zone 2 | 1 | 1 | 01-Dec-17 | 01-Dec-17 |
| K-1A-SV2-6140 | Review Report for Pumping test for excavation in Zone 2 | 7 | 7 | 02-Dec-17 | 09-Dec-17 |
| **Excavation and ELS Construction** | | 68 | 68 | 02-Dec-17 | 26-Feb-18 |
| K-1A-SV2-6200 | Excavation and Lateral Support (S1) to +1.95mPD | 18 | 18 | 02-Dec-17 | 22-Dec-17 |
| K-1A-SV2-6250 | Excavation and Lateral Support (S2) to -2.20mPD | 23 | 23 | 23-Dec-17 | 22-Jan-18 |
| K-1A-SV2-6560 | Construction of temporary steel decking and platforms along the westbound diaphram walls | 50 | 50 | 23-Dec-17 | 26-Feb-18 |
| **SUS Structure from CH6+291 to 6+467 in Zone 3** | | 160 | 83 | 29-Jun-17 A | 11-Jan-18 |
| **Excavation and ELS Construction** | | 160 | 83 | 29-Jun-17 A | 11-Jan-18 |
| K-1A-SV3-5600 | Breaking existing concrete slab / Excavation and Lateral Support (S1) to +1.95mPD | 31 | 0 | 29-Jun-17 A | 30-Sep-17 |
| K-1A-SV3-5650 | Excavation and Lateral Support (S2) to -2.20mPD | 24 | 20 | 25-Aug-17 A | 25-Oct-17 |
| K-1A-SV3-5700 | Excavation and Lateral Support (S4) to -6.20mPD | 25 | 25 | 07-Oct-17 | 06-Nov-17 |
| K-1A-SV3-5750 | Excavation and Lateral Support (S5) to -10.20mPD | 27 | 27 | 07-Nov-17 | 07-Dec-17 |
| K-1A-SV3-5800 | Excavation and Lateral Support (S6) to -14.20mPD | 27 | 27 | 08-Dec-17 | 11-Jan-18 |
| K-1A-SV3-5910 | Construction of temporary steel decking and platforms along the westbound diaphram walls | 65 | 25 | 12-Aug-17 A | 01-Nov-17 |
| **SUS Structure from CH6+467 to 6+568 in Zone 4** | | 151 | 92 | 19-Apr-17 A | 22-Jan-18 |
| **E/B Construction of D-Wall** | | 14 | 5 | 05-Aug-17 A | 07-Oct-17 |
| K-1A-SV4-2460 | Toe Grouting Works | 14 | 5 | 05-Aug-17 A | 07-Oct-17 |
| **Construction of Socketed H-Pile** | | 13 | 13 | 29-Sep-17 A | 17-Oct-17 |
| K-1A-SV4-3600 | Installation of Socketted H-piles (CH6+560 to CH6+565) | 13 | 13 | 29-Sep-17 A | 17-Oct-17 |
| **W/B and End Construction of D-Wall in TTA Stage 1A** | | 56 | 4 | 19-Apr-17 A | 06-Oct-17 |
| K-1A-SV4-4750 | Testing of D-wall (Sonic test and IC) (CH6+510 to CH6+568 and End Wall) | 18 | 0 | 19-Apr-17 A | 30-Sep-17 A |
| K-1A-SV4-4760 | Toe Grouting Works | 14 | 4 | 22-Jul-17 A | 06-Oct-17 |
| **Pumping Test** | | 51 | 25 | 19-Aug-17 A | 01-Nov-17 |

中國路橋工程有限責任公司 CHINA ROAD AND BRIDGE CORPORATION

◆ Milestone
Critical Activity
Non-Critical Activity
Remaining Level of Effort
Actual Work

## 3 MRP Oct 2017 - Dec 2017



Project ID :22 3MPR Oct - Dec 17
Layout : KL201403 3MRP


3 Months Rolling Programme

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 30-Sep-17 | Oct 17 - Dec 17 | | |

Hyder - Meinhardt JV

# KL/2014/03 Kai Tak Development - Stage 3 Infrastructure Works for Developments at the Southern Part of the Former Runway

CEDD 土木工程拓展署 Civil Engineering and Development Department 九龍拓展處 Kowloon Development Office

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish |
|---|---|---|---|---|---|
| K-1A-SV4-5000 | Installation of Dewatering Well, Observation Well and Recharging Well at CH6+467 to CH6+550 | 38 | 10 | 19-Aug-17 A | 13-Oct-17 |
| K-1A-SV4-5005 | Installation of Dewatering Well, Observation Well and Recharging Well at CH6+550 to CH6+568 | 8 | 8 | 30-Sep-17 | 11-Oct-17 |
| K-1A-SV4-5100 | Initial Dewatering to verify the Discharge Rates of Wells for Pumping Test for Excavation in Zone 4 | 1 | 1 | 14-Oct-17 | 14-Oct-17 |
| K-1A-SV4-5110 | Dewatering to Required Levels and Maintained for 48 Hours for Pumping Test for Excavation in Zone 4 | 3 | 3 | 16-Oct-17 | 18-Oct-17 |
| K-1A-SV4-5120 | Ground Water Recovery Stage for Pumping Test for Excavation in Zone 4 | 3 | 3 | 19-Oct-17 | 21-Oct-17 |
| K-1A-SV4-5130 | Review stage for Pumping test for excavation in Zone 4 | 1 | 1 | 23-Oct-17 | 23-Oct-17 |
| K-1A-SV4-5140 | Review Report for Pumping test for excavation in Zone 4 | 7 | 7 | 24-Oct-17 | 01-Nov-17 |
| **Excavation and ELS Construction** | | 93 | 92 | 25-Aug-17 A | 22-Jan-18 |
| K-1A-SV4-5530 | Installation of Steel Bridge for Temporary Vehicular Access at CH6+482 | 10 | 2 | 12-Sep-17 A | 03-Oct-17 |
| K-1A-SV4-5540 | Laying Sheetpiles and Concretng for Temporary Vehicular Access at CH6+482 | 10 | 10 | 04-Oct-17 | 16-Oct-17 |
| K-1A-SV4-5550 | Miscellaneous Activities for Temporary Vehicular Access at CH6+482 | 5 | 5 | 17-Oct-17 | 21-Oct-17 |
| K-1A-SV4-5555 | Breaking existing concrete slab / Excavation to +2.5mPD from CH6+467 to CH6+530 | 17 | 10 | 25-Aug-17 A | 25-Oct-17 |
| K-1A-SV4-5600 | Excavation and Lateral Support (S1) to +0.84mPD | 14 | 14 | 24-Oct-17 | 09-Nov-17 |
| K-1A-SV4-5650 | Excavation and Lateral Support (S2) to -4.20mPD | 18 | 18 | 10-Nov-17 | 30-Nov-17 |
| K-1A-SV4-5700 | Excavation and Lateral Support (S3) to -9.20mPD | 20 | 20 | 01-Dec-17 | 23-Dec-17 |
| K-1A-SV4-5750 | Excavation and Lateral Support (S4) to -14.20mPD | 22 | 22 | 27-Dec-17 | 22-Jan-18 |
| **Section 4B of the Works- Construction of Subway B (Subject to Excision)** | | 0 | 0 | 30-Sep-17 | 30-Sep-17 |
| **Bay 1 & 2** | | 0 | 0 | 30-Sep-17 | 30-Sep-17 |
| K-4B-BAY-3100 | Handover of Portion B | 0 | 0 | | 30-Sep-17* |
| **Bay 3 & 4** | | 0 | 0 | 30-Sep-17 | 30-Sep-17 |
| K-4B-BAY-2480 | Interface Connection Details for HKCN of subway B | 0 | 0 | 30-Sep-17 | |
| **Section 5 of the Works-Completion of All Landscape Softworks** | | 90 | 90 | 30-Sep-17 | 28-Dec-17 |
| K-05-LCS-1000 | Procurement of plant species | 90 | 90 | 30-Sep-17 | 28-Dec-17 |
| **Section 7 of the Works-Preservation and Protection of Existing Trees** | | 1200 | 660 | 04-Jan-16 A | 21-Jul-19 |
| K-07-001-1000 | Section 7 of the Works-Preservation and Protection of Existing Trees | 1200 | 660 | 04-Jan-16 A | 21-Jul-19 |
| **Sections Completion Date** | | 0 | 0 | 30-Sep-17 | 30-Sep-17 |
| K-PK-SCC-2100 | Completion of Section 2-Demolition of Radar Tower and Guard House | 0 | 0 | | 30-Sep-17 |




中國路橋工程有限責任公司 CHINA ROAD AND BRIDGE CORPORATION

◆ Milestone
Critical Activity
Non-Critical Activity
Remaining Level of Effort
Actual Work

## 3 MRP Oct 2017 - Dec 2017

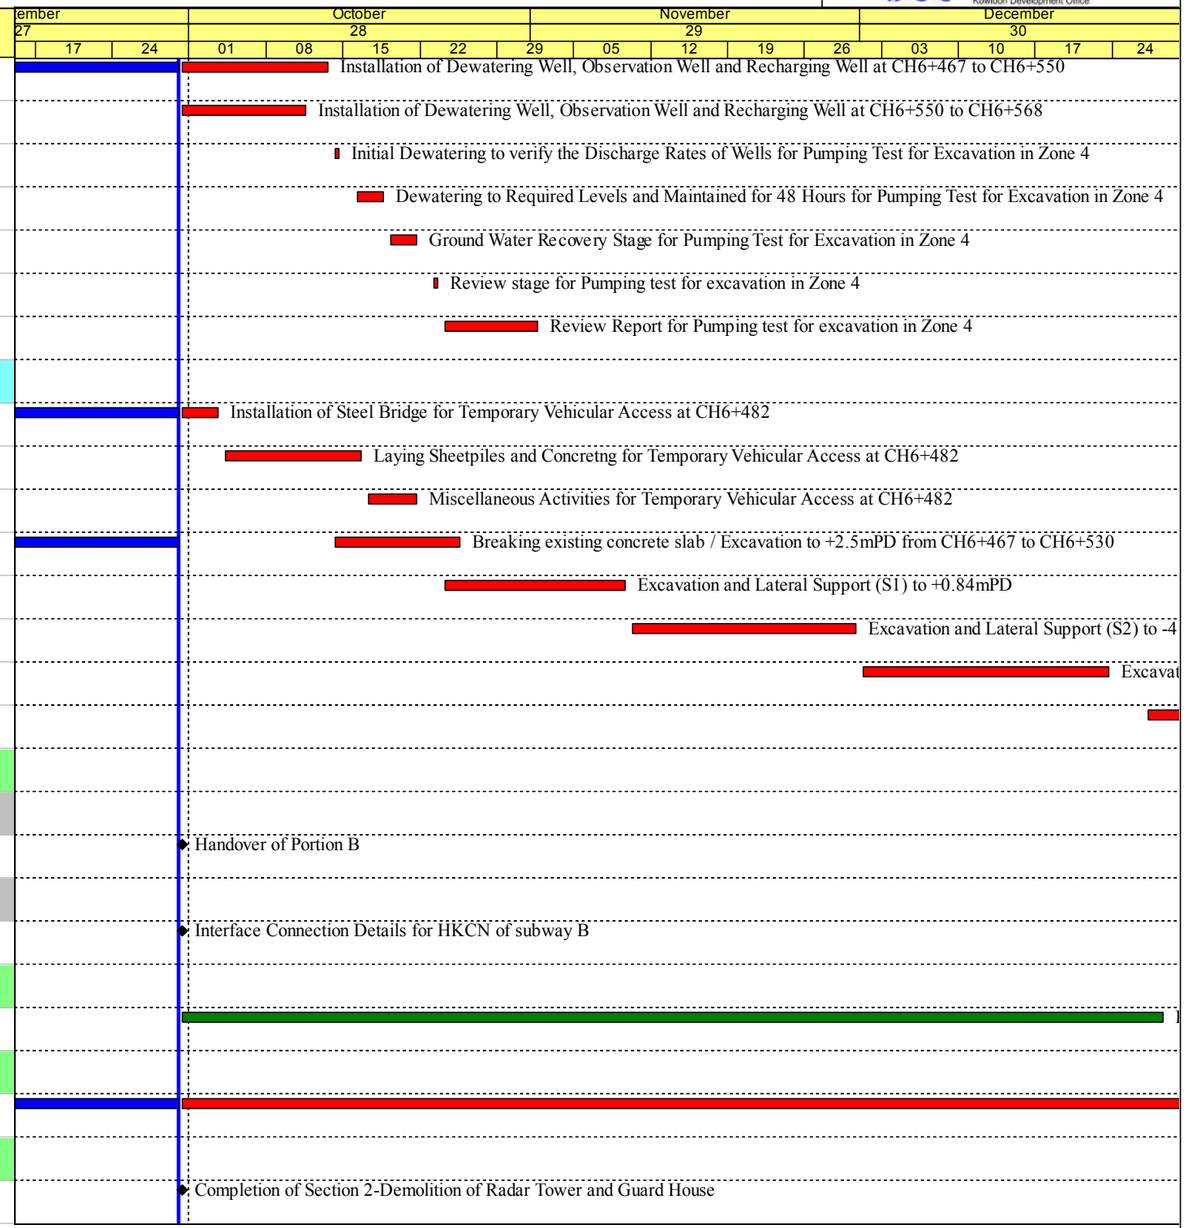

Project ID :22 3MPR Oct - Dec 17
Layout : KL201403 3MRP
Page 6 of 6

| 3 Months Rolling Programme | | | |
|---|---|---|---|
| Date | Revision | Checked | Approved |
| 30-Sep-17 | Oct 17 - Dec 17 | | |
