

Page 1 of 29

Data Date: 04-Dec-21

◆ Milestone

Planned Bar

Critical Activity

◆ Actual Milestone

Actual Work

◆ Baseline Milestone

Baseline Bar

Summary


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES

TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

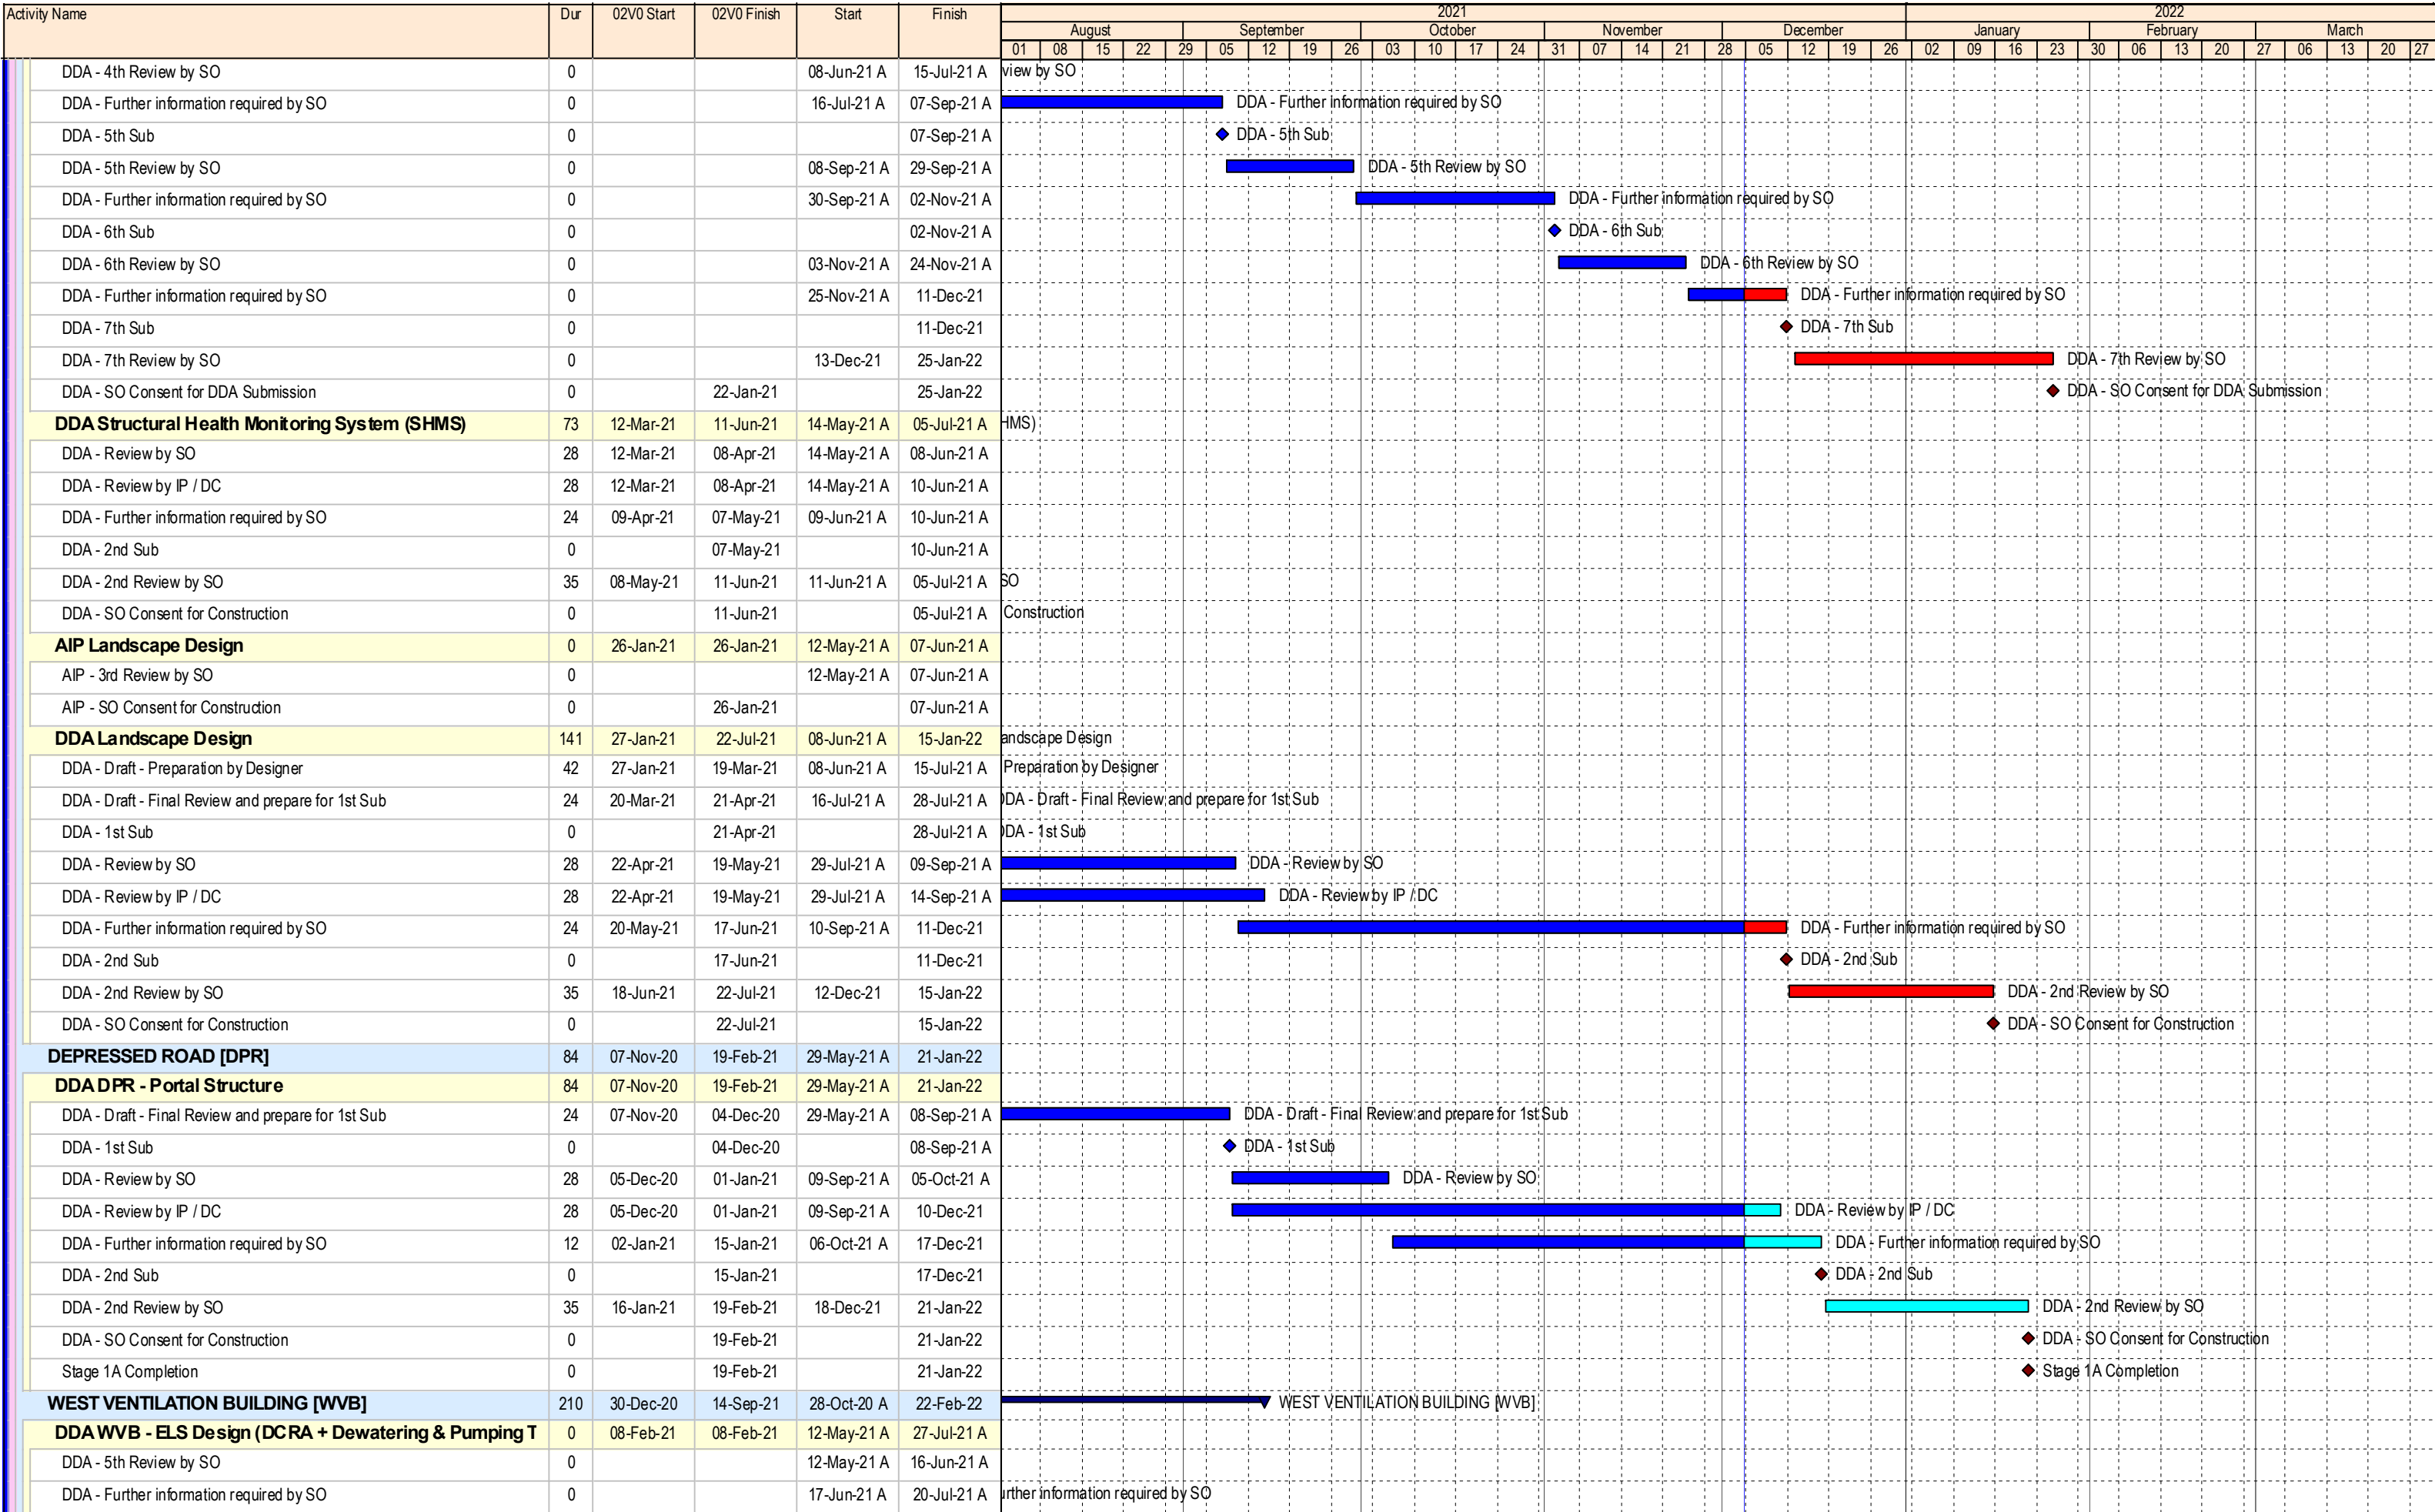

Page 3 of 29
Data Date: 04-Dec-21

 Milestone
 Planned Bar
 Critical Activity
 Actual Milestone
 Actual Work
 Baseline Milestone
 Baseline Bar

 Summary

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 4 of 29 Data Date: 04-Dec-21	◆ Milestone ▬ Planned Bar ▬ CriticalActivity ◆ Actual Milestone ▬ Actual Work ◆ Baseline Milestone ▬ Baseline Bar Summary	ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Nov-21)	BOUYGUES TRAVAUX PUBLICS <table> <tr> <th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr> <tr> <td>18-Dec-19</td><td>00V1</td><td>WYu</td><td></td></tr> <tr> <td>22-Feb-20</td><td>01V0</td><td>SPa/LLo</td><td>WYu</td></tr> <tr> <td>09-Apr-20</td><td>01V1</td><td>SPa/LLo</td><td>WYu</td></tr> <tr> <td>17-Jul-20</td><td>01V2</td><td>SPa/LLo</td><td>WYu</td></tr> <tr> <td>09-Oct-20</td><td>01V3</td><td>SPa/LLo</td><td>WYu</td></tr> <tr> <td>02-Jul-21</td><td>02V0</td><td>SPa/LLo</td><td>WYu</td></tr> </table>	Date	Revision	Checked	Approved	18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu	02-Jul-21	02V0	SPa/LLo	WYu
Date	Revision	Checked	Approved																												
18-Dec-19	00V1	WYu																													
22-Feb-20	01V0	SPa/LLo	WYu																												
09-Apr-20	01V1	SPa/LLo	WYu																												
17-Jul-20	01V2	SPa/LLo	WYu																												
09-Oct-20	01V3	SPa/LLo	WYu																												
02-Jul-21	02V0	SPa/LLo	WYu																												

Page 5 of 29
Data Date: 04-Dec-21

◆ Milestone

Planned Bar

Critical Activity

◆ Actual Milestone

Actual Work

◆ Baseline Milestone

Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES
TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 6 of 29

Data Date: 04-Dec-21

Milestone

Planned Bar

Critical Activity

Actual Milestone

Actual Work

Baseline Milestone

Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES

TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 7 of 29

Data Date: 04-Dec-21

Milestone

Planned Bar

Critical Activity

Actual Milestone

Actual Work

Baseline Milestone

Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 8 of 29
Data Date: 04-Dec-21

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Nov-21)

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 9 of 29

Data Date: 04-Dec-21

◆ Milestone

▬ Planned Bar

▬ Critical Activity

◆ Actual Milestone

▬ Actual Work

◆ Baseline Milestone

▬ Baseline Bar


▬ Summary


ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES
TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

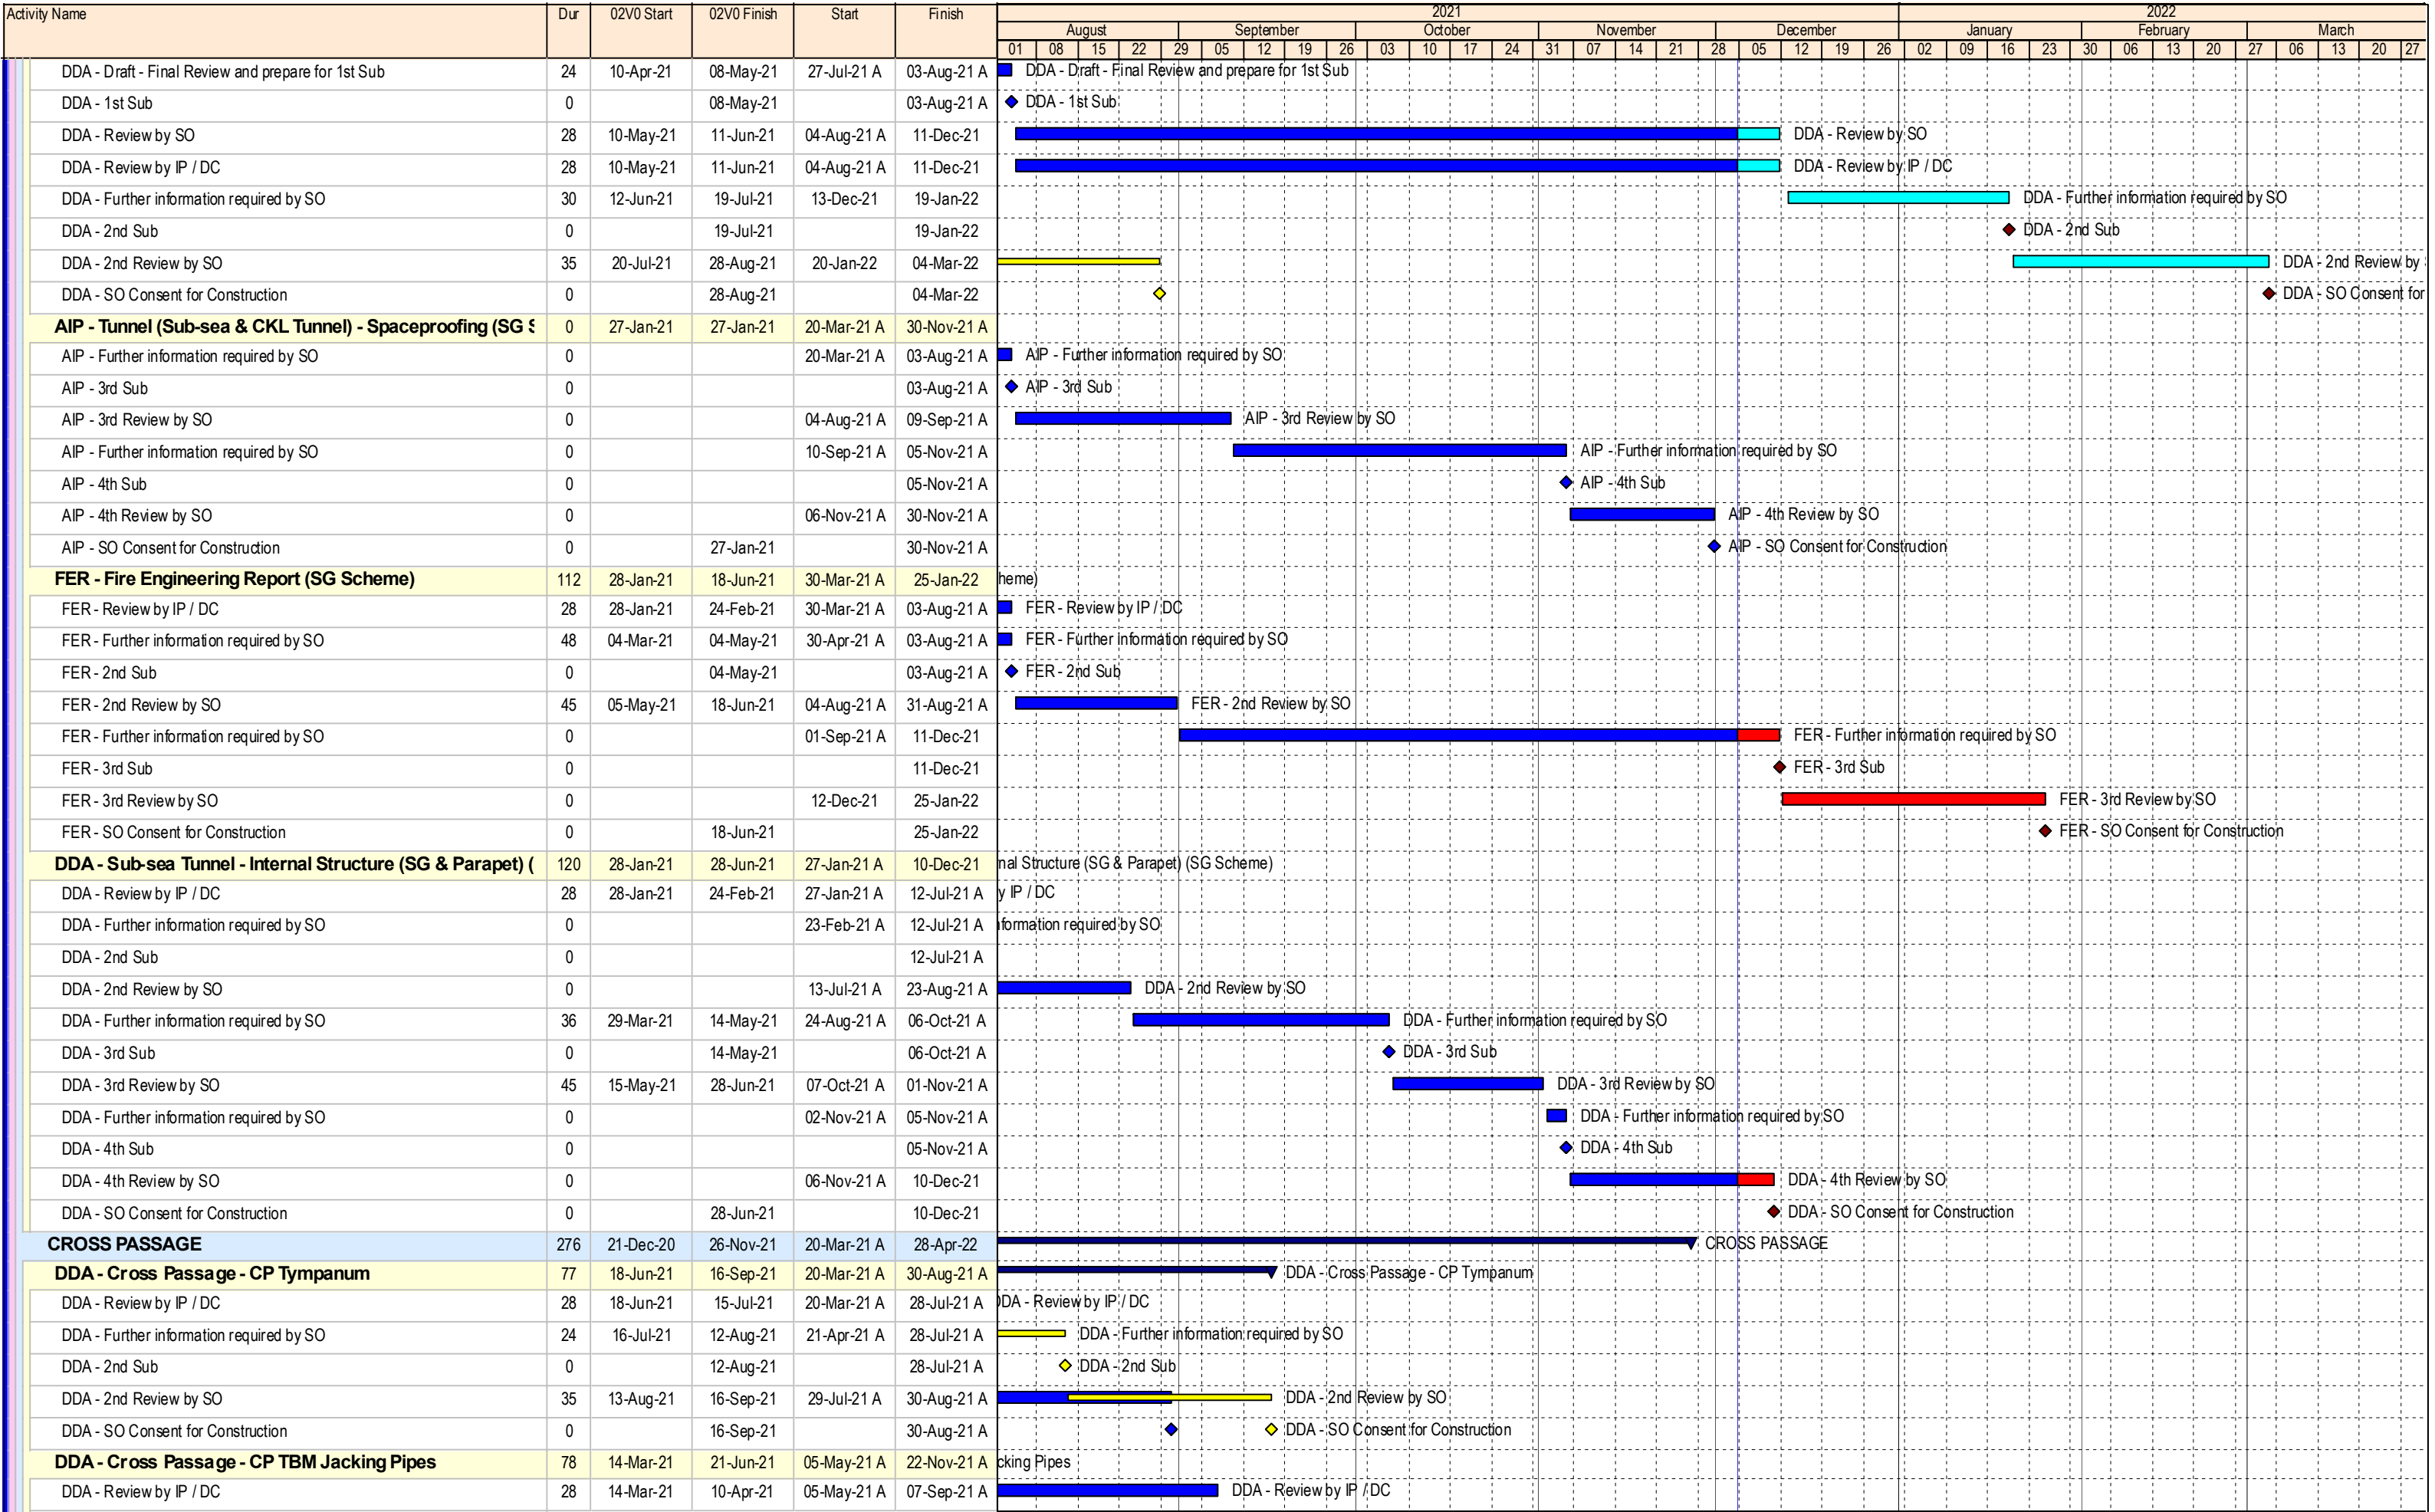

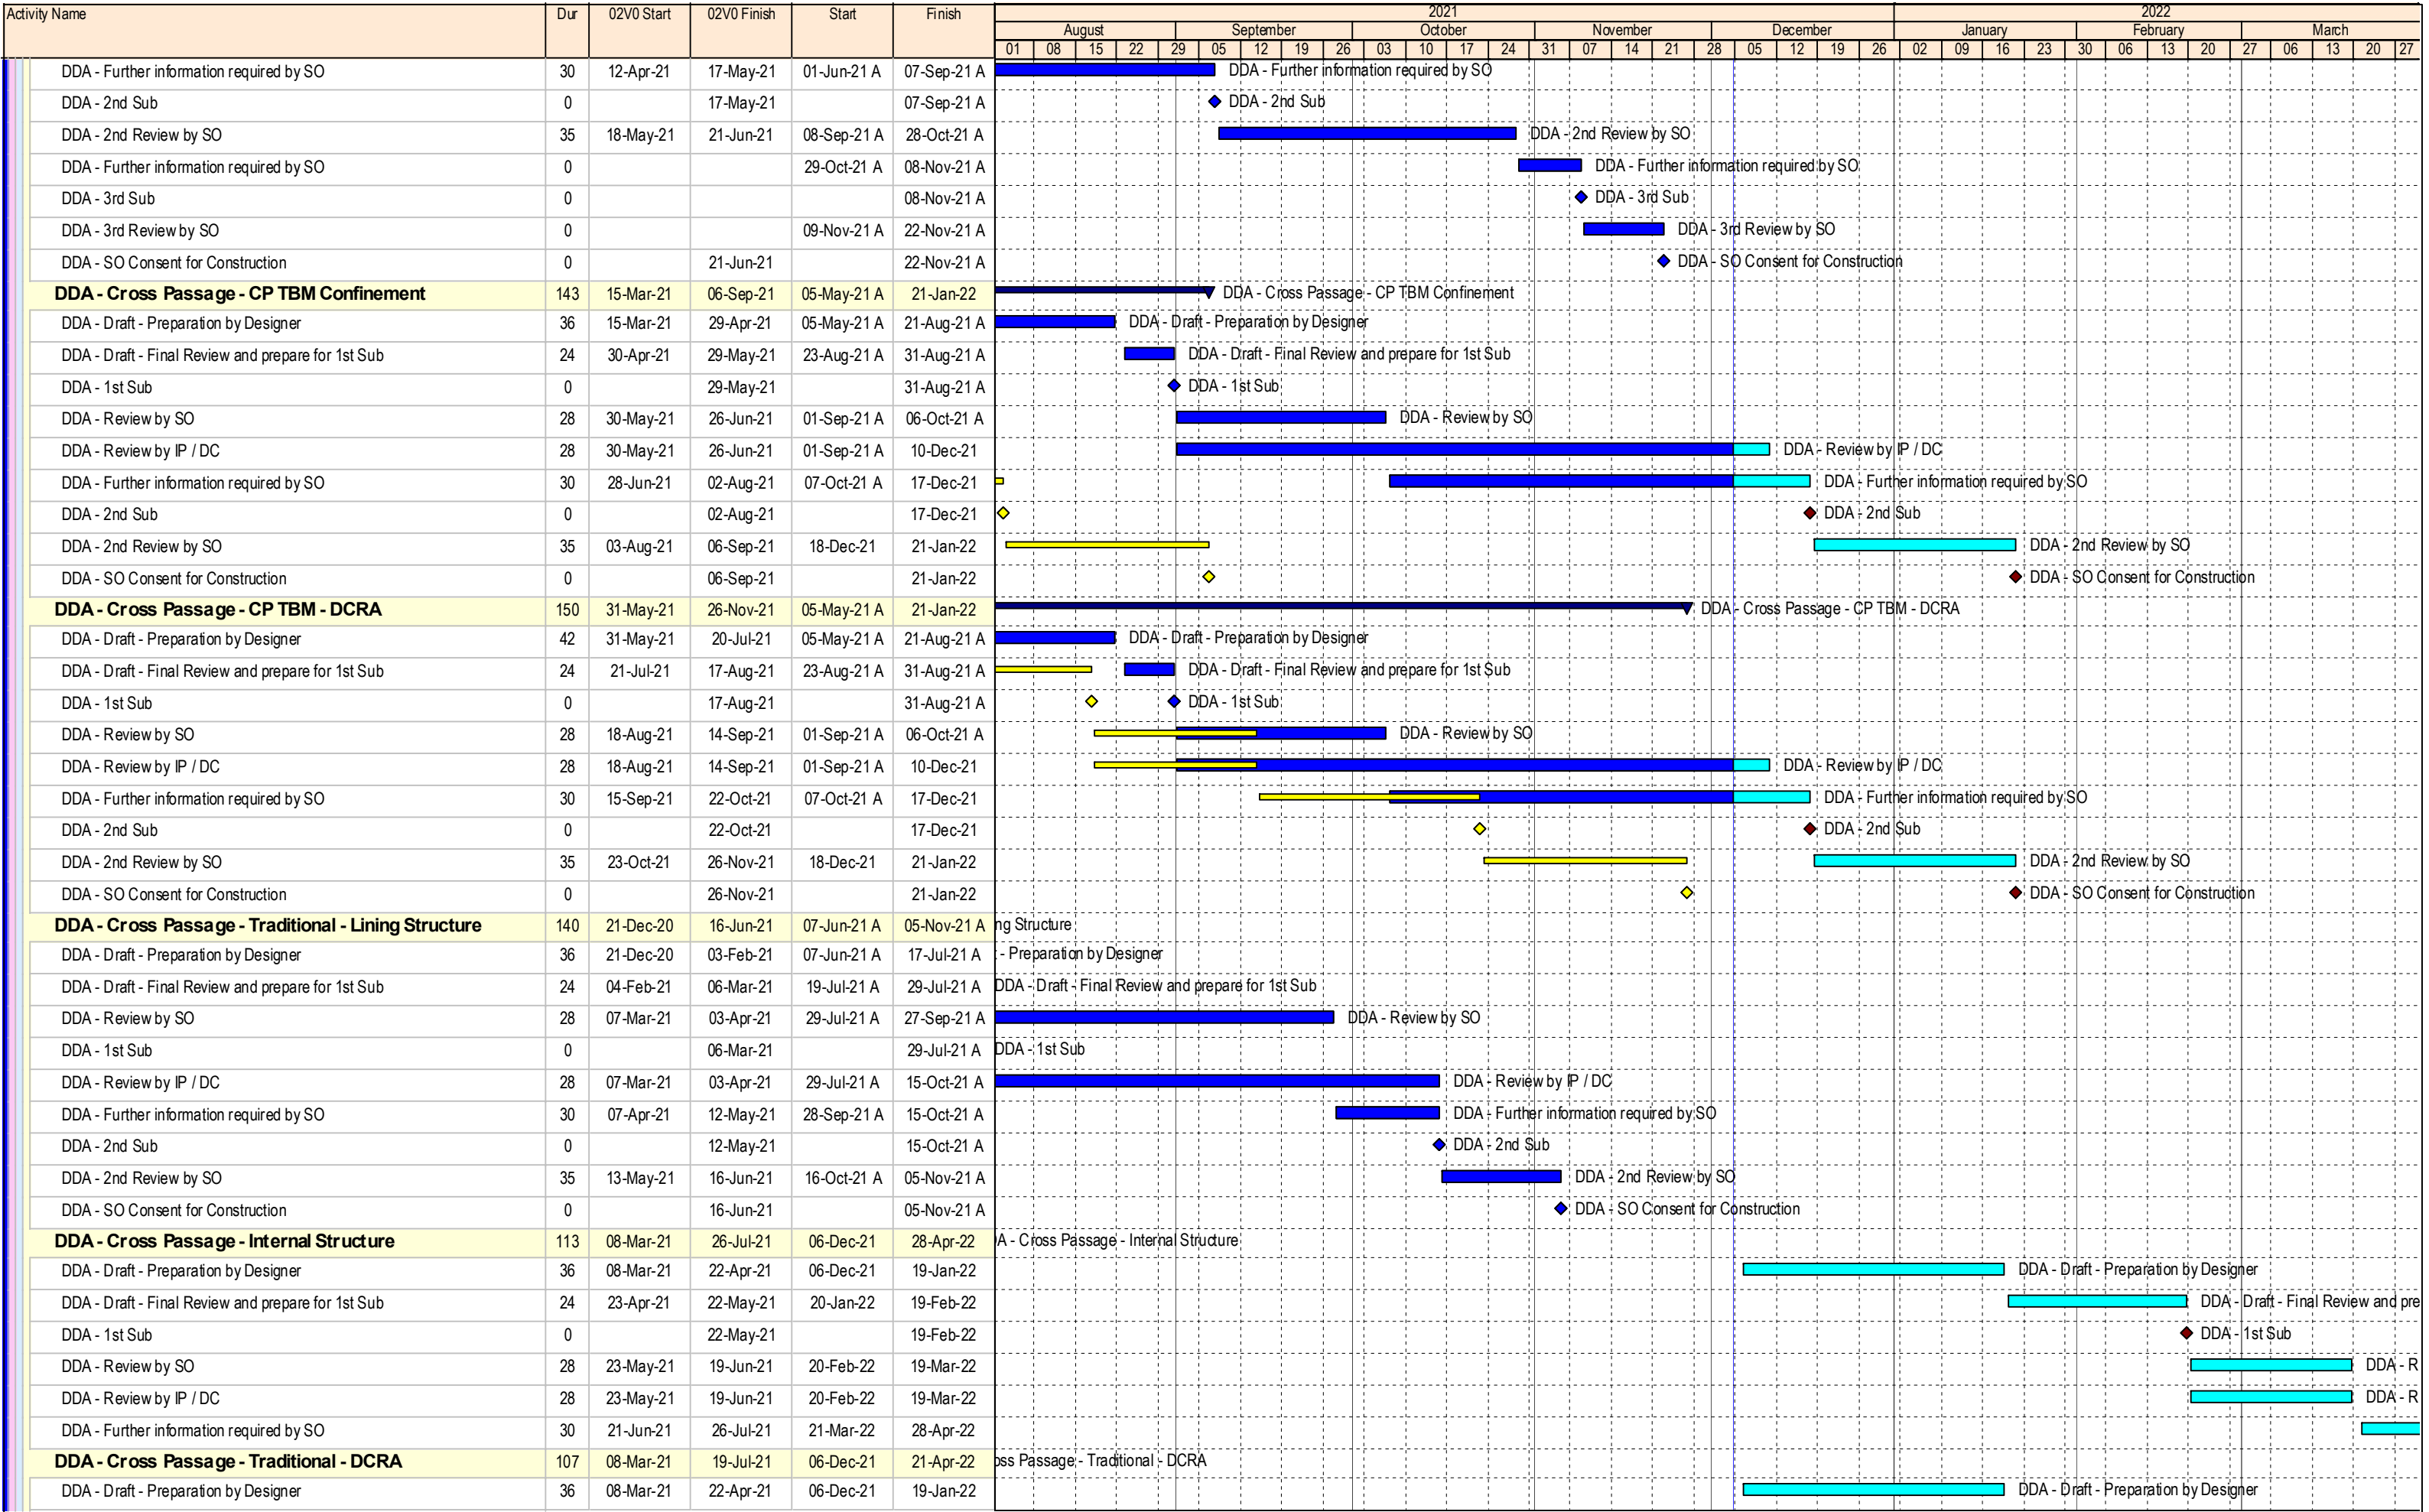

Page 12 of 29

Data Date: 04-Dec-21

◆ Milestone

▬ Planned Bar

▬ Critical Activity

◆ Actual Milestone

▬ Actual Work

◆ Baseline Milestone

▬ Baseline Bar

▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES

TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 13 of 29

Data Date: 04-Dec-21

◆ Milestone

▬ Planned Bar

▬ CriticalActivity

◆ Actual Milestone

▬ Actual Work

◆ Baseline Milestone

▬ Baseline Bar

▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works

for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES


TRAVAUX PUBLICS


Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 14 of 29
Data Date: 04-Dec-21

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Nov-21)

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

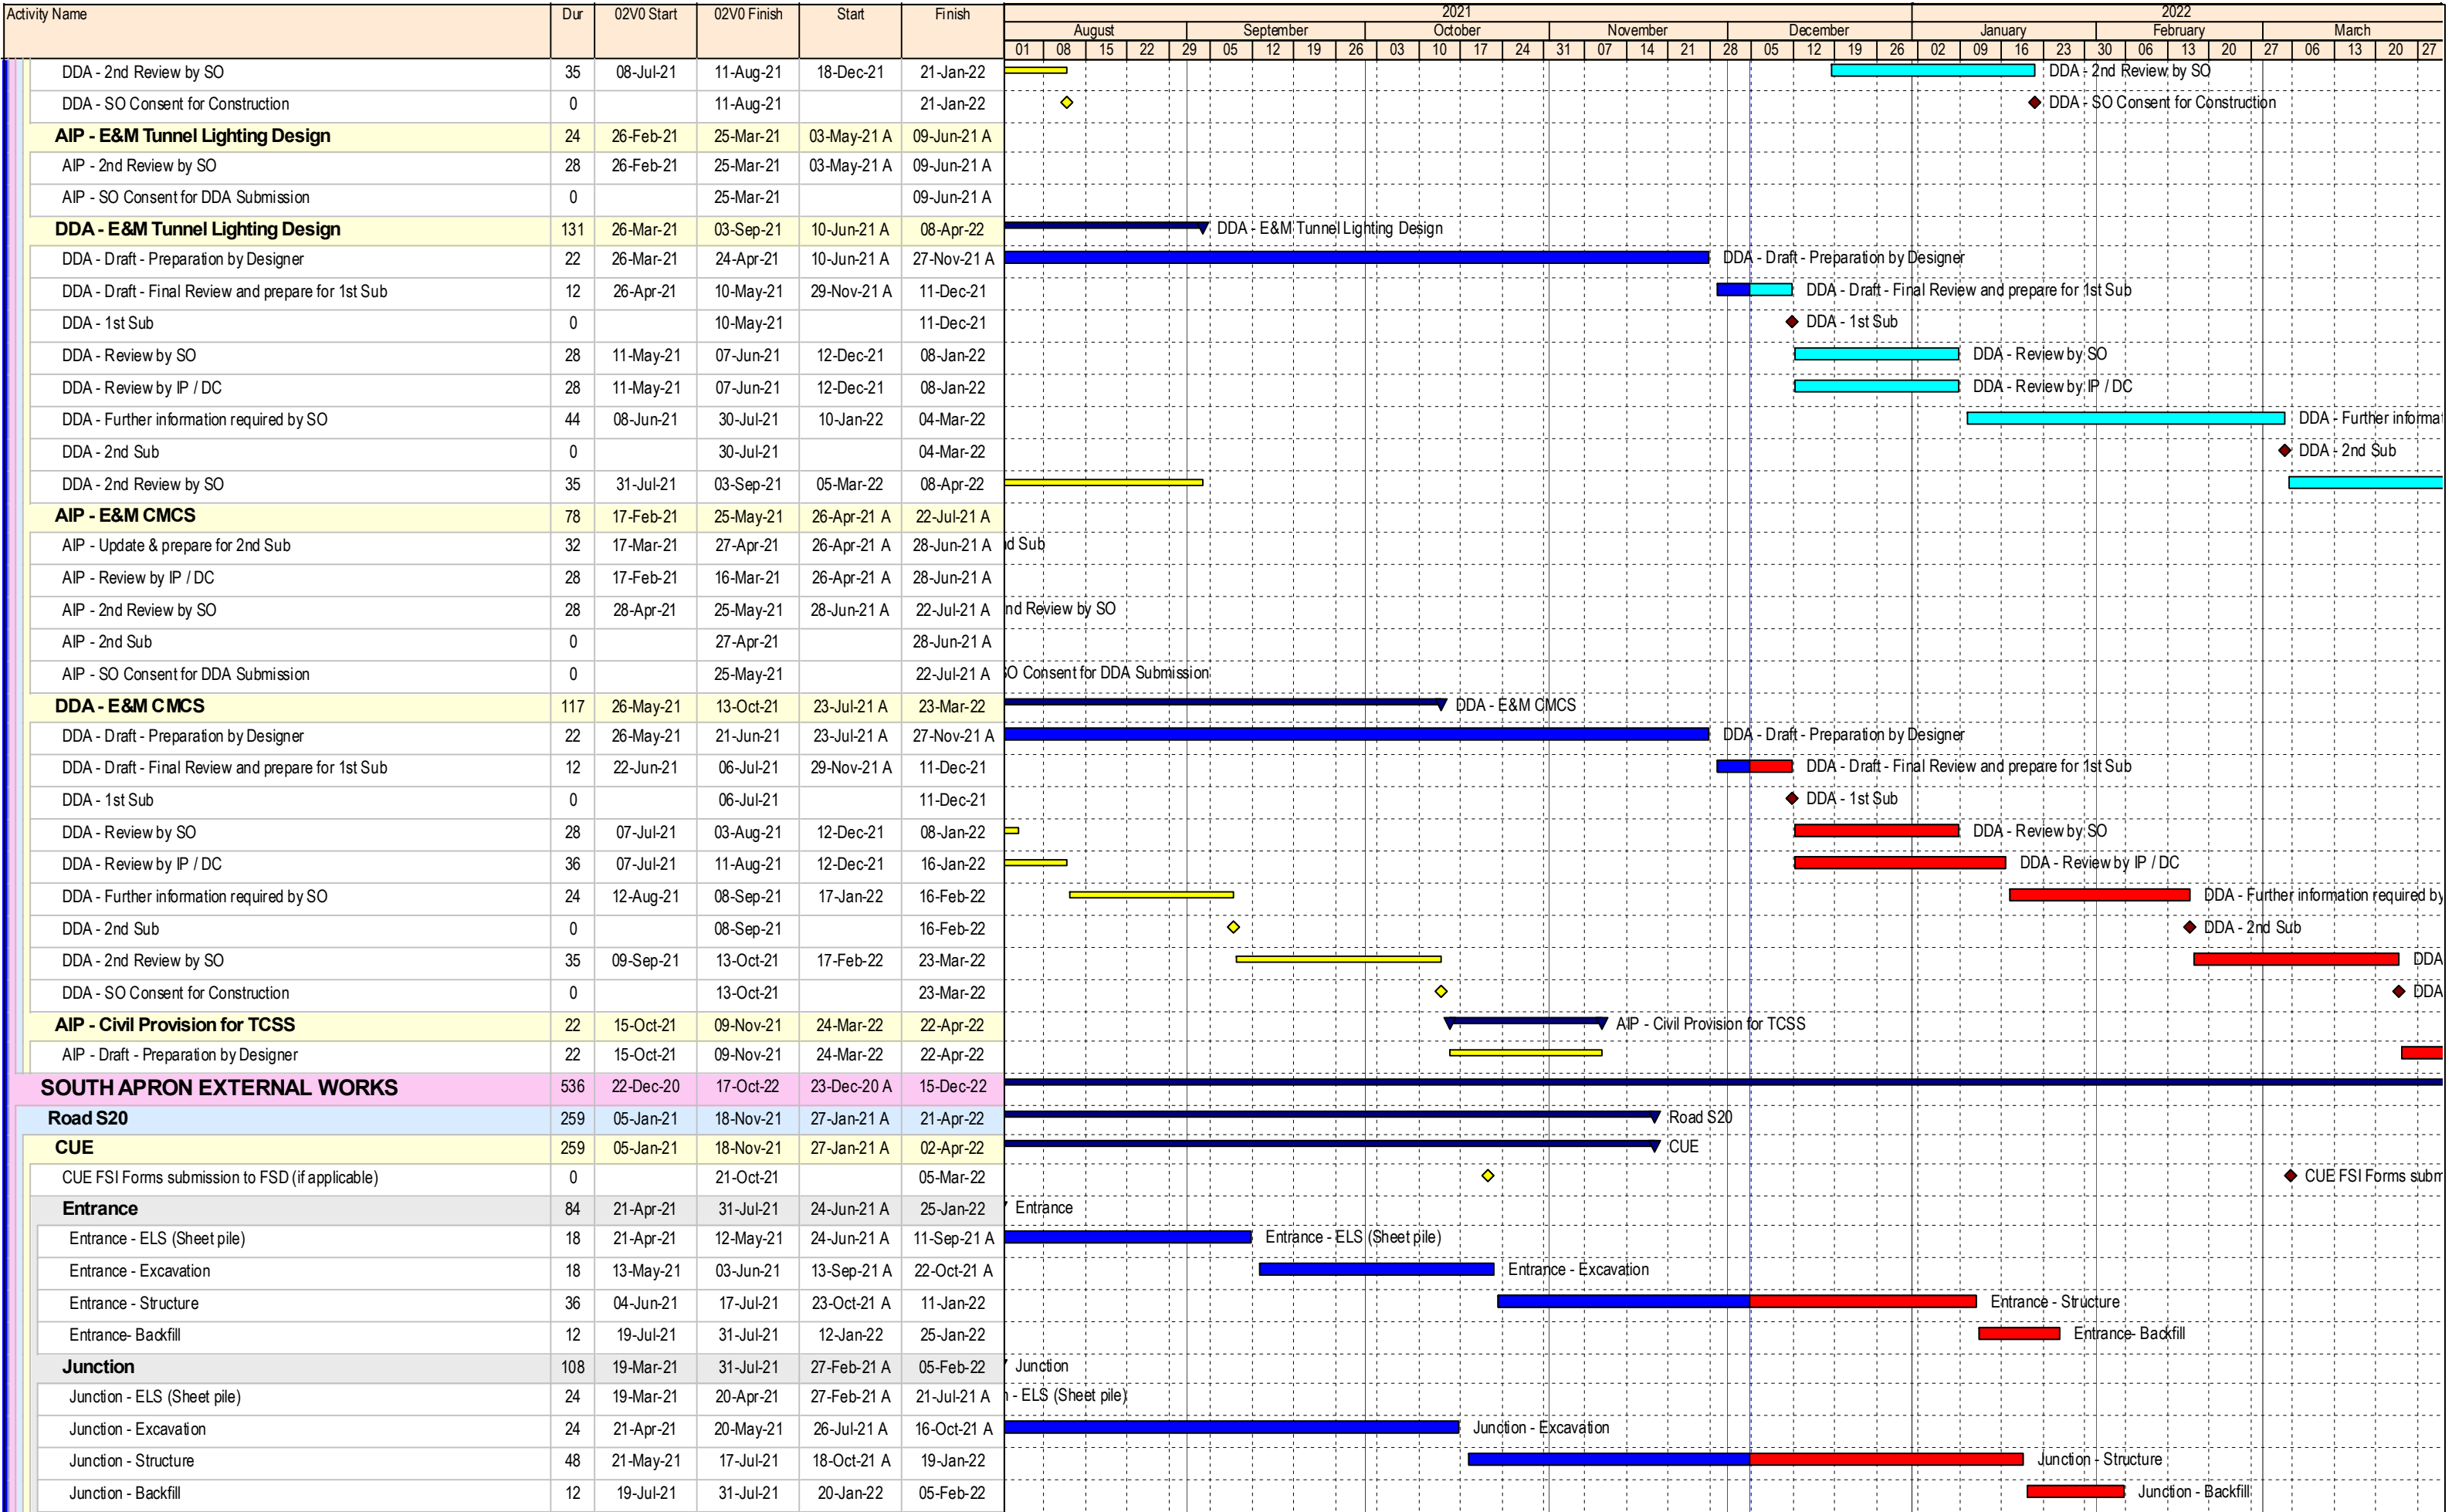

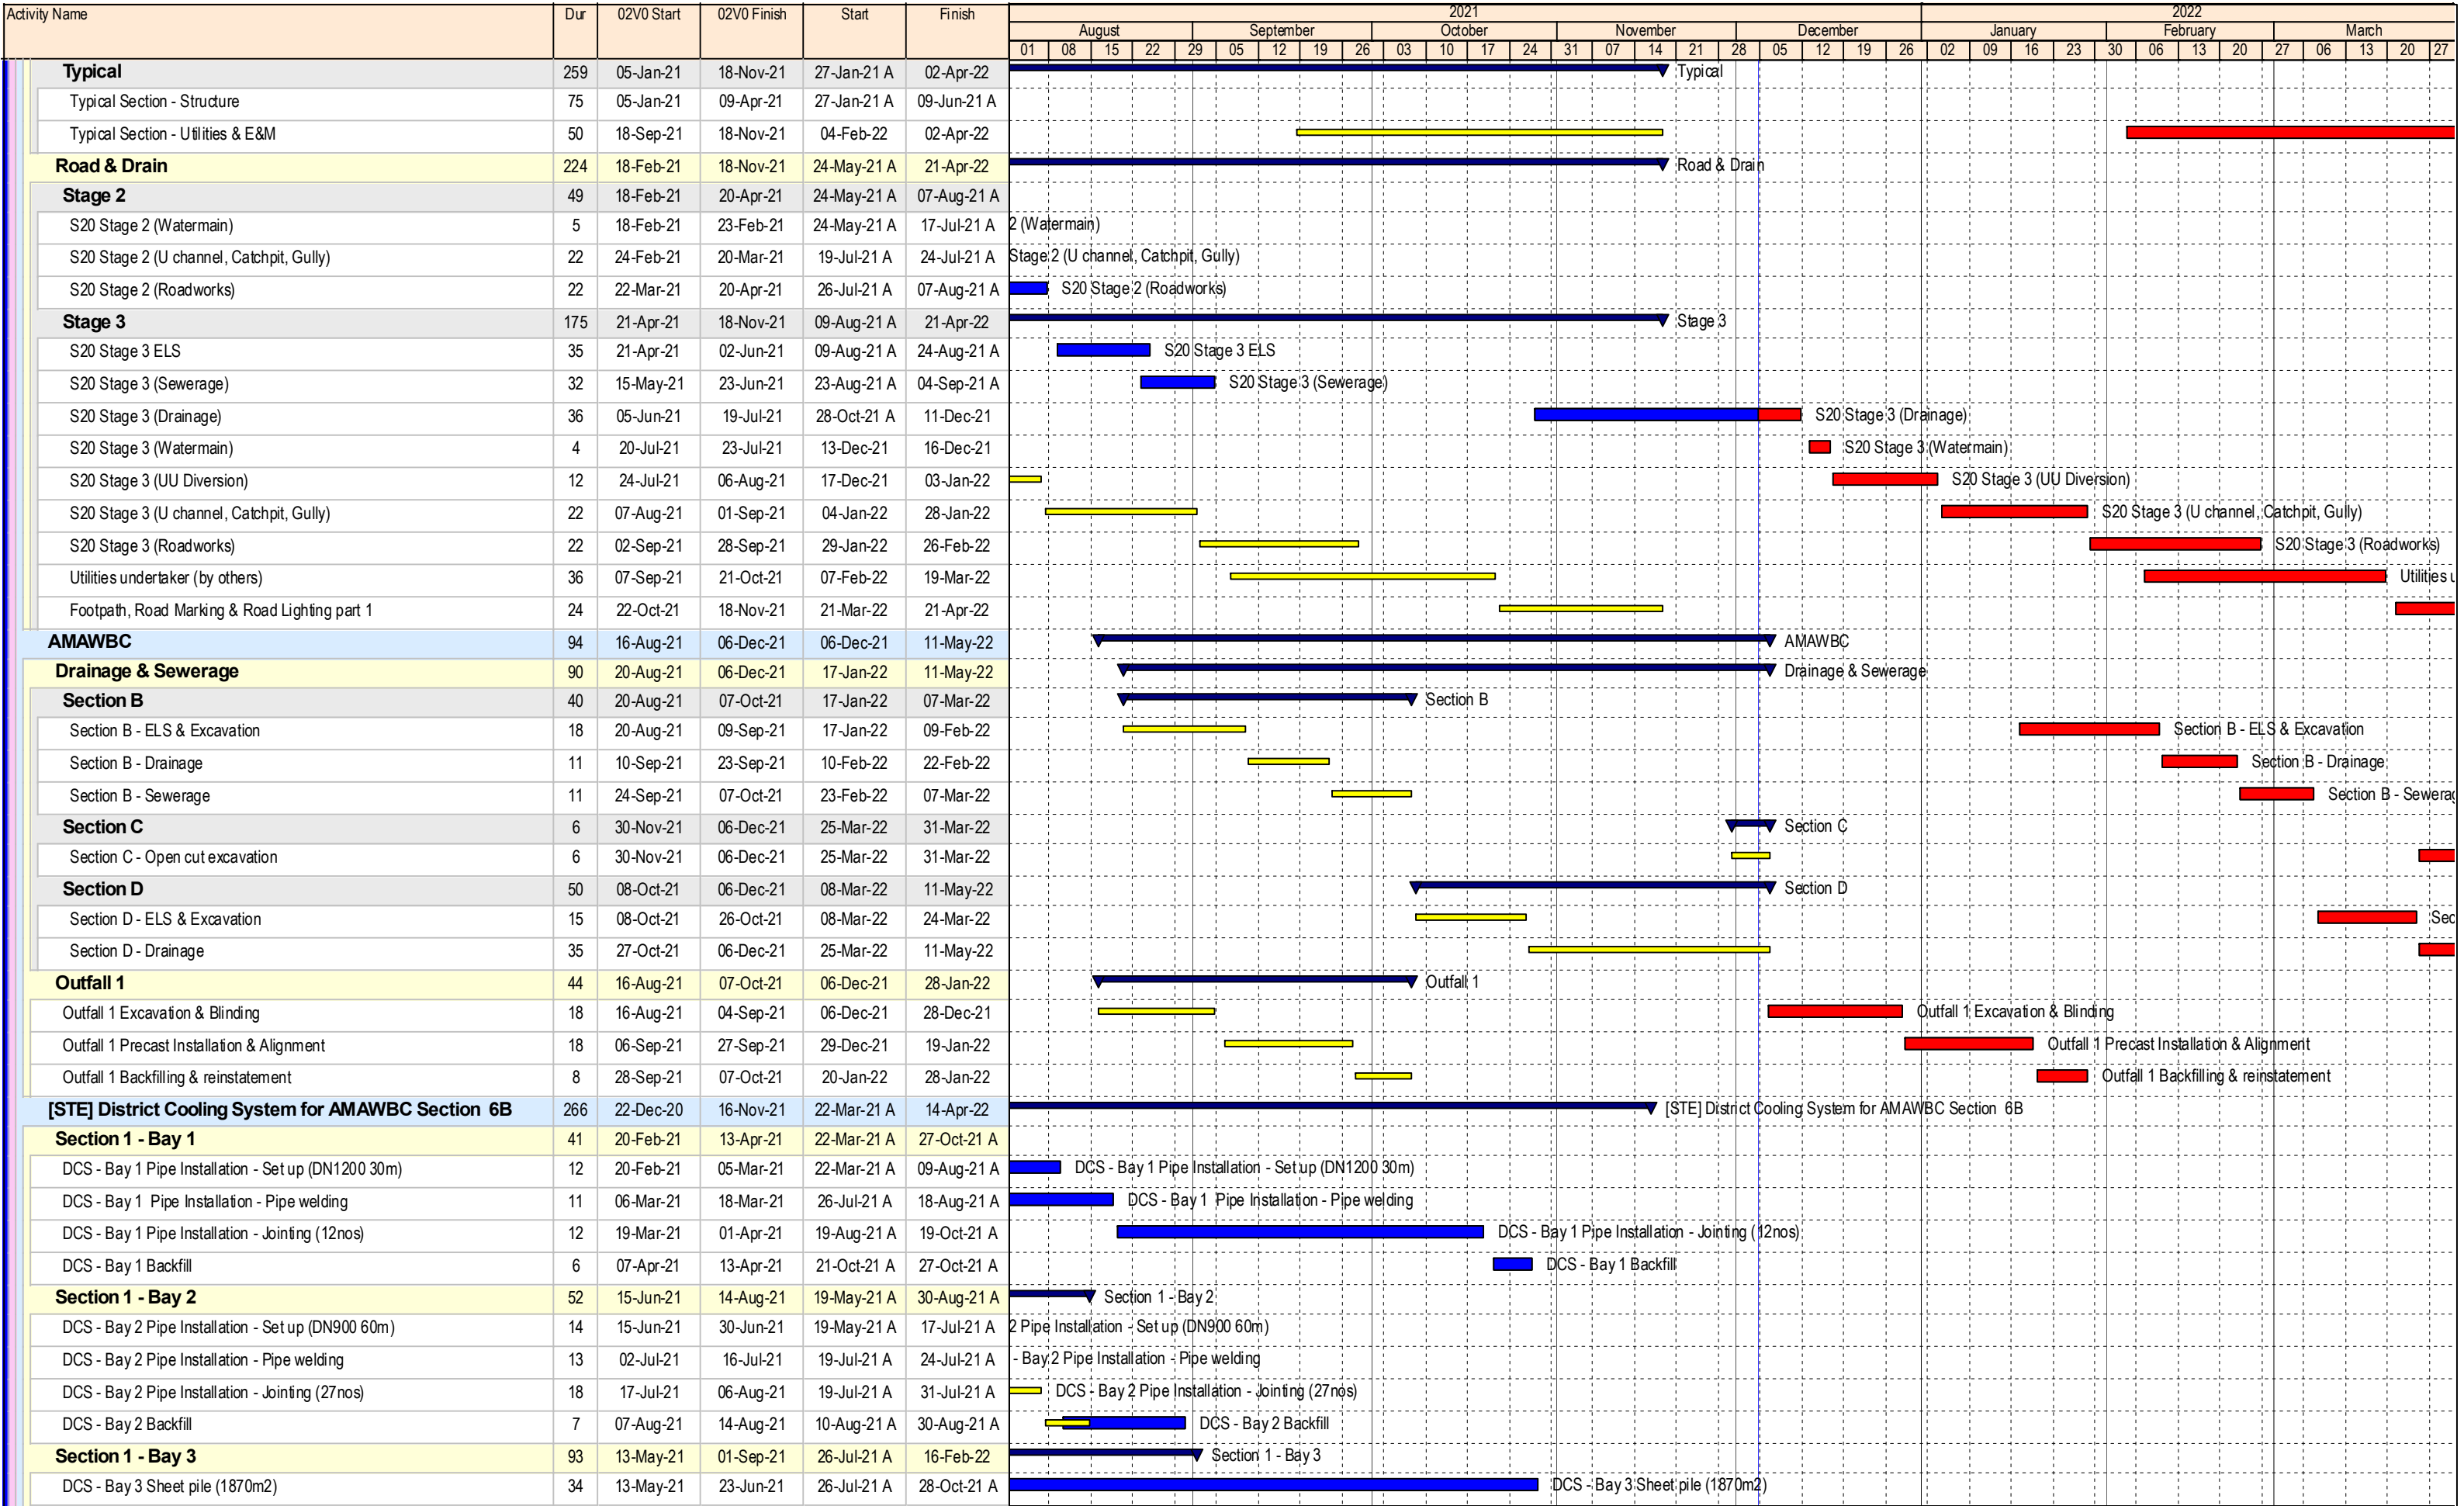

Milestone

Planned Bar

Critical Activity

Actual Milestone

Actual Work


Baseline Milestone

Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 17 of 29

Data Date: 04-Dec-21

◆ Milestone
 ▶ Summary

Planned Bar

Critical Activity

◆ Actual Milestone

Actual Work

◆ Baseline Milestone


Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Nov-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

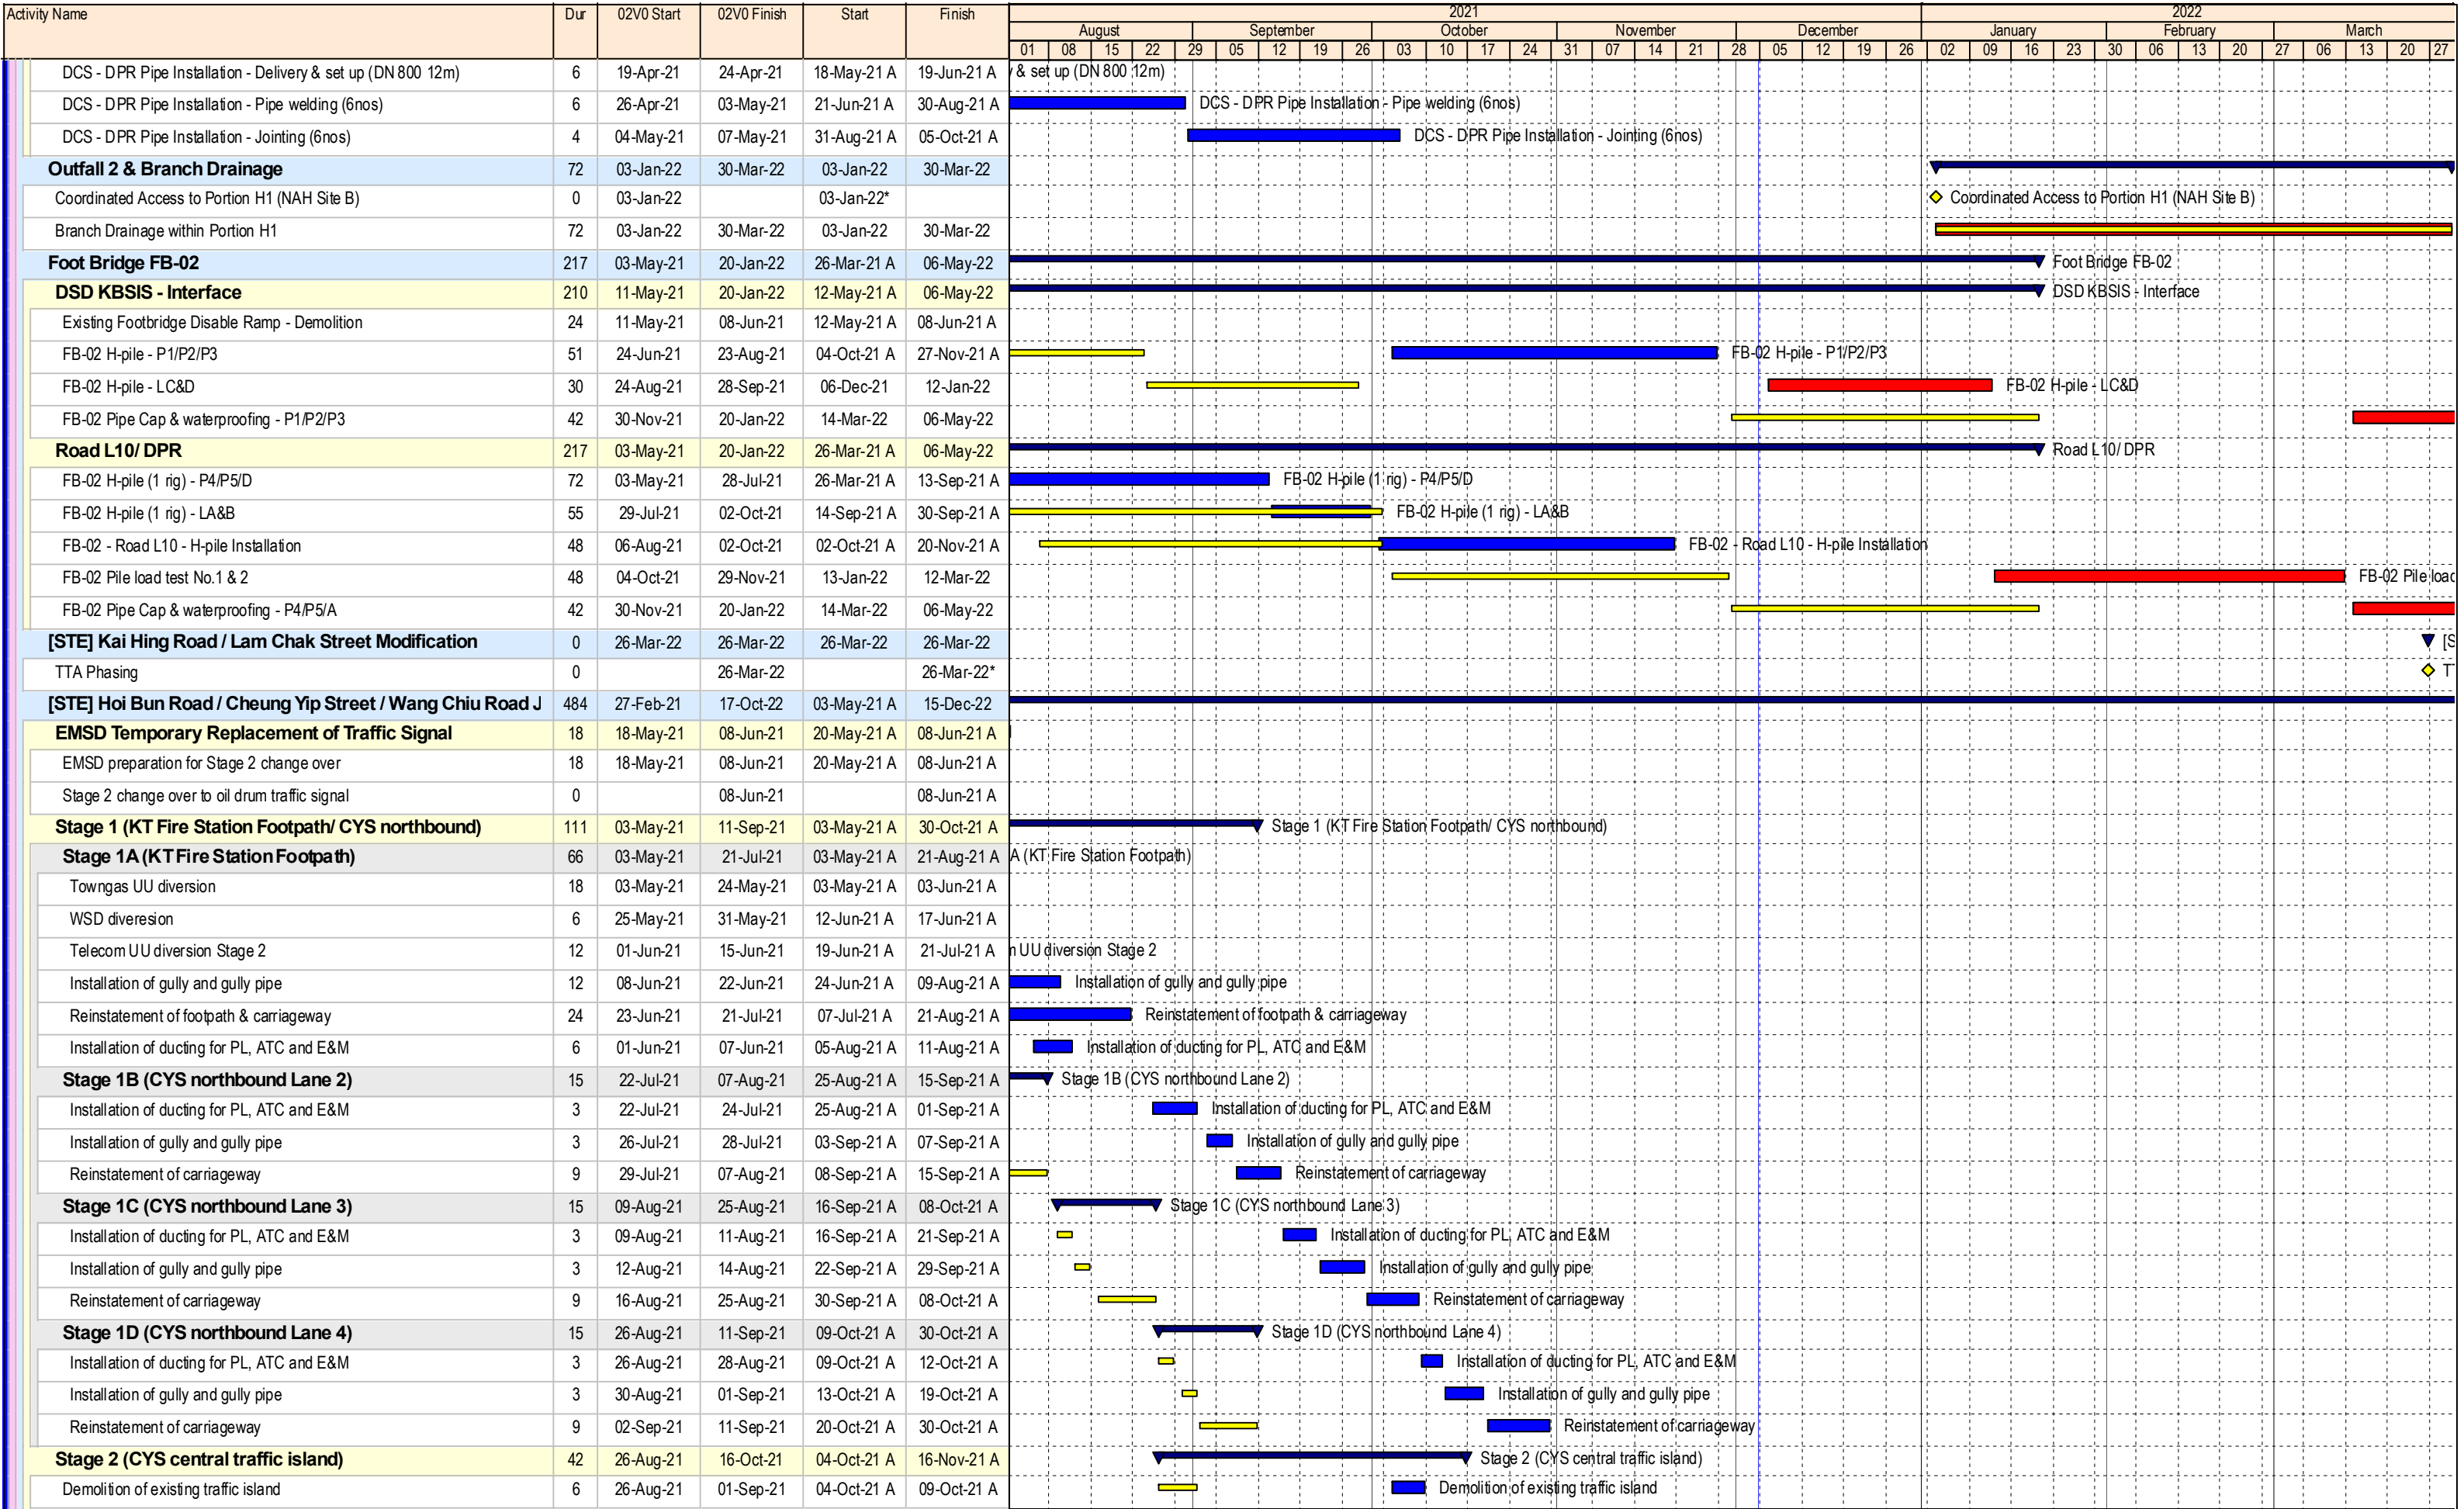

Page 19 of 29
Data Date: 04-Dec-21

◆

Milestone

▬

Planned Bar

▬

Critical Activity

◆

Actual Milestone

▬

Actual Work

◆

Baseline Milestone

▬


Baseline Bar


➤


Summary


ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)

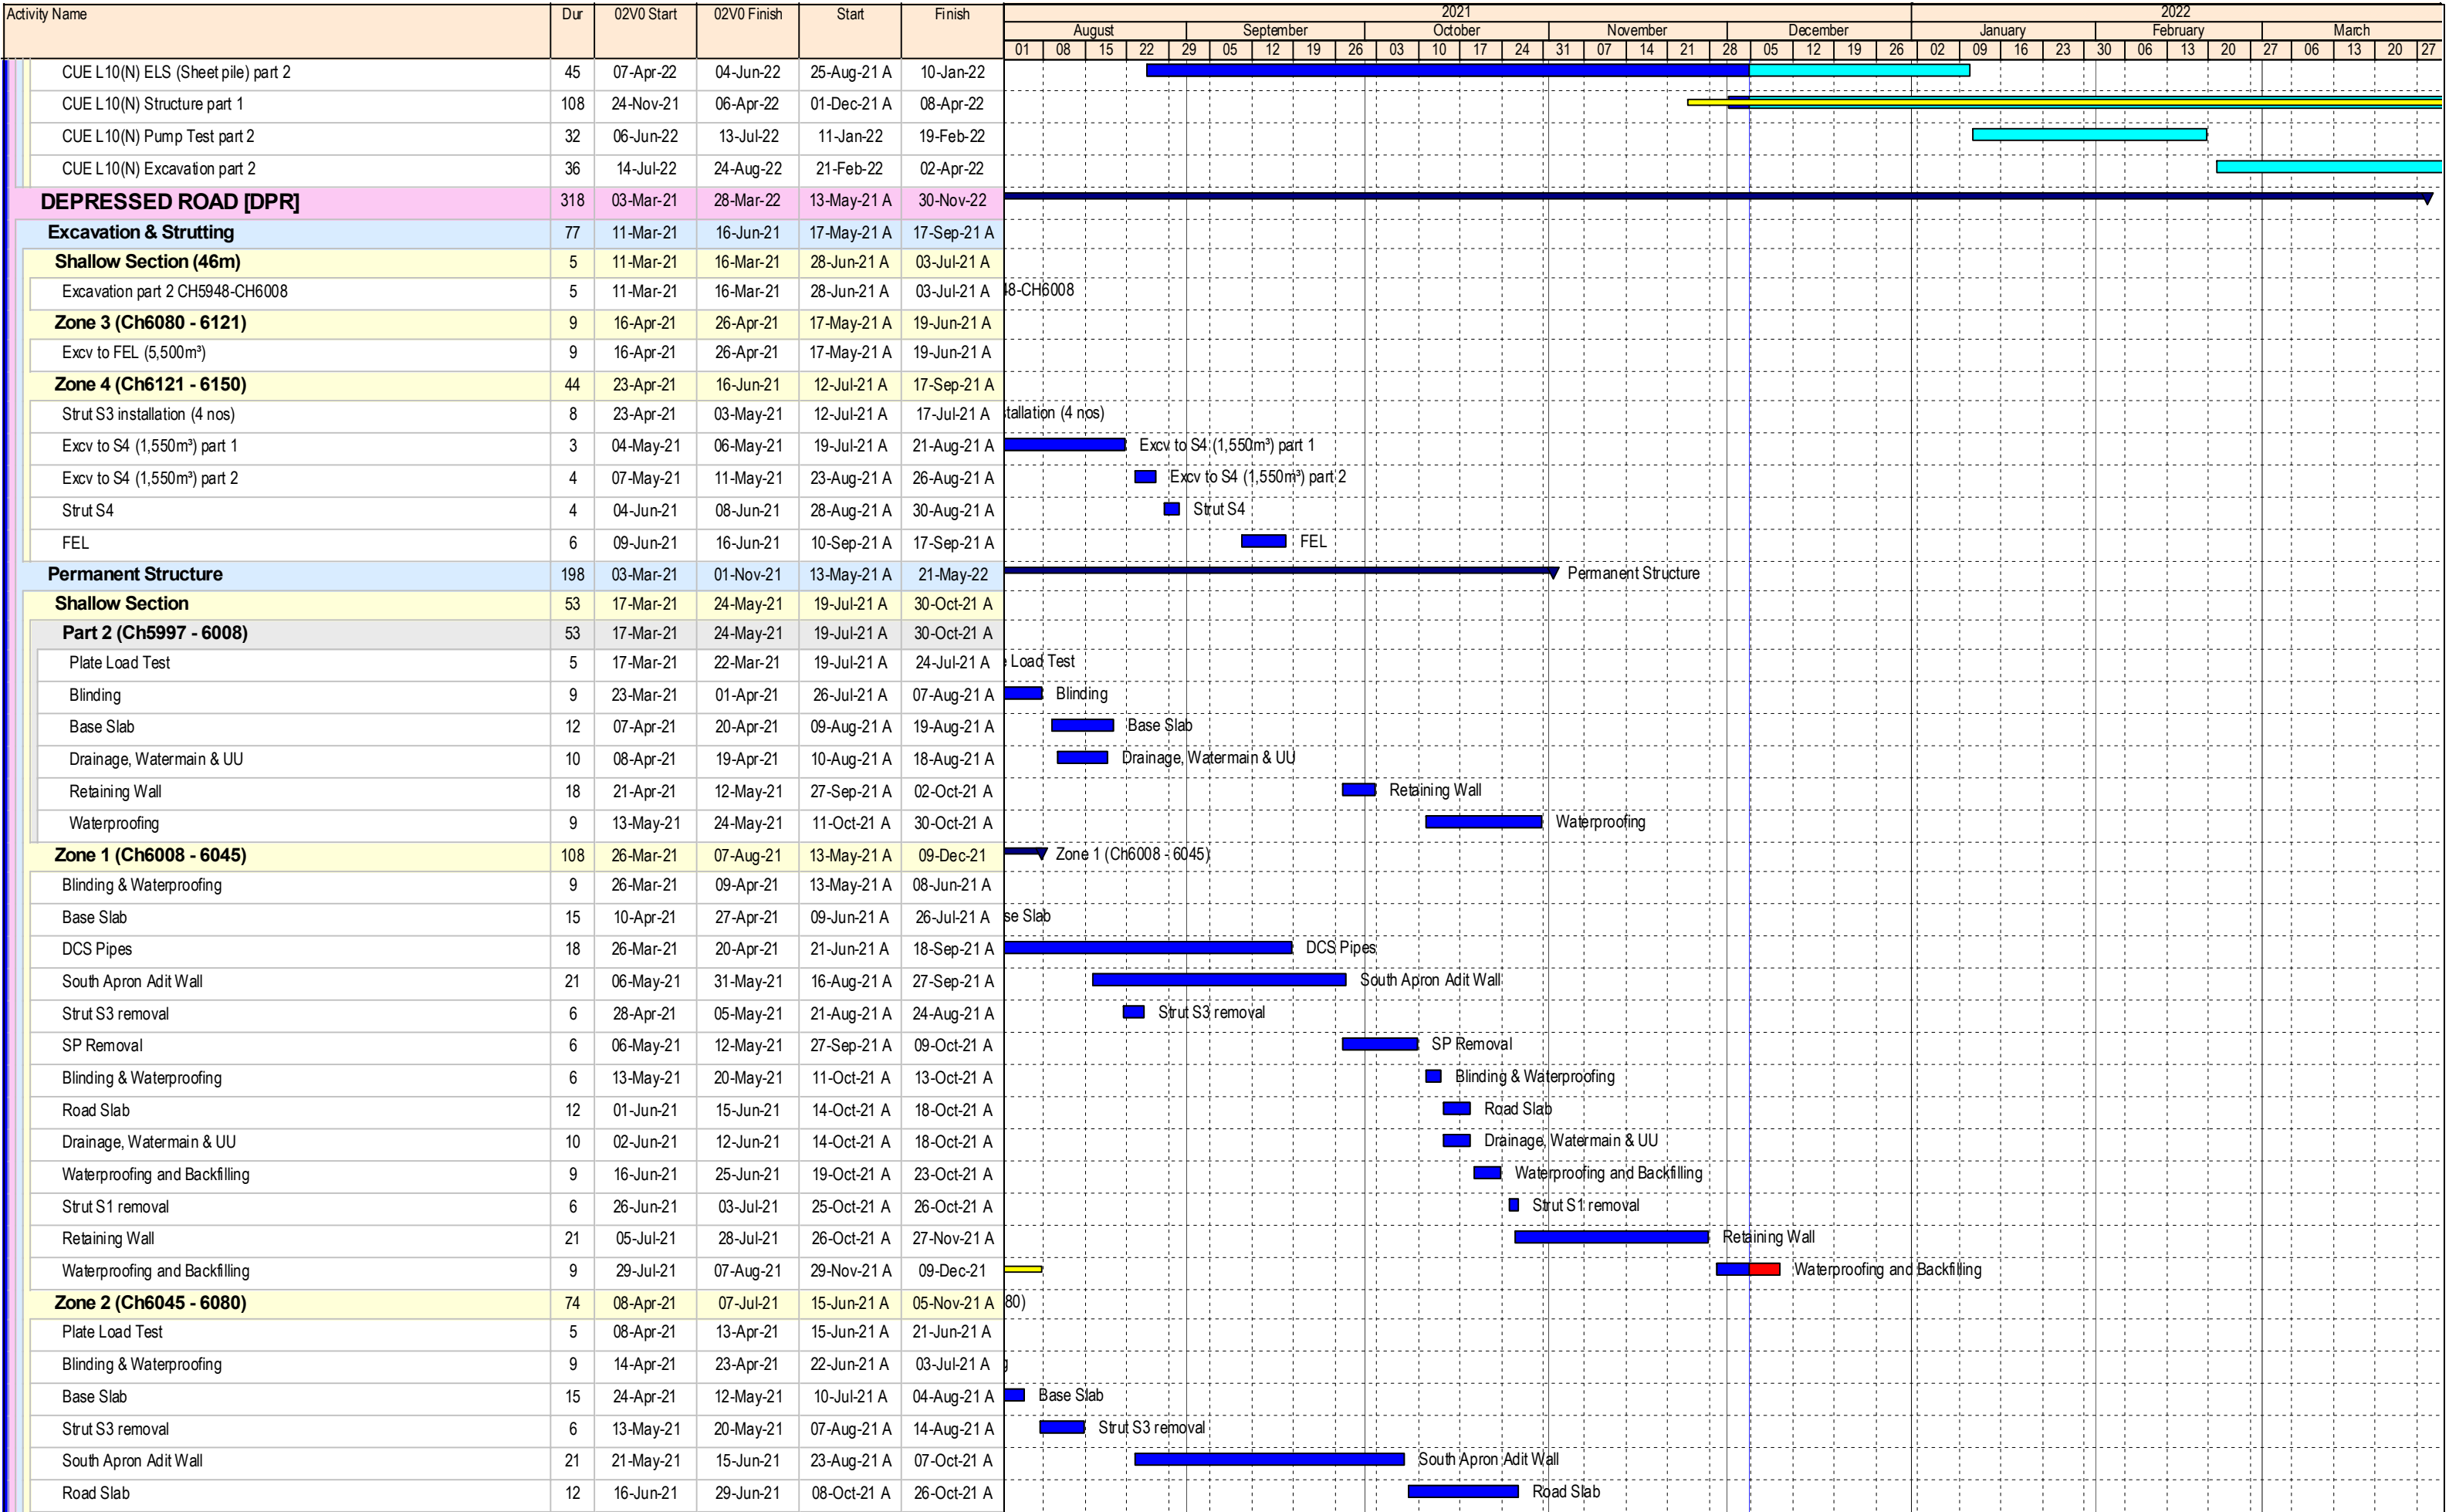

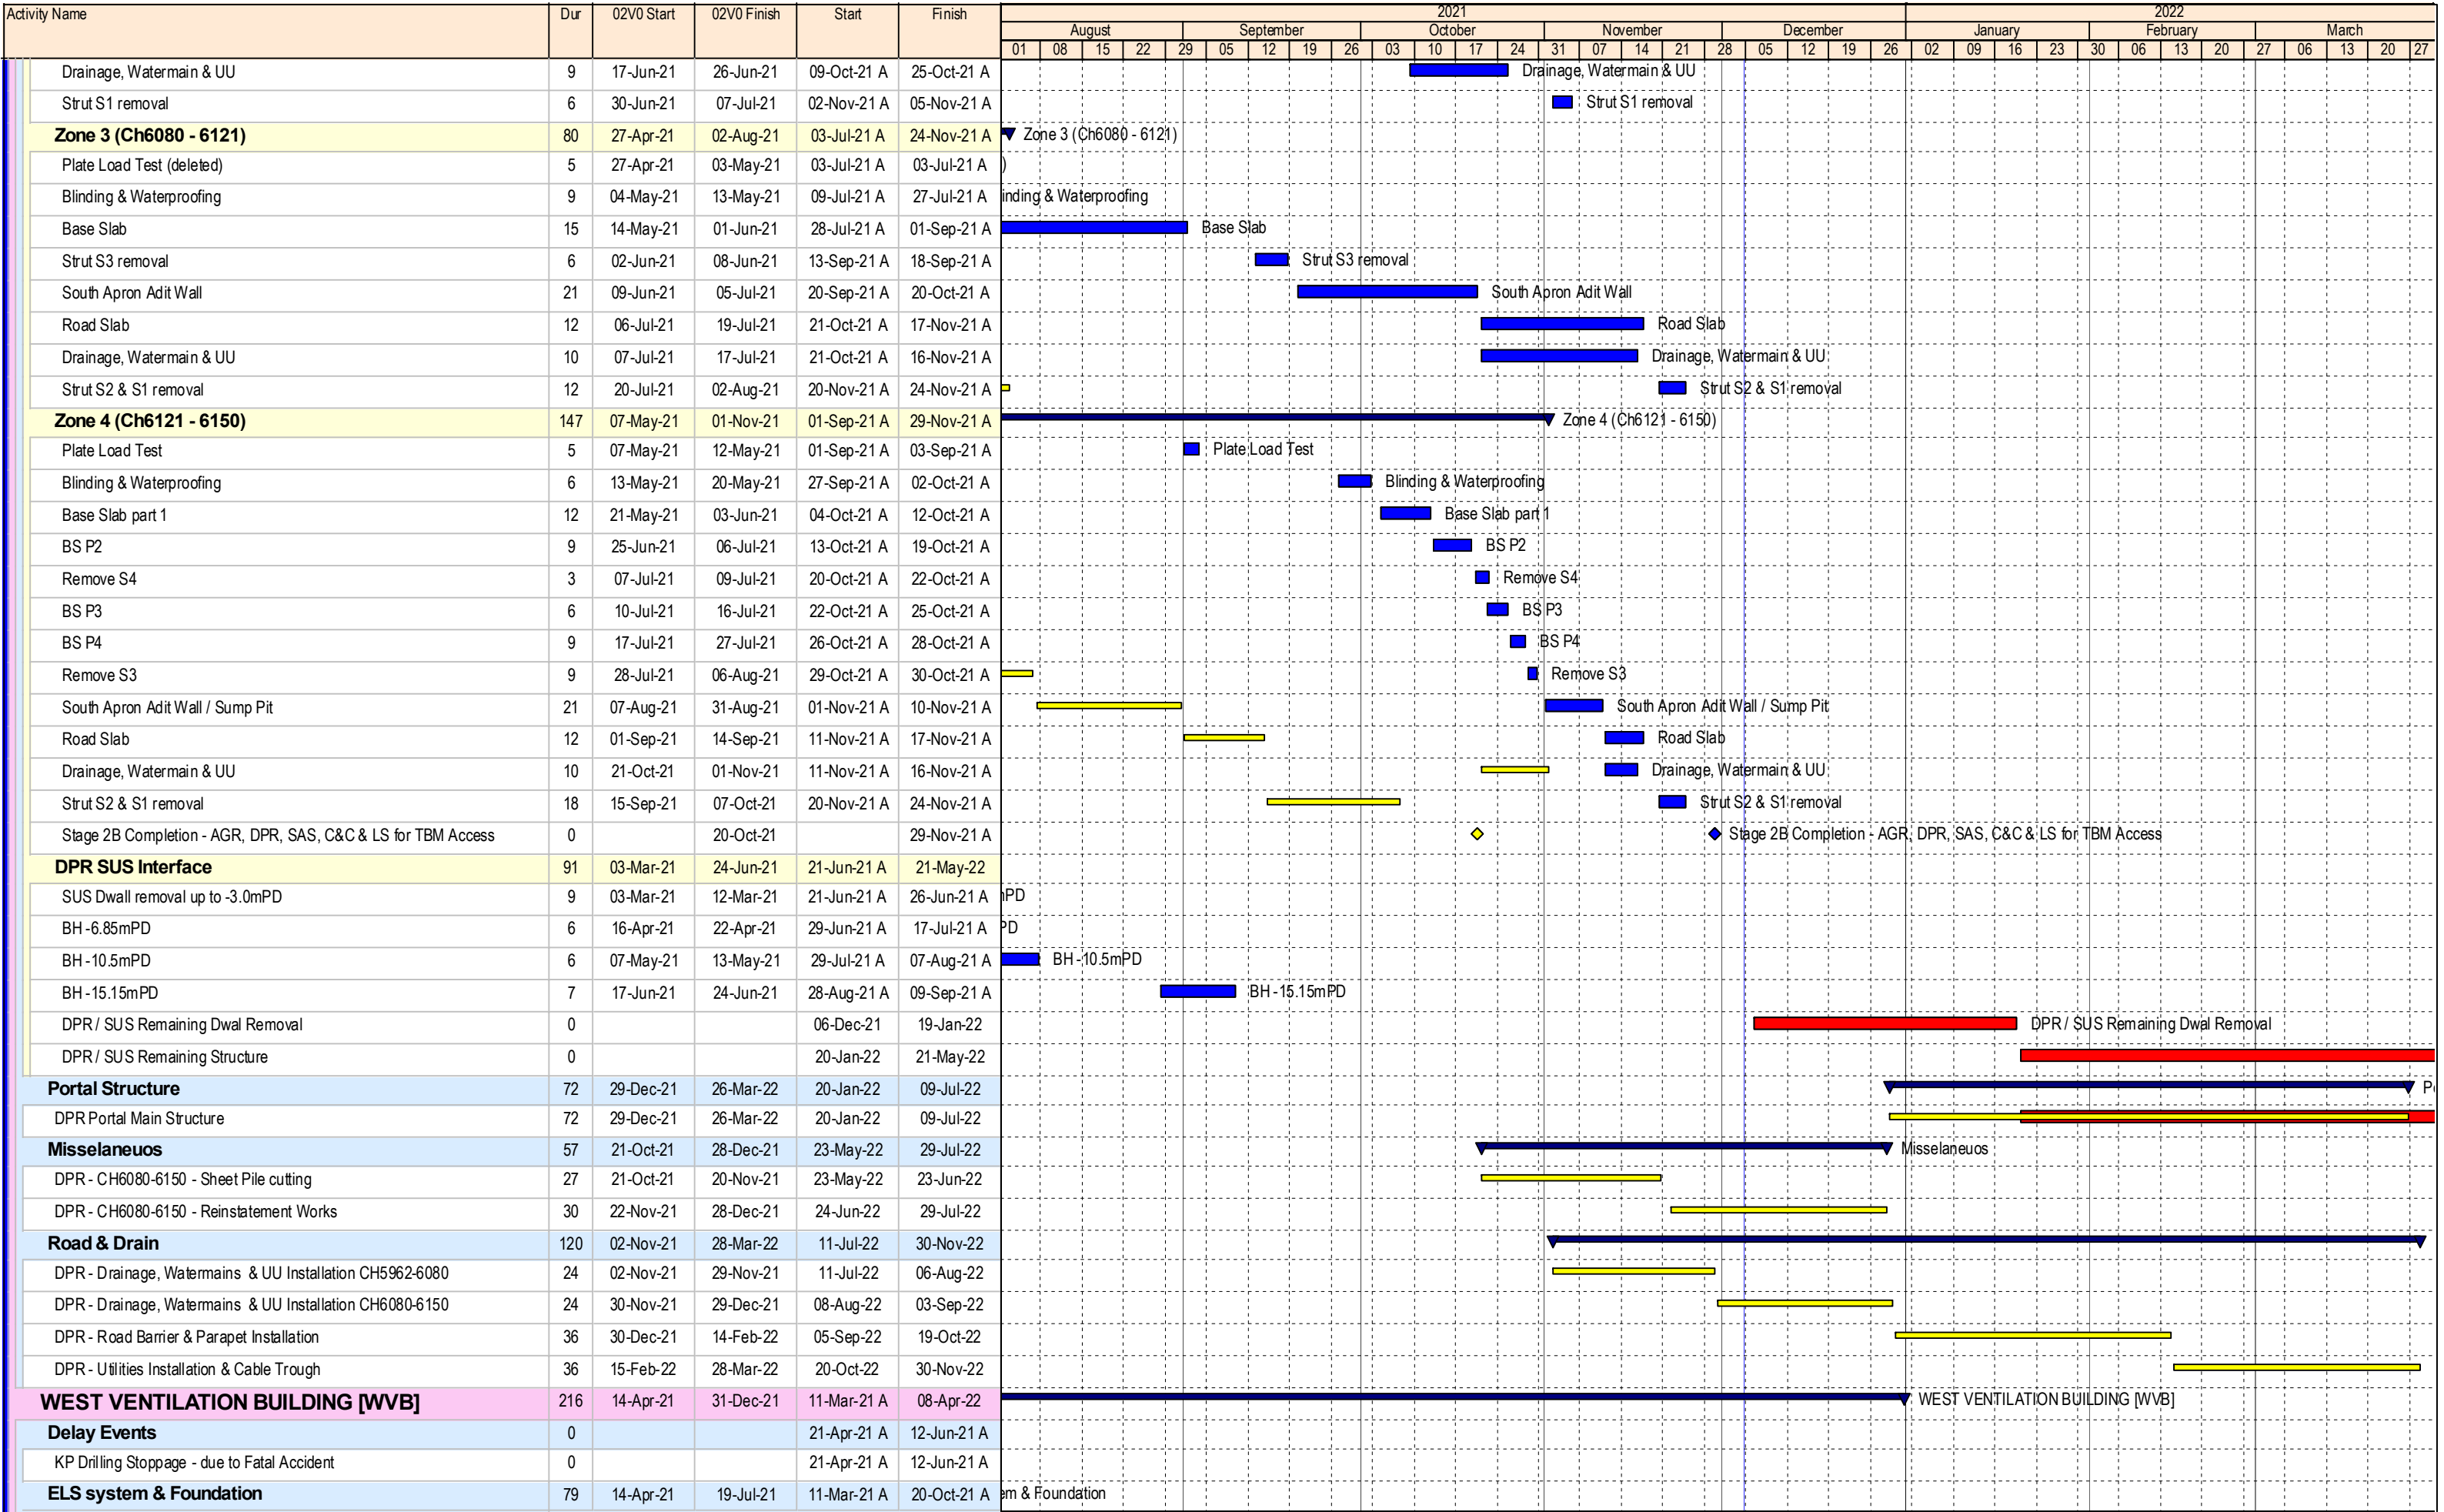

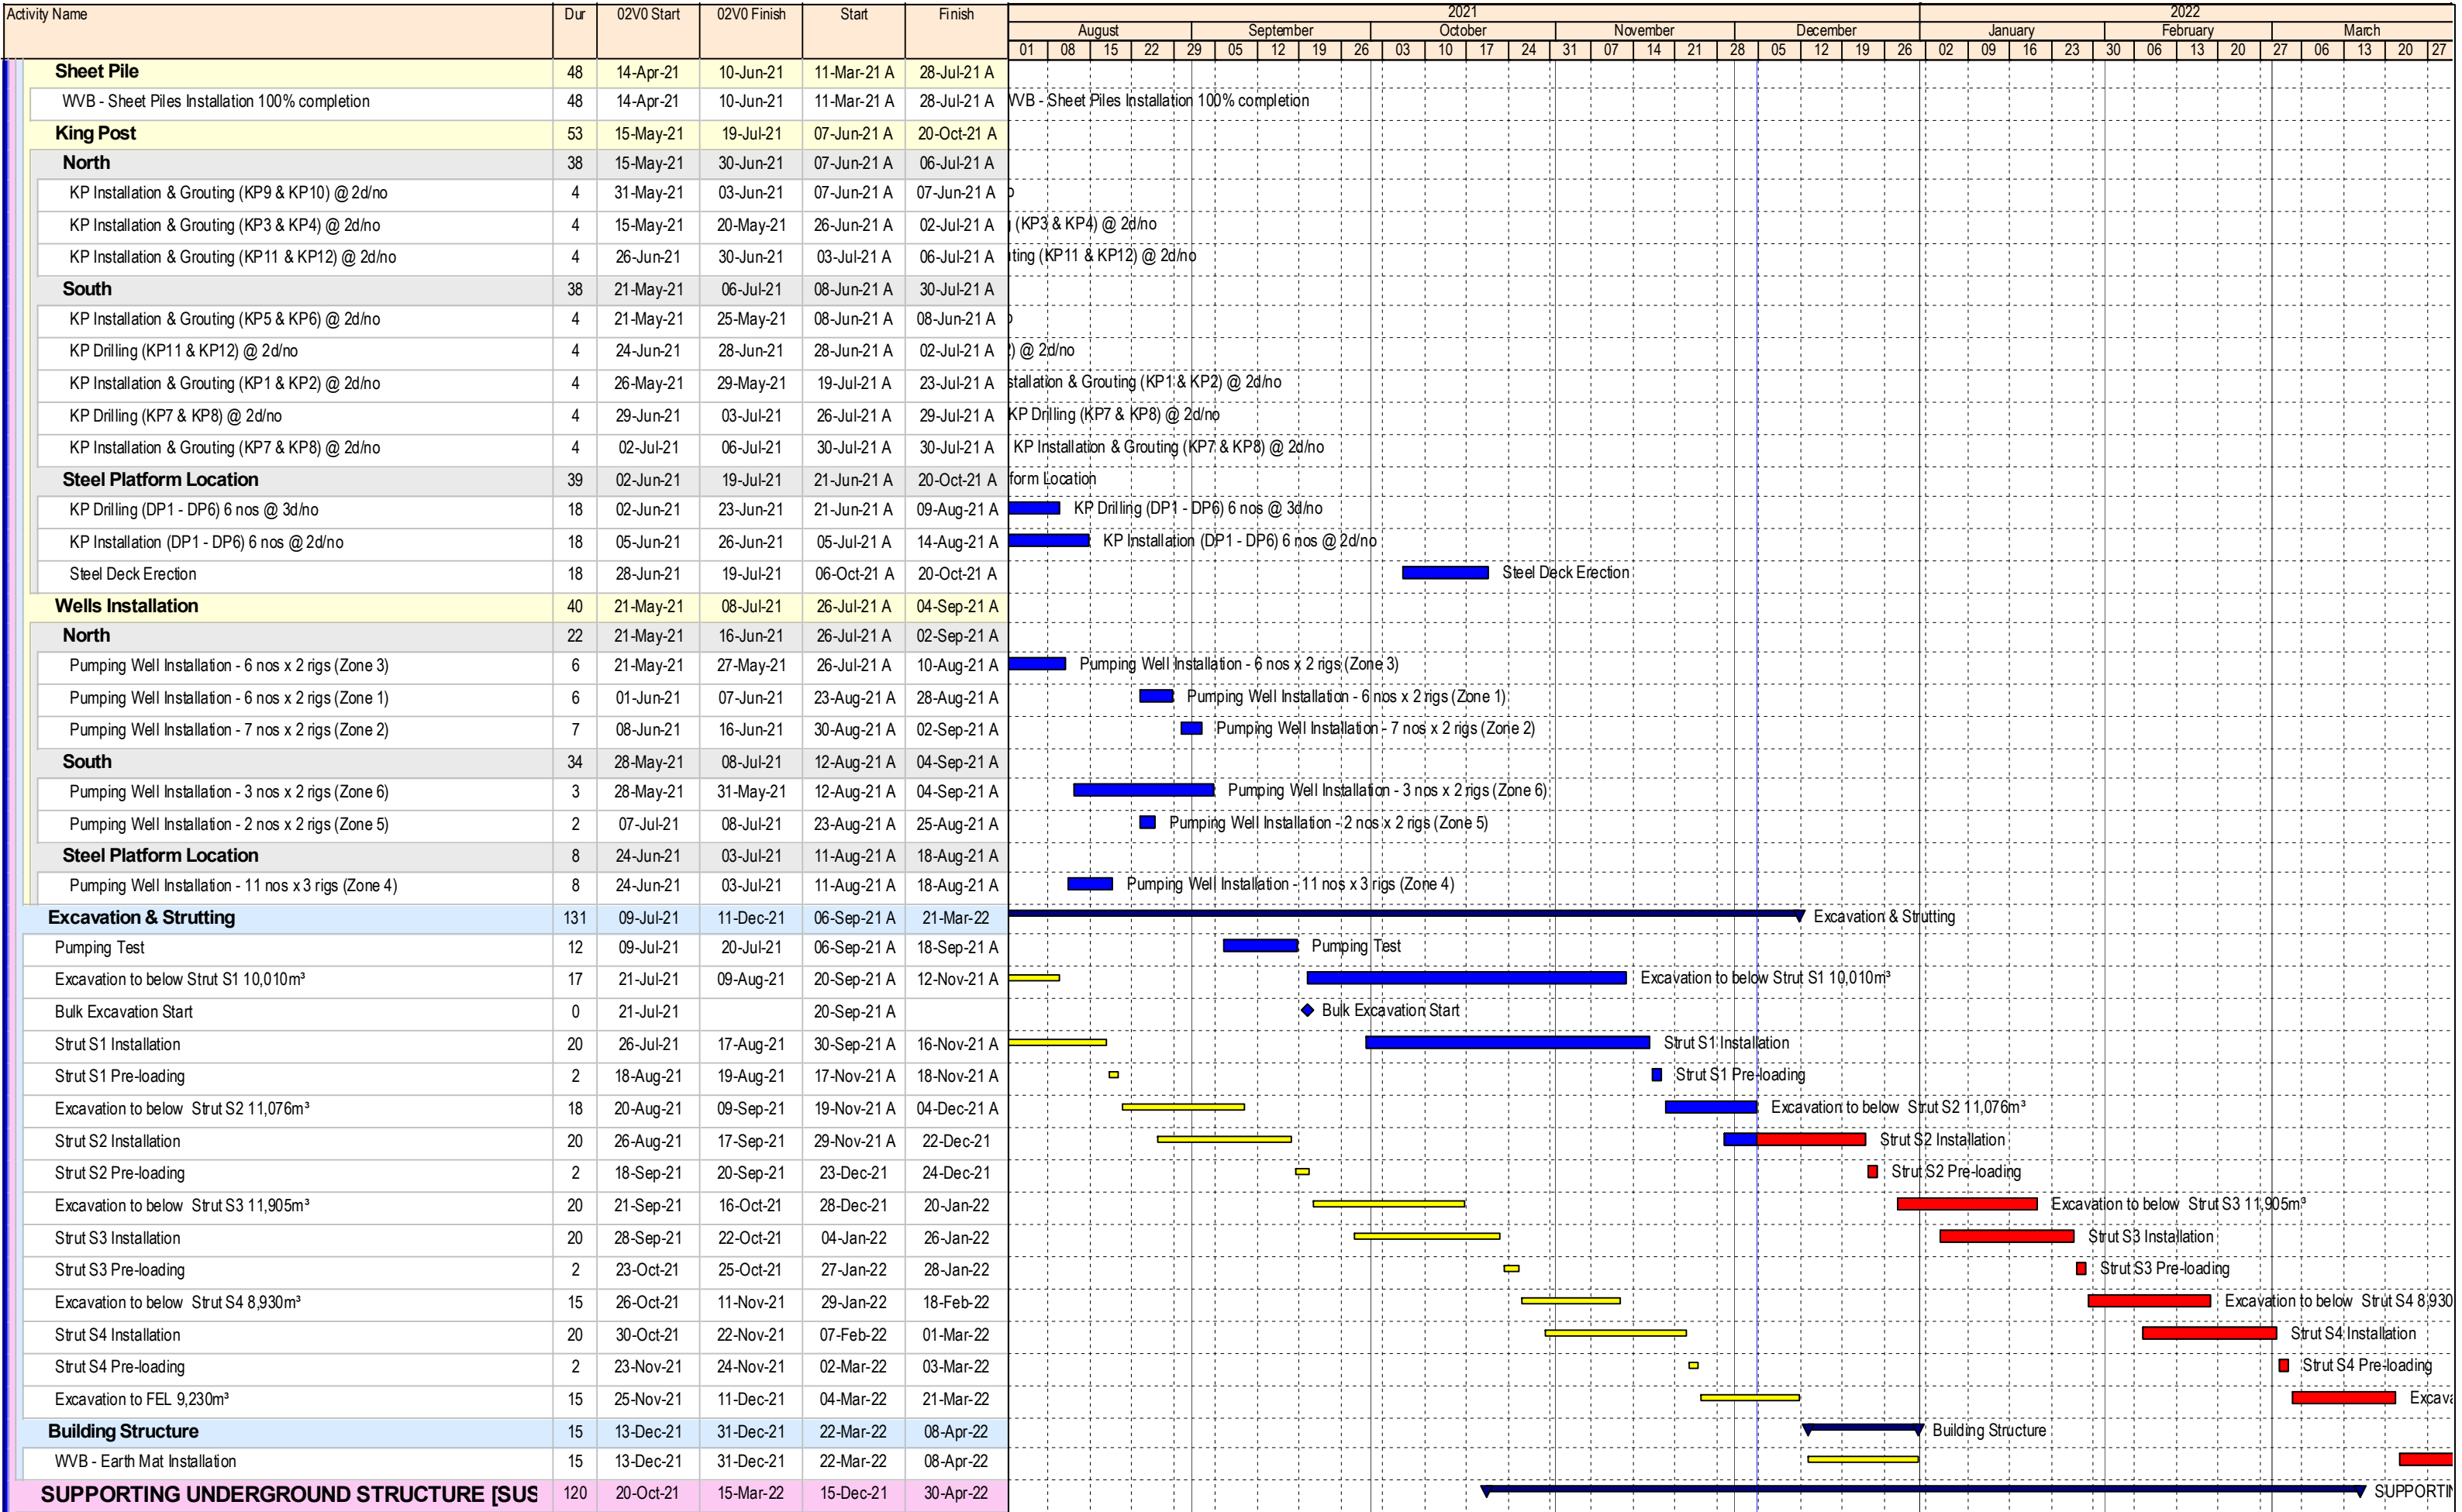

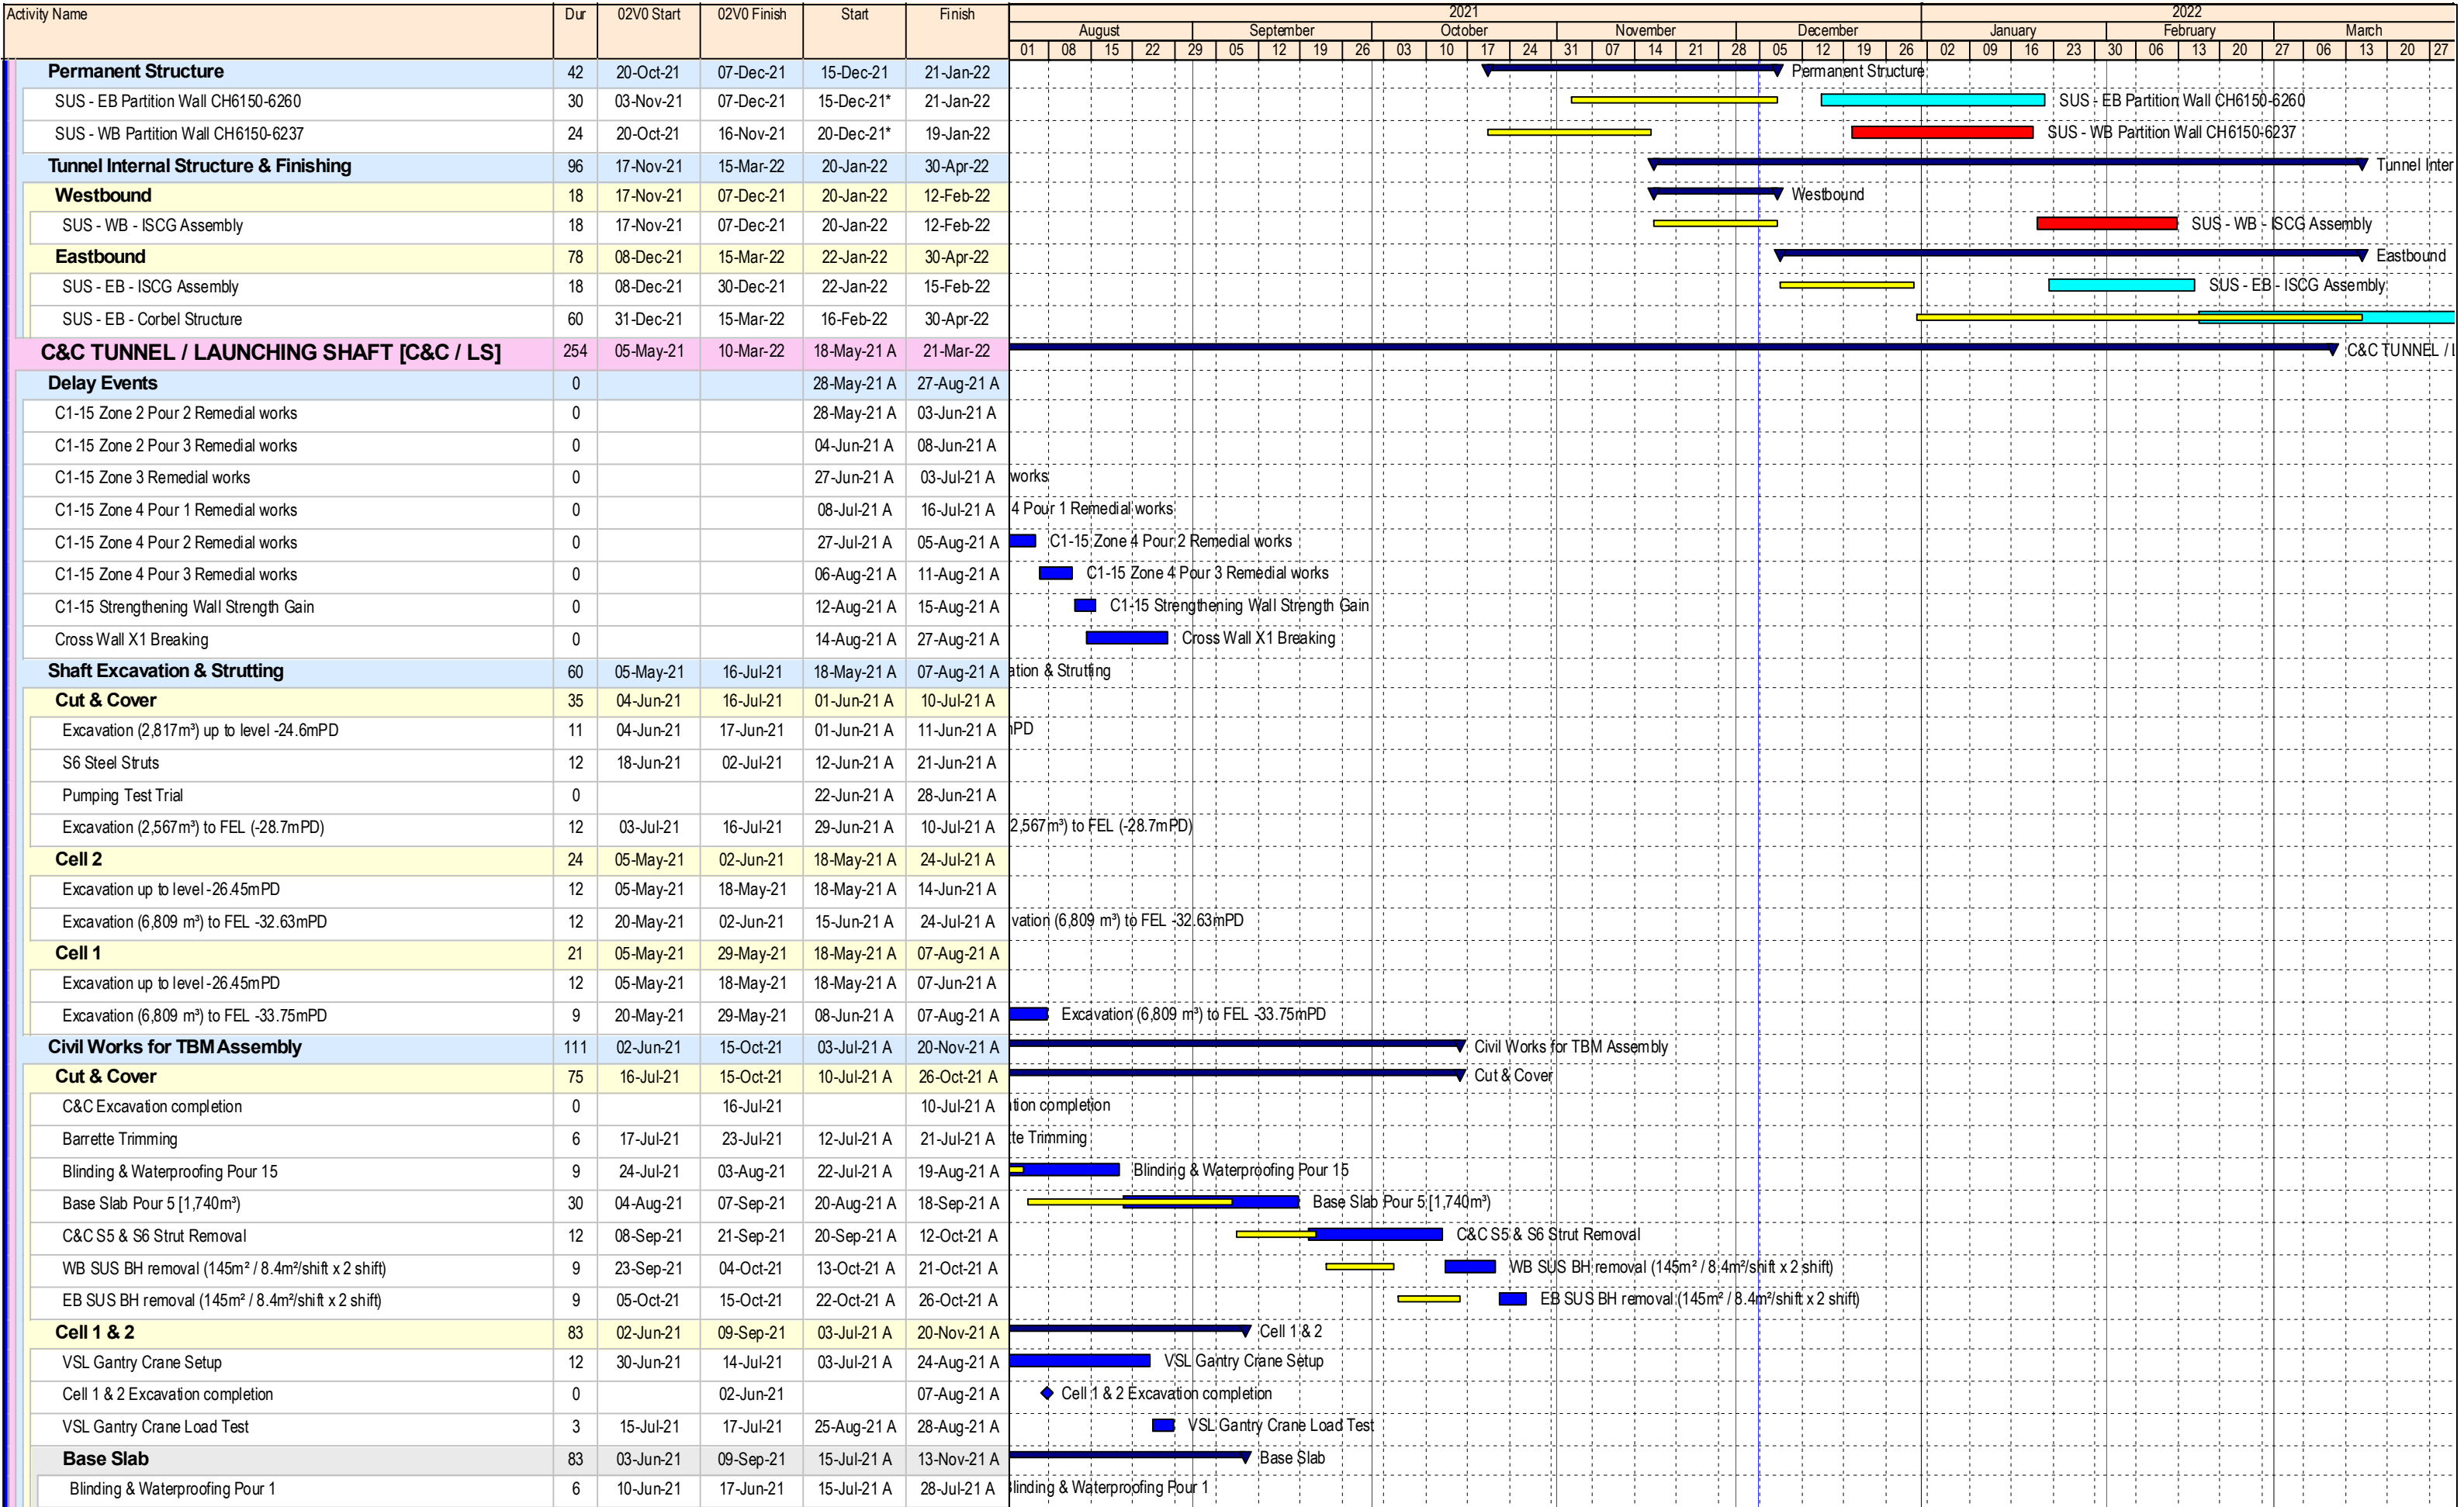

Milestone

Planned Bar

Critical Activity

Actual Milestone

Actual Work


Baseline Milestone

Baseline Bar


Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

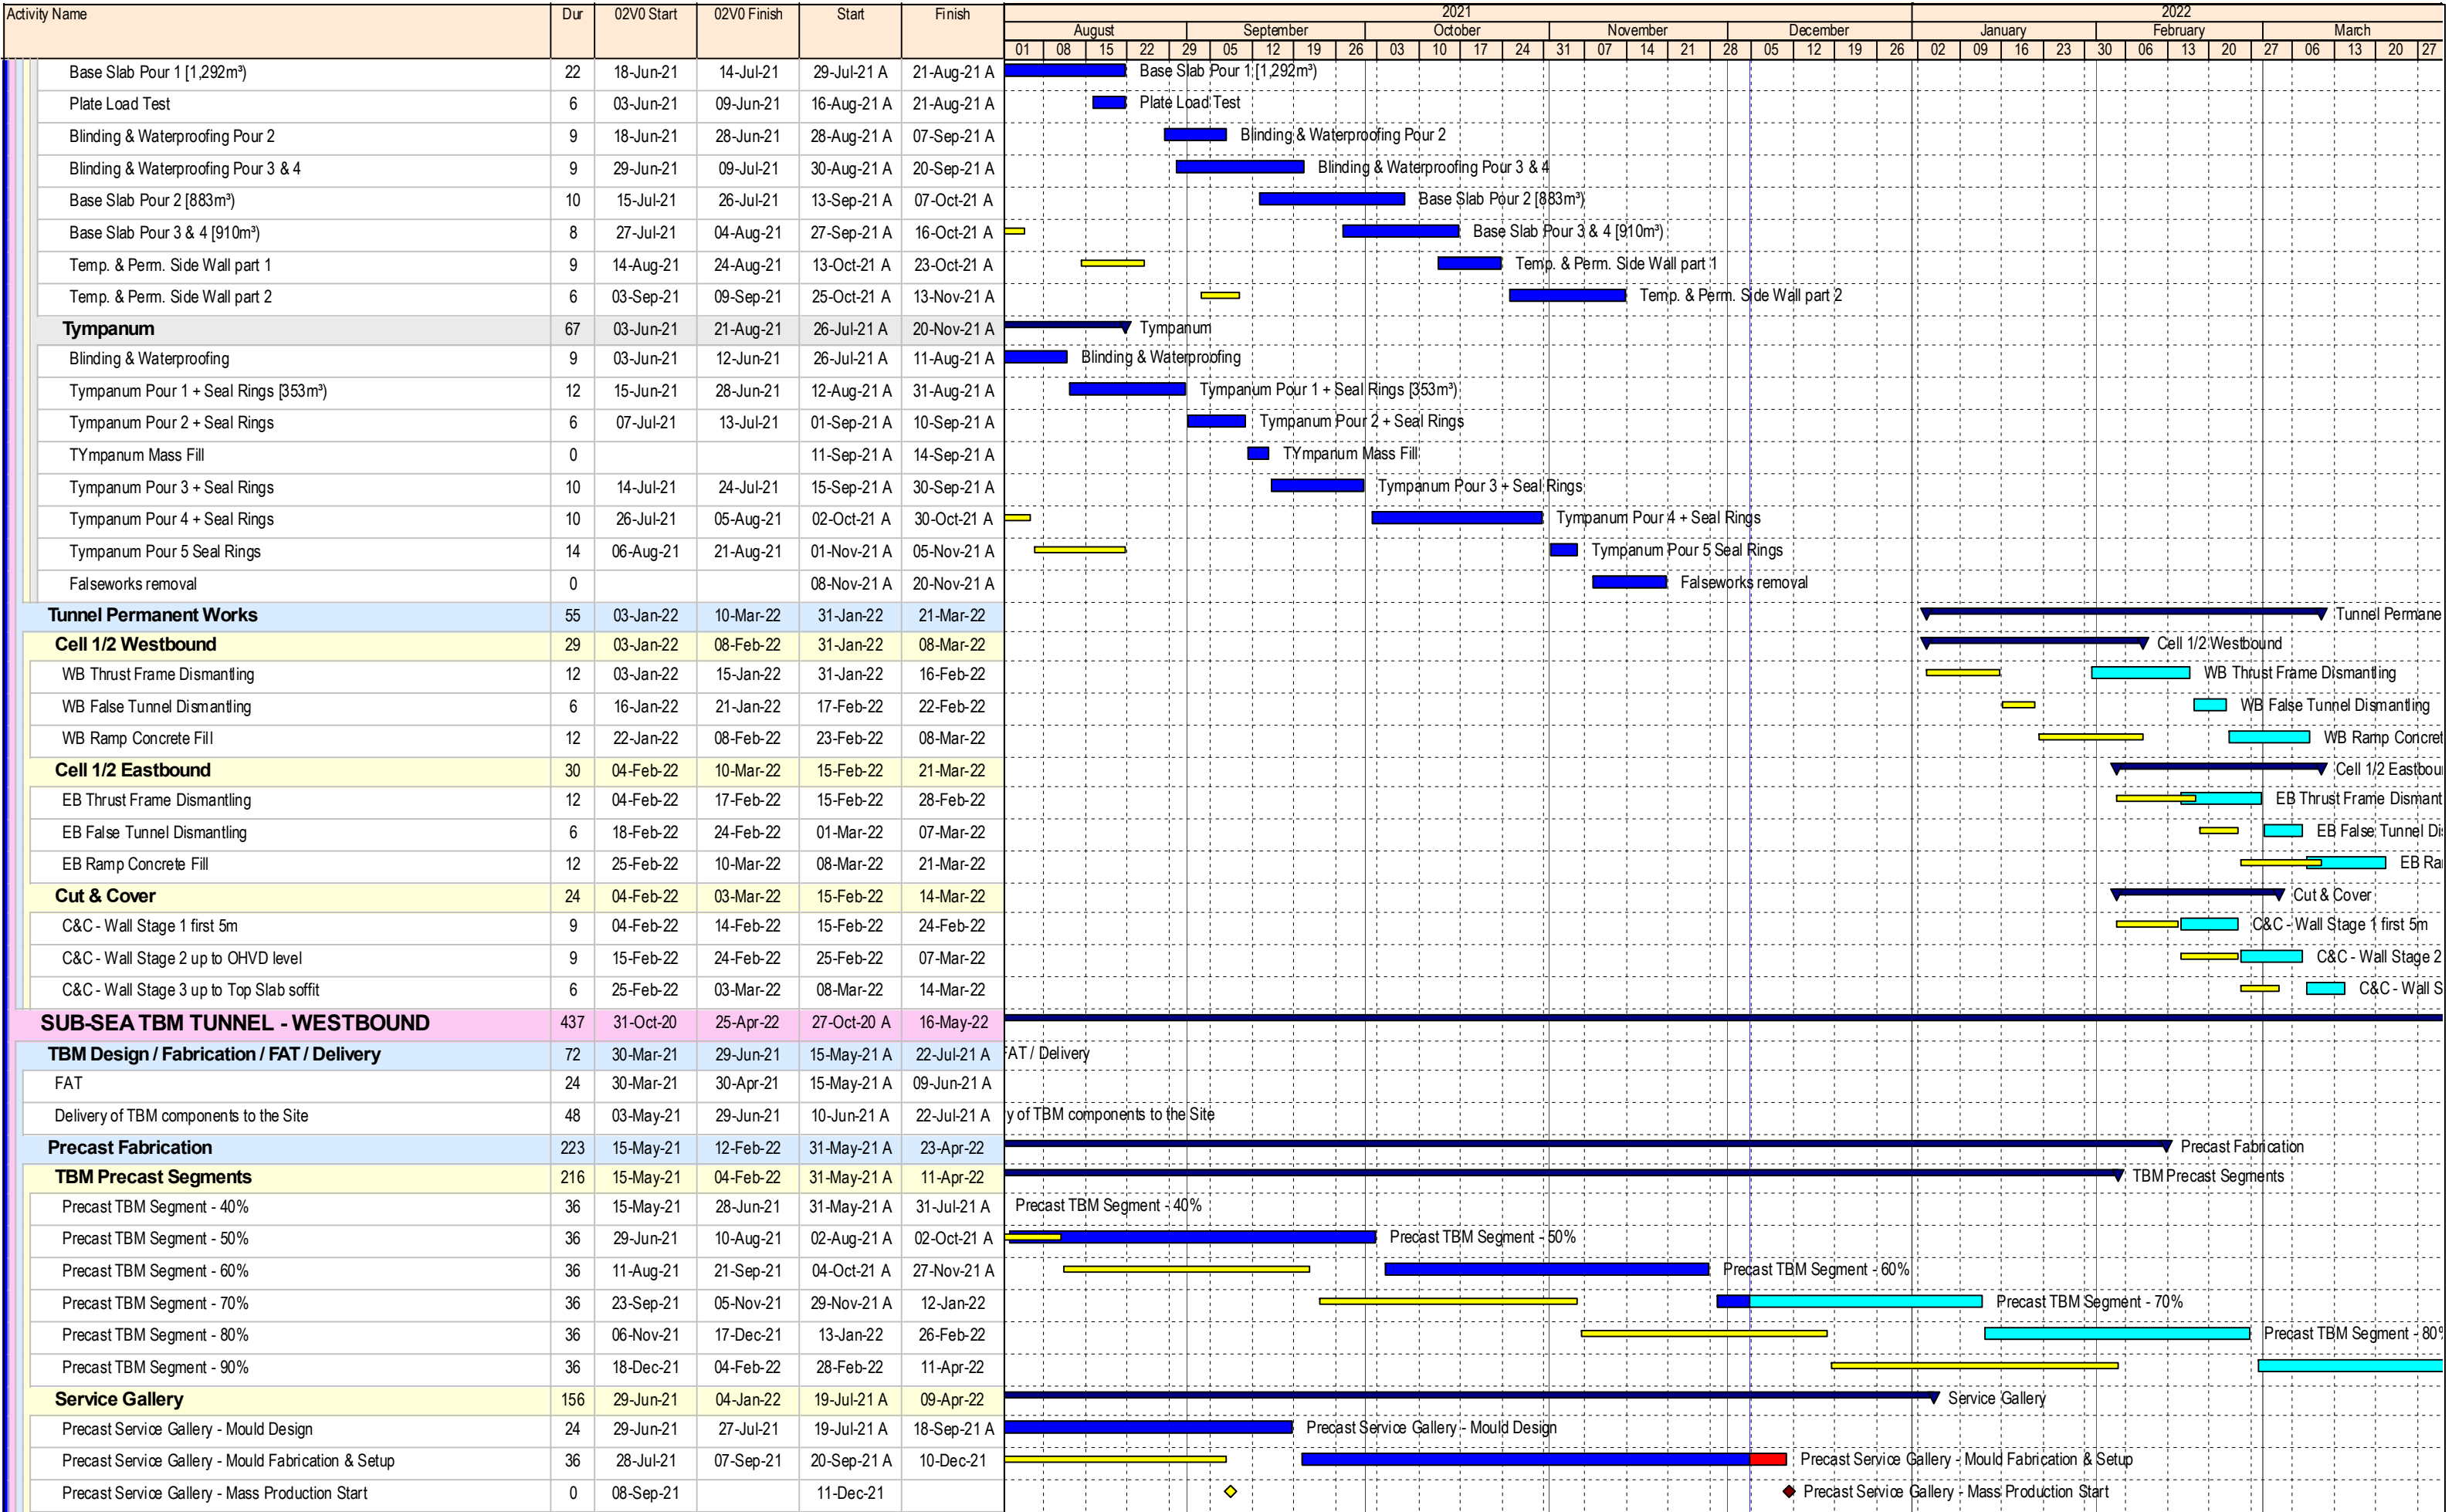

Page 25 of 29

Data Date: 04-Dec-21

◆ Milestone

Planned Bar

Critical Activity

◆ Actual Milestone

Actual Work

◆ Baseline Milestone

Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES

TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 26 of 29
Data Date: 04-Dec-21

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Nov-21)

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Page 27 of 29

Data Date: 04-Dec-21

◆ Milestone

Planned Bar

Critical Activity

◆ Actual Milestone

Actual Work

◆ Baseline Milestone

Baseline Bar

Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Nov-21)

BOUYGUES

TRAVAUX PUBLICS

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

